



March 27, 2026

TO: DISTRIBUTION

FROM: ALBERT SOLIZ,
DEPUTY EXECUTIVE OFFICER,
PROJECT MANAGER

SUBJECT: DIVISION 20 PORTAL WIDENING
QUARTERLY PROJECT STATUS REPORT
FY26 Q3 MARCH 2026

Enclosed herewith is the Quarterly Project Status Report for the Division 20 Portal Widening Turnback Project. This report contains the Los Angeles County Metropolitan Transportation Authority's (LACMTA) representation of the Division 20 Portal Widening Turnback Project status for the period ending March 31, 2025.

If you have any questions regarding this report or its supporting information, please contact Alexander Lampros, Deputy Executive Officer, Program Control at (213) 407-0978.

Enclosure

Division 20 Portal Widening Turnback Project

QUARTERLY PROJECT STATUS REPORT



March 2026

TABLE OF CONTENTS

Project Overview 3

Executive Summary 4

 Project Scope 6

 Risk and Management Issues..... 7

 Construction Progress Photos 8

Project Status 17

 Project Schedule..... 17

 Project Summary Schedule 18

 Planned vs. Actual Progress..... 19

 Key Activities and Milestones Six-Month Look Ahead 20

 Critical Path 20

 Risk Management Narrative 21

 Project Cost 22

 Project Cost Status & Analysis 22

 Cost Contingency Drawdown & Analysis..... 23

 Summary of Construction Contract Modifications 24

 Financial/Grant 25

Project Staffing 26

Quality Assurance Report 29

Environmental 30

Appendix 31

 Chronology of Events.....31

PROJECT OVERVIEW

Project Background

Per the project's Full Funding Grant Agreement (FFGA) for Section 1 of the Westside Purple Line Extension (WPLE), Metro is obligated to operate service at four-minute headways on the future Metro Purple Line. As a result of reduced headways, Metro will need to coordinate headways for Purple and Red Lines in the shared trunk portion of the tunnel system from Wilshire Vermont Station through 7th and Metro and Union Station.

Currently, the Metro Red/Purple Line trains "turn-back" at Union Station, reversing direction from east to west. The current minimum headway that can be achieved at Union Station is approximately four-minute service for combined Purple/Redline service (or seven-and-a-half minutes on the branches), but that will become impracticable and less efficient once the Westside Purple Line Extension begins operating and more trains are using the same tracks.



At present, non-revenue Metro B (Red)/ D (Purple) Line trains proceed south of Union Station and through the portal just south of the US 101 Freeway before entering a complex set of switches in the Division 20 rail yard. To increase train speeds and ensure the reliability of operations, the existing tunnel portal must be widened to accommodate additional tracks and switches that diverge to become the turnback and yard leads.

The trackwork at the portal will be reconfigured to connect to new storage tracks to the south and west side of the yard. The reconfiguration of the yard will not preclude a potential future revenue station at 6th Street. Construction and pre-revenue testing of the portal widening and turnback facility must be completed before WPLE Section 1 opens for revenue service.

EXECUTIVE SUMMARY

Metro awarded the Division 20 Portal Widening Turnback Facility Contract C1136 on February 25, 2020, and issued Notice to Proceed (NTP) on April 8th, 2020. Contract C1136 is a Design Bid-Build (DBB) contract with a 52-month forecast for construction.

Status through March 2026:

Division 20 Portal Widening Turnback Facility overall project progress is 88%. Project commitments and expenditures through March 2026 indicate that the current budget does not require increasing contract modification authority for the next reporting period.

The project's substantial completion was previously forecasted at the end of 2025, in addition, the project schedule continues to be updated as the project team is working with the contractor to develop an updated schedule and in coordination with the completion of Westside Purple Line Extension Section 1 (PLE1). The project team continues to work with Tutor Perini to update the schedule, and to review mitigation opportunities to improve the schedule and reduce impacts to the project budget.

Current Quarterly Accomplishments

Center Street / Temple Street Entrance

- Installed gate and fences.
- Coordinated energizing of light poles at JK / TP Street.

East Portal / East Section / East Slab Areas

- Performed final excavation after demolition of the existing portal.
- Compacted and fine graded under slab areas in East Section 1.
- Poured mud slab in East Section 1.
- Installed micropiles on the east side of SD pipes, phase 3.
- Fine graded East Slab Pour 2 / Section 1.
- Fine graded East Slab Pour 4 / Section 3.

East Wall / Portal Interface / Bungalow Area

- Installed lighting ductbank and manholes.
- Backfilled lighting ductbank and manhole work.

EXECUTIVE SUMMARY *cont'd.*

East Walkway

- ETS conduit installation on the east walkway is ongoing.
- Exit Stairs Area- Installed and welded exit stairs

Crossing 4A Lighting

- Excavated, installed, and backfilled lighting ductbank and manholes after AR down.

South Ladder Tracks

- Excavated and installed Line CS-13A work.
- Excavated, installed, and backfilled ETS ductbank work.
- Performed termination work at existing Switch Assembly #7.
- Excavated, installed, and backfilled lighting ductbank and manholes across the south ladder tracks.

Road D / South Ladder Turnouts

- Demolished remaining south ladder tracks and turnouts.
- Performed sawcut and demolition of remaining AC paving.

North Storage Yard

- North Storage Yard work is ongoing.

Drainage Work Areas

- SD / drainage work is ongoing.

Mainline Track Area

- Mainline track demolition and new mainline track installation are ongoing.

Bungalow A

- CO 284 civil work is ongoing.

Project Scope

The scope of work is composed of several major construction elements, each with its own subset of work components. The major elements are portal widening; First Street Bridge modification & seismic upgrade trackwork; power substation; system installation and integration and not precluding future 6th Street station.

Turnback Facility (3 pocket tracks)

- Mainline Trackwork and Special Trackwork Construction
- Signals and Communication Lines (CCTV, PA, Telephone, Radio, Fire Alarm) and New Duct banks
- Portal Widening (Shoring, Excavations, Soil testing and Soil Disposal)
- Modifications to 1st Street Bridge
- Two Storage Yards (North and South) with Cleaning Platforms
- Demolition of MOW 61A and Viertel's Buildings
- Center Street Improvements
- Surface Parking at Viertel's Tow Yard
- Utility Protection and Relocation
- Drainage
- Yard Perimeter (Retaining Walls, Fences, and gates)
- Access Roads
- TPSS Pads and Connections (Removal of Existing TPSS)
- Yard and Surface Parking Lighting
- Trackwork/Emergency walkway Modifications at East US Double Crossover
- Communications Conduits for Metro Center Project
- Yard Tower – Control Room Equipment
- System Integration Testing and Start-up

Adjacent Projects Coordination

- Early Demolition Contract
- TPSS Early Procurement Contractor (C1184)
- Pickle Works Building Demolition by City
- Early Construction of Duct banks
- Sixth Street Bridge
- Metro Center Street Project Construction
- Link US
- Purple Line Extension Section 1 – Rail Welding
- Eastside CTS Bus Bridge by Regional Connector
- Demolition of MOW Buildings B&C
- MOW 61A Equipment Relocation, Vacation and Abatement
- Shop Building Expansion
- Metro Rail Car Delivery Program
- Southern California Gas Co.

Project Facts

- Approximately 16 miles of duct banks installation
- Track installation of 28,217 feet of ballasted track and 4,294 feet of direct fixation tracks
- Approximately additional 6 acres added to the Division 20 yard Additional storage capacity of 120 train vehicles

Risk and Management Issues Management Issues

1. MOD No.20 (CN006) - *executed*

- Major design changes (e.g., track spacing)
- Work not completed from previous contracts (early utilities)
- Specs and criteria changes/updates
- Responses to bidders' questions
- Completed negotiations with Contractor

2. Long Lead Items

- Contract provisions for long lead items
- Identify Multiple Suppliers
- ~~Weekly meetings with Nortrak - *completed*~~
- ~~Shortage of fiber optic cable - *completed*~~

3. Modification of Construction Scope within the Yard during Construction

- Modifications to design should be avoided. However, if mitigation is required, timely design changes and review cycles to be implemented
- Alert contractor to upcoming changes to avoid rework and obtaining contractor input to help mitigate time delay caused by RFI process

4. Maintaining Train Operations during Construction

- Develop intricate staging plan with Metro Operations & Maintenance approval
- Allow for single tracking to the yard to expedite construction delivery
- Develop and maintain an O&M plan during construction & a Metro Ops staffing plan
- Close coordination with contractor

5. Install Conduits to Regional Connector to Bus Bridge Start. - *completed*

- Provide Access to Construction Crew for Installation of Communications Fiber, Overlapping with Regional Connector Activities
- Frequent coordination between both contractors
- Collaborate between Metro and both contractors, a solution for temporary connection

~~6. Completion of Design /Construction by DWP to Energize New TPSS - *completed*~~

- ~~Active and continuous coordination/bi-weekly meetings with DWP~~

7. Significant number of Contractor questions regarding the design

- Design inconsistencies noted between drawings and details causing the contractor to submit multiple RFIs.

8. MOD No.151- *executed*

- Time Impact 3 Settlement for Schedule Impacts, Extension of Time Impacts, and associated costs related to, among other items, the 1st Street Bridge/1st Street Viaduct

9. MOD No.161.1- *executed*

- Resequenced schedule to achieve Substantial Completion by December 31, 2025

10. MOD No.162.1- *executed*


- Time Impact 4 Settlement for Schedule Impacts, Extension of Time Impacts, and associated costs related to, among other items, revised Contract Milestones

Construction Progress Photos


Portal Area Aerial Fly Over



North Storage Area Aerial Fly Over

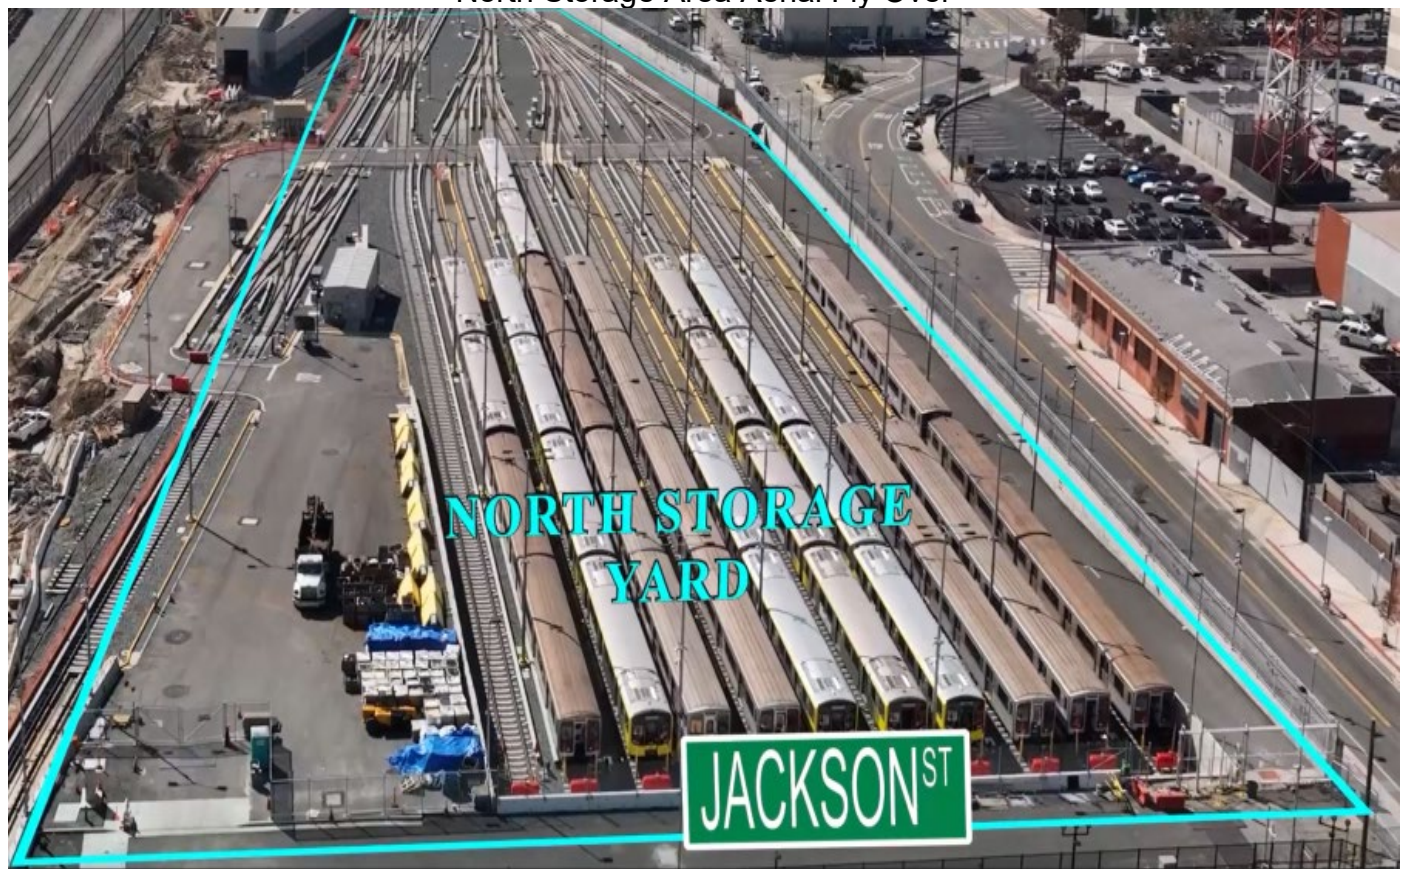

Construction Progress Photos *cont'd*
South Storage Area Aerial Fly Over

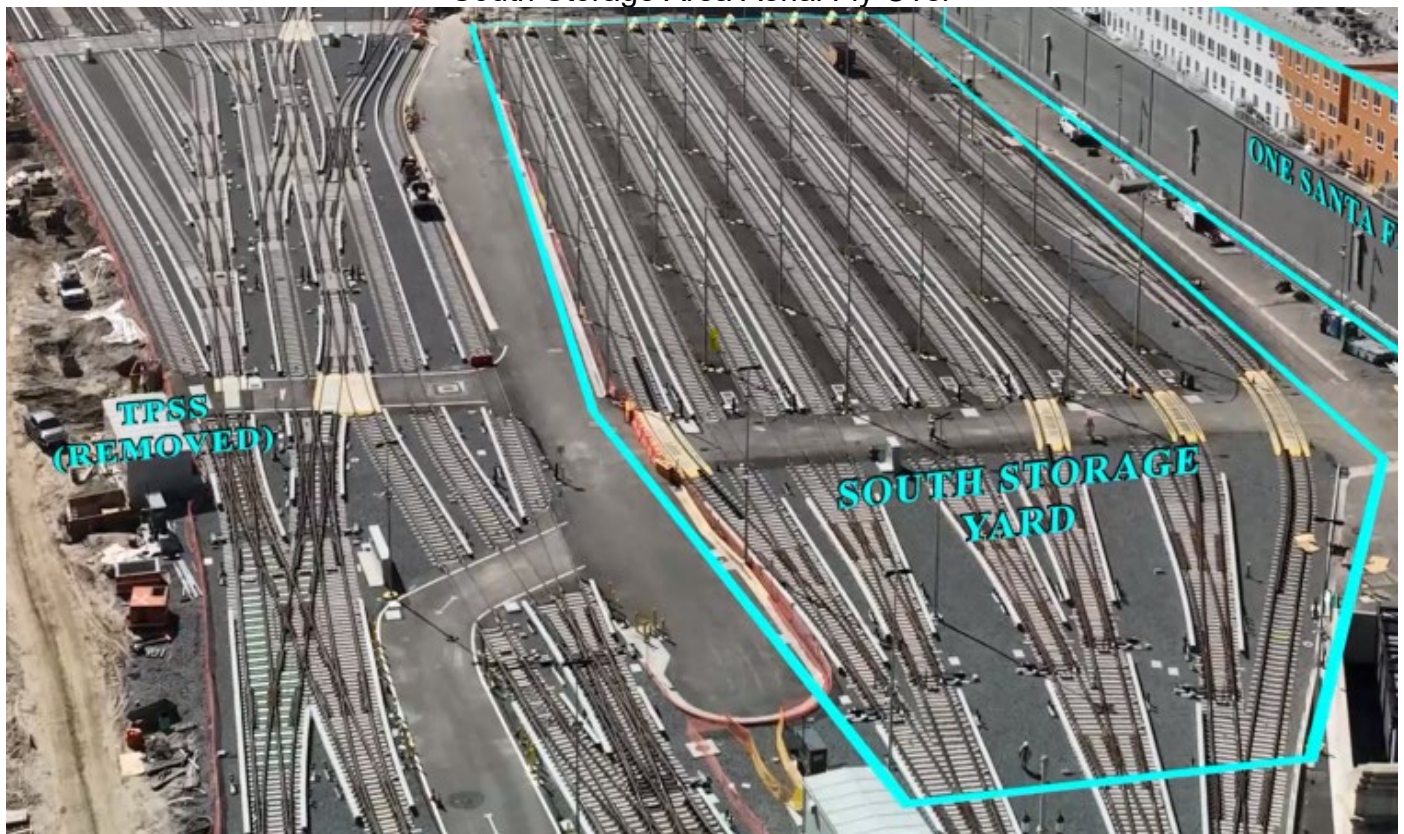


Turnback and Track Tail End Area Aerial Fly Over



Construction Progress Photos *cont'd*
Installed gate and fences Road C/G



Energizing of light poles at Center and Temple Streets

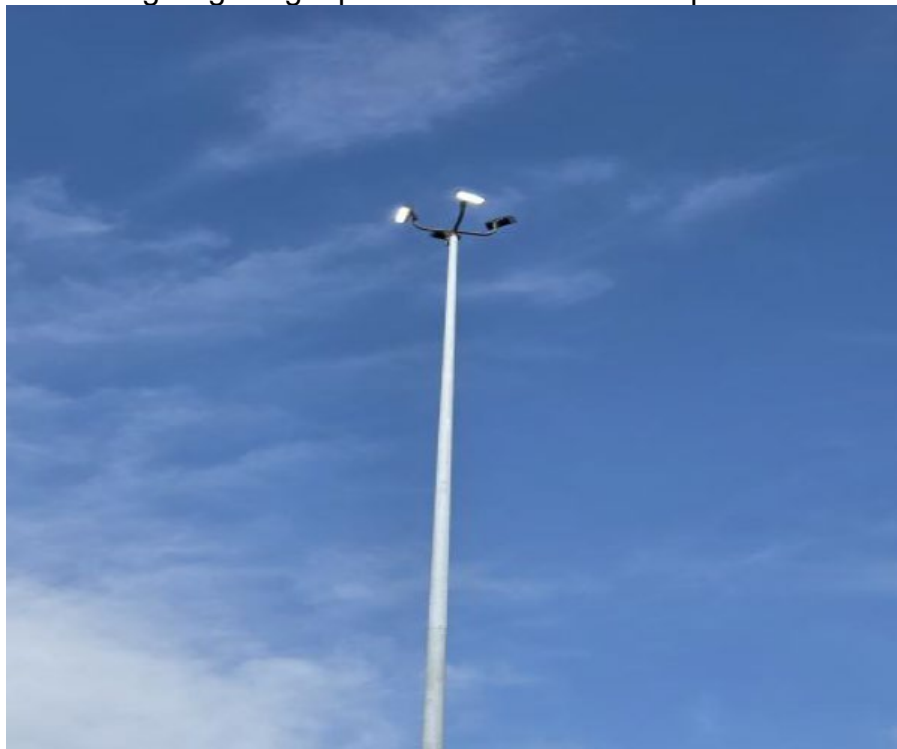

Construction Progress Photos *cont'd*

Installation of Micropiles



840 Ducommun St
Los Angeles CA 90012
United States

Thursday, January 8, 2026 at 11:47:15 AM

Construction Progress Photos *cont'd*

East Portal invert slab grading.



Install/pouring lighting ductbank



Construction Progress Photos *cont'd*

Grading under the east walkway near Road E.



Excavating for the lighting DB




Construction Progress Photos *cont'd*

South Ladder Tracks Line CS-13A work



Termination work at existing Switch Assembly #7

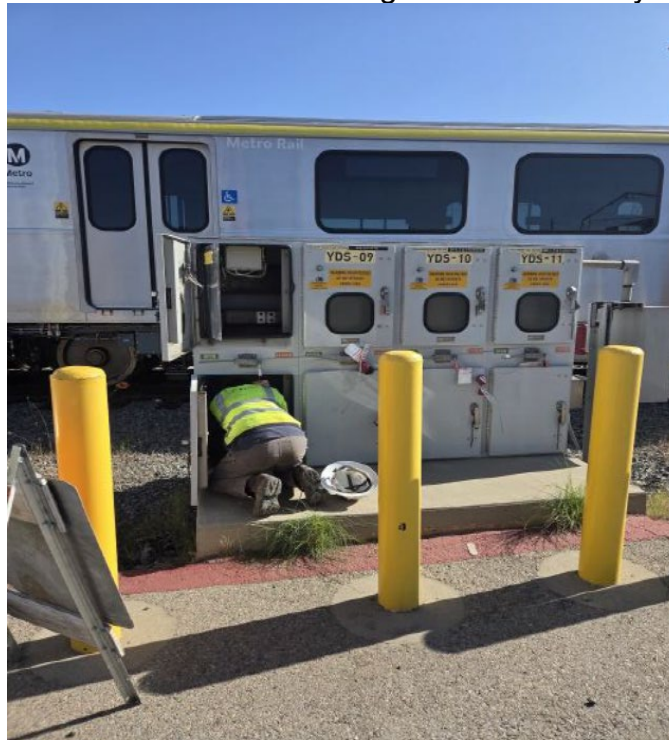


Construction Progress Photos *cont'd*

Installed LA-4 lighting duct bank



SD Line L3.1A concrete encasement

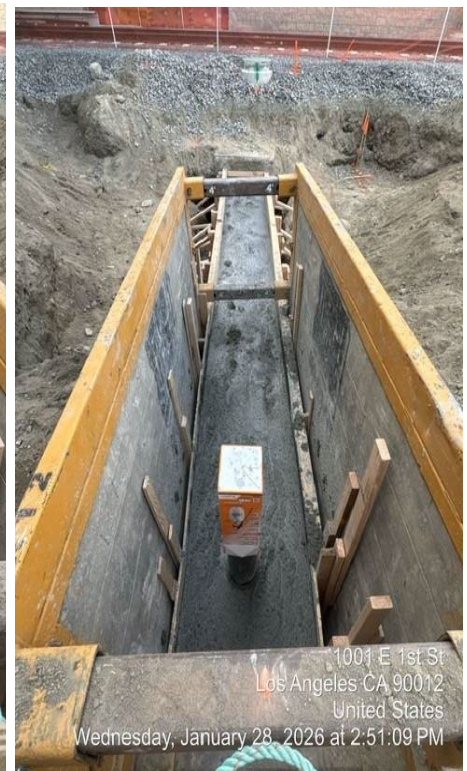


Construction Progress Photos *cont'd*

Installed contact rail ductbank at mainline track



Demoing cable out of manhole C-15 mainline track

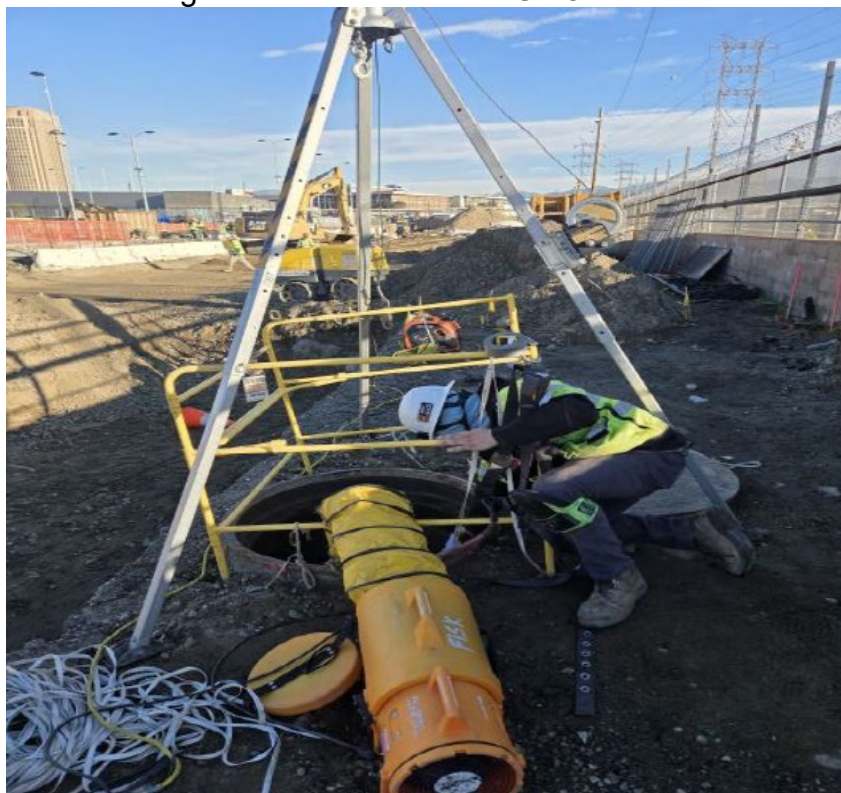

PROJECT STATUS

SAFETY

C1136 (TPC)

- Ongoing monitoring of construction activities to ensure safety compliance.
- TPC (contractor) reported 1,590,978 total man hours period ending March 2026 with 1,242 calendar days without a loss time incident.

C1184 (C3M)

- Participated in meetings, reviewed, and approved submittals.
- Conduct safety and security sweeps.
- C3M and their subcontractors continue to report zero incidents period ending December 2025.

PROJECT SCHEDULE


Project Summary Updates

The Notice to Proceed for the main construction contract was issued in April 2020. The Notice to Proceed for the main construction contract was issued in April 2020. Since then, the major project elements that have been completed are: demolition and excavation of existing structures, City of Los Angeles 1st Viaduct and Bridge modifications and repairs, Center St improvements, North and South Storage Yards and tracks, Traction Power Substation (TPSS) and Emergency Backup Power Supply (EPBS) installed and energized, new train control bungalows B, C and Pockets, Portal West and East demolitions, reconstruction of new plinths, AL tracks installed, (2) 144 pair fiber optic cable pulled from Union Station TC&C to Yard Tower and recently the completion of Cutover A.

Work in Q3, Fiscal Year 26 continues with gate and fencing installation at Center and Temple streets, and energizing light poles by Jackson Street. The East Portal East Section and Slab Areas performed final excavations and demolition, poured mud slabs, installed micropiles and fine graded slab pours at sections 1 and 3. At the Portal Interface by the East Wall and Bungalow Area continued with lighting ductbank and manholes, the East Walkway had ETS conduit installation and installed and welded exit stairs. In the south end of the yard, the South Ladder Tracks excavated and installed Line CS-13A and ETS ductbank, backfilled lighting ductbank and manholes, and performed termination work at existing Switch Assembly #7. Road D and South Ladder Turnouts demolished remaining south ladder tracks and turnouts and performed sawcut and demolition of remaining AC paving. The Mainline Track Area continues with demolition and track installation while work continues to progress through the North Storage yard and Storm Drain areas. Bungalow A, located at the southernly end of the Division 20 yard has civil commences to prepare the site for civil work.


As of FY26 Q3, and in coordination with the completion of Westside Purple Line Extension Section 1 (PLE1), the completion of Cutover A, which supports PLE1 RSD requirements, allows for the storage of rail vehicles in the north storage yard. The project team continues to work with the contractor to develop an updated schedule to achieve substantial completion.

Project Summary Schedule

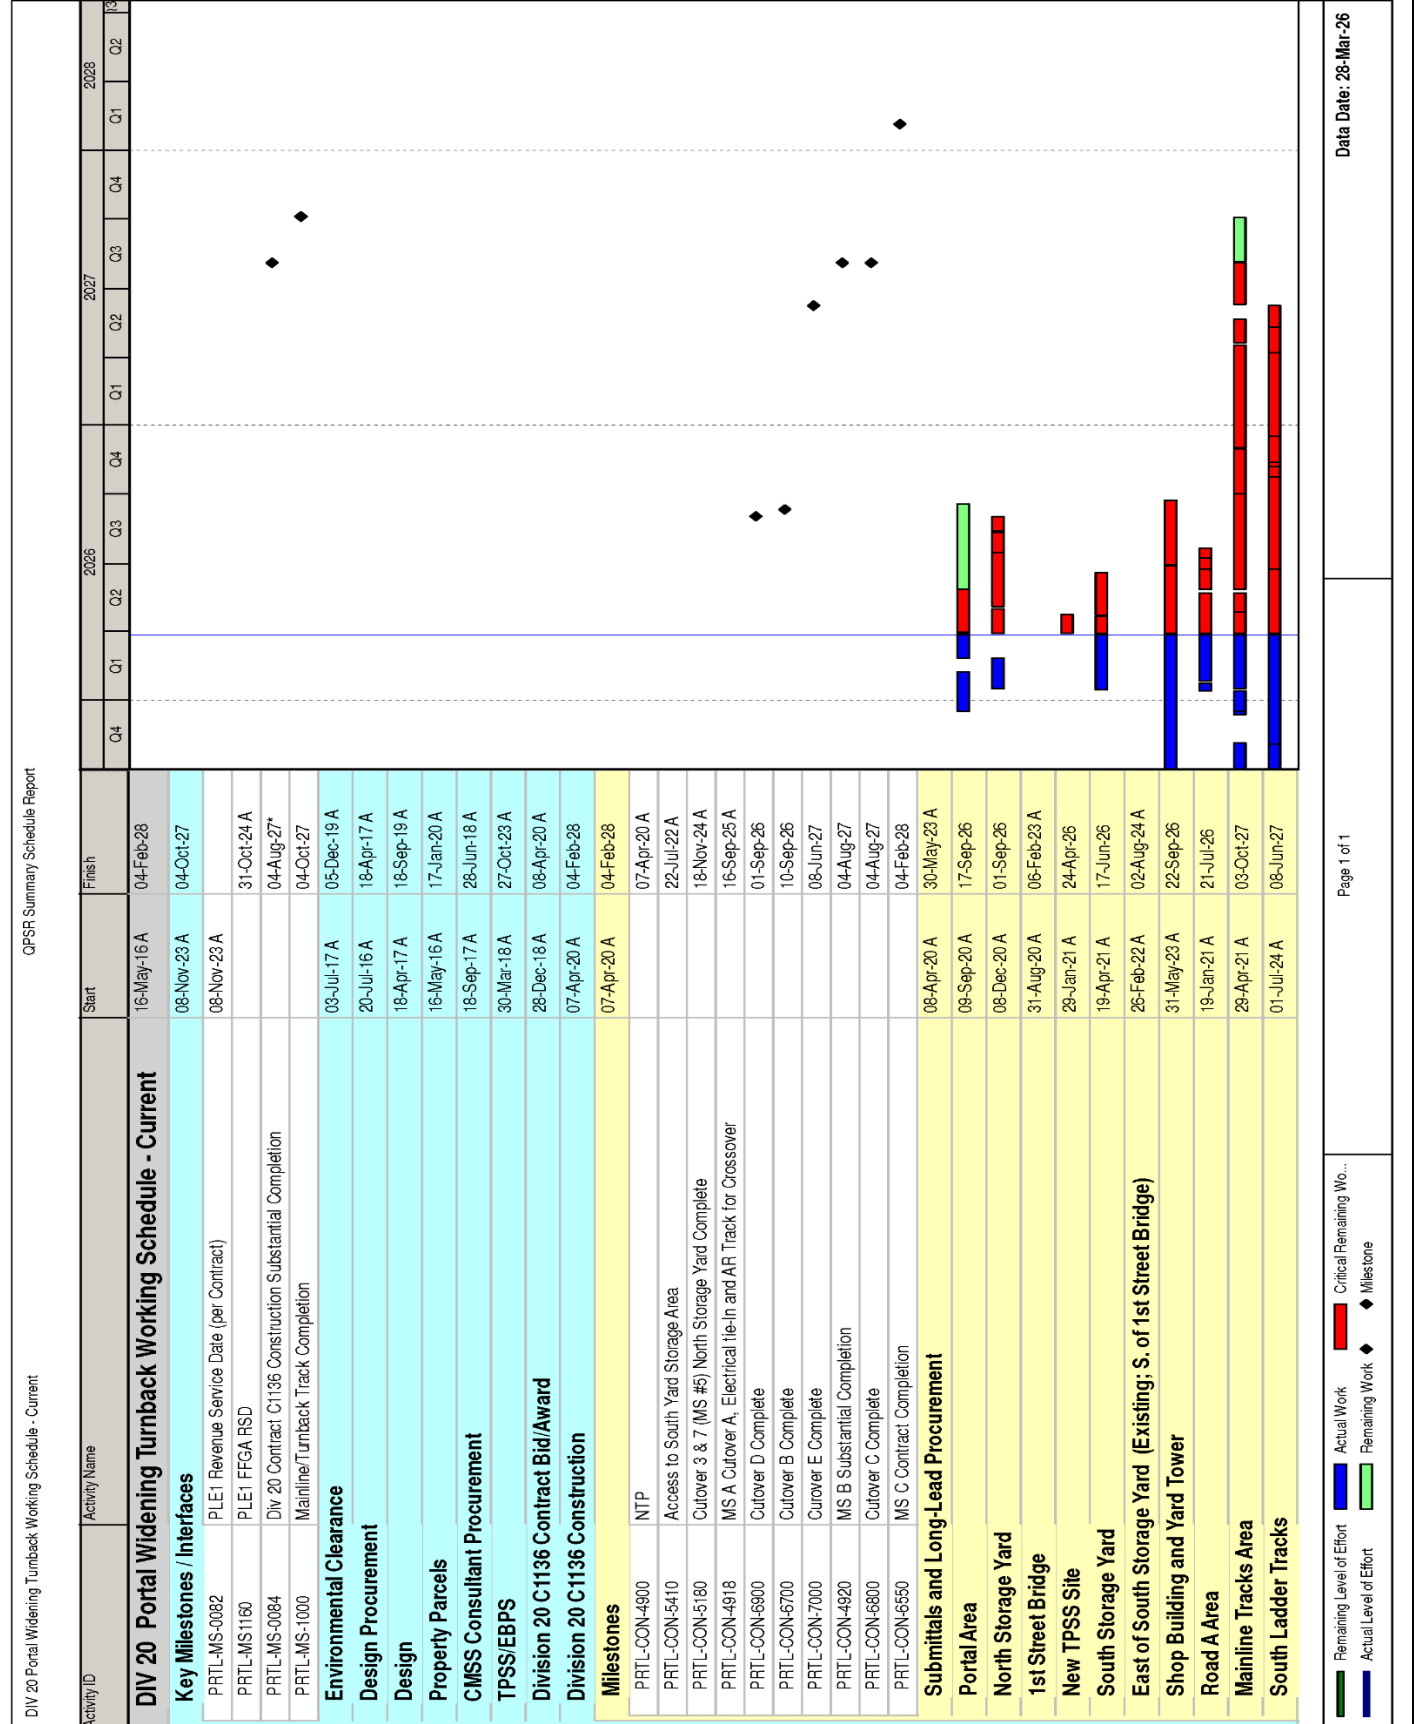

Planned vs. Actual Progress

C1136 Construction Progress

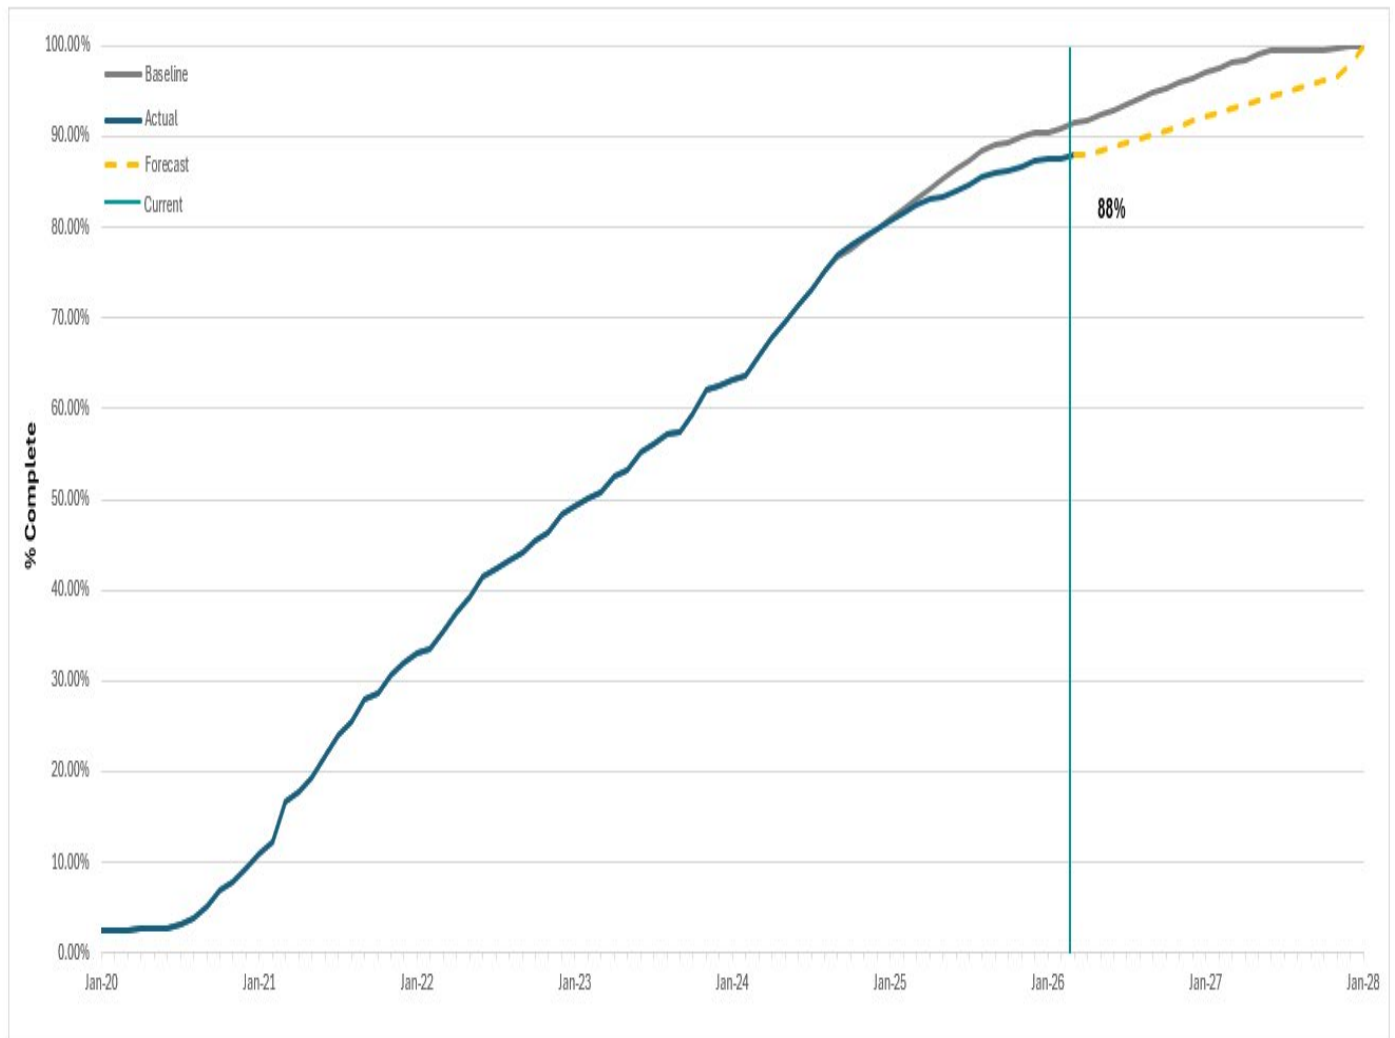

The actual overall project progress is 88% versus an early planned of 95% (or late planned of 90%) through March 2026. The progress curves represent the physical progress of work performed to complete the current contract. The early and late planned % curves are based on the Contractor's schedule dates from the approved baseline schedule.

The physical progress percentage excludes non-construction items such as contractor's construction mobilization costs and all general requirement costs not tied to construction work effort.


Key Activities and Milestone Six-Month Look Ahead

Milestone Date	Apr-26	May-26	Jun-26	Jul-26	Aug-26	Sep-26
C1136 Portal Widening Turnback						
Cutover B - Mainline - Install Track					☐	
Cutover B - Mainline - Install Train Control					☐	
Cutover C - TPSS by EAST PORTAL - Pull/Terminate +/- Cables	☐					
Cutover C - Mainline - East Cross Over - Install Train Control	☐					
Cutover C - Mainline - East Cross Over - SIT			☐			
Cutover C - East Portal - Form/Pour Portal Walls					☐	
Cutover C - East Portal - Form/Pour Emergency Walkway						☐
Cutover D - South Yard Storage - NSY SIT			☐			
Cutover D - South Yard Storage - SSY SIT						☐
Cutover D - South Yard Storage - Complete						☐

	MTA Staff		MTA Design Consultant		MTA Board Action
	Other Agencies		C1136		New Date
			C1184		

Project Critical Path

The critical path activities are shown in the schedule below.

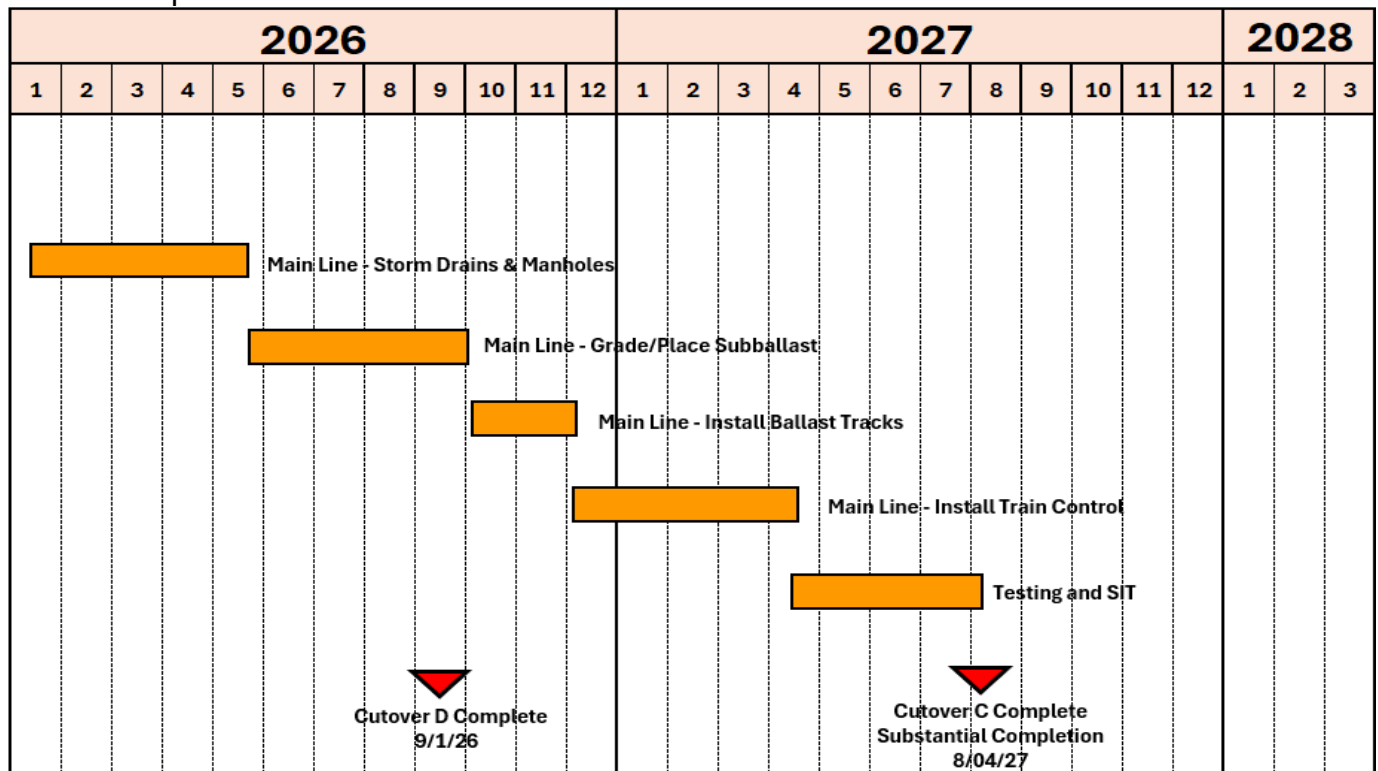

Risk Management Narrative

Summary of Risks

The risk register was last updated in February 2026 during the third (3) quarter FY26 from the previous Quarterly December 2025 report. There is a total of twenty-five (25) active risks remaining to be managed. Of the twenty-five (25) risks, three (3) are scored high (11 to 20 rating), four (4) medium (4 to 10 risk rating), and eighteen (18) as low (less than 3 risk rating).

Top Risks

The table below shows the top six (6) project risks.

Risk ID	Risk Description	Risk Score	Action Items
001	Contaminated water may be encountered which is not in the spec.	15	1. Remove when encountered. 2. Research possible alternative uses for water.
004	Modification to scope of construction within the yard during construction	11	1. Modifications to design should be avoided, but if mitigation is required, timely design changes and review cycles to be implemented. 2. Alert contractor to upcoming changes to avoid rework and obtaining contractor input to help mitigate time. delay caused by RFI process.
013	Metro Ops request to replace an existing Bungalow which would increase costs and could delay schedule.	10	1. Coordinate with Metro Ops. 2. Identify scope of work and performing parties. 3. Proceed with design change if approved. Scope /design to be done by others. 4. Funding provided by Metro Ops . Project Team to mitigate schedule to avoid delays.
011	Encountering unknown and surprise underground utilities and inaccurate as-builts on utilities (Type II DSC) during construction project-wide.	9	1. Contractor will perform potholing. Included in LOP contingency. Updated and improved methods to be put in place and MTA team more responsive .
012	Excessive amount of Cos/rework are affecting the progress of the contract work with potential claims , but are necessary precursors.	9	1. Ongoing mitigation measures.
028	Limited space within work area	8	1. Identify/coordinate additional locations and clearly identify available locations for consideration during bid. 2. Additional sites are being explore.

Newly Identified Risks

No new identified risks for this period.

Actions in the Next Reporting Cycle

Continuous efforts in Risk Management will be made at the next workshop to update the register. Next upcoming Risk Workshop is anticipated before the end of Quarter 4 FY26.

PROJECT COST

Project Cost Analysis

DIVISION 20 PORTAL WIDENING
 LOS ANGELES COUNTY METROPOLITAN TRANSPORTATION AUTHORITY
 COST REPORT BY ELEMENT
 PERIOD ENDING: MARCH 2026
 UNITS IN DOLLARS

PROJECT 865519

DESCRIPTION	ORIGINAL LOP BUDGET	CURRENT BUDGET		COMMITMENTS			EXPENDITURES			CURRENT FORECAST	
		APPROVED	TO DATE	PERIOD	TO DATE	REMAINING BUDGET	PERIOD	TO DATE	% SPENT	PERIOD	TO DATE
EARLY DEMOLITION	\$ 36,350,437.00	\$ -	\$ 39,489,733.12	\$ -	\$ 39,489,733.12	\$ -	\$ -	\$ 39,479,775.17	100%	\$ -	\$ 39,489,733.12
TPSS DESIGN/BUILD	\$ 19,124,984.00	\$ -	\$ 21,908,129.00	\$ -	\$ 21,908,129.00	\$ 1,400,000.00	\$ -	\$ 21,049,868.85	96%	\$ -	\$ 23,308,129.00
PORTAL WIDENING	\$ 447,575,987.00	\$ (567,755.43)	\$ 591,929,416.91	\$ 391,631.00	\$ 591,929,416.91	\$ 12,248,304.97	\$ 1,306,663.66	\$ 538,526,344.85	91%	\$ (6,415,671.55)	\$ 604,177,721.88
TOTAL CONSTRUCTION	\$ 503,051,418.00	\$ (567,755.43)	\$ 653,327,279.03	\$ 391,631.00	\$ 653,327,279.03	\$ 13,648,304.97	\$ 1,306,663.66	\$ 599,055,988.87	92%	\$ (6,415,671.55)	\$ 666,975,584.00
RIGHT OF WAY	\$ 103,210,416.00	\$ -	\$ 106,558,107.88	\$ -	\$ 106,557,513.15	\$ 594.73	\$ 41,496.31	\$ 106,302,927.64	100%	\$ -	\$ 106,558,107.88
THIRD PARTY	\$ 5,000,432.00	\$ -	\$ 10,510,658.59	\$ -	\$ 10,510,658.59	\$ -	\$ 10,037.78	\$ 6,818,271.30	65%	\$ -	\$ 10,510,658.59
PROFESSIONAL SERVICES	\$ 97,708,756.00	\$ 567,755.43	\$ 231,405,342.16	\$ 491,256.92	\$ 223,683,475.08	\$ 36,942,965.45	\$ 3,499,933.73	\$ 195,504,561.44	84%	\$ 6,415,671.55	\$ 260,626,440.53
PROJECT CONTINGENCY	\$ 92,778,555.00	\$ -	\$ 54,678,189.34	\$ -	\$ -	\$ 11,808,786.00	\$ -	\$ -	0%	\$ (0.00)	\$ 11,808,786.00
TOTAL	\$ 801,749,577.00	\$ (0.00)	\$ 1,056,479,577.00	\$ 882,887.92	\$ 994,078,925.85	\$ 62,400,651.15	\$ 4,858,131.48	\$ 907,681,749.25	86%	\$ 0.00	\$ 1,056,479,577.00

Original Budget

In December 2019, the Metro Board Approved the LOP Budget of \$801,749,577. At that time the project budget was allocated to match the forecasts for construction, third party, right of way, professional services, and contingency, as was indicated in December 2019 Board report.

Current Budget

Since the start of the project there have been two LOP increases. The first occurred in February 2022, when the Board approved the LOP increase of \$75,000,000, bringing the LOP budget to \$876,749,577. The second occurred in April 2023, where the Board approved the LOP increase of \$80 million, increasing the Total LOP Current Budget to \$956,749,577. A third LOP increase of \$99.73 million was approved in October 2024, increasing the Total LOP Budget to \$1,056,479,577.

Commitments

Commitments increased by \$.89 million this period (FY26 Q3) to \$994.1 million, which represents 94.1% of the current budget. There was a \$.49 million increase in commitments for this period under professional services, and \$0.39 million increase in construction.

Expenditures


Expenditures increased by \$4.9 million this period (FY26 Q3) to \$907.7 million, which represents 86% of the current budget. The total increase is for costs associated with construction and professional services.

Current Forecast (expressed in millions)

The overall project forecast is \$1,056,479,577 this reporting period.

- The forecast for Construction is \$666.89 for this reporting quarter.
- The forecast for Professional Services is \$260.0 for this reporting quarter.
- The forecast for Right of Way is \$106.5 for this reporting quarter.
- The forecast for Third Party Services is \$10.5 for this reporting quarter.
- The forecast for Contingency is \$11.8 for this reporting quarter.

Cost Contingency Drawdown

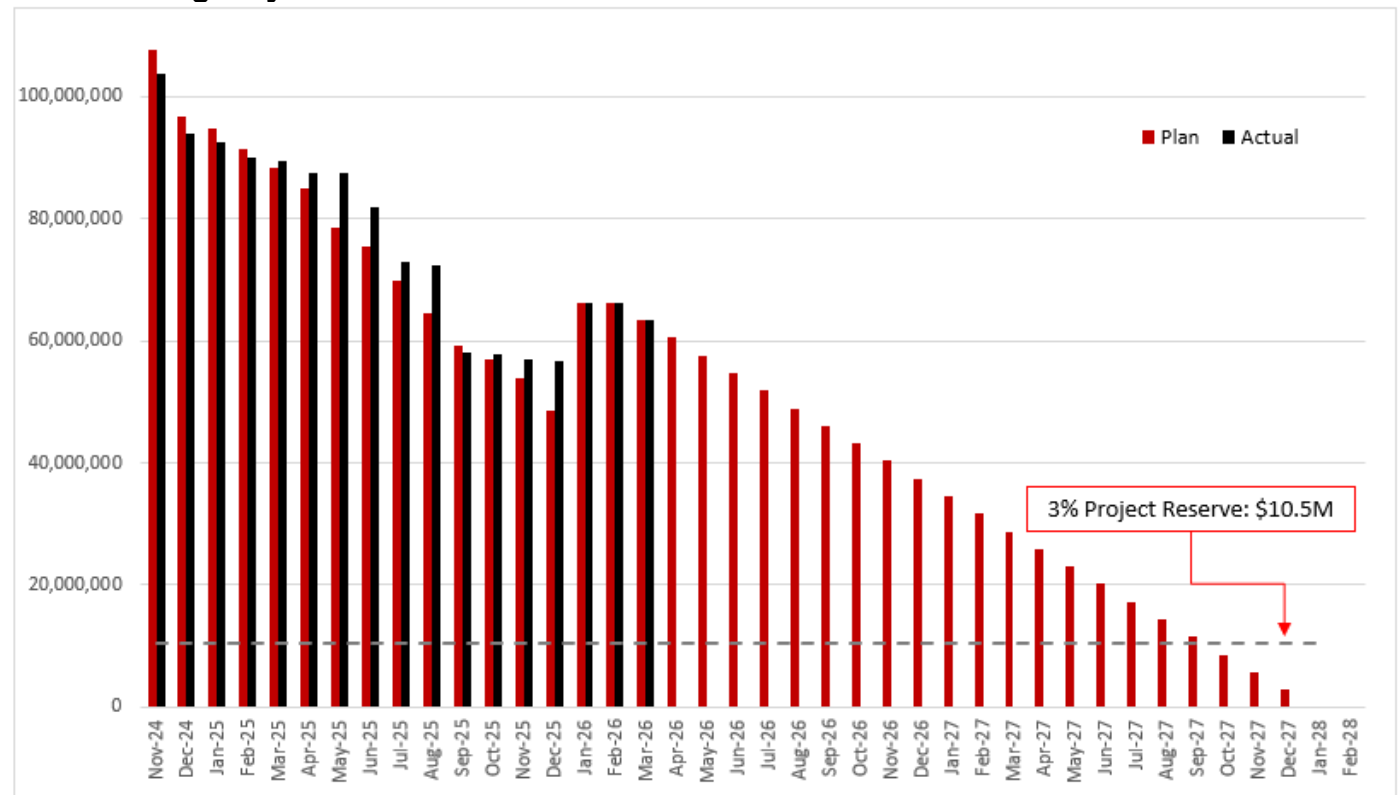

Cost Contingency Drawdown Analysis


The Cost Contingency Drawdown curve reflects cost commitments and forecast exposure, thereby providing a depiction of overall contingency status. Basing the drawdown on exposures (issuances of change notices) rather than executed contract modifications, eliminates the administrative processing time involved to finalize contract modifications from the drawdown projections. Planned expenditures per quarter have also been updated to reflect the current schedule and risks.

Total Contingency is \$409.2 million with \$61.7 million in Allocated Contingency and \$347.5 million in Unallocated Contingency. An LOP increase of \$80 million and budget reallocation within the project at the end of Fiscal Year 2023 Quarter 4 reestablished project contingency levels. An additional LOP increase of \$99.73 million in October 2024, FY25 Q2, reestablished project contingency levels.

In Fiscal Year 2026 Quarter 3, the remaining total project contingency (allocated and unallocated) is \$62,400,869.

PROJECT COST CONTINGENCY					
UNITS in DOLLARS					
	LOP Contingency	Previous Period	Current Period	To-Date	Remaining Contingency (Forecast)
Allocated Contingency	61,665,813	(61,665,813)	-	(61,665,813)	-
Unallocated Contingency	347,508,555	(281,384,534)	(3,723,152)	(285,107,686)	62,400,869
Total	409,174,368	(343,050,347)	(3,723,152)	(346,773,499)	62,400,869

Summary of Construction Contract Modifications

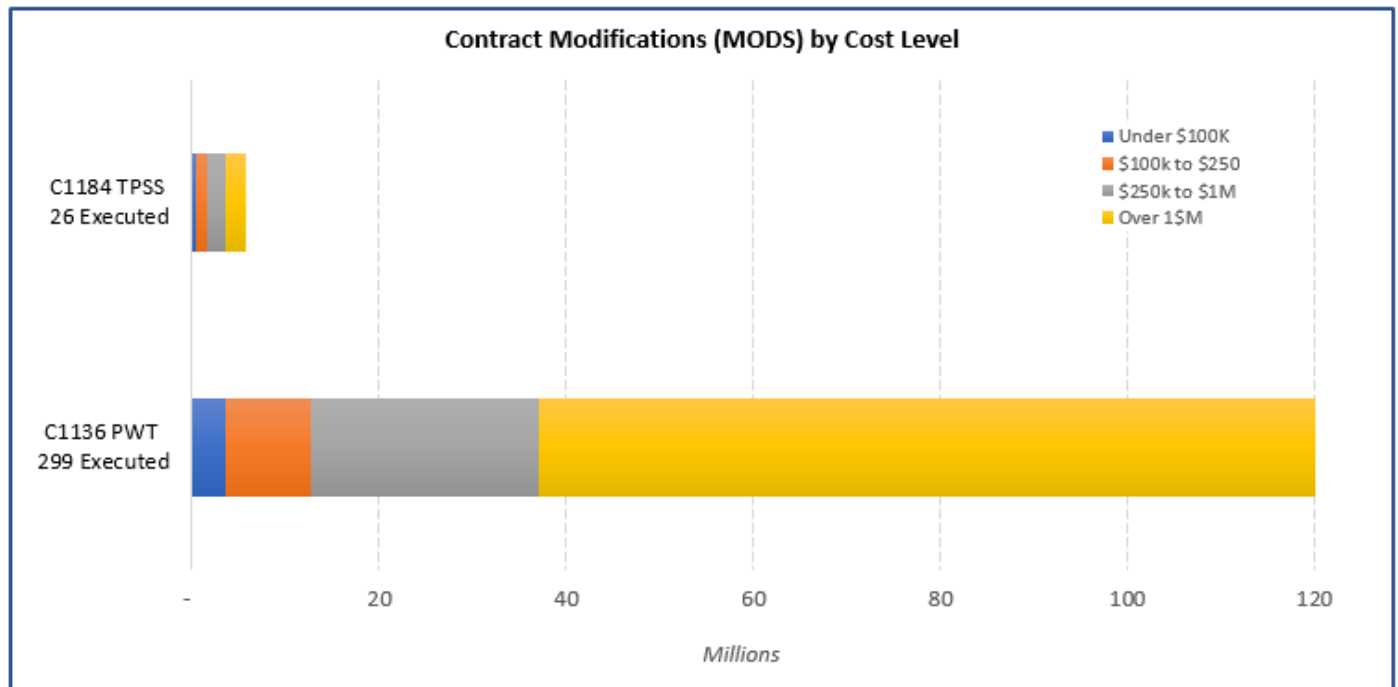

Cost Level		C1136 PWT 299 Executed		C1184 TPSS 26 Executed	
Under \$100K	155	3,595,249	14	372,140	
\$100k to \$250	57	9,141,668	7	1,268,309	
\$250k to \$1M	53	24,393,659	4	1,968,976	
Over 1\$M	34	128,801,059	1	2,101,007	
Total Contract MODs		299	165,931,635	26	5,710,432
Contract Award Amount			431,777,000		16,187,495
% of Contract MODs			28%		26%

Two Hundred and Ninety-Three (299) Contract MODs with a total value of \$165.9 million have been executed since the award of Contract C1136 – Portal Widening Turnback by Tutor Perini Corporation.

Twenty-Six (26) Contract MODs with a total value of \$5.7 million have been executed since the award of Contract C1184 – Transfer Power Substation by C3M.

FINANCIAL/GRANT

State of Funds Anticipated

Revised: updated October 2024

Proposed Funding (\$1,000s)						
FUND SOURCE	Prior	FY23	FY24	FY25	FY26	TOTAL
TIRCP	44.68	24.53	0.00			69.21
State SB1 LPP	45.90	39.41	14.71	33.07		133.09
Local Funds	444.97	108.81	101.09	71.60	127.71	854.18
TOTAL FUNDS	535.55	172.75	115.80	104.67	127.71	1,056.48

Superseded - Previous Statement April 2023

Proposed Funding (\$1,000s)						
FUND SOURCE	Prior	FY23	FY24	FY25	FY26	TOTAL
TIRCP	22,830		46,380			69,210
State SB1 LPP		20,000	84,090	29,000		133,090
Local Funds	512,720	147,150	8,960	56,000	29,620	754,450
TOTAL FUNDS	535,550	167,150	139,430	85,000	29,620	956,750

Superseded - Previous Statement July 2023

Proposed Funding (\$1,000s)						
FUND SOURCE	Prior	FY22	FY23	FY24	FY25	TOTAL
TIRCP	4,772	0	16,880	47,550		69,202
State SB1 LPP	16,880	37,510	35,080	43,790		133,260
Local Funds	345,980	128,250	99,040	16,660	84,350	674,280
TOTAL FUNDS	367,632	165,760	151,000	108,000	84,350	876,742

TIRCP is the Transit and Intercity Rail Capital Program for Metro Red Line and Purple Line Core Capacity Improvements. The TIRCP grant provides partial project funding of \$62,209 million for the additional yard capacity located at Metro's Division 20 to accommodate the augmenting expansion of the Purple Line Extension as well as not to preclude a future revenue station in the Arts District.

SB 1 is the California Senate Bill 1 also known as the Road Repair and Accountability Act of 2017. The SB1 Grant is a Local Partnership Program (LPP).

The LPP Road Repair and Accountability Act of 2017 (Senate Bill 1) created the Local Partnership Program and continuously appropriates \$200 million annually from the Road Maintenance and Rehabilitation Account to local and regional transportation agencies that have sought and received voter approval of taxes or that have imposed fees, which taxes or fees are dedicated solely for transportation improvements.

Ref. <https://catc.ca.gov/programs/sb1/local-partnership-program>


The SB1 LPP grant provides partial project funding of \$133,090 million.

Local Funds comprise of Measure M and Measure R Los Angeles sales tax. Local Funds provides remaining project funds of \$754,450 million.

PROJECT ORGANIZATION AND STAFFING

The design-bid-build contract is being managed by Metro and consultant personnel jointly located at the Integrated Project Management Office (IPMO). Below is the organization chart for the project team and project staffing for engineering services consultants.

Division 20 Portal Widening Turnback Management Organization and Staff

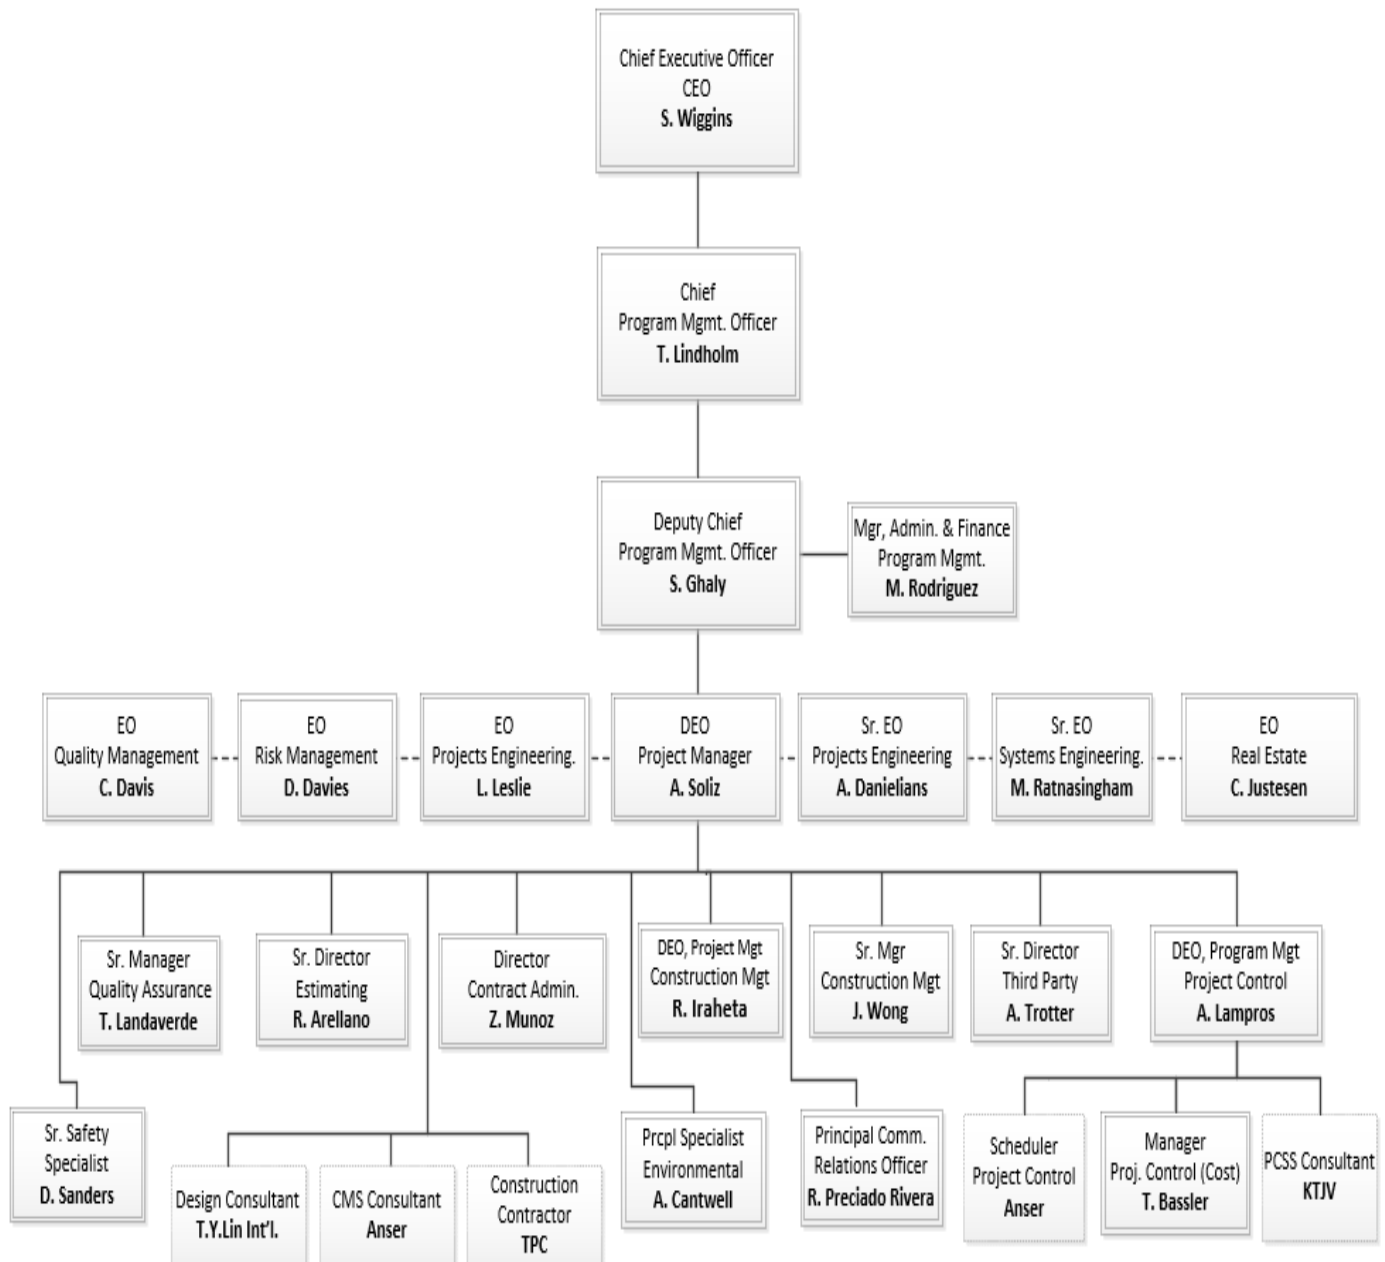

Issue Date: 09/30/2025

Metro Staff ☐
Consultant ☐

Staffing by Group


The opposing graphs represent Planned vs. Actual staffing levels by group. Metro staffing includes full-time staff located in the IPMO as well as part-time support located at Gateway Headquarters. Staffing plans are developed for each fiscal year based on Project needs.

The total budgeted FY26 Total Project Staffing plan averaged 93 FTEs per month. The total actual project staffing for March 2026 is comprised of 17 FTEs for Metro's Project Administration staff and 58 FTEs for consulting staff. Consulting staff FTEs are based on monthly invoice billable hours. Review of staffing plans is on-going to ensure staffing needs are appropriately managed.


Note: Systems Engineering was not previously included in data and now increases budgeted and actual FTE by 8.

FTEs – Full Time Equivalents


Total Project Staffing – Metro and Consultants

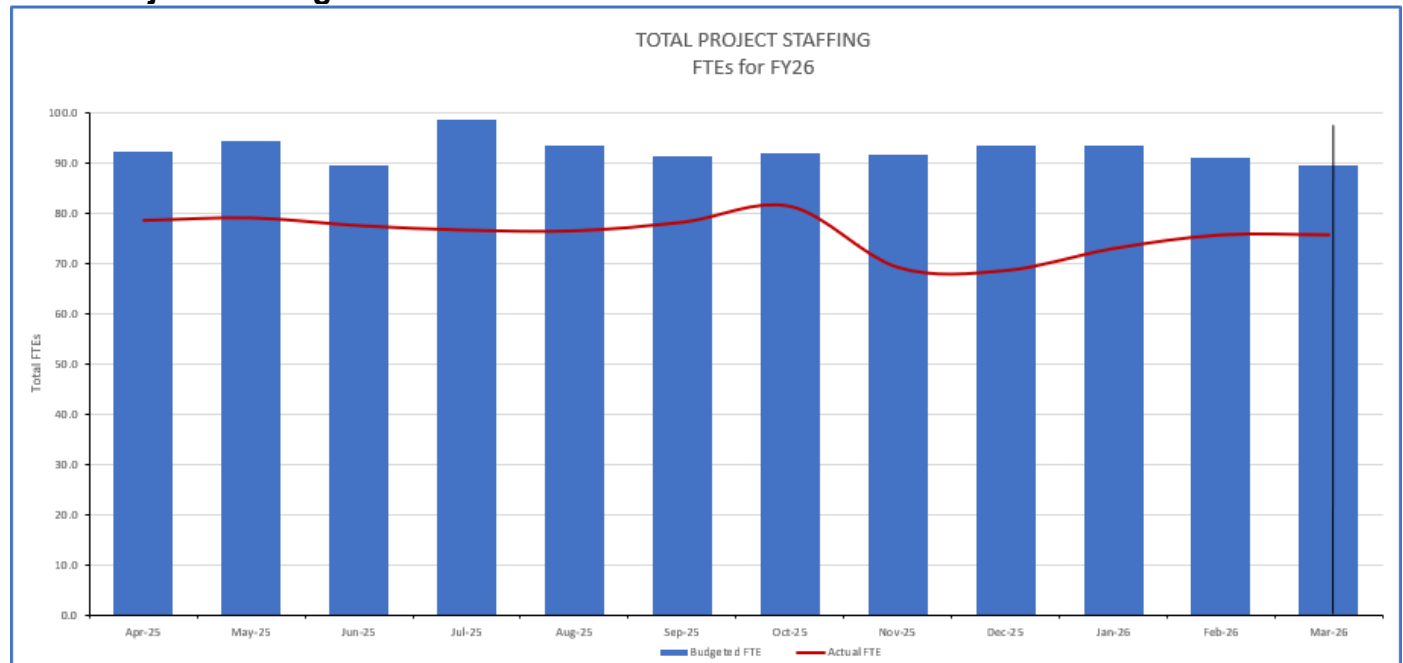


Metro Staff

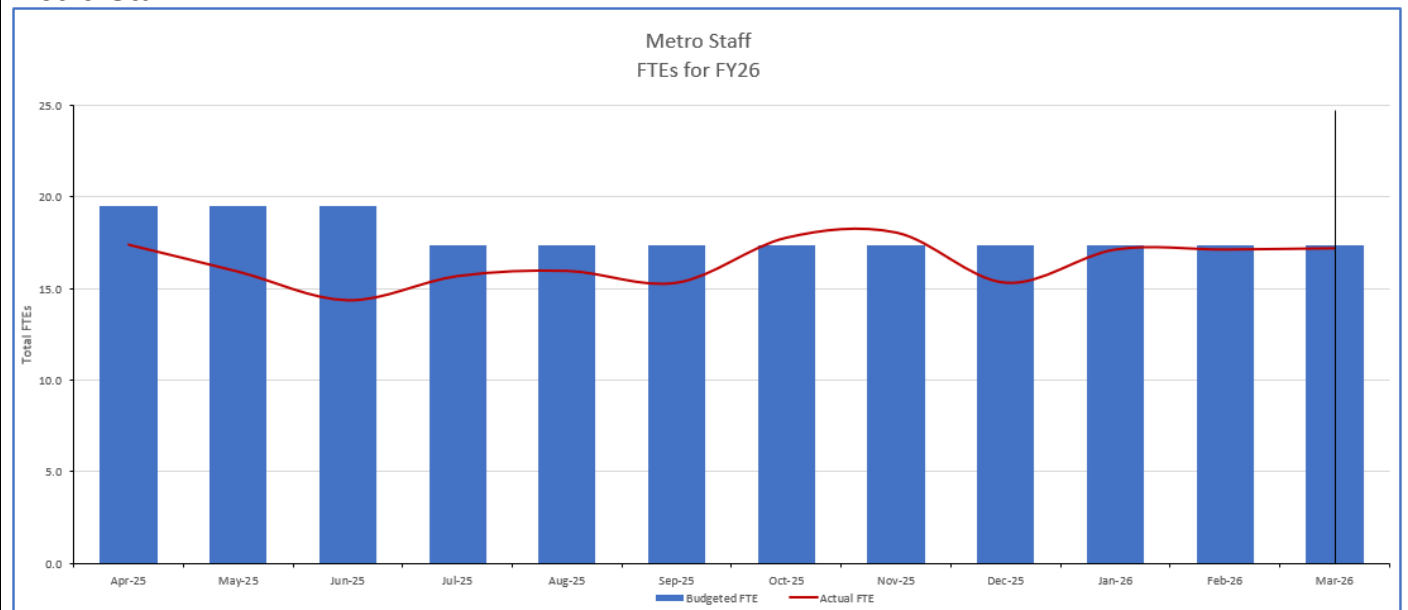

Engineering Services Staff (Consultant)

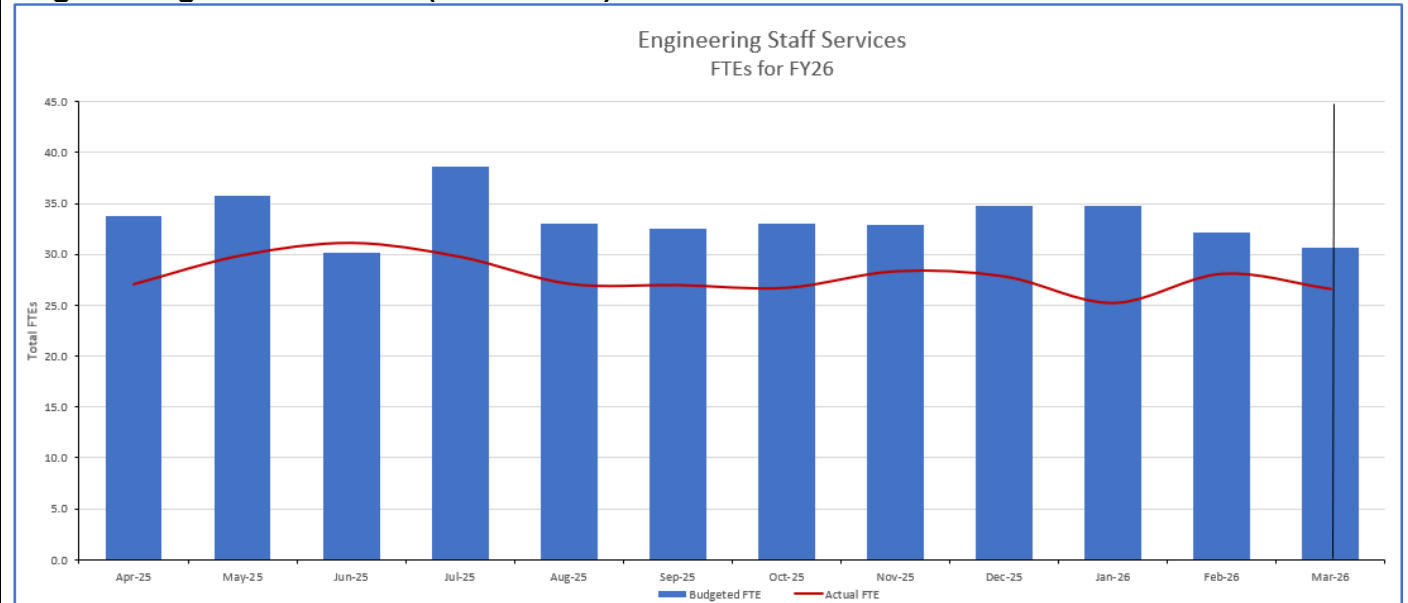

Construction Management Support Services (Consultant)

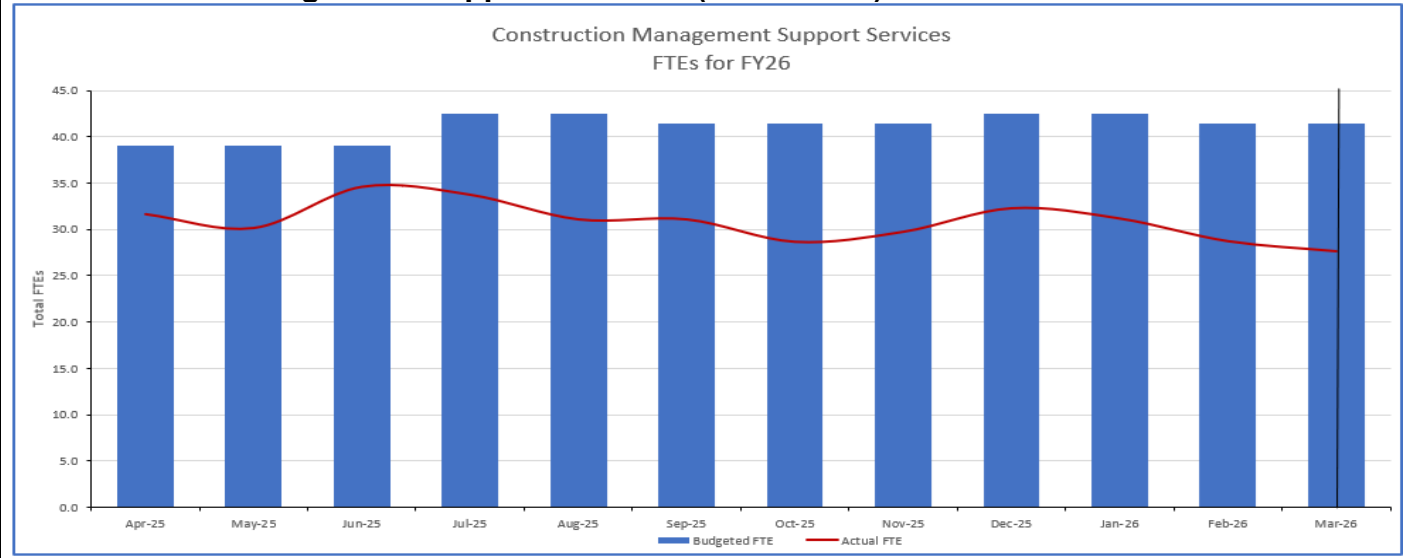

QUALITY ASSURANCE

- Worked in conjunction with the contractor's Quality Management team to resolve items which have resulted in documented deficiencies.
- Facilitated dialogue with the contractor's Quality Group to continue Improvements in quality control processes and document control management.
- Coordinated with Metro's Verification Testing Laboratory consultant (Ninyo and Moore) to provide continued support with the inspection and testing of the Division 20 Project work activities.
- Performed reviews of the contractor's quality submittals and Construction Work Plans for compliance with contract requirements.
- Worked closely with the contractor's Project Quality Manager to assess and manage work activities which require additional attention.
- Continued evaluations of the contractor's inspection report, test results and associated quality records.
- Implementing new Metro Quality Management Oversight System (QMO) in this Project.

ENVIRONMENTAL

The following is a listed series of items that consolidates the scope of all the consultants' task orders and finally the completion of Enabling Contract.

- Participated in various Project coordination meetings and evaluated progress and schedules for environmental compliance and sustainability efforts.
- Provided environmental awareness training as needed.
- Conducted field environmental monitoring and spot check inspections for construction noise and vibration, stormwater and fugitive dust BMPs, and Metro's Green Construction Policy.
- Reviewed and provided responses to various contractor submittals and requests for information related to environmental matters.
- Performed archaeological/paleontological and cultural monitoring activities as needed during various excavation activities.
- Complied with various SCAQMD rules and permits including VOC and dust monitoring.
- Operate and maintain dewater treatment system in compliance with Project contract and City of Los Angeles sanitary sewer discharge permit.

APPENDIX CHRONOLOGY OF EVENTS

May 2016	Division 20 Portal Widening Turnback Project Initiated
March 2017	Design Engineering Contract AE66758000
July 2017	Real Estate Acquisition ADCO 200-234 N. Center Street
January 2018	Real Estate Acquisition Viertel's Tow Yard 500 N. Center Street
June 2018	Construction Management Support Services Contract AE4863MC074
October 2018	Certified Final Environmental Impact Report and Related Actions
January 2019	Real Estate Acquisition 100-120 N. Santa Fe
January 2019	Portal Widening Construction Contract C1136 Issue for Bid
February 2019	Real Estate Acquisition Pickle Works 1001 East First Street
February 2019	Transfer Power Substation Contract C1184 Issue for Bid
June 2019	Transfer Power Substation Contract C1184 Notice of Award
July 2019	Transfer Power Substation Contract C1184 Notice of Proceed
December 2019	Board Approved Life of Project Budget
February 2020	Portal Widening Construction Contract C1136 Notice of Award
March 2020	Completion of Enabling Project Contract PS69133 Notice of Award
April 2020	Portal Widening Construction Contract C1136 Notice of Proceed
March 2020	Completion of Enabling Project Contract PS69133 Notice of Award
December 2020	Completion of Enabling Project Contract PS69133 Completed

APPENDIX CHRONOLOGY OF EVENTS *cont'd*

January 2021	Contract C1184 ongoing LADWP coordination. Contract C1136 ordering of third rail; portal timber logging & Installation of temporary power poles
February 2021	Installation of Temporary No.8 turnout for PLE1 transport of CWR into tunnel. Contract C1184 submittals to continue the fabrication of TPSS station, Switch gear & emergency backup generator
March 2021	Relocation of Amtrak fence to initiate walkway along Road A; continuation of duct bank and water lines install. Contract C1184 resolution of seismic design
April 2021	Ordering of third rail; initiate bridge removals. Contract C1184 additional submittals to continue the fabrication of the TPSS station
May 2021	Installation of temporary power poles and cables. Continuation of duct banks and waterlines
June 2021	Support of Excavation and Lagging on the Portal Wall is complete
September 2021	C1136 MOD20 /CN6 Executed
September 2021	Commence Microlok Cut Over
November 2021	Microlok II cutover successfully complete
December 2021	1 st . Street Bridge poured footings and commence the installment of thirty-seven casted girders
January 2022	Installation of timber treated lagging at the Portal (East/West)
February 2022	Demolition of Smoke Slab on 1 st Street bridge
March 2022	Shoofly Cutover Tail Track 2 (TT2) to Track 1
May 2022	North Yard Storage Tracks asphalt cap
June 2022	TPSS Foundation Pour
August 2022	1 st Street Bridge Bent 16 Demolition
September 2022	Northern Yard Storage Track Installation
November 2022	North Storage Yard Paving, Ballast Placement and Storage Track Substantially complete EBPS Generator pad completed (C1184 TPSS)

APPENDIX CHRONOLOGY OF EVENTS *cont'd*

December 2022	Contract Milestone 2 - Portal Wall Demolition started Transformer pad completed Metering Switchgear Installed (C1184 TPSS)
January 2023	1 st Street Bridge Bent 13 Demolition
February 2023	Ducommun St. Protection slab and the first invert at the portal
March 2023	West Portal Retaining Wall foundation/slab
April 2023	Emergency Back up Power Supply (EBPS) delivery and setting
June 2023	Contract Milestone 3 - Completion of Portal Wall and conduits MCP site
June 2023	Traction Power Substation (TPSS) delivery and setting – 4 out of 6 sections
August 2023	Traction Power Substation (TPSS) delivery and setting – final 2 sections
August 2023	Contract Milestone 4 - Completion on Traction Power cable installation related to TPSS/EPBS Equipment Installation
October 2023	TPSS Local Field Acceptance Testing (LFAT)
December 2023	DWP TPSS Energization
March 2024	Train Control Bungalows – final setting of 4 train control bungalows
May 2024	4 new Train Control bungalows installed
June 2024	North Storage Yard Complete
October 2024	Division 20 Maintenance and Shop Building power cutover to new TPSS
November 2024	Trainway Feeder to Union Station Tunnel cutover to new TPSS
January 2025	Center Street Improvements completion Union East software cutover
August 2025	Demolished existing TPSS
October 2025	Milestone A - Cutover A
December 2025	Portal Demolition East
