


SCRTD
1985-
.M46
R46
no. 59



LOS ANGELES **METRO RED LINE** PROJECT

MONTHLY CONTRACT PERFORMANCE REPORT

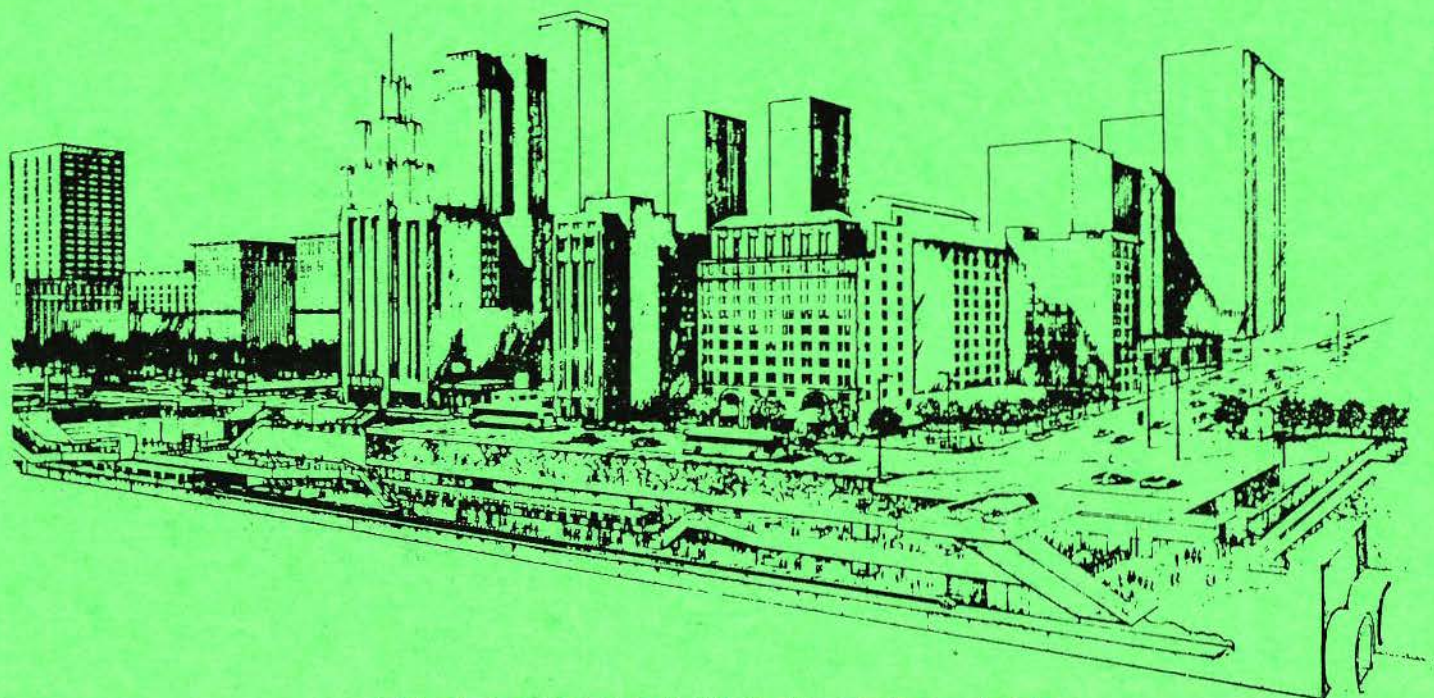

REPORT NUMBER 59
MAY 1989

PDCC

A Joint Venture of The Ralph M. Parsons Co., Dillingham Construction N. A. Inc., and De Leuw, Cather & Co.,

**MONTHLY CONTRACT
PERFORMANCE REPORT**

for the

LOS ANGELES **METRO RED LINE** PROJECT

MAY 1989

presented to

Southern California Rapid Transit District

CONTRACT NO. 3369

The preparation of this Document has been financed in part through grants from the State of California, the City of Los Angeles, the Los Angeles County Transportation Commission and the U. S. Department of Transportation, Urban Mass Transportation Administration, under the Urban Mass Transportation Act of 1964, as amended.

Month MAY Year 1989

14406

MAR 18 '93

SCRTD
1985-
.M46
R46
no. 59



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

TABLE OF CONTENTS

	Page
I. Construction Manager's Summary Statement	1
II. Manpower Performance	8
III. Equal Opportunity Performance	15
IV. Schedule Performance	17
V. Cost Performance	20
VI. Additional Activities Performed in May	26
VII. Summary of Activities Planned for June	40
VIII. Subcontractor/Consultant Status	45
IX. Construction Progress Photos	

SECTION I

CONSTRUCTION MANAGER'S

SUMMARY STATEMENT



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

I. CONSTRUCTION MANAGER'S SUMMARY STATEMENT

MAJOR CM ACTIVITIES

This Contract Performance Report (CPR) for the month of May 1989 is the eleventh CPR in the Fifth Annual Work Plan (5th AWP) and covers the period April 29 through May 26, 1989. The following is a summary, by functional organization, of major CM activities during this period:

CONSTRUCTION OPERATIONS: Continued construction management (CM) services for 16 Facility Contracts and 11 Systems Contracts, monitoring of utilities relocations, and performance of submittal reviews. Continued conducting QC inspections of work for compliance to plans and specifications. Monitored contractor progress to approved project schedules. Assisted contractors in coordination with local public agencies in areas of community impact, permits and traffic access. Continued to conduct safety inspections of all contractor activities. Responded to contractor document clarification requests as appropriate.

Environmental Activities: Continued monitoring of ground water and construction water discharges at A141, A144, A145, A146, A165, A171 and A175. Continued monitoring Discharge Monitoring Stations at the Ballona Creek and Los Angeles River. Prepared and submitted March Discharge Monitoring Report (DMR) to the California Regional Water Quality Board (CRWQCB). Prepared and submitted March LA River Dissolved Solids Report to Central and West Basin Water Replenishment District (CWBWRD). Coordinated and inspected installation of water treatment facilities at A141. Inspected asbestos abatement at the Equitable Building, A145. Reviewed and approved final asbestos submittal and reviewed clearance report for asbestos abatement at REA building, A135. Completed and submitted closure report for 4 tank abandonments at A165. Properly abandoned underground storage tanks at A145. Monitored removal, relocation and disposal of contaminated soil at A175. Coordinated acceptance of contaminated soil from A146 at Class II landfill.

Utilities and Traffic Activities: Continued coordination of traffic control plans and street closures with city agencies for A130, A141, A145, and A165. Continued coordination of MOS-1 inspections with LADOT. Processed a total of 18 Traffic and Utilities related submittals.

Surveying Activities: Continued monitoring instrumentation, building and ground settlement points on A135, A141, A145, A146, A165, A171 and A175. Continued location survey at yards and shop contracts. Checked slabs poured at A141 and A175 excavation. Continued performing as-built cross section of AR Tunnel invert pour (A171). Continued checking arch form alignment AL tunnel (A171). Performed tunnel alignment check AR tunnel (A141). Continued tunnel alignment check at AL tunnel (A146). Checked layout of A165 station.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

PROJECT CONTROLS: Processed 30 Change Requests as follows: 4 for A112; 1 for A130; 4 for A135; 3 for A141; 1 for A145/A145A; 2 for A146; 11 for A165; 1 for A175; and 3 for A610/A115. Processed 28 Change Notices as follows: 3 for A130; 2 for A141; 4 for A145/A145A; 2 for A146; 9 for A165; 2 for A175; 1 for A610/A115; 1 for A620; 1 for A630; 2 for A640; and 1 for A710. Processed 68 Change Orders as follows: 7 for A112; 4 for A130; 7 for A135; 9 for A141; 5 for A145/A145A; 4 for A146; 9 for A165; 7 for A175; 12 for A610/A115; 1 for A616; 2 for A620; and 1 for A640. Processed 27 executed Change Orders through TRACS as follows: 1 for A112; 2 for A130; 2 for A135; 3 for A141; 5 for A144; 4 for A145/A145A; 4 for A146; 1 for A165; 3 for A175; 1 for A610/A115; and 1 for A745. Processed 31 Potential Claims as follows: 1 for A145/A145A; 28 for A165; and 2 for A610/A115. Processed 23 Change - Technical Evaluations as follows: 4 for A112; 1 for A135; 2 for A141; 3 for A145/A145A; 6 for A165; 1 for A175; 5 for A610/A115; and 1 for A620. Processed 17 Force Account Change Packages as follows: 3 for A145/A145A; 3 for A146; 2 for A165; 1 for A171; 4 for A175; 4 for A750. Processed 19 Monthly Payment Estimates. Completed close-out reconciliations on 10 Force Account Change Orders as follows: 5 for A145/A145A; 2 for A146; 2 for A165; and 1 for A175. Continued testing PC TRACS for use on the project. Reviewed Contractor Monthly Progress Reports. Prepared inputs to RTD Monthly Status Report. Reviewed A167 Part I Schedule Submittal - Rejected.

Cost Estimates for Changes and Proposals: A112-CR-068: Lighting system conduits. Reviewed scope of work and quantities with Contractor. A130-CR-025: Prepared estimate; assisted in negotiated settlement with Contractor. A130-CR-016: Reviewed estimate and contractor proposal; assisted in negotiated settlement with contractor. A135-CR-004: Continued review of proposals and changes for LAUPT Baggage Handling Facilities; A135-CR-005: Reviewed contractor proposal for REA building demolition. A135-CR-011: Received west entrance drawings, made preliminary review. A135-CR-029: Reviewed concrete water cement ratio change with RTD and Contractor, breakdown for payment. A135-CR-032: Began preparation of estimate for police room LAUPT. A141-CR-040: Began review of incoming electrical service room change. A141-CR-097A: Completed estimate additional strain gauges on struts. A145-CR-122, 123 & 128: Prepared estimates, escalator wellway, engagement access, and elevator machine room. A145-CR-141: Reviewed scope of work and prepared estimate for station grounding General System. A146: Met with Contractor and RTD re: tunnel equipment rates for Force Accounts, began rebuttal to Contractor questions and objections. A165-CR-010: Prepared revised electrical estimate, miscellaneous changes. A165-CR-044: Began preparation of final estimate Hydraulic elevator lines and conduits. A165-CR-049: Reviewed final design east bulkhead, provided data to Resident Engineer for negotiations. A165: Prepared detailed takeoff of decking in support of final pay quantities. A620-CR-018: Completed estimate for deletion of ACTV coaxial cable installation. A620-CR-008: Prepared estimate for additional corrosion control requirements. A620-CR-020: Reviewed contractor estimate for trap circuit deletion. A710-CR-002, 003: Prepared R.O.M. estimates for elevator cab changes. Prepared revised instructions on Finding-of-Fact preparation, Claims Log Update, Change Request Preparation and Force Account processing. Met with DOT audit



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

team and provided requested information.

CONTRACTS/PROCUREMENT: Prepared amendments to increase funding for subcontracts with Martin and Huang and Construction Control Services Corporation to cover remaining AWP-5 requirements. Prepared and submitted for District approval an Amendment to the Construction Photographic Services Subcontract to incorporate Change Orders No. 2 and 3, to increase AWP-5 funding and to remove unexpended AWP-4 funding. Received District approval and issued Amendments to increase AWP-5 funding for temporary personnel services subcontract with WCI. Following District approval, issued purchase orders for 12 PC's and related software. Issued Request for Quotations for renewing annual agreement covering reproduction services.

ENGINEERING SERVICES: Completed site geologic inspection of A146 AL tunnel and began compiling geologic profile for use in predicting the geology along the AR tunnel alignment. Coordinated with MRTC to develop an acceptable method for taking tunnel liner distortion measurements in Contract A146, where the shield configuration precludes use of the specified method. Recommended and coordinated the reduction of the Contractor's Civic Center Station strain gauge readings from once per day to once per week. Reviewed the A130 Contractor's method of orienting the horizontal chemical grout holes to be drilled beneath the Santa Ana Freeway. Inspected drilling of A130 pre-grouting proof test sample holes. Completed reviewing and cross checking results of Proctor testing performed by Smith-Emery Company. Completed data gathering phase of the A141 Design Verification Study Plan, Task C. Researched question of whether sub-ballast material is acceptable as crushed aggregate material throughout the A610/A115 job site. Responded to 98 requests for information or documentation clarification from various contractors. Processed 8 field inquiries with MRTC to obtain clarification of design requirements. Coordinated with the FLSC Fire Chiefs, MRTC, and A146 Contractor regarding fire protection system at cross passages.

During this period 325 Contractor submittals were processed as follows:

For Contract A112	- Approved - 5; Approved-as-Noted - 7; Rejected - 1.	
For Contract A130	- Approved - 14; Approved-as-Noted - 8; Rejected - 3;	For Record Only - 2.
For Contract A135	- Approved - 8; Approved-as-Noted - 3; Rejected - 6.	
For Contract A135BH	- Approved - 11; Approved-as-Noted - 9; Rejected - 5.	
For Contract A141	- Approved - 17; Approved-as-Noted - 13;	For Record Only - 1.
For Contract A145	- Approved - 7; Approved-as-Noted - 12;	For Record Only - 2.
For Contract A146	- Approved - 1.	
For Contract A165	- Approved - 31; Approved-as-Noted - 46; Rejected - 2;	For Record Only - 1.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

For Contract A171	- Approved - 14; Approved-as-Noted - 7; Rejected - 3.
For Contract A175	- Approved - 12; Approved-as-Noted - 3; Rejected - 5; For Record Only - 1.
For Contract A610/A115	- Approved - 11; Approved-as-Noted - 2; Rejected - 4.
For Contract A612	- Approved - 1.
For Contract A620	- Approved - 12; Approved-as-Noted - 1.
For Contract A630	- Approved-as-Noted - 1; Rejected - 5.
For Contract A640	- Approved - 5; Approved-as-Noted - 3; Rejected - 5; For Record Only - 1.
For Contract A710	- Approved - 4; Approved-as-Noted - 2.
For Contract A740	- Approved-as-Noted - 2; Rejected - 1.
For Contract A745	- Approved - 1; Approved-as-Noted - 1.
For Contract A750	- Approved-as-Noted - 1.
For Contract A795	- Approved - 2.

TOTAL	<u>156</u>	<u>121</u>	<u>40</u>	<u>8</u> = 325
-------	------------	------------	-----------	----------------

SAFETY/SECURITY: Performed daily site safety, health and security surveillances on a two shift basis and prepared written reports for 10 construction projects. Coordinated activities of the Systemwide Security Guard Service and the Systemwide Clean-up Service Subcontractors.

COMMUNITY RELATIONS - Coordinated community notifications for A141, A145, A146, A165 and A175 and LAPD traffic control assistance for A141. Coordinated mitigation of traffic concerns for tenants along Hill St. affected by A141 and A145 traffic access plans, and for tenants in the 7th and Flower area affected by A165 and A146 traffic plans. Provided assistance to A141, A145, A146 and A165 for problems caused by street closures and lane restrictions, blocked access, noise and accidents. Assisted RTD with coordination of the "hole-thru" media event for Civic Center Station. Assisted RTD in coordination for the LAUPT 50th Anniversary Celebration event. Coordinated safety and security meeting with LAPD. Provided assistance to PDCD/RTD in coordinating site visits and responding to media requests. Processed 24 inquiries/complaints.

QUALITY ASSURANCE/QUALITY CONTROL - Conducted field surveillance of welding activities in support of Contracts A135, A145, A165, A171 and shop fabrication surveillance at Paramount Steel, COWELCO, and Angeles Steel. Finalized "Preparation of As-Built Drawings Procedure" based on anticipated PDCD responsibility for contract "as-built" preparation. Met with A112 R.E. to review proposed physical close-out procedure. Continued to conduct training classes to prepare inspectors for ACI Concrete Technician I certification. Finalized and transmitted Acromedia (Bechtel subcontractor on A640) Audit Report. Witnessed acceptance testing at Ayden



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

Controls, Bechtel A640 subcontractor. Continued monitoring of Testing Lab (Smith-Emery) performance and costs. Continued surveillance of HDPE installation (A141, A165, A171 and A175) and witnessing of fire protection system hydrostatic tests at A165 and A175. Conducted field QA audit of lift drawings (A130 and A141) to verify conformance with review and approval process.

EQUAL OPPORTUNITY - Monitored Equal Opportunity reporting requirements for 27 contracts. Conducted project site visits/employee interviews at 10 construction sites. Processed penalty assessments for the late submittal of the Monthly Employment Utilization Reports for 7 Contracts.

MANPOWER PERFORMANCE

The manpower performance for May is measured against the approved planned staffing for the 5th AWP. During May, the actual staff level was 205 vs. the planned staff level of 193. Therefore, the actual staff count for May was 12 over the planned staffing level. The staff breakdown by company was 137 for the Joint Venture firms and 68 for the Associate Subcontractors. The increased staff was required for the processing of excessive field submittals and correspondence and for multishift inspection of construction work at various jobsites.

The May period had 160 available workhours/person. The plan provided for expenditure of 30,400 hours, including "as-required" manhours which would have generated a projected equivalent head count of 190.0 personnel at 160 hours/person. Actual hours expended were 31,753 which translates into a 198.456 equivalent head count at 160 hours/person including temporary personnel, resulting in the equivalent of 8.456 personnel over the plan.

Cumulative total hours incurred through May were 335,037 against a plan of 324,368 resulting in an over plan variance of 10,669 hours.

EQUAL OPPORTUNITY (EO) PERFORMANCE

EO performance for PDCD in May measured on a cost accrual basis under four categories - DBE, WBE and Minority and Women Affirmative Action was as follows:

- o Cumulative DBE participation for the Fifth Annual Work Plan through the month, measured against a total cost basis was 18.3%, 1.3% over the goal of 17%.
- o Cumulative WBE participation for the Fifth Annual Work Plan through the month, measured against a total cost basis was 4.6%, 1.6% over the goal of 3%.
- o Minority and Women Affirmative Action performance for the month exceeded the established goals of 17% and 8% by 20% and 0.3% respectively.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

SCHEDULE PERFORMANCE

- o **Contractor Submittals** - During this period, 339 submittals were received per contract number as follows: A112 (19), A130 (26), A135 (21), A135BH (15), A141 (37), A145 (25), A146 (8), A165 (83), A171 (21), A175 (20), A610/A115 (18), A612 (0), A615 (1), A616 (5), A620 (12), A630 (4), A640 (12), A710 (5), A732 (0), A740 (3), A745 (1), A750 (2) and A795 (0); of the 339 received this period plus the 206 carryover from April, 325 packages were processed and returned to the contractors; the balance of 220 remain in review.
- o **Constructibility Reviews** - Completed review for A117/100%, Yard Site Lighting and started review of A187/100%, Wilshire/Alvarado Station, Stage II.

COST PERFORMANCE - Fifth Annual Work Plan

- o Total incurred costs of \$1,476,145 for CM Direct Services (excluding General Condition Items) for the period were over the plan of \$1,432,056 by \$44,089. This variance results from the net effect of Other Direct Costs (ODCs) being over the plan by \$14,953 and labor expenditures (total PDCD and subcontractors) being over the plan by \$29,136.
- o The cumulative costs for Total CM Services (Including General Condition Items) incurred through May were \$15,728,859 against a plan of \$15,821,617 resulting in an under plan of \$92,758.
- o The May CPR indicates an estimate at completion for the 5th AWP (including General Condition Items) of \$17,505,517 versus a plan of \$17,625,378 for an underexpenditure of \$119,861.

GENERAL CONDITION ITEMS

General Condition Items (GCI's) expenditure of \$76,214 for the period were over the plan of \$44,192 for the period by \$32,022. This report forecasts an estimate at completion (EAC) in the 5th AWP period for GCI's of \$893,303, which is over the plan of \$664,300 by \$229,003.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

GENERAL

- o This "Monthly Contract Performance Report" covers progress relative to PDCD's CM Services contract with the RTD. By RTD direction PDCD no longer produces the "Monthly Construction Performance Report". An equivalent document is now produced by RTD with PDCD input and is entitled the "Monthly Status Report." A copy of the RTD report is distributed to previous recipients of the PDCD report as required.


Melvin L. Polacek
Construction Manager

SECTION II
MANPOWER PERFORMANCE



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

II. MANPOWER PERFORMANCE

This CPR for the month of May compares actual manpower to the planned manpower in the approved 5th AWP. Table II-1, Page 10, illustrates planned staff vs. actual staff and variances for May.

During May, personnel assignments/deletions included the addition of 1 Jr. Engr.-Change Control, 1 Inspector, 1 Electrical Engineer (as-required, A/R), and 1 Cost Engineer (as-required, A/R); and the deletion of 1 Sr. Secretary, 1 Data Technician-Documents Control, and 1 Jr. Engineer-Geotech.

For the May period, under the approved 5th AWP, the total planned staffing level (including regular and as-required classifications) is 193. The actual staff (including regular, as-required and temporary classifications) was 205 resulting in 12 over the plan. The current actual staff by company for the May period is as follows:

<u>Company</u>	<u>Staff Level</u>	<u>Company</u>	<u>Staff Level</u>
The Ralph M. Parsons Company	58	Jenkins, Gales & Martinez, Inc.	9
Dillingham Construction, Inc.	57	Kal Krishnan Consulting	2
De Leuw, Cather & Company	22	Martin & Huang International	5
Better Personnel Employment Services	10	North Pacific Construction Management	5
Construction Control Services Corporation	19	Ochoa & Sillas	-
Dames & Moore	1	Randolph & Tate Associates	-
D'Leon Consulting	1	Transmetrics	1
Engineering-Science, Inc.	3	WCI	3
Jacobs Associates	9		

The PDCD Manpower Chart on Page 11 illustrates planned manpower for Construction Services for the Fifth Annual Work Plan period. Actual equivalent manpower is shown for the months of July through May.

The May period had 160 available workhours/person. The plan provided for an expenditure of 30,400 hours, including "as-required" manhours, which would have generated a projected equivalent head count of 190.0 personnel @160 hrs/person. Actual hours expended were 31,753 which translates into an equivalent head count of 198.456 @ 160 hrs/person including temporary personnel, resulting in the equivalent of 8.456 personnel over the plan.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

The hours expended for the period were 31,753 versus a plan of 30,400. The 1353 manhours variance for the period is calculated as follows:

8.45625 equivalent staff over plan @ 160
hours/period in plan =

1353 hours

MAY MANHOUR VARIANCE TO PLAN

1353 hours

Cumulative total hours incurred through May were 335,037 against a plan of 324,368 resulting in an over plan variance of 10,669 hours. (Page 22)



LOS ANGELES METRO RED LINE

CONTRACT PERFORMANCE REPORT

PDCD

PERIOD MAY 1989

**TABLE II-1 CONSTRUCTION MANAGEMENT STAFF COUNT - MAY
FIFTH ANNUAL WORK PLAN**

Phase II Construction Services			
Regular/As-required/Temporary			
Position	Planned	Actual	Variance
Construction Manager	1	1	0
Manager, Safety and Security	1	1	0
Safety Inspectors	2	2	0
Manager, Quality Assurance	1	1	0
Quality Assurance Engineer	1	1	0
QA/QC Inspector	1	1	0
Secretarial/Word Processing/Clerical/ Drafting/Courier	15	17	2
Labor Relations	0	0	0
Legal Counsel	0	0	0
Subtotal	22	25	3
Manager, Administration and Staff Support	1	1	0
Manager, Project Administration/Accounting	1	1	0
Senior Accountant	1	1	0
Senior Accounting Clerks	2	2	0
Office Manager	1	1	0
Arts Coordinator	0	0	0
Manager, Community Relations	1	1	0
Community Relations Coordinator	1	1	0
Manager, EO Administration	1	1	0
EO Administrator	1	1	0
(3) Lead Document Control Specialist	1	1	0
Document Control Specialist	1	1	0
Shop Drawing Coordinator	1	1	0
Data Technician	2	4	2
File Clerk	1	2	1
Subtotal	16	19	3
DCM, Project Controls/Engineering Services	1	1	0
Manager, Project Controls	1	1	0
Technical Data Coordinator	1	1	0
Lead Cost Engineer	1	1	0
Cost Engineers	4	5	1
Lead Change Control	1	1	0
Change Control Specialist	1	1	0
Claims Proc. Spec.	1	1	0
Data Technician	1	1	(0)
Lead Planner/Scheduler	1	1	0
Planner/Schedulers	6	8	2
Lead Estimator	1	1	0
Estimators	5	2	(3)
Sr. Data Technician	1	1	0
Computer Support	0	0	0
Subtotal	26	26	(0)
Manager, Contracts/Procurement	1	1	0
Sr. Contract Administrator	2	2	0
Subtotal	3	3	0

Phase II Construction Services			
Regular/As-required/Temporary			
Position	Planned ⁽¹⁾	Actual ⁽²⁾	Variance
Manager, Engineering Services/ Systems Integration	1	1	0
Drafting Technicians	3	1	(2)
Lead Architect	1	1	0
Architect	0	0	0
Lead Electrical Engineer	1	1	0
Electrical Engineer	1	3	2
Lead Engineer, Geotech. Section	1	1	0
Engineers, Geotech. Section	7	4	(3)
Lead Mechanical Engineer	1	1	0
Mechanical Engineer	1	1	0
Lead Structural Engineer	1	1	0
Sr. Struct./Struct. Engineers	2	4	2
Lead Systems Engineer	1	1	0
Systems Engineer	2	1	(1)
Office Engineer	0	1	1
Subtotal	23	22	(1)
DCM, Operations	1	1	0
Manager, General Services	1	1	0
Lead Utilities Engineer	1	1	0
Utility Engineer	1	1	0
Chief of Surveys	1	1	0
Party Chief	1	1	0
Instrument Person	2	2	0
Rod Person	1	2	1
Lead Environmental Engineer	1	1	0
Environmental Specialists	3	3	0
Engineer	0	0	0
Engineering Technician/Coordinator	1	1	0
Resident Engineers	9	10	1
Chief Inspectors	8	9	1
Sr. Inspectors/Inspectors	37	39	2
Office Engineers	11	12	1
Field Secretaries/Clerical	14	13	(1)
Manager, Systemwide Construction	1	1	0
Office Engineer	2	3	1
Resident Engineers	4	4	0
Secretary	2	4	2
Inspector	1	0	(1)
Subtotal	103	110	7
Totals	193	205	12

NOTES:

- (1) The "Planned" staff count is taken directly from the RTD approved PDCD 5th AWP. It is the planned staff count for the reported month and includes both "Regular" and "As-required" classifications.
- (2) The "Actual" staff count is the total actual staff count by Job Position. Included are regular, as-required and temporary staff.
- (3) Effective February 1, 1989, the Document Control Section, previously in the DCM, Project Controls/Engineering Services group, was transferred to the Manager, Administration and Staff Support group.




LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

FIFTH ANNUAL WORK PLAN

PERIOD MAY 1989

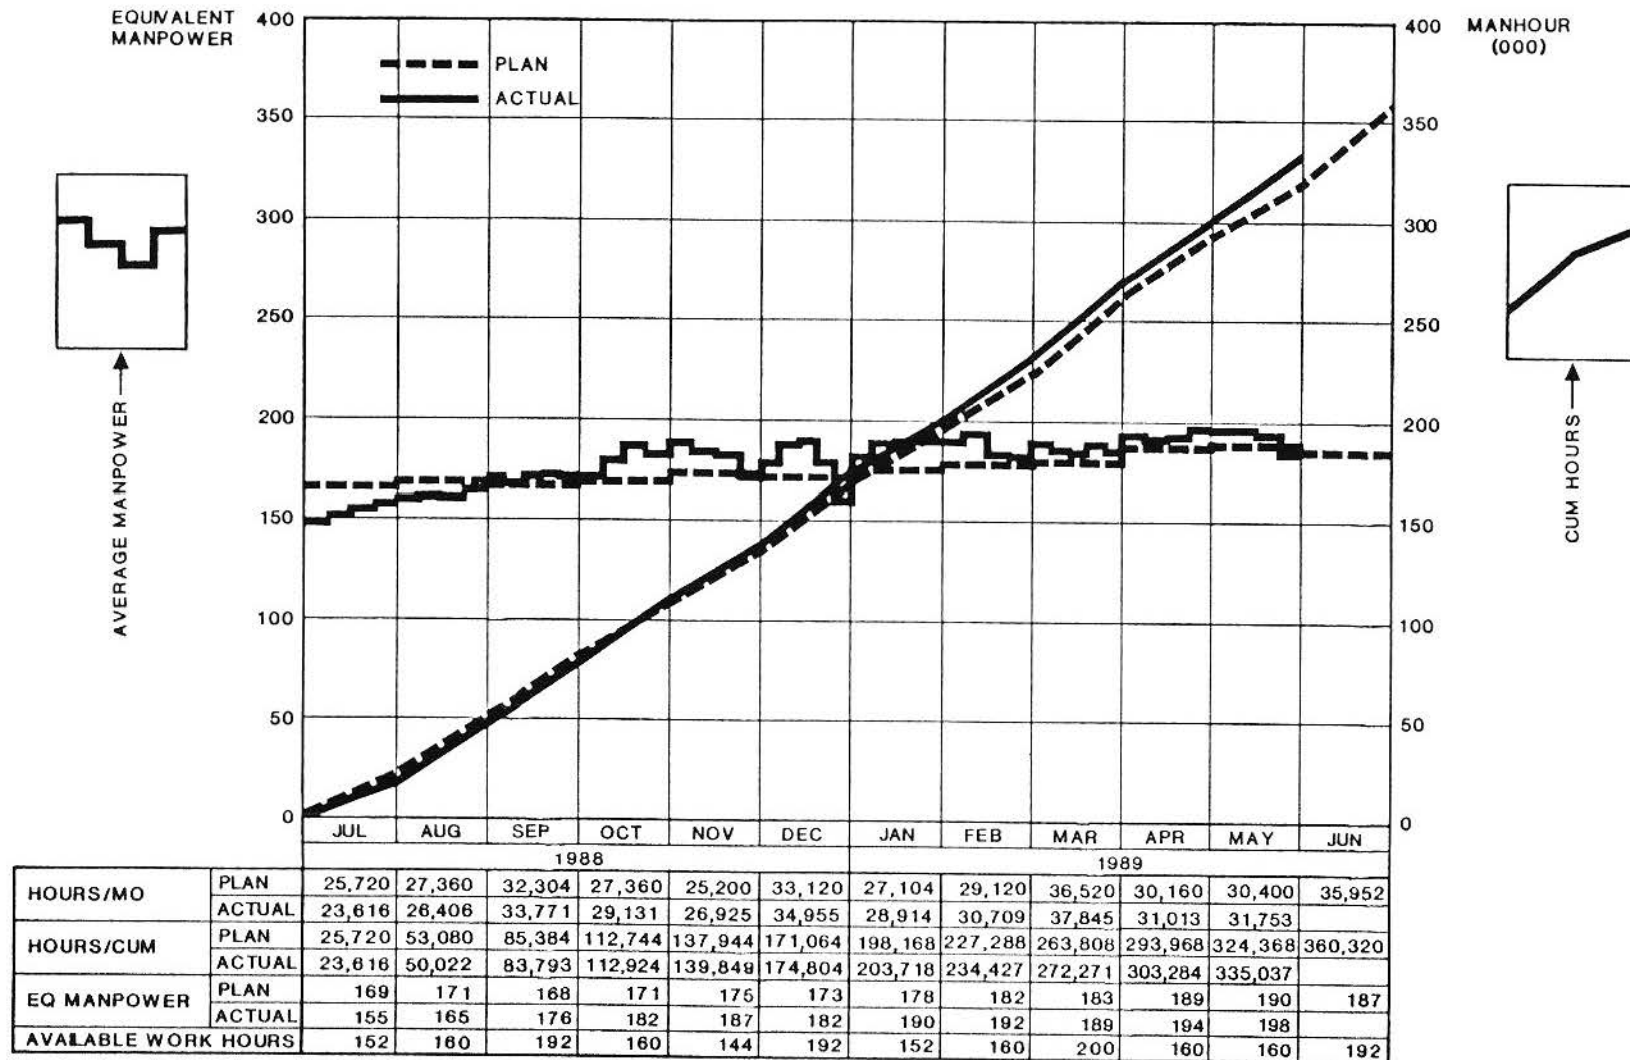

PDCD MANPOWER

Parsons-Dillingham-De Leuw, Cather



LOS ANGELES METRO RED LINE

CONTRACT PERFORMANCE REPORT

PDCD

PERIOD MAY 1989

FIFTH ANNUAL WORK PLAN PDCD MANHOURS BY FUNCTIONAL DEPARTMENT

PAGE 1 OF 3

			1988						1989						
DESCRIPTION (MHS)			JULY	AUGUST	SEPTEMBER	OCTOBER	NOVEMBER	DECEMBER	JANUARY	FEBRUARY	MARCH	APRIL	MAY	JUNE	TOTALS
MANHOURS BY FUNCTIONAL DEPARTMENT															
A Project Management and Secretarial	Plan	current	2,736	2,880	3,456	2,880	2,592	3,456	2,736	2,880	3,600	2,880	2,880	3,456	36,432
		cumulative	2,736	5,616	9,072	11,952	14,544	18,000	20,736	23,616	27,216	30,096	32,976	36,432	
	Actual	current	3,052	3,037	3,625	3,063	2,619	3,625	3,274	3,414	4,154	3,716	3,558		
		cumulative	3,052	6,089	9,714	12,777	15,396	19,021	22,295	25,709	29,863	33,579	37,137		
C Facilities Construction Management	Plan	current	9,400	10,160	11,984	10,320	9,536	12,368	10,320	11,120	14,200	11,840	12,160	14,208	137,616
		cumulative	9,400	19,560	31,544	41,864	51,400	63,768	74,088	85,208	99,408	111,248	123,408	137,616	
	Actual	current	9,697	10,632	13,438	12,086	11,439	15,144	12,354	13,150	16,050	12,949	13,276		
		cumulative	9,697	20,329	33,767	45,853	57,292	72,436	84,790	97,940	113,990	126,939	140,215		
E Systemwide Construction Management	Plan	current	1,304	1,200	1,584	1,200	1,392	1,616	1,456	1,360	1,840	1,520	1,520	1,776	17,768
		cumulative	1,304	2,504	4,088	5,288	6,680	8,296	9,752	11,112	12,952	14,472	15,992	17,768	
	Actual	current	895	1,062	1,378	1,252	1,046	1,375	1,047	1,075	1,463	1,357	1,495		
		cumulative	895	1,957	3,335	4,587	5,633	7,008	8,055	9,130	10,593	11,950	13,445		
F General Services	Plan	current	1,984	2,080	2,464	1,920	1,744	2,272	1,832	1,920	2,360	1,920	1,920	2,272	24,688
		cumulative	1,984	4,064	6,528	8,448	10,192	12,464	14,296	16,216	18,576	20,496	22,416	24,688	
	Actual	current	2,083	2,408	3,642	2,644	2,554	3,051	2,172	2,155	2,888	2,370	2,066		
		cumulative	2,083	4,491	8,133	10,777	13,331	16,382	18,554	20,709	23,597	25,967	28,033		
K Project Controls	Plan	current	4,184	4,480	5,264	4,560	4,032	5,456	4,336	4,560	5,840	4,720	4,720	5,616	57,768
		cumulative	4,184	8,664	13,928	18,488	22,520	27,976	32,312	36,872	42,712	47,432	52,152	57,768	
	Actual	current	2,882	3,203	3,498	3,743	3,275	4,353	3,765	4,050	5,306	4,326	4,854		
		cumulative	2,882	6,085	9,583	13,326	16,601	20,954	24,719	28,769	34,075	38,401	43,255		
L Contracts/Procurement	Plan	current	456	480	576	480	432	576	456	480	600	480	480	576	6,072
		cumulative	456	936	1,512	1,992	2,424	3,000	3,456	3,936	4,536	5,016	5,496	6,072	
	Actual	current	445	471	509	407	388	447	385	422	447	354	442		
		cumulative	445	916	1,425	1,832	2,220	2,667	3,052	3,474	3,921	4,275	4,717		
M Engineering Services/ Systems Integration	Plan	current	2,976	2,960	3,536	2,960	2,672	3,536	3,128	3,600	4,280	3,520	3,520	3,968	40,656
		cumulative	2,976	5,936	9,472	12,432	15,104	18,640	21,768	25,368	29,648	33,168	36,688	40,656	
	Actual	current	2,440	3,048	4,247	3,784	3,063	3,762	3,329	3,847	4,164	3,194	3,358		
		cumulative	2,440	5,488	9,735	13,019	16,082	19,844	23,173	27,020	31,184	34,378	37,736		
N Community Relations	Plan	current	304	320	384	320	288	384	304	320	400	320	320	384	4,048
		cumulative	304	624	1,008	1,328	1,616	2,000	2,304	2,624	3,024	3,344	3,664	4,048	
	Actual	current	293	290	361	310	249	292	248	204	375	304	233		
		cumulative	293	583	944	1,254	1,503	1,795	2,043	2,247	2,622	2,926	3,159		



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

FIFTH ANNUAL WORK PLAN PDCD MANHOURS BY FUNCTIONAL DEPARTMENT

PAGE 2 OF 3

			1988						1989						TOTALS
DESCRIPTION (MHS)			JULY	AUGUST	SEPTEMBER	OCTOBER	NOVEMBER	DECEMBER	JANUARY	FEBRUARY	MARCH	APRIL	MAY	JUNE	
P Safety and Security	Plan	current	456	480	576	480	432	576	456	480	600	480	480	576	6,072
		cumulative	456	936	1,512	1,992	2,424	3,000	3,456	3,936	4,536	5,016	5,496	6,072	
	Actual	current	272	320	352	344	416	512	424	464	544	424	432		
		cumulative	272	592	944	1,288	1,704	2,216	2,640	3,104	3,648	4,072	4,504		
Q Quality Assurance	Plan	current	304	480	384	320	208	464	224	400	320	240	240	464	4,048
		cumulative	304	784	1,168	1,488	1,696	2,160	2,384	2,784	3,104	3,344	3,584	4,048	
	Actual	current	240	263	441	406	352	481	406	411	681	552	510		
		cumulative	240	503	944	1,350	1,702	2,183	2,589	3,000	3,681	4,233	4,743		
R Project Administration	Plan	current	912	960	1,152	960	864	1,152	912	960	1,200	960	960	1,312	12,304
		cumulative	912	1,872	3,024	3,984	4,848	6,000	6,912	7,872	9,072	10,032	10,992	12,304	
	Actual	current	752	798	1,327	905	742	1,021	865	910	1,023	870	807		
		cumulative	752	1,550	2,877	3,782	4,524	5,545	6,410	7,320	8,343	9,213	10,020		
S EO Administration	Plan	current	304	320	384	320	288	384	304	320	400	320	320	384	4,048
		cumulative	304	624	1,008	1,328	1,616	2,000	2,304	2,624	3,024	3,344	3,664	4,048	
	Actual	current	152	152	152	192	272	360	261	266	387	262	352		
		cumulative	152	304	456	648	920	1,280	1,541	1,807	2,194	2,456	2,808		
T Labor Relations	Plan	current	0	0	0	0	0	0	0	0	160	0	160	0	320
		cumulative	0	0	0	0	0	0	0	0	160	160	320	320	
	Actual	current	0	0	9	9	0	4	0	0	4	8	4		
		cumulative	0	0	9	18	18	22	22	22	26	34	38		
U Legal Counsel	Plan	current	0	0	0	0	0	160	0	160	0	160	0	160	640
		cumulative	0	0	0	0	0	160	160	320	320	480	480	640	
	Actual	current	0	0	0	0	0	5	0	0	0	0	0		
		cumulative	0	0	0	0	0	5	5	5	5	5	5		
Subtotal (HOURS)	Plan	current	25,320	26,800	31,744	26,720	24,480	32,400	26,464	28,560	35,800	29,360	29,680	35,152	352,480
		cumulative	25,320	52,120	83,864	110,584	135,064	167,464	193,928	222,488	258,288	287,648	317,328	352,480	
	Actual	current	23,203	25,684	32,979	28,645	26,415	34,432	28,530	30,368	37,486	30,686	31,387		329,815
		cumulative	23,203	48,887	81,866	110,511	136,926	171,358	199,888	230,256	267,742	298,428	329,815		



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

FIFTH ANNUAL WORK PLAN PDCD MANHOURS BY FUNCTIONAL DEPARTMENT

PAGE 3 OF 3

			1988												1989	
DESCRIPTION (MHS)			JULY	AUGUST	SEPTEMBER	OCTOBER	NOVEMBER	DECEMBER	JANUARY	FEBRUARY	MARCH	APRIL	MAY	JUNE	TOTALS	
Other Direct Labor																
R. M. Parsons																
K Project Controls	Plan	current	0	0	0	80	80	80	0	80	0	80	0	80	480	
		cumulative	0	0	0	80	160	240	240	320	320	400	400	480		
		Actual	0	582	8	65	82	76	68	44	52	32	134			
L Procurement	Plan	current	0	0	0	0	0	0	0	0	0	0	0	0	0	
		cumulative	0	0	0	0	0	0	0	0	0	0	0	0	0	
		Actual	0	0	0	0	2	0	0	0	0	(11)	0			
N Engineering Services/ Systems Integration	Plan	current	160	320	320	320	320	320	320	160	160	160	160	160	2880	
		cumulative	160	480	800	1,120	1,440	1,760	2,080	2,240	2,400	2,560	2,720	2,880		
		Actual	341	(189)	507	243	511	418	200	148	121	179	103			
D Quality Assurance	Plan	current	0	0	0	0	80	80	80	80	80	80	80	80	640	
		cumulative	0	0	0	0	80	160	240	320	400	480	560	640		
		Actual	0	0	0	0	0	0	0	0	0	0	0	0		
R Administration	Plan	current	0	0	0	0	0	0	0	0	0	0	0	0	0	
		cumulative	0	0	0	0	0	0	0	0	0	0	0	0	0	
		Actual	0	83	80	(96)	61	73	52	96	148	90	113			
	Actual	cumulative	0	83	163	67	128	201	253	349	497	587	700			
		Billingham Construction														
		K Project Controls	Plan	current	0	0	0	0	0	0	0	0	160	160	160	160
cumulative	0			0	0	0	0	0	0	0	0	160	320	480	640	
Actual	0			0	0	0	0	0	0	0	0	0	0	0	0	
N Engineering Services/ Systems Integration	Plan	current	0	0	0	0	0	0	0	0	0	0	0	0	0	
		cumulative	0	0	0	0	0	0	0	0	0	0	0	0	0	
		Actual	72	152	148	272	(160)	4	0	0	0	0	0	0	0	
	Actual	cumulative	72	224	372	644	484	488	488	488	488	488	488			
		DeLeuw, Cather														
		F General Services	Plan	current	80	80	80	80	80	80	80	80	80	80	80	80
cumulative	80			160	240	320	400	480	560	640	720	800	880	960		
Actual	0			0	0	0	0	0	0	0	0	0	0	0	0	
N Engineering Services/ Systems Integration	Plan	current	160	160	160	160	160	160	160	160	240	240	240	240	2240	
		cumulative	160	320	480	640	800	960	1,120	1,280	1,520	1,760	2,000	2,240		
		Actual	0	94	49	2	14	2	64	53	38	27	16			
	Actual	cumulative	0	94	143	145	159	161	225	278	314	343	359			
		Subtotal														
		Plan	current	400	560	560	640	720	720	640	560	720	800	720	800	7,840
cumulative	400		960	1,520	2,160	2,880	3,600	4,240	4,800	5,520	6,320	7,040	7,840			
Actual	413		722	792	486	510	523	384	341	359	327	366				
	Actual	cumulative	413	1,135	1,927	2,413	2,923	3,446	3,830	4,171	4,530	4,857	5,223			
		TOTAL DIRECT LABOR HOURS														
		Plan	current	25,720	27,360	32,304	27,360	25,200	33,120	27,104	29,120	36,520	30,160	30,400	33,952	360,320
cumulative	25,720		53,080	85,384	112,744	137,944	171,064	198,168	227,288	263,808	293,968	324,368	360,320			
Actual	23,616		26,406	33,771	29,131	26,925	34,955	28,914	30,708	37,845	31,613	31,753				
# Negative due to correction to prior period accruals.	Actual	cumulative	23,616	50,022	83,793	112,924	139,849	174,804	203,718	234,426	272,271	303,284	335,037			

SECTION III

**EQUAL OPPORTUNITY
PERFORMANCE**



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

III. EQUAL OPPORTUNITY PERFORMANCE

DBE Participation

The monthly DBE participation for the Fifth Annual Work Plan for May measured on the basis of accrued total cost was 17.1%, 0.1% above the 17% goal. The cumulative percentage for the Fifth Annual Work Plan was 18.3%, 1.3% above the 17% goal (Figure 1).

WBE Participation

The monthly WBE participation for the Fifth Annual Work Plan for May, measured on the basis of accrued total cost was 4.4%, 1.4% above the 3% goal. The cumulative percentage for the Fifth Annual Work Plan was 4.6%, 1.6% above the 3% goal (Figure 2).

Affirmative Action Analysis

The Affirmative Action Analyses for minorities and women, as indicated in Figures 3 and 4, exceeds the established goals of 17% for minorities, and 8% for women by 20% and 0.3% respectively. Minority count adjusted to correct a previous miscalculation in the accumulated total to date.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

FIFTH ANNUAL WORK PLAN

PERIOD MAY 1989

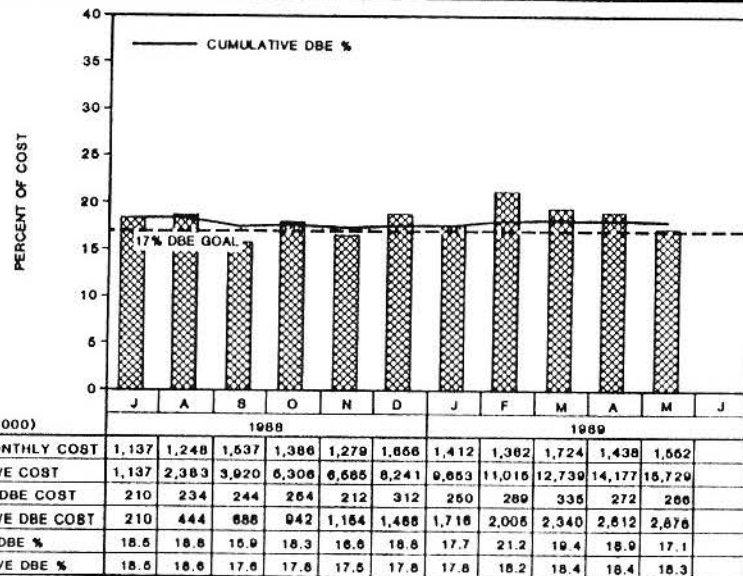


FIGURE 1 - DBE ANALYSIS

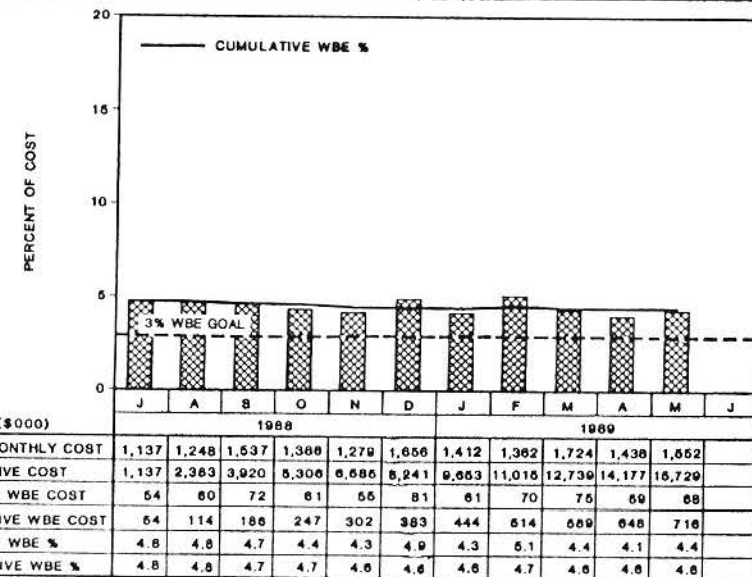


FIGURE 2 - WBE ANALYSIS

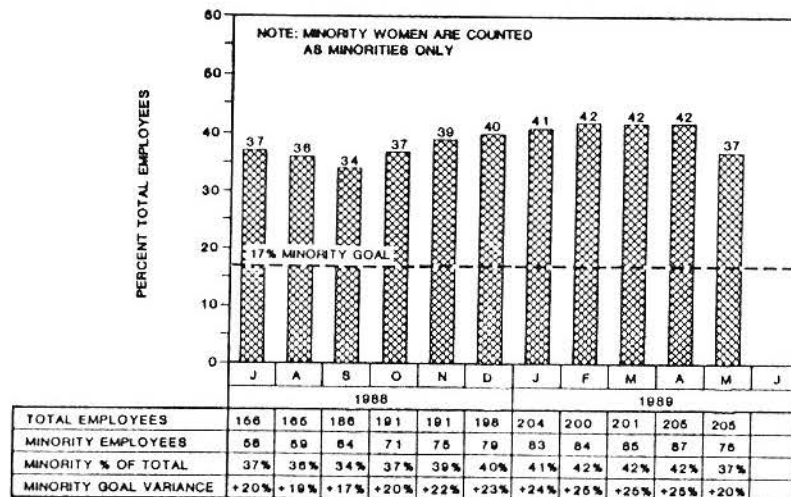


FIGURE 3 - MINORITY AFFIRMATIVE ACTION ANALYSIS

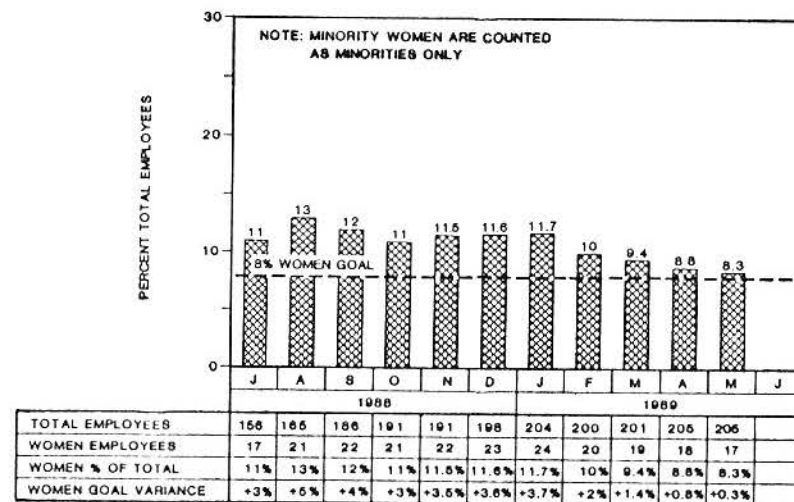


FIGURE 4 - WOMEN AFFIRMATIVE ACTION ANALYSIS

SECTION IV

SCHEDULE PERFORMANCE

MTA LIBRARY



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

IV. SCHEDULE PERFORMANCE

CONTRACTOR SUBMITTALS - During this period, 339 submittals were received from the Construction Contractors and 206 were carried over from April. 325 packages were processed (approved, approved-as-noted, rejected and reviewed for record only) and returned to the Contractors as shown in the following tabulation. The balance (220) are still under review.

<u>Contracts</u>	<u>Carryover From April</u>	<u>No. of Submittals Received in May</u>	<u>Submittals Processed Within 30 Days</u>	<u>Submittals Processed In Over 30 Days</u>	<u>Carryover to June</u>
A112	9	19	10	3	15
A130	25	26	27	0	24
A135	7	21	17	0	11
A135BH	25	15	24	1	15
A141	16	37	25	6	22
A145/A145A	12	25	21	0	16
A146	0	8	1	0	7
A165	56	83	77	3	59
A167	0	1	0	0	1
A171	18	21	20	4	15
A175	13	20	20	1	12
A610/A115	4	18	17	0	5
A612	1	0	1	0	0
A615	0	1	0	0	1
A616	1	5	0	0	6
A620	5	12	12	1	4
A630	4	4	6	0	2
A640	2	12	8	6	0
A710	3	5	5	1	2
A732	1	0	0	0	1
A740	1	3	3	0	1
A745	1	1	2	0	0
A750	0	2	1	0	1
A795	2	0	2	0	0
Total	206	339	299	26	220



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

Construction Package Reviews - Analysis of the activities on the "Design Packages Status Window Report, Current Period", (Page 19), shows the following document review:

- o Constructibility Reviews - Completed constructibility review for A117/100%, Yard Site Lighting and Started A187/100%, Wilshire/Alvarado Station, Stage II.

Training Programs

(None)



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

DESIGN PACKAGE STATUS WINDOW REPORT - CURRENT PERIOD 4-29-89 TO 5-26-89

Contract #	Description	Pkg Type	Review Code	Schedule Receipt	Received	Schedule Complete	Actual Complete	SC	Remarks
A-117	YARD SITE LIGHTING	DWGS	DC100%		03-31-89	05-05-89	05-10-89		*NOT SCHEDULED, IN-HOUSE TARGET DATE.
A-117	YARD SITE LIGHTING	SPEC	DC100%		03-31-89	05-05-89	05-10-89		*NOT SCHEDULED, IN-HOUSE TARGET DATE.
**									
A-187	WILSHIRE/ALVARADO STATION (STAGE II)	DWGS	FS100%	06-01-89	05-22-89	06-12-89			ADVANCE DWGS.
**									

3 records listed. 3 values listed .

Review Codes :	LT60 - Less than 60%	IP60 - In progress 60%	PF85 - Prefinal 85%
	PF90 - Prefinal 90%	FS100 - Final submittal 100%	DC100 - Final design complete 100%
	CAR- Claims Avoidance Review	CE - Check Estimate	

NOTE : Based on 6-1-89, MRTC Design Review Schedule



SECTION V

COST PERFORMANCE



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

V. COST PERFORMANCE

FIFTH ANNUAL WORK PLAN

Total incurred costs of \$1,476,145 (Page 25) for CM Direct Services (without General Condition Items) for the period were over the plan of \$1,432,056 by \$44,089. This variance results from the net effect of Other Direct Costs (ODCs) being over the plan by \$14,953 and Labor expenditures (total PDCD and subcontractors) being over the plan by \$29,136.

The cumulative costs for Total CM Services (including General Condition Items) incurred through May were \$15,728,859 against a plan of \$15,821,617 resulting in an under plan expenditure of \$92,758 (Page 25).

The May CPR forecasts (Page 25) an estimate at completion of \$17,505,517 versus a plan of \$17,625,378 for an underexpenditure of \$119,861. Extracting the General Condition Items and reporting them separately, the May CPR forecasts a CM Direct Services estimate at completion of \$16,612,214 versus a plan of \$16,961,078 for an under plan expenditure of \$348,864.

GENERAL CONDITION ITEMS

General Condition Items (GCI's) expenditure of \$76,214 were over the plan of \$44,192 for the period by \$32,022. This report forecasts an estimate at completion (EAC) in the 5th AWP period for GCI's of \$893,303 versus a plan of \$664,300, for a projected overplan expenditure of \$229,003. (Page 24)

LABOR COSTS

The average hourly labor rate, including burdens and fees, experienced for the period was \$41.47/hr. compared to a plan rate of \$42.36 (-)/hr., resulted in a difference of \$0.89 (-) per hour.

The variances can be summarized into two categories:

STAFFING VARIANCE

8.456 equivalent staff over plan @ 160
hours at \$42.3552/hour =

IMPACT ON MAY COSTS

\$ 57,307



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989RATE VARIANCE198,456 actual staff equivalent @ 160 hours
@ \$0.08872/hour =

(28,171)

MAY COST VARIANCE TO PLAN

\$ 29,136OTHER DIRECT COSTSOther Direct Costs (ODCs) were over the plan for the period by a net of \$14,953 as follows:

DESCRIPTION	CURRENT PERIOD DOLLARS			CUMULATIVE DOLLARS		
	BUDGET	ACTUAL	VARIANCE	BUDGET	ACTUAL	VARIANCE
(1)Field Office Expenses	60,324	54,945	- 5,379	656,511	578,371	- 78,140
(2)Office Equipment	16,371	62,832	-46,461	165,529	155,935	- 9,594
(3)Travel & Relocation	28,550	8,514	-20,036	296,450	134,578	-161,872
(4)Vehicles & Maintenance	5,189	3,436	- 1,753	87,375	47,105	- 40,270
(5)Reproduction	5,980	3,569	- 2,411	68,448	55,572	- 12,876
(6)Telephone & Telex	7,396	5,603	- 1,793	84,656	59,475	- 25,181
(7)Computer Operation Support	3,242	5,354	2,112	35,662	25,148	- 10,514
(8)Gross Receipt Tax	7,893	9,000	1,107	84,587	84,408	- 179
(9)Field Equipment	9,513	6,158	- 3,355	96,187	53,919	- 42,268
S/T ODC's	144,458	159,411	<u>14,953</u>	1,575,405	1,194,511	-380,894

NOTES

- (1) Field Office Expenses - underexpenditure due to underrun in equipment maintenance and supplies.
- (2) Office Equipment - overexpenditure due to the purchase of Personal Computers and related software.
- (3) Travel and Relocation - Due to lower than planned expenditures combined with an accrual adjustment.
- (4) Vehicles & Maintenance - underexpenditure due to lower than planned maintenance costs.
- (5) Reproduction - underexpenditure due to lower than planned reproduction.
- (6) Telephone and Telex - underexpenditure due to lower communications cost.
- (7) Computer Operation Support - overexpenditure due to higher than normal DMCS costs.
- (8) Gross Receipt Tax - varies directly with the actual cumulative rate of expenditure per period.
- (9) Field Equipment - underexpenditure due to lower than planned expenditures.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

CM COST PERFORMANCE - MAY 1989 FIFTH ANNUAL WORK PLAN

(\$000)

	PLANNED	ACTUAL	VARIANCE	%
PDCD				
LABOR, BURDENS, FEE				
CUMULATIVE THROUGH APRIL	\$ 7931	\$ 7984	\$ 53	0.67%
CURRENT MONTH	808	871	63	7.80%
CUMULATIVE THROUGH MAY	\$ 8739	\$ 8855	\$ 116	1.33%
TRAVEL AND ODC'S				
CUMULATIVE THROUGH APRIL	\$ 1431	\$ 1,035	\$ (396)	-27.67%
CURRENT MONTH	145 *	160	15	10.34%
CUMULATIVE THROUGH MAY	\$ 1576	\$ 1,195	\$ (381)	-24.18%
SUBCONTRACTORS				
CUMULATIVE THROUGH APRIL	\$ 4,508	\$ 4,422	\$ (86)	-1.91%
CURRENT MONTH	479	445	(34)	-7.10%
CUMULATIVE THROUGH MAY	\$ 4,987	\$ 4,867	\$ (120)	-2.41%
SUBTOTAL CM DIRECT SERVICES				
CUMULATIVE THROUGH APRIL	\$ 13,870	\$ 13,441	\$ (429)	-3.09%
CURRENT MONTH	1,432	1,476	44	3.07%
CUMULATIVE THROUGH MAY	\$ 15,302	\$ 14,917	\$ (385)	-2.52%
GENERAL CONDITION ITEMS				
CUMULATIVE THROUGH APRIL	\$ 476	\$ 736	\$ 260	54.62%
CURRENT MONTH	44	76	32	72.73%
CUMULATIVE THROUGH MAY	\$ 520	\$ 812	\$ 292	56.15%
TOTAL CM SERVICES				
CUMULATIVE THROUGH APRIL	\$ 14,346	\$ 14,177	\$ (169)	-1.18%
CURRENT MONTH	1,476	1,552	76	5.15%
CUMULATIVE THROUGH MAY	\$ 15,822	\$ 15,729	\$ (93)	-0.59%
HOURS				
CUMULATIVE THROUGH APRIL	293,968 hrs	303,284 hrs	9,316 hrs	3.17%
CURRENT MONTH	30,400	31,753	1,353	4.45%
CUMULATIVE THROUGH MAY	324,368 hrs	335,037 hrs	10,669 hrs	3.29%

* OFF BY 1 DUE TO ROUNDING




LOS ANGELES METRO RED LINE

PDCD


CONTRACT PERFORMANCE REPORT

FIFTH ANNUAL WORK PLAN


PERIOD MAY 1989

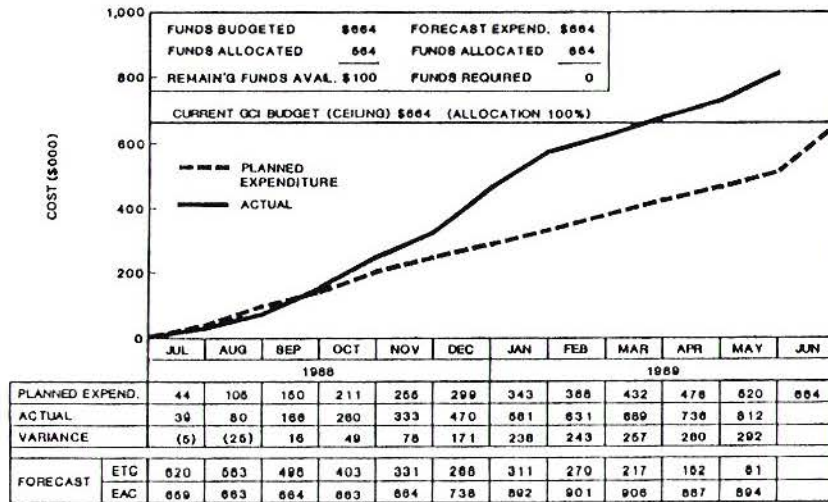

GENERAL CONDITION ITEMS CUMULATIVE COST PERFORMANCE

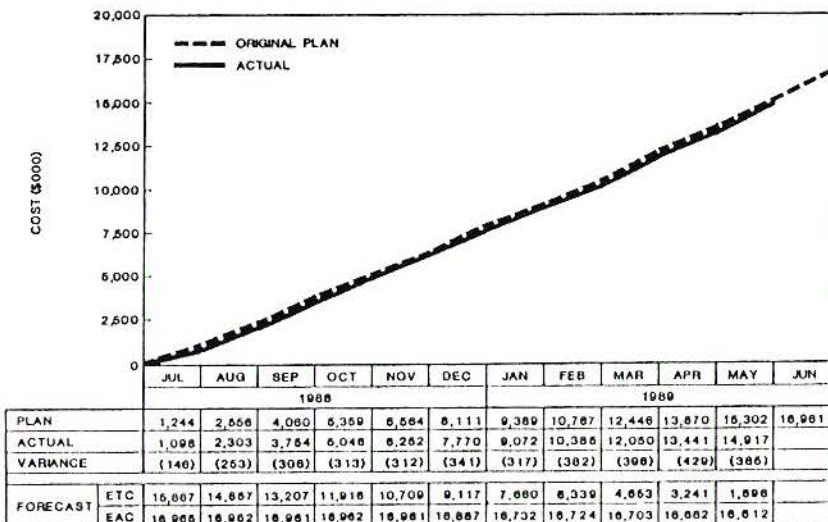

CM DIRECT SERVICES CUMULATIVE COST PERFORMANCE

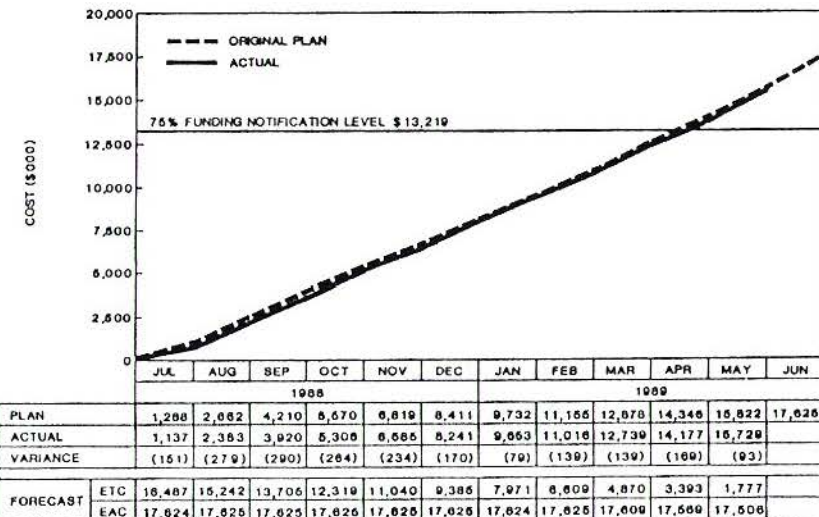

TOTAL CM SERVICES (INCLUDING G.C.I.'s) CUMULATIVE COST PERFORMANCE



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

PDCD CM SERVICES - 5TH ANNUAL WORK PLAN COST REPORT FOR MONTH ENDING MAY 26, 1989 REPORT SUMMARIZED BY RESPONSIBILITY

GENERAL CONDITION ITEMS

RESPONSIBILITY CD-DESCRIPTION	CURRENT PERIOD DOLLARS			CUMULATIVE DOLLARS			ESTIMATE TO COMPL	AT COMPLETION DOLLARS		
	BUDGET	ACTUAL	VAR.	BUDGET	ACTUAL	VARIANCE		BUDGET	ESTIMATE	VARIANCE
B GUARD SERVICES	7,750	6,120	-1,630	85,250	65,941	-19,309	7,750	93,000	73,691	-19,309
D FIELD OFFICE TRAILERS	0	0	0	34,000	0	-34,000	0	34,000	0	-34,000
E CLEAN-UP OF FIELD SITES	0	1,675	1,675	0	16,688	16,688	2,000	0	18,688	18,688
F WTF EXPENSES	0	0	0	0	24,703	24,703	0	0	24,703	24,703
G SIGNS AND BARRICADES	0	-2,000	-2,000	0	40,317	40,317	0	0	40,317	40,317
X CONSTRUCTION PHOTO	3,525	4,995	1,470	38,775	50,955	12,180	6,525	42,300	57,480	15,180
Y TESTING PROGRAM	32,917	65,424	32,507	362,087	613,424	251,337	65,000	395,000	678,424	283,424
S/T ALLOCATED	44,192	76,214	32,022	520,112	812,028	291,916	81,275	564,300	893,303	329,003
Z UNALLOCATED	0	0	0	0	0	0	0	100,000	0	-100,000
S/T GEN. COND. ITEMS	44,192	76,214	32,022	520,112	812,028	291,916	81,275	664,300	893,303	229,003



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

PDCD CM SERVICES - 5TH ANNUAL WORK PLAN COST REPORT FOR MONTH ENDING MAY 26, 1989 REPORT SUMMARIZED BY RESPONSIBILITY

RESPONSIBILITY CD-DESCRIPTION	CURRENT PERIOD DOLLARS BUDGET	ACTUAL	VAR.	CUMULATIVE DOLLARS BUDGET	ACTUAL	VARIANCE	ESTIMATE TO COMPL	AT COMPLETION DOLLARS BUDGET	ESTIMATE	DOLLARS VARIANCE
A PROJECT MANAGEMENT	82,933	89,970	7,037	949,581	917,796	-31,785	96,916	1,049,100	1,014,712	-34,388
C FAC. CONSTRUCTION	450,231	499,588	49,357	4,606,613	5,106,635	500,022	604,042	5,131,561	5,710,677	579,116
E SYSTEMWIDE CONST	51,287	64,424	13,137	545,784	553,678	7,894	76,485	605,480	630,163	24,683
F GENERAL SERVICES	85,389	86,807	1,418	984,584	1,114,851	130,267	99,217	1,084,962	1,214,068	129,106
K PROJECT CONTROLS	215,231	205,482	-9,749	2,323,315	1,819,025	-504,290	248,116	2,581,921	2,067,141	-514,780
L PROCUREMENT	21,331	19,911	-1,420	244,242	210,786	-33,456	26,003	269,840	236,789	-33,051
M ENG. SVCS./SYST. INTEGR.	184,794	171,565	-13,229	1,910,084	2,058,907	148,823	190,860	2,108,035	2,249,767	141,732
N COMMUNITY RELATIONS	12,181	9,534	-2,647	139,470	123,374	-16,096	16,343	154,087	139,717	-14,370
P SAFETY	22,141	20,470	-1,671	253,512	204,582	-48,930	26,949	280,081	231,531	-48,550
Q QUALITY ASSURANCE	16,322	24,517	8,195	206,370	232,064	25,694	25,319	232,452	257,383	24,931
R PROJECT ADMIN.	33,723	31,279	-2,444	386,131	371,469	-14,662	42,369	436,598	413,838	-22,760
S EQUAL OPPORTUNITY	14,803	14,640	-163	169,497	119,369	-50,128	16,268	187,260	135,637	-51,623
T LABOR RELATIONS	10,702	262	-10,440	21,405	2,492	-18,913	0	21,405	2,492	-18,913
U LEGAL	0	0	0	60,000	3,887	-56,113	0	80,000	3,887	-76,113
S/T LABOR-BRDN & OH	1,201,068	1,238,449	37,381	12,800,588	12,838,915	38,327	1,468,887	14,222,782	14,307,802	85,020
1 FIELD OFFICE EXPENSES	60,324	54,945	-5,379	656,511	578,371	-78,140	48,725	718,100	627,096	-91,004
2 OFFICE EQUIPMENT	16,371	62,832	46,461	165,529	155,935	-9,594	22,619	181,900	178,554	-3,346
3 TRAVEL & RELOCATION	28,550	8,514	-20,036	296,450	134,578	-161,872	14,170	325,000	148,748	-176,252
4 VEHICLES & MAINT.	5,189	3,436	-1,753	87,375	47,105	-40,270	5,009	93,600	52,114	-41,486
5 REPRODUCTION	5,980	3,569	-2,411	68,448	55,572	-12,876	7,185	75,600	62,757	-12,843
7 TELEPHONE & TELEX	7,396	5,603	-1,793	84,656	59,475	-25,181	5,000	93,500	64,475	-29,025
8 COMPUTER OPERATION SUPPT.	3,242	5,354	2,112	35,662	25,148	-10,514	3,000	38,900	28,148	-10,752
9 GROSS RECEIPT TAX	7,893	9,000	1,107	84,587	84,408	-179	9,511	94,230	93,919	-311
A FIELD EQUIPMENT	9,513	6,158	-3,355	96,187	53,919	-42,268	7,513	105,700	61,432	-44,268
S/T ODC'S	144,458	159,411	14,953	1,575,405	1,194,511	-380,894	122,732	1,726,530	1,317,243	-409,287
W PDCD FEE	50,000	50,000	0	550,000	550,000	0	45,000	595,000	595,000	0
X S/C FEE	36,530	28,285	-8,245	375,512	333,405	-42,107	58,764	416,766	392,169	-24,597
S/T FEES	86,530	78,285	-8,245	925,512	883,405	-42,107	103,764	1,011,766	987,169	-24,597
S/T CM DIRECT SVCS	1,432,056	1,476,145	44,089	15,301,505	14,916,831	-384,674	1,695,383	16,961,078	16,612,214	-348,864
S/T GEN. COND. ITEMS	44,192	76,214	32,022	520,112	812,028	291,916	81,275	664,300	893,303	229,003
TOTAL CM SERVICES	1,476,248	1,552,359	76,111	15,821,617	15,728,859	-92,758	1,776,658	17,625,378	17,505,517	-119,861

PERCENT OF BUDGET EXPENDED = 89%

NEGATIVE VARIANCE INDICATES UNDERRUN

SECTION VI

ADDITIONAL ACTIVITIES

PERFORMED IN MAY



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

VI. ADDITIONAL ACTIVITIES PERFORMED IN MAY

The following activities performed by the CM functional organization are in addition to the activities presented in other sections of this report.

A. ADMINISTRATION AND ACCOUNTING

- (1) Continued to assist the Resident Engineers in the supply of administrative material and the assignment/orientation of new field personnel at the field offices.
- (2) Continued processing of personnel (acquisition and termination).
- (3) Coordinated audit responses from Associate Subcontractors to RTD Audit Department.

B. Quality Assurance

- (1) Conducted field surveillance of welding activities in support of Contracts A135, A145, A165, A171 and shop fabrication surveillance at Paramount Steel, COWELCO, and Angeles Steel.
- (2) Finalized "Preparation of As-Built Drawings Procedure" based on PDCD responsibility for "as-built" drawings preparation.
- (3) Met with A112 R.E. to review proposed contract physical close-out procedure.
- (4) Continued to conduct training classes to prepare inspectors for ACI Concrete Technician I certification.
- (5) Finalized and transmitted Acromedia (Bechtel subcontractor on A640) Audit Report.
- (6) Witnessed acceptance testing at Ayden Controls, Bechtel A640 subcontractor.
- (7) Continued monitoring of Testing Lab (Smith-Emery) performance and costs.
- (8) Continued surveillance of HDPE installation (A141, A165, A171 and A175) and witnessing of fire protection system hydrostatic tests at A165 and A175.
- (9) Conducted field QA audit of lift drawings (A130 and A141) to verify conformance with review and approval process.

C. Equal Opportunity Administration

- (1) Monitored Equal Opportunity reporting requirements (i.e. SSA&P Report, Monthly Employment Utilization Reports, Certified Payroll) for Contract Nos. A112, A130, A135, A141, A145, A146, A165, A167, A171, A175, A610/A115, A612, A615, A616, A620, A640, A710, A732, A740, A745, A750 and A795.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

- (2) Conducted project site visits/employee interviews at the following sites: A112, A130, A135, A141, A145, A146, A165, A171, A175 and A610/A115.
- (3) Processed penalty assessments for the late submittal of the Monthly Employment Utilization Reports for Contracts A112, A130, A135, A141, A144, A145, A165 and A175.

D. Contracts and Procurement

- (1) Prepared amendments to increase funding for subcontracts with Martin and Huang and Construction Control Services Corporation to cover remaining AWP-5 requirements.
- (2) Prepared and submitted for District approval an Amendment to the Construction Photographic Services Subcontract to incorporate Change Orders No. 2 and 3, to increase AWP-5 funding and to remove unexpended AWP-4 funding.
- (3) Received District approval and issued Amendments to increase AWP-5 funding for temporary personnel services subcontract with WCI.
- (4) Following District approval, issued purchase orders for 12 PC's and related software.
- (5) Issued Request for Quotations for renewing annual agreement covering reproduction services.

E. Community Relations

- (1) Coordinated community notifications for A141, A145, A146, A165 and A175 and LAPD traffic control assistance for A141.
- (2) Coordinated mitigation of traffic concerns for tenants along Hill St. affected by A141 and A145 traffic access plans, and for tenants in the 7th/Flower area affected by A165 and A146 traffic plans.
- (3) Provided assistance to A141, A145, A146 and A165 for problems caused by street closures and lane restrictions, blocked access, noise and accidents.
- (4) Assisted RTD with coordination of the "hole thru" media event for Civic Center Station.
- (5) Assisted RTD in coordination for the LAUPT 50th Anniversary Celebration event.
- (6) Coordinated safety and security meeting with LAPD.
- (7) Provided assistance to PDCD/RTD in coordinating site visits and responding to media requests.
- (8) Processed 24 inquiries/complaints.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

F. Safety and Security

- (1) Performed daily construction site safety, health and security surveillances on a two shift basis and prepared written reports for the A112, A130, A135, A141, A145, A146, A165, A171, A175 and A610/A115 construction projects.
- (2) Coordinated activities of the Systemwide Security Guard Service and the Systemwide Clean-up Service subcontractors.

G. Construction Operations

- (1) Continued construction management (CM) services for Contracts A112, A130, A135, A141, A143, A144, A145/A145A, A146, A165, A167, A171, A175, A610/A115, A612, A615, A616, A620, A630, A640, A710, A732, A740, A745, A750 (4984, 4986, 4988) and A795; monitoring of Master Agreement Work and submittal reviews.
- (2) Continued coordination of traffic control plans and street closures with city agencies for A130, A141, A145, and A165.
- (3) Continued coordination of MOS-1 inspections with LADOT.
- (4) Processed a total of 18 Traffic and Utilities related submittals.
- (5) Continued monitoring of ground water and construction water discharges at A141, A144, A145, A146, A165, A171 and A175.
- (6) Continued monitoring Discharge Monitoring Stations at the Ballona Creek and Los Angeles River.
- (7) Prepared and submitted March Discharge Monitoring Report (DMR) to the California Regional Water Quality Board (CRWQCB).
- (8) Prepared and submitted March LA River Dissolved Solids Report to Central and West Basin Water Replenishment District (CWBWRD).
- (9) Coordinated and inspected installation of water treatment facilities at A141.
- (10) Inspected asbestos abatement at the Equitable Building, A145.
- (11) Reviewed and approved final asbestos submittal and reviewed clearance report for asbestos abatement at REA building, A135.
- (12) Completed and submitted closure report for 4 tank abandonments at A165.
- (13) Properly abandoned underground storage tanks at A145.
- (14) Monitored removal, relocation and disposal of contaminated soil at A175.
- (15) Coordinated acceptance of contaminated soil from A146 at Class II landfill.

MTA LIBRARY



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

- (16) Continued monitoring instrumentation, building and ground settlement points on A135, A141, A145, A146, A165, A171 and A175.
- (17) Continued location survey at yards and shop contracts.
- (18) Checked slabs poured at A141 and A175 excavation.
- (19) Continued performing as-built cross section of AR Tunnel invert pour (A171).
- (20) Continued checking arch form alignment AL tunnel (A171).
- (21) Performed tunnel alignment check AR tunnel (A-141).
- (22) Continued tunnel alignment check at AL tunnel (A146).
- (23) Checked layout of A165 station.

H. Engineering Services

- (1) Completed site geologic inspection of A146 AL tunnel and began compiling geologic profile for use in predicting the geology along the AR tunnel alignment.
- (2) Coordinated with MRTC to develop an acceptable method for taking tunnel liner distortion measurements in Contract A146, where the shield configuration precludes use of the specified method.
- (3) Recommended and coordinated the reduction of the Contractor's Civic Center Station strain gauge readings from once per day to once per week.
- (4) Reviewed the A130 Contractor's method of orienting the horizontal chemical grout holes to be drilled beneath the Santa Ana Freeway.
- (5) Inspected drilling of A130 pre-grouting proof test sample holes.
- (6) Completed reviewing and cross checking results of Proctor testing performed by Smith-Emery Company.
- (7) Completed data gathering phase of the A141 Design Verification Study Plan, Task C.
- (8) Researched question of whether sub-ballast material is acceptable as crushed aggregate material throughout the A610/115 job site.
- (9) Responded to 98 requests for information or documentation clarification from various contractors.
- (10) Processed 8 field inquiries with MRTC to obtain clarification of design requirements.
- (11) Coordinated with the FLSC Fire Chiefs, MRTC, and A146 Contractor regarding fire protection system at cross passages.
- (12) For Contract A112 - Approved 5 Contractor submittals for HVAC details, emergency trip stations, switches, receptacles, cover plates, first floor plumbing plans, and finish carpentry sample particle board.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

Approved -as-Noted 7 Contractor submittals for metal decking, fire sprinkler calculations, sump pump water heaters, diesel generator data, HVAC operation & maintenance manual, and wheel truing pit car puller.

Rejected 1 Contractor submittal for welding procedures & welder qualifications.

- (13) For Contract A130 - Approved 14 Contractor submittals for manganese anodes data sheet, shoring for jack pits, fire protection product data for expansion joints & temperature ratings, alternative tieback/soldier pile data, design of end bulkhead, pipe supports for utilities, piped utilities G5 traffic valve, rebar mill test reports for slurry wall panels, rebar mill certificates, box invert, and HDPE qualified personnel.

Approved-as-Noted 8 Contractor submittals for slurry wall layout & design drawings, utilities concrete vault, utilities backflow preventer, instrumentation resumes organizational charts & forms, traffic control drawings, cast-in-place underpinning piles/lift drawings, and shoring systems drawings for two cell box.

Rejected 3 Contractor submittals for lift drawing for west retaining wall, dewatering data, and vent systems data sheets.

Reviewed For Record Only 2 Contractor submittals for "proposed Compaction Grouting Program Commercial Street Vicinity, and inclinometer #4 installation notes & soil samples.

- (14) For Contract A135 - Approved 8 Contractor submittals for light standards, rebar mill test reports for slurry wall panel, rebar mill test reports for platform, concrete pull box, platform #3 canopy extension, temporary vehicular bridge, and various Certificates of Compliance.

Approved-as-Noted 3 Contractor submittals for temporary railroad bridge, tieback & anchor design calculations for slurry wall, and pullbox for ductbank.

Rejected 6 Contractor submittals for fire system welding procedures, service walkway precast concrete unit, 36" I.D. reinforced manhole specification sheets & certifications, demolition of REA Bldg., manhole plan & details, and monthly status report.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

- (15) For Contract A135BH (Baggage Handling) - Approved 11 Contractor submittals for concrete inserts, mechanical parts & manufacture data for custom conveyors, fire proofing material certifications, 6" fire protection check valves, conveyor anchoring detail, aggregate, and material certifications for fasteners and metal decking.

Approved-as-Noted 9 Contractor submittals for HVAC layout in basement and street level, basement piping, material certifications, panel boards/circuit breakers, structural steel modifications, anchor bolt details, welding procedures, and ceramic tile.

Rejected 5 Contractor submittals for temperature control, drinking fountain catalog data, elastometric coating, unit substation, and 225 KVA transformer.

- (16) For Contract A141 - Approved 17 Contractor submittals for rebar reinforcement drawings, concrete lift drawings, grating grounding sketch, split couplings catalog data, cast metal auxiliary junction box data, chemical admixture for concrete, ground resistance test results, reinforced concrete pipe product design, excavation support for blast relief shafts, pipe assembly details for 36" vent line, concrete inserts, backfill & base slab mix designs, and storm drainage system certificates of compliance.

Approved-as-Noted 13 Contractor submittals for tunnel cross passage support system, various rebar drawings, various concrete lift drawings, air test procedure for station drain piping, NBRS backfill support plan and bulkhead report, ground surface settlement points, structural backfill test reports, and rebar certificates.

Reviewed for Record Only 1 Contractor submittal for monthly status & narrative.

- (17) For Contract A145 - Approved 7 Contractor submittals for fire protection coating for pipe sleeves, haul route for contaminated materials, calculations for long span lagging, rebar bent supplement, sanitary sewer line C temporary support, revised limits of lagging, and manufacturer's data and samples.

Approved-as-Noted - 12 Contractor submittals for HDPE panel layout drawings, HDPE weld test method, revised CPM baseline (Part II) schedule, welder's qualifications, base slab bulkhead form & screed details, lift drawings for inverts, rebar drawings and grade beam details, column form drawing & calculations, mezzanine falsework & forms, and exterior wall form at mezzanine level.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

Reviewed For Record Only 2 Contractor submittals for Equitable Bldg. electrical drawing, and concrete mix data for slurry backfill.

(18) For Contract A146 - Approved 1 Contractor submittal for temporary vent shaft details.

(19) For Contract A165 - Approved 31 Contractor submittals for various lift drawings, various rebar drawings for exterior wall and base slab, test procedures for fire protection, mechanical piping welder qualifications, PA speaker mounting details, split couplings, Certificates of Compliance for fire protection, acid resistant coating for Battery Room, and rebar mill test reports.

Approved-as-Noted 46 Contractor submittals for sewer specification; various lift drawings for roof slab, LRT platform, interior walls, exterior walls, and base slab; various rebar drawings for base slab and interior walls, miscellaneous HVAC data & specification sheets, excavation support system east bulkhead - 7th Street, Certificate of Compliance nitrile gasket, and lift drawings for Roosevelt Bldg. footings and columns.

Rejected 2 Contractor submittals for fire protection data, and excavation support system for 7th St. west bulkhead.

Reviewed For Record Only 1 Contractor submittal for water quality discharge log sheet.

(20) For Contract A171 - Approved 14 Contractor submittals for concrete anchors, electrical material channel clamps, wet standpipe system, cold galvanized coating repair compound, wire & cables, wet standpipe welding procedures, invert concrete repair, fluorescent lamps for Type X tunnel lighting fixtures, liquid-tight flexible conduit, and welding procedures for backing rings.

Approved-as-Noted 7 Contractor submittals for tunnel light fixtures Type X, wet standpipe system, cathodic protection materials test box, fixture wire, and walkway lift drawings.

Rejected 3 Contractor submittals for revised Part II Schedule update, tunnel lighting fixture - Type X, and wet standpipe system.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

- (21) For Contract A175 - Approved 12 Contractor submittals for rebar drawings, trackwork lateral turnout, samples of elastomer pad material, hardware for lifts formwork, welding procedures for structural steel, revised rebar details, rebar ties at column lines, welding certificates and masonry walls.

Approved-as-Noted 3 Contractor submittals for reinforcing drawings, concrete mix design, and column junction boxes and electrical conduit.

Rejected 5 Contractor submittals for temporary ventilation, column forms, soffit rebar, and concrete mix design.

Reviewed For Record Only 1 Contractor submittal for schedule modifications.

- (22) For Contract A610/A115 - Approved 11 Contractor submittals for standard joint bar; #10 lateral turnout, switch drawing, closure rail, and frog drawing; Wilshire/Alvarado lateral turnout, switch drawing, closure rail, and frog drawing; protective covering for concrete sewer manholes, and revised Part II CPM Schedule.

Approved-as-Noted 2 Contractor submittals for Monthly Progress Status report, and ground test procedures.

Rejected 4 Contractor submittals for casing and sleeves, traffic control @ 4th St. Santa Fe Ave. for storm drain line, CWR destressing procedure for yard trackage, and 2 rail thermometer.

- (23) For Contract A612 - Approved 1 Contractor submittal for proposed test procedures.

- (24) For Contract A620 - Approved 12 Contractor submittals for barchart schedule & narrative, receiver coil interface details, track circuit design wayside loops, code rate generator P.C. board, overspeed governor details, brake assurance details, battery data & installation details, track circuit qualification test reports (partial), Public Utilities Commission (CPUC) requirements for vehicle ATP equipment, EMC test reports, and factory acceptance test reports for AW signals.

Approved-as-Noted 1 Contractor submittal for factory acceptance test reports for speed fraters.

- (25) For Contract A630 - Approved-as-Noted 1 Contractor submittal for test program.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

Rejected 5 Contractor submittals for design test report, test report for 38KV circuit breaker, AC/DC conversion equipment, design test reports for aluminum enclosed bus duct, and AD/DC conversion equipment & auxiliary power transformers.

- (26) For Contract A640 - Approved 5 Contractor submittals for drawing tree & list, heat loads for RCC & TC&C equipment, EMC control plan, PA manufacturer's literature, and control area floor plans.

Approved-as-Noted 3 Contractor submittals for radio manufacturer's literature, closed circuit T.V. sub-system, and preliminary design review data package mobile radio sub-system.

Rejected 5 Contractor submittals for radio frequency power documentation, FCT display plans & sequences, Halon calculations, preliminary design data package for CTS telephone, and PA schematics & wiring diagrams.

Reviewed For Record Only 1 Contractor submittal for power battery sizing calculations.

- (27) For Contract A710 - Approved 4 Contractor submittals for escalator configuration drawing, escalator wires & cable catalog cuts, escalator layout, and samples of elevator fixtures.

Approved-as-Noted 2 Contractor submittals for elevator wiring diagrams, and doors & frames for elevator hoistway.

- (28) For Contract A740 - Approved-as-Noted 2 Contractor submittals for test procedure for motors, and progress report and schedule.

Rejected 1 Contractor submittal for fan silencers test report.

- (29) For Contract A745 - Approved 1 Contractor submittal for QA inspection & test checklist for subcontractors.

Approved-as-Noted 1 Contractor submittal for progress report and schedule.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

- (30) For Contract A750 - Approved-as-Noted 1 Contractor submittal for final report for handling treatment & disposal of hazardous materials.
- (31) For Contract A795 - Approved 2 Contractor submittals for barchart schedules, and Contractor's schedule of values.

I. Project Controls

- (1) Processed Change Requests: A112-CR-119, A112-CR-120, A112-CR-121, A112-CR-122, A130-CR-026, A135-CR-044, A135-CR-047, A135-CR-048, A135-CR-049, A141-CR-110, A141-CR-115, A141-CR-040, A145/145A-CR-140, A146-CR-034, A146-CR-035, A165-CR-025, A165-CR-064A, A165-CR-067, A165-CR-068, A165-CR-070, A165-CR-071, A165-CR-072, A165-CR-076, A165-CR-077, A165-CR-078, A165-CR-079, A175-CR-045, A610/115-CR-064, A610/115-CR-066, and A610-CR-068.
- (2) Processed Change Notices: A130-CN-010, A130-CN-016, A130-CN-018, A141-CN-058, A141-CN-068, A145/145A-CN-038, A145/145A-CN-140, A145/145A-CN-041, A145/145A-CN-042, A146-CN-025, A146-CN-027, A165-CN-011, A165-CN-012, A165-CN-019, A165-CN-020, A165-CN-021, A165-CN-023, A165-CN-024, A165-CN-027, A165-CN-029, A175-CN-019, A175-CN-029, A610/115-CN-033, A620-CN-026, A630-CN-001, A640-CN-003A, A640-CN-005, and A710-CN-001.
- (3) Processed Change Orders: A112-CO-008B, A112-CO-042A, A112-CO-043A, A112-CO-049, A112-CO-050, A112-CO-051, A112-CO-053, A130-CO-004, A130-CO-015A, A130-CO-020, A130-CO-021, A135-CO-001G, A135-CO-002S, A135-CO-002T, A135-CO-002U, A135-CO-002V, A135-CO-019, A135-CO-021, A141-CO-010F, A141-CO-010G.1, A141-CO-010M.1, A141-CO-010N.1, A141-CO-033A, A141-CO-039A, A141-CO-042, A141-CO-044, A141-CO-045, A145/145A-CO-042A, A145/145A-CO-078, A145/145A-CO-085, A145/145A-CO-086, A145/145A-CO-087, A146-CO-021, A146-CO-021F, A146-CO-021G, A146-CO-021H, A165-CO-003A, A165-CO-012, A165-CO-019, A165-CO-019A, A165-CO-020A, A165-CO-027, PT.1, A165-CO-029D, A165-CO-032A, A165-CO-035, A175-CO-024C, A175-CO-025A, A175-CO-026, PT.II, A175-CO-027, A175-CO-028, A175-CO-029, A175-CO-030, A610/115-CO-014D, A610/115-CO-025A, A610/115-CO-028, A610/115-CO-033, A610/115-CO-039, A610/115-CO-041, A610/115-CO-043, A610/115-CO-044, A610/115-CO-045, A610/115-CO-046, A610/115-CO-047, A610/115-CO-049, A616-CO-011, A620-CO-005, A620-CO-007, and A640-CO-003A.
- (4) Processed through TRACS, executed Change Orders: A112-CO-004C, A130-CO-014, A130-CO-015, A135-CO-011, A135-CO-012, A141-CO-010G/010G1, A141-CO-010M, A141-CO-039, A144-CO-011, A144-CO-013, A144-CO-014, A144-CO-015, A144-CO-016, A145-CO-076, A145-CO-077, A145-CO-077A, A145-CO-082, A146-CO-021C, A146-CO-021D, A146-CO-021E, A146-CO-022, A165-CO-018, A175-CO-021, A175-CO-023, A175-CO-024, A610-CO-035, and A745-CO-003.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

- (5) Processed Potential Claims: A145-PC-093, A165-PC-004, A165-PC-005, A165-PC-014, A165-PC-023, A165-PC-024, A165-PC-025, A165-PC-027, A165-PC-029, A165-PC-032, A165-PC-036, A165-PC-044, A165-PC-047, A165-PC-049, A165-PC-050, A165-PC-052, A165-PC-053, A165-PC-056, A165-PC-057, A165-PC-058, A165-PC-060, A165-PC-061, A165-PC-062, A165-PC-065, A165-PC-066, A165-PC-071, A165-PC-103, A165-PC-107, A165-PC-119, A610/115-PC-032 and A610/115-PC-036.
- (6) Processed Change Technical Evaluations: A112-CR-117, A112-CR-119, A112-CR-120, A112-CR-121, A135-CR-047, A141-CR-109, A141-CR-111, A145-145A-CR-135, A145-145A-CR-137, A145-145A-CR-138, A165-CR-018, A165-CR-042, A165-CR-050, A165-CR-066, A165-CR-068, A165-CR-070, A175-CR-045, A610/115-CR-048, A610/115-CR-061, A610/115-CR-065, A610/115-CR-066, A610/115-CR-068, and A620-CR-207.
- (7) Processed Force Account Change Packages: A145-145A-CO-019, A145-145A-CO-020, A145-145A-CO-033, A146-CO-012, A146-CO-013, A146-CO-013A, A165-CO-021, A165-CO-029A, A171-CO-008, A175-CO-003, A175-CO-010A, A175-CO-014, A175-CO-015A, A751-CO-007, A753-CO-003, A754-CO-001, and A755-CO-005.
- (8) Processed Monthly Payment Estimates for 19 Contracts: A112, A130, A135, A141, A144, A145, A146, A165, A171, A175, A610/A115, A616, A620, A640, A710, A732, A740, A745, and A750.
- (9) Completed a Close-out reconciliation on 10 Force Account Change Orders: A145-CO-011, A145-CO-019, A145-CO-020, A145-CO-033, A145-CO-049, A146-CO-013, A146-CO-018, A165-CO-001, A165-CO-013, and A175-CO-003/003A.
- (10) Continued testing PC TRACS for use on the project.
- (11) Reviewed Contractor Monthly Progress Reports.
- (12) Prepared inputs to RTD Monthly Status Report.
- (13) Reviewed A167 Part I Schedule Submittal - Rejected.
- (14) A112-CR-068 Lighting system conduits. Reviewed scope of work and quantities with Contractor.
- (15) A130-CR-016 Prepared evaluation of Contractors proposal.
- (16) A130-CR-025 Prepared estimate, and assisted in a negotiated settlement with Contractor.
- (17) A130-CR-016 Reviewed estimate, contractor proposal, and negotiated settlement with contractor.
- (18) A135-CR-004 Continued review of proposals and changes for LAUPT Baggage Handling Facilities.
- (19) A135-CR-005 Reviewed contractor proposal for REA building demolition.
- (20) A135-CR-011 Received west entrance drawings, made preliminary review.
- (21) A135-CR-029 Reviewed concrete water cement ratio change with RTD and Contractor, breakdown for payment.
- (22) A135-CR-032 Began preparation of estimate for police room LAUPT.
- (23) A141-CR-040 Began review of incoming electrical service room change.
- (24) A141-CR-097A Completed estimate additional strain gauges on struts.
- (25) A145-CR-122, 123 & 128 Prepared estimates, escalator wellway, engagement access, and elevator machine room.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

- (26) A145-CR-141 Reviewed scope of work and prepared estimate for station grounding General System.
- (27) A146 Met with Contractor and RTD re: tunnel equipment rates for Force Accounts, began rebuttal to Contractor questions and objections.
- (28) A165-CR-010 Prepared revised electrical estimate, miscellaneous changes.
- (29) A165-CR-044 Began preparation of final estimate Hydraulic elevator lines and conduits.
- (30) A165-CR-049 Reviewed final design east bulkhead, provided data to Resident Engineer for negotiations.
- (31) A165 Reviewed numerous contractor proposals, provided data to Resident Engineer.
- (32) A165 Prepared detailed takeoff of decking in support of final pay quantities.
- (33) A620-CR-018 Completed estimate for deletion of ACTV coaxial cable installation.
- (34) A620-CR-008 Prepared estimate for additional corrosion control requirements.
- (35) A620-CR-020 Reviewed contractor estimate for trap circuit deletion.
- (36) A710-CR-002, 003 Prepared R.O.M. estimates for elevator cab changes.
- (37) Prepared revised instructions on Finding-of-Fact preparation, Claims Log Update, Change Request Preparation and Force Account processing.
- (38) Met with DOT audit team and provided requested information.

J. CM Meetings in May 1989

<u>Date</u>	<u>Agency/Company</u>	<u>General Subject</u>
April 27	RTD/PC	Delay Claims/Documentation
May 1, 8, 15, 22	RTD	CCB Meetings
May 2, 9, 19	RTD/TSP/Elec. Sub.	A130-CR-026 Negotiations Commun. Duct bank
May 2	Cal-OSHA, RTD, DIA	The Return of Cal-OSHA
May 2, 15	LAPD	Safety at Metro Red Line sites and RTD & PDCD office areas
May 2	RTD/QA	Close-out Procedures
May 2, 9, 16, 23	RTD/MRTC	Project Status Review
May 3	RTD	A620-CR-008, 018, 020 Review estimates and negotiate position
May 3, 24	RTD/ MRTC	Project Controls Meeting



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

<u>Date</u>	<u>Agency/Company</u>	<u>General Subject</u>
May 3	RTD, MRTC, LACoSD, LAPD, BAH, RTD Police	General Project Security, including operations
May 3	RTD, MRTC, LACoFD, BAH	General Project Safety, including operations
May 3, 10	LADOT	Weekly LADOT MOS-1 Inspection
May 4	CRWQCB	Metro Red Line Discharges and Permit Renewal Application
May 4	RTD/TSP	A135-CR-029, CR-005 Review changes concrete water cement ratio and REA building demolition
May 4	A165	Smith-Emery Non Conformance
May 5	RTD/CC	Configuration Control
May 5	American Society of Civil Engineers	Metro Red Line presentation
May 5, 12, 19	RTD	CM Progress Review
May 5	RTD/OCPM	Claims Log Update
May 8	MRTC	A141 Settlement Indicator over storm drain
May 8	MRTC	A130 Chemical Grouting
May 8, 9	Engineering News Record	ENR article on Metro Red Line
May 10	Flakt	A745 Plant Inspection of Equipment Assembly
May 10, 23	Contractors, DIA, RTD Argonaut, LAFD	Project Safety Review
May 11	Contractors, Brokers, Insurance Co.	AGC of California Safety Committee New Cal-OSHA and Environmental Legislation, General Safety
May 11	L.A. City Fire Chiefs	A171 Settlements around fire station at access shaft
May 11	COWELCO	On the spot WPS Review (A135 BH)
May 11	SCRTD	A135 PacBell Master Agreement Work
May 12	RTD/OCPM	A171/A175 Claims
May 15	RTD/Government Affairs	Prepare for Congressman Lehman tour to A141 and A165
May 16	LACTC, RTD	Metro Blue Line briefing



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

<u>Date</u>	<u>Agency/Company</u>	<u>General Subject</u>
May 17	RTD, MRTC	Claims Seminar
May 17	RTD/QA	Safety Certification A121
May 18	LACTC	Metro Blue Line tour
May 18	RTD/ Shank	A146 Review tunnel equipment rates for Force Account
May 22	Paramount Steel	Inspection of Tunnel Rings for A145 and Stud Welding
May 22	FLSC Fire Chiefs, S-0	A146/A171 Fire Protection System at Cross Passages
May 23	RTD/TSP	A130-CR-026 netotiated settlement agreement, diff. site conditions
May 24	RTD/TSP	A135-CR-004 LAUPT baggage handling, settled rough carpentry proposal
May 24	BAH, RTD, MRTC	Safety Certification Review
May 23	RTD	UMTA Tour
May 25	RTD/ LGCA	Prepare for G. Swanson tour
May 25	A640 Communication	Acceptance Test Aydin Controls Ft. Washington, PA
May 26	RTD	Congressman Lehman tour
May 26	Scott Mech (T-S Sub-contractor)	A167 Air Handling Equipment
May 25	RTD	A135-CR-004 LAUPT baggage handling, review position on closure walls

SECTION VII

SUMMARY OF ACTIVITIES

PLANNED FOR JUNE



LOS ANGELES METRO RED LINE

CONTRACT PERFORMANCE REPORT

PDCD

PERIOD MAY 1989

VII. SUMMARY OF ACTIVITIES PLANNED FOR JUNE 1989

A. Administration and Accounting

- (1) Continue to provide priority administrative and accounting assistance to construction field operations.
- (2) Continue the recruitment and termination of personnel as required.
- (3) Continue to coordinate RTD's auditing process with Associate Subcontractors.

B. Quality Assurance

- (1) Continue to review welding activities and conduct fabrication inspections as required to support facilities and system procurement contracts.
- (2) Continue to monitor testing and test laboratory activities.
- (3) Continue to participate in A112 close-out activities.
- (4) Conduct "hands on" training session for inspectors preparing for ACI Concrete Technician 1 certification. Administer test to approximately 30 inspectors.
- (5) Finalize QA audit/surveillance of inspection reports and preparation of red-lined drawings at field sites.
- (6) Perform QA audit of A112 safety certification documentation.
- (7) Conduct QA audits of prime contractor and subcontractor activities on contracts A640, A740 and A745.

C. Equal Opportunity Administration

- (1) Conduct contract compliance site visits, employee interviews and monitor reporting requirements for Contract Nos. A112, A130, A135, A141, A145, A146, A165, A167, A171, A175, A610/A115, A612, A615, A616, A620, A640, A710, A732, A740, A745, A750 and A795.

D. Contracts and Procurement

- (1) Upon receipt of District approval, issue purchase orders for rental/purchase of OVA meter and to establish publication update services in support of QA.
- (2) Upon receipt of District approval, issue an Amendment to the Construction Photographic Services Subcontract to incorporate Change Orders No. 2 and 3, to increase AWP-5 funding and to remove unexpended AWP-4 funds.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

- (3) Prepare and submit for District approval Amendments for all Associate Subcontracts and other Subcontracts covering requirements for the Sixth Annual Work Plan.
- (4) Issue Requests for Quotations to renew annual equipment maintenance agreements and, after evaluation and receipt of District approval, issue Blanket Agreements for Photographic and Reproduction Services for AWP-6.
- (5) Issue Request for Proposal for temporary personnel services covering the 6th AWP.

E. Community Relations

- (1) Continue tenant notifications on traffic access issues for A141, A145, A146, A165 and A175.
- (2) Continue expanded communication activities with A130, A145, A146, A165 and A175 tenants regarding ongoing and pending construction activities.
- (3) Assist RTD/Governmental Affairs in planning and executing community outreach to Building Managers in the downtown area, including extending promotional activities for the Project Streetwise Hotline and the Information Centers.
- (4) Continue implementing CR Work Plan; conduct community presentations; the dissemination of construction information; and responding to complaints and inquiries.

F. Safety and Security

- (1) Continue to monitor safety, health and security activities on all active construction sites on a two shift basis.
- (2) Provide specialized underground safety training/indoctrination for PDCD staff, SCRTD, MRTD and visitors.
- (3) Continue to monitor activities of the Security Guard Service and the Site Clean-up Service subcontractors.
- (4) Upon receipt, review A167 Safety/Security Plan and proposed Safety Representative.
- (5) Upon receipt, review replacement Safety Representatives for the A146 and A610/A115 Projects.

G. Construction Operations

- (1) Continue construction management (CM) services at Contracts A112, A130, A135, A141, A143, A144, A145/A145A, A146, A165, A167, A171, A175, A610/A115, A612, A615, A616, A620, A630, A640, A710, A732, A740, A745, A750, (4984, 4986, 4988) and A795; monitoring of Master Agreement work and submittal reviews.



LOS ANGELES METRO RED LINE

POCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

- (2) Continue coordination with governmental agencies and MOS-1 inspection with LADOT.
- (3) Continue to process submittals and Master Agreement invoices on as-needed basis.
- (4) Continue monitoring of ground water and construction water discharges at A141, A144, A145, A146, A165, A171 and A175.
- (5) Continue monitoring Discharge Monitoring Stations at Ballona Creek and Los Angeles River.
- (6) Prepare and submit April and May Discharge Monitoring Reports (DMR) to the California Regional Water Quality Control Board (CRWQCB).
- (7) Prepare and submit April and May LA River Dissolved Solids Reports to Central and West Basin Water Replenishment District (CWBWRD).
- (8) Review and approval final asbestos submittal and clearance report for asbestos abatement by others at Roosevelt Building, A165.
- (9) Complete and submit closure report for tank abandonment at A-145.
- (10) Continue monitoring removal, relocation and disposal of contaminated soil at various project sites.
- (11) Prepare and submit application packages for permanent and temporary NPDES discharge stations.
- (12) Continue to monitor instrumentation, building and ground settlement marks, various contracts.
- (13) Continue to check Contractor's control points and layout.
- (14) Continue to perform survey tasks as requested by R.E.'s.
- (15) Continue to perform as-built survey of tunnels for Contracts A141 and A146.
- (16) Continue location surveys in shop and yard contracts.
- (17) Continue to check slab pours for Contracts A141, A165 and A175.
- (18) Perform high precision control survey through AL and AR Tunnels (A171).
- (19) Continue to check arch form alignment for AL Tunnel (A171).

H. Engineering Services

- (1) Continue inspecting instrumentation and analyzing data in Contracts A130, A135, A141, A145, A146, A165 and A175.
- (2) Continue to process Contractor's submittals for Contracts A112, A130, A135, A135BH, A141, A145, A146, A165, A171, A175, A610/A115, A612, A615, A616, A620, A630, A640, A710, A732, A740, A745, A750, and A795.
- (3) Continue production of A161 as-built drawings.
- (4) Continue to track A145 geology and instrumentation data as part of A141 Design Criteria Verification Study, Task B.
- (5) Complete interim study report for A141 Design Criteria Verification Study Task C.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

- (6) Complete the "as-predicted" geologic profile for the A146 AR tunnel.
- * (7) Complete constructibility review for Contract A187 Wilshire/Alvarado Station Stage II final documents.

I. Project Controls

- (1) Process Monthly Payment Estimates for all active contracts.
- (2) Process all the executed Change Orders through TRACS
- (3) Continue close-out reconciliations for Force Account Change Orders.
- (4) Plan for PC TRACS implementation.
- (5) Input Contract A167 into TRACS.
- (6) Review Monthly Contractor Progress Reports.
- (7) Prepare Scheduling inputs to RTD Monthly Status Report.
- (8) Review A167 Part I/II Schedule Submittal.
- (9) Review A610 Part II Schedule Revision.

* See Page 44.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

DESIGN PACKAGE STATUS WINDOW REPORT - NEXT 30 DAYS 5-27-89 TO 6-30-89

Contract #	Description	Pkg Type	Review Code	Schedule Receipt	Received	Schedule Complete	Actual Complete	SC	Remarks
A-187	WILSHIRE/ALVARADO STATION (STAGE II)	DWGS	FS100%	06-01-89	05-22-89	06-12-89			ADVANCE DWGS.
A-187	WILSHIRE/ALVARADO STATION (STAGE II)	SPEC	FS100%	06-01-89		06-12-89			

**

2 records listed. 2 values listed .

Review Codes :	LT60 - Less than 60%	IP60 - In progress 60%	PF85 - Prefinal 85%
	PF90 - Prefinal 90%	FS100 - Final submittal 100%	DC100 - Final design complete 100%
	CAR- Claims Avoidance Review	CE - Check Estimate	

NOTE : Based on 6-1-89, MRTD Design Review Schedule

SECTION VIII
SUBCONTRACTOR/CONSULTANT
STATUS



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

VIII. SUBCONTRACTOR/CONSULTANT STATUS

The following 5th AWP Subcontract Status Report provides a current status of subcontracts awarded to the twelve associate and four consultant subcontractors. The Report shows major milestones for each subcontractor action from receipt of the requisition, execution of the document and includes an abbreviated description of the subcontract amendment issued.

FIFTH ANNUAL WORK PLAN SUBCONTRACT STATUS REPORT

MAY 26, 1989

SUBCONTRACT NUMBER	SUBCONTRACTOR	REQUI- SITION	REQ FOR PROPOSAL	NEGOTIATION COMPLETE	JV APPROVAL	DATE TO SC	RETURNED FROM SC	CONSENT REQUESTED	CONSENT RECEIVED	NTE AMOUNT	DATE EXECUTED	REMARKS
1-SC-3369-1	BETTER PERSONNEL EMPLOYMENT SERVICES											
	AMEND. NO. 11	08/03/88	04/08/88	06/08/88	07/25/88	06/13/88	06/13/88	06/14/88	08/11/88	\$420,632	08/11/88	FIFTH AWP
	CHANGE ORDER NO. 4	N/A	N/A	N/A	N/A	11/04/88	11/08/88	N/A	N/A	N/C	11/04/88	ADMINISTRATIVE
2-SC-3369-1	CONSTRUCTION CONTROL SERVICES CORP.											
	AMEND. NO. 11	08/03/88	04/08/88	06/08/88	07/25/88	06/17/87	06/20/88	06/27/88	08/15/88	\$1,482,039	08/31/88	FIFTH AWP
	CHANGE ORDER NO. 3	N/A	N/A	N/A	N/A	11/04/88	11/28/88	N/A	N/A	N/C	11/04/88	ADMINISTRATIVE
	AMEND. NO. 12	N/A	N/A	N/A	N/A	05/15/89		N/A	N/A	\$1,617,039		INCREASES FUNDS
3-SC-3369-1	DAMES & MOORE											
	AMEND. NO. 10	08/03/88	04/08/88	06/08/88	07/25/88	06/27/88	06/28/88	06/30/88	08/15/88	\$234,577	08/16/88	FIFTH AWP
	CHANGE ORDER NO. 3	N/A	N/A	N/A	N/A	11/04/88	11/15/88	N/A	N/A	N/C	11/04/88	ADMINISTRATIVE
4-SC-3369-1	ENGINEERING-SCIENCE											
	AMEND. NO. 10	08/03/88	04/08/88	06/20/88	07/25/88	07/06/88	07/15/88	07/18/88	08/12/88	\$228,002	08/15/88	FIFTH AWP
	CHANGE ORDER NO. 3	N/A	N/A	N/A	N/A	11/04/88	12/07/88	N/A	N/A	N/C	11/04/88	ADMINISTRATIVE
	AMEND. NO. 11	12/30/88	N/A	N/A	* *	01/16/89	01/25/89	01/27/89	04/25/89	\$477,824	04/25/89	INCREASES FUNDS
5-SC-3369-1	HAYAKAWA ASSOCIATES											
	AMEND. NO. 10	08/03/88	04/08/88	07/15/88	07/25/88	08/02/88	08/19/88	08/24/88	09/16/88	\$133,484	09/16/88	FIFTH AWP (TERMINATED)
6-SC-3369-1	JACOBS ASSOCIATES											
	AMEND. NO. 13	08/03/88	04/08/88	06/09/88	07/25/88	06/22/87	06/28/88	06/30/88	08/15/88	\$596,419	08/16/88	FIFTH AWP
	CHANGE ORDER NO. 4	N/A	N/A	N/A	N/A	11/04/88	12/06/88	N/A	N/A	N/C	11/04/88	ADMINISTRATIVE
7-SC-3369-1	JENKINS, GALES & MARTINEZ, INC.											
	AMEND. NO. 13	08/03/88	04/08/88	06/08/88	07/25/88	07/18/88	07/29/88	07/29/88	08/23/88	\$738,465	08/23/88	FIFTH AWP
**IN PROCESS	CHANGE ORDER NO. 3	N/A	N/A	N/A	N/A	11/04/88	11/15/88	N/A	N/A	N/C	11/04/88	ADMINISTRATIVE



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

FIFTH ANNUAL WORK PLAN SUBCONTRACT STATUS REPORT (Contd)

MAY 26, 1989

SUBCONTRACT NUMBER	SUBCONTRACTOR	REQU- SITION	REQ FOR PROPOSAL	NEGOTIATION COMPLETE	JV APPROVAL	DATE TO SC	RETURNED FROM SC	CONSENT REQUESTED	CONSENT RECEIVED	NTE AMOUNT	DATE EXECUTED	REMARKS
9-SC-3369-1	MARTIN & HUANG INTERNATIONAL											
	AMEND. NO. 11	08/03/88	04/08/88	06/08/88	07/25/88	07/13/88	07/18/88	07/25/88	08/18/88	\$485,299	08/18/88	FIFTH AMP
	CHANGE ORDER NO. 4	N/A	N/A	N/A	N/A	10/06/88	10/17/88	N/A	N/A	N/C	10/06/88	REVISED IPR
	CHANGE ORDER NO. 5	N/A	N/A	N/A	N/A	10/31/88	11/02/88	N/A	N/A	N/C	10/31/88	ADMINISTRATIVE
	AMEND. NO. 12	N/A	N/A	N/A	N/A	05/24/89		N/A	N/A	\$534,659		INCREASES FUNDS
9-SC-3369-1	NORTH PACIFIC CONSTRUCTION MANAGEMENT											
	AMEND. NO. 13	08/03/88	04/08/88	06/29/88	07/25/88	07/18/88	07/29/88	08/03/88	08/23/88	\$435,803	08/23/88	FIFTH AMP
	CHANGE ORDER NO. 5	N/A	N/A	N/A	N/A	11/04/88	11/15/88	N/A	N/A	N/C	11/04/88	ADMINISTRATIVE
10-SC-3369-1	UCHOA & SILLAS											
	AMEND. NO. 7	08/03/88	04/08/88	06/14/88	N/A	07/19/88	07/21/88	07/25/88	08/15/88	\$79,600	08/16/88	FIFTH AMP
11-SC-3369-1	RANDOLPH & TATE ASSOCIATES											
	AMEND. NO. 7	08/03/88	04/08/88	04/10/88	N/A	07/20/88	08/08/88	08/08/88	08/18/88	\$10,000	08/18/88	FIFTH AMP
15-SC-3369-1	MUESER RUTLEDGE CONSULTING ENGINEERS (JAMES GOULD, P.E.)											
	AMEND. NO. 6	09/23/88	N/A	06/15/88	N/A	06/21/88	06/21/88	06/23/88	08/12/88	\$20,000	08/12/88	FIFTH AMP
18-SC-3369-1	GEO GRAY/ PHOTOGRAPHY											
	AMEND. NO. 3	06/13/88	N/A	N/A	N/A	08/18/88	08/19/88	07/01/88	08/18/88	\$42,300	08/22/88	FIFTH AMP
	CHANGE ORDER NO. 2	N/A	N/A	N/A	N/A	07/13/88	07/20/88	N/A	N/A	N/C	07/20/88	ADMINISTRATIVE
	CHANGE ORDER NO. 3	N/A	N/A	N/A	N/A	05/10/89	05/10/89	N/A	N/A	N/C	05/10/89	ADDS ITEMS
	AMEND. NO. 4	N/A	N/A	N/A	N/A			05/19/89		\$65,000		INCREASES FUNDS
19-SC-3369-1	WORK CENTER, INC.											
	AMEND. NO. 5	05/25/88	N/A	N/A	N/A	08/12/88	08/26/88	06/27/88	08/11/88	\$60,000	08/26/88	FIFTH AMP
	AMEND. NO. 6	N/A	N/A	N/A	N/A	11/07/88	12/20/88	N/A	N/A	N/C	12/20/88	ADMINISTRATIVE
	AMEND. NO. 7	02/08/89	N/A	N/A	N/A	05/10/89	05/17/89	02/09/89	05/01/89	\$78,000	05/05/89	INCREASES FUNDS
	AMEND. NO. 8	05/22/89	N/A	N/A	N/A	05/22/89		05/01/89	05/11/89	\$110,000		INCREASES FUNDS

**IN PROCESS



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

FIFTH ANNUAL WORK PLAN SUBCONTRACT STATUS REPORT (Contd)

MAY 26, 1989

SUBCONTRACT NUMBER	SUBCONTRACTOR	REQUI- SITION	REQ FOR PROPOSAL	NEGOTIATION COMPLETE	JV APPROVAL	DATE TO SC	RETURNED FROM SC	CONSENT REQUESTED	CONSENT RECEIVED	NTE AMOUNT	DATE EXECUTED	REMARKS
21-SC-3369-1	SMITH EMERY CO.											
	AMEND NO. 3	06/13/88	N/A	N/A	07/25/88	08/23/88	08/29/88	06/16/88	08/29/88	\$395,000	08/31/88	FIFTH AMP
	CHANGE ORDER NO. 4	N/A	N/A	N/A	N/A	12/30/88		N/A	N/A	N/C	12/30/88	ADDS ITEMS
	AMEND. NO. 4	04/15/89	N/A	N/A	* *	04/05/89	04/05/89	02/15/89	04/03/89	\$595,000	04/05/89	INCREASES FUNDS
22-SC-3369-1	COLEMAN SECURITY SERVICES INC.											
	AMEND. NO. 3	06/13/88	N/A	N/A	N/A	08/15/88	08/17/88	06/15/88	08/15/88	\$93,000	08/18/88	FIFTH AMP
29-SC-3369-1	SUBWAY TERMINAL BLDG (A145/146 SITE OFFICE LEASE)	N/A	N/A	N/A	N/A	N/A	N/A	06/01/88	06/02/88	\$56,910	N/A	EXER 1YR OPT
33-SC-3369-1	F.E. ENDACOTT (CONSULTING AGREEMENT)	05/16/88	N/A	N/A	N/A	06/16/88	07/05/88	07/06/88	08/16/88	\$61,000	08/16/88	FIFTH AMP
34-SC-3369-1	BASMACHION-DARNELL INC. (COMPLETED)											
35-SC-3369-1	MARY & SON MAINTENANCE (SITE CLEAN-UP)	06/27/88	06/27/88	07/21/88	07/25/88	08/10/88	08/11/88	07/13/88	08/12/88	\$60,000	08/15/88	FIFTH AMP
36-SC-3369-1	STANLITE SAFETY SUPPLIES (COMPLETED)											
37-SC-3369-1	KAL KRISHNAM	08/25/88	09/12/88	10/19/88	N/A	12/15/88	12/19/88	11/04/88	12/12/88	\$98,000	12/20/88	NEW ASSOCIATE
	AMEND. NO. 1	N/A	N/A	02/11/89	N/A	02/23/89		N/A	N/A	\$94,130		RATE ADDITIONS
38-SC-3369-1	EDWARD D. GRAF (CONSULTING AGREEMENT)	08/10/88	N/A	N/A	N/A	08/12/88	08/16/88	08/10/88	09/07/88	\$50,000	09/07/88	
39-SC-3369-1	OLLEON CONSULTING ENGINEERS CO.	08/25/88	09/12/88	10/18/88	N/A	12/15/88	12/29/88	11/04/88	12/12/88	\$99,075	12/30/88	NEW ASSOCIATE
40-SC-3369-1	TRANSMETRICS	08/25/88	09/12/88	10/19/88	N/A	12/15/88	12/29/88	11/04/88	12/12/88	\$55,350	12/29/88	NEW ASSOCIATE
**IN PROCESS	CHANGE ORDER NO. 1	N/A	N/A	N/A	N/A	01/26/89	02/01/89	N/A	N/A	N/C	01/26/89	ADMINISTRATIVE

SECTION IX

CONSTRUCTION PROGRESS

PHOTOS



LOS ANGELES METRO RED LINE

PDCD


CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989


MAIN SHOP BUILDING CONTRACT A112



CONTROL TOWER - SUBSTANTIALLY COMPLETE

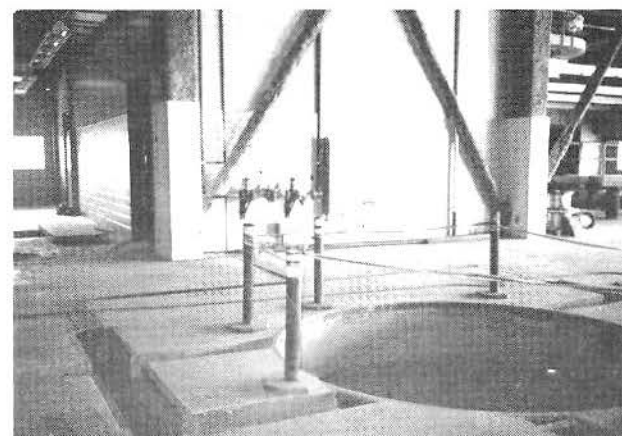

TURNTABLE 124-2F PIT SUBSTANTIALLY COMPLETE.
NOTE RAIL POCKETS, WALL AND BACKFLOW PREVENTER

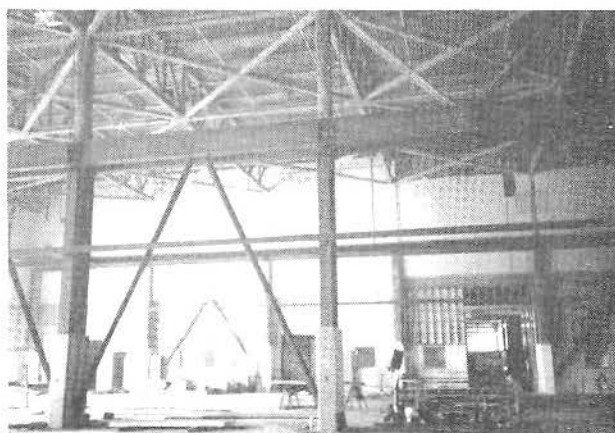

LINE D - SIDING COMPLETE TO LINE 5.
NOTE JIB CRANE ON SLAB



COLUMN COVER BEING INSTALLED ON "B" LINE



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

MAIN SHOP BUILDING CONTRACT A112 (Contd)



FRONT VIEW OF MAIN SHOP BUILDING (WEST SIDE)
SHOWING MAIN ENTRANCE



NORTHSIDE OF BUILDING SHOWING CONTROL TOWER
AND S & I PIT ENTRANCES

Parsons-Dillingham-De Leuw, Cather




LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989


YARD LEADS & TRANSFER ZONE CONTRACT A130

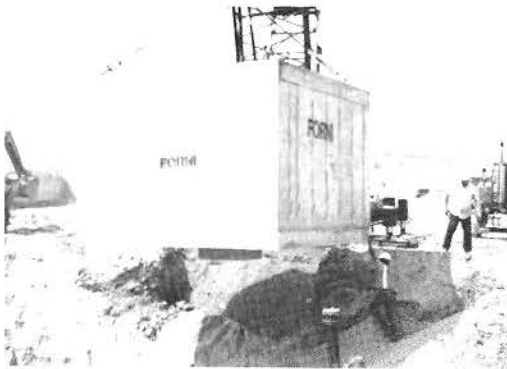

INSTALLING VAULT FOR
COMMUNICATION DUCT BANK



"U" WALL STRUCTURE -
RETAINING WALLS COMPLETE

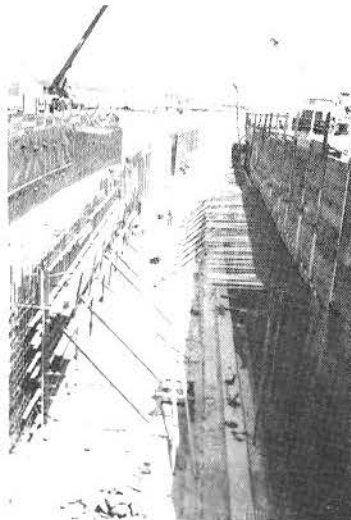

PLACING CONCRETE IN BOX
STRUCTURE WALLS



DRILLING HOLES FOR CHEMICAL GROUT
STABILIZATION

Parsons-Dillingham-De Leuw, Cather



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

UNION STATION CONTRACT A135



INSTALLATION OF CABLE IN NEW PULL BOX #7
WITHIN LAUPT TRACKYARD



PLACING CONCRETE FOR SLURRY WALL PANEL
IN PHASE I STAGE I SECTION



CONVEYOR INSTALLATION AT TRACK LEVEL IN
THE BAGGAGE HANDLING FACILITY



DEMOLITION OF UTILITY TUNNEL, PASSENGER RAMPS
AND PLATFORMS WITHIN LAUPT TRACKYARD

Parsons-Dillingham-De Leuw, Cather



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989


CIVIC CENTER STATION AND TUNNEL CONTRACT A141



BREAK THRU OF AR TUNNEL INTO NORTH END OF
CIVIC CENTER STATION



MOVING TUNNELING MACHINE THROUGH S CURVE TO
AL TUNNEL AT SOUTH END OF CIVIC CENTER STATION

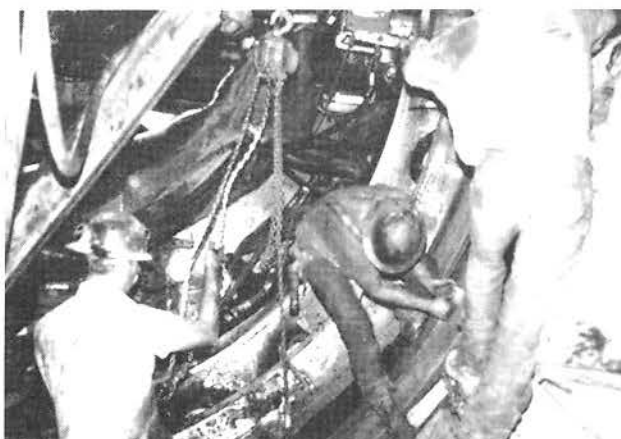

INSTALLING TUNNEL SUPPORT RING IN AR TUNNEL
NORTH CIVIC CENTER STATION

Parsons-Dillingham-De Leuw, Cather

MTA LIBRARY



LOS ANGELES METRO RED LINE

CONTRACT PERFORMANCE REPORT


PDCD

PERIOD MAY 1989

CIVIC CENTER STATION AND TUNNEL CONTRACT A141 (Contd)



POURING CONCRETE COLUMN IN
CIVIC CENTER STATION

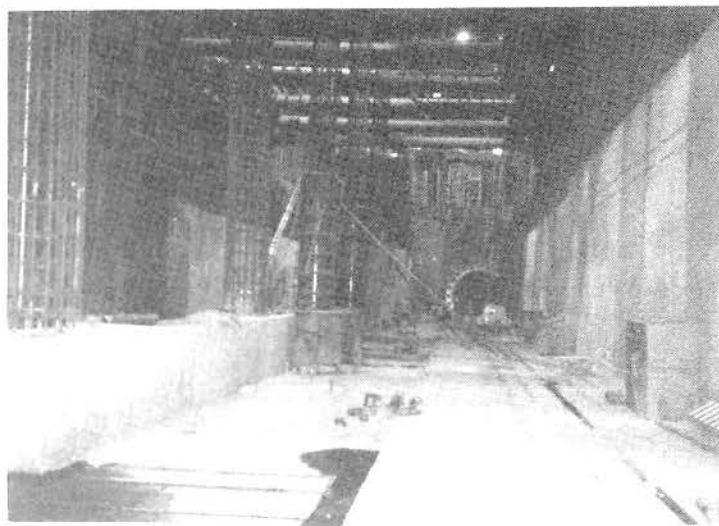

CIVIC CENTER STATION SEVERAL DAYS PRIOR TO TUNNEL
BREAK THRU, LOOKING SOUTH

Parsons-Dillingham-De Leuw, Cather




LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

5TH/HILL UTILITY RELOCATION AND 5TH/HILL STATION STAGE I CONTRACT A145/A145A

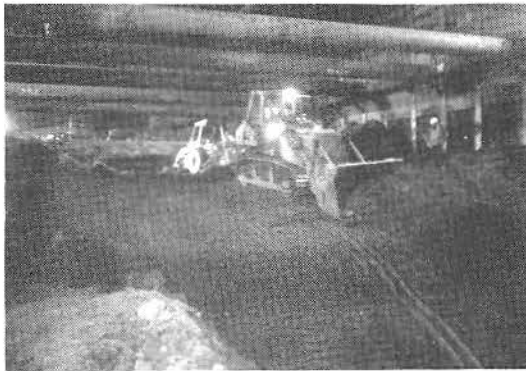

STATION'S NORTH END EXCAVATION OPERATIONS



SANITARY SEWER MANHOLE C-1
INSTALLATION IN 4TH STREET



TEMPORARY SANITARY SEWER LINE-C
IN 4TH STREET



ELECTRICAL GROUND MAT INSTALLATION
IN THE SOUTH END OF STATION

Parsons-Dillingham-De Leuw, Cather




LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989


TUNNELS FROM 5TH/HILL TO 7TH/FLOWER CONTRACT A146

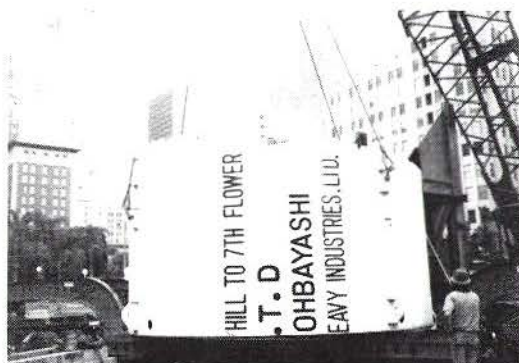


PART OF SHIELD FOR AR TUNNEL BEING
UNLOADED FROM TRAILER



PART OF SHIELD FOR AR TUNNEL BEING
LOWERED ONTO BLOCKS

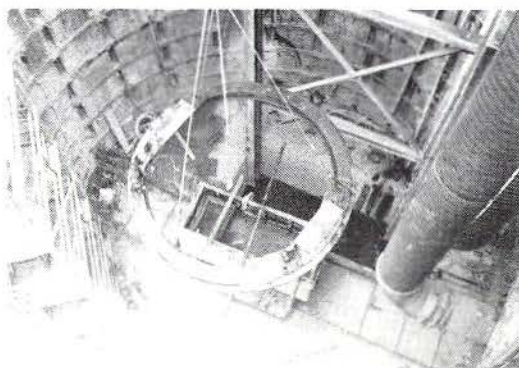

PART OF SEGMENT ERECTOR FROM AL SHIELD
BEING REMOVED FROM ACCESS SHAFT

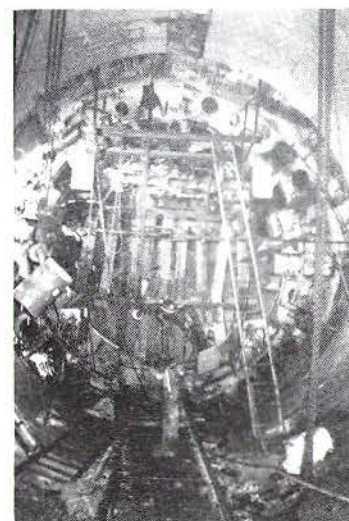

VIEW LOOKING WEST IN THE AL TUNNEL SHOWING THE TEMPORARY
WOODEN BULKHEAD PRIOR TO BREAK THRU TO 7TH/FLOWER
STATION. TUNNEL MACHINE SHIELD REMAINS IN PLACE

Parsons-Dillingham-De Leuw, Cather



LOS ANGELES METRO RED LINE

PDCD


CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989


7TH/FLOWER STATION CONTRACT A165



LRT INTERIOR WALLS

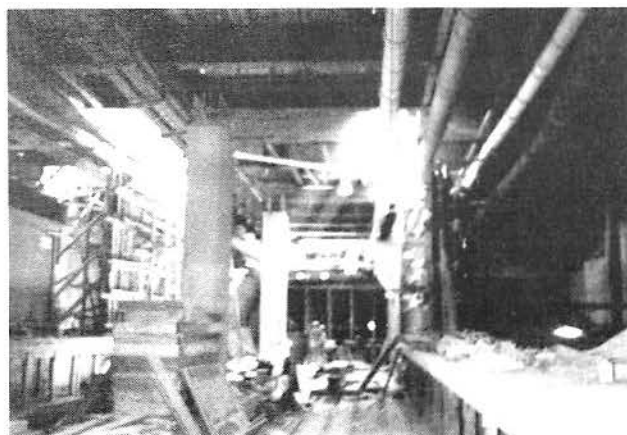

LRT INTERIOR COLUMNS

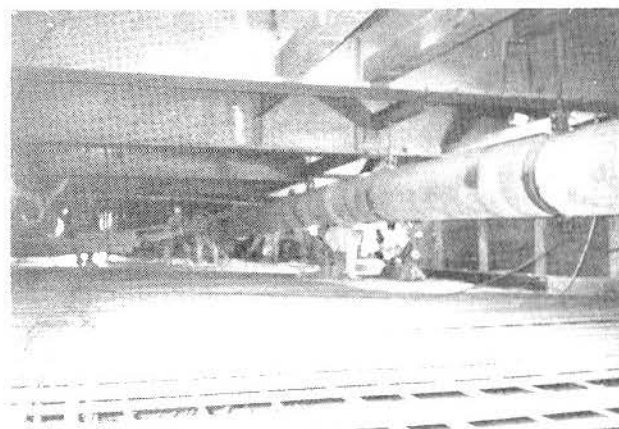

REBAR FOR LRT ROOF SLAB



LOS ANGELES METRO RED LINE

PD CD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

7TH/FLOWER STATION CONTRACT A165 (Contd)



SUPPORTED UTILITIES ABOVE LRT ROOF SLAB



MRT BASE SLAB



DEMOLITION AT ROOSEVELT BUILDING
(OLD REPUBLIC BANK)




LOS ANGELES METRO RED LINE

CONTRACT PERFORMANCE REPORT

PDCD

PERIOD MAY 1989

LINE SECTION - 7TH/FLOWER TO WILSHIRE/ALVARADO CONTRACT A171

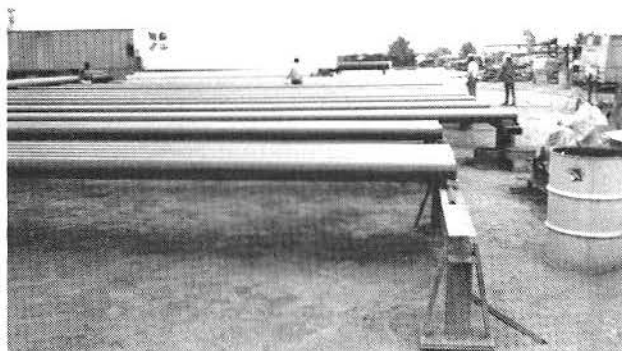

8" STANDPIPE WITH PRIMER AND 2ND COAT OF
PAINT AT THE FABRICATION PLANT



WALKWAY FORM UNDER FABRICATION IN STEEL SHOP



A165/A171 INTERFACE WITH A171'S SHIELD AND
THE CONCRETE BULKHEAD INSIDE THE A165
STATION LIMITS



LOS ANGELES METRO RED LINE

CONTRACT PERFORMANCE REPORT


PDCD

PERIOD MAY 1989

LINE SECTION - 7TH/FLOWER TO WILSHIRE/ALVARADO CONTRACT A171 (Contd)



AL TUNNEL ARCH LOOKING EAST AT STA. 242+50

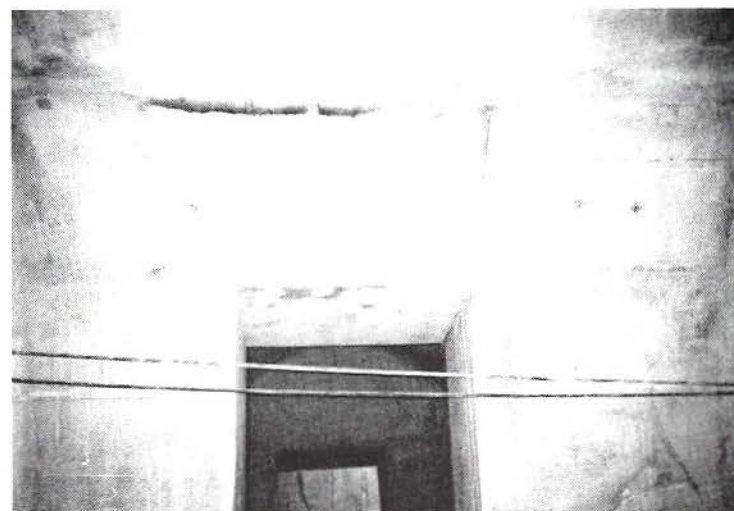

AL TUNNEL AT CROSS PASSAGE #13 STA. 234+58;
FINISHED ARCH, TIED TO CROSS PASSAGE




LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989

WILSHIRE/ALVARADO STATION - STAGE I CONTRACT A175

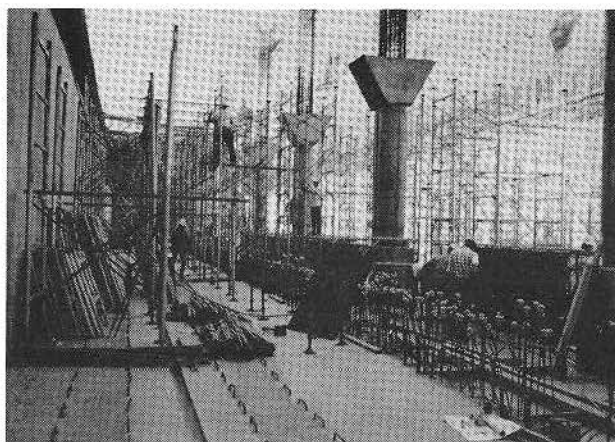


INSTALLATION OF MEZZANINE SLAB SUPPORT



PLACEMENT OF WALLS FOR THE SOUTH INTAKE
AND EXHAUST SHAFTS



EXCAVATION AND SUPPORT OF EXCAVATION AT
A171/A175 INTERFACE

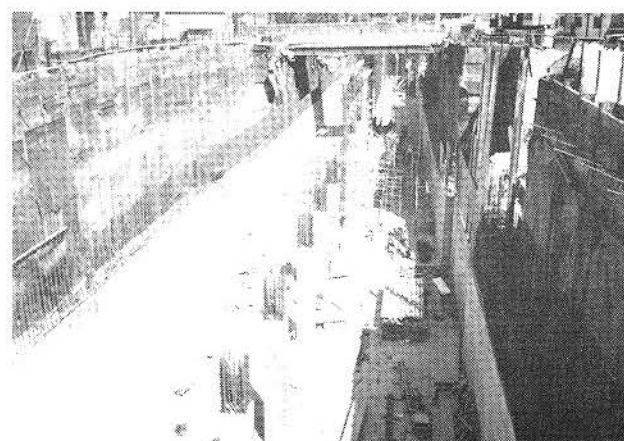

GENERAL VIEW OF STATION PROGRESS,
INCLUDING SLABS, WALLS AND COLUMNS

Parsons-Dillingham-De Leuw, Cather



LOS ANGELES METRO RED LINE

PDCD


CONTRACT PERFORMANCE REPORT

PERIOD MAY 1989


TRACKWORK INSTALLATION/YARD STORAGE AREA CONTRACT A610/A115



PERMANENT PAVEMENT RESTORATION AT 3RD STREET
IN CONNECTION WITH SEWER LINE WORK,
LOOKING WEST FROM SANTA FE AVENUE

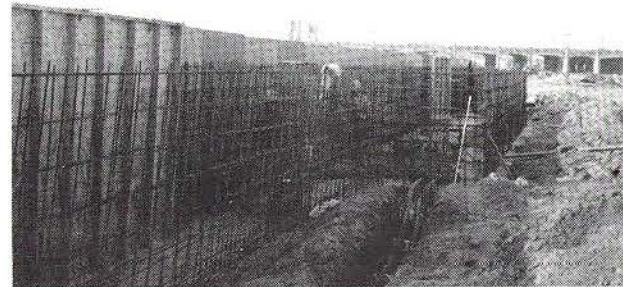

FORMING WALL PANELS FOR HEAVY CAR CLEANING
PLATFORM, LOOKING SOUTH TOWARDS
4TH STREET BRIDGE

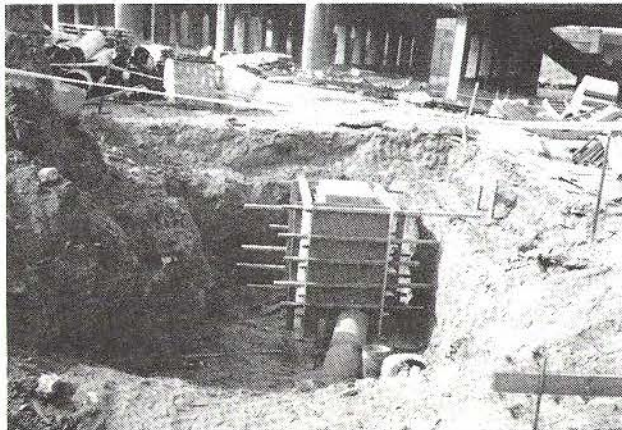

FORMWORK FOR STORM DRAIN CATCH BASIN SD 2,
LOOKING SOUTH TOWARDS 4TH STREET BRIDGE



DUCT BANKS LEADING TO OPERATING PLATFORM NO. 3,
LOOKING SOUTHWEST TOWARDS SANTA FE AVENUE

Parsons-Dillingham-De Leuw, Cather
