


SCRTD
1985-
M46
R46
no. 64

RTD


LOS ANGELES **METRO RED LINE** PROJECT MONTHLY CONTRACT PERFORMANCE REPORT

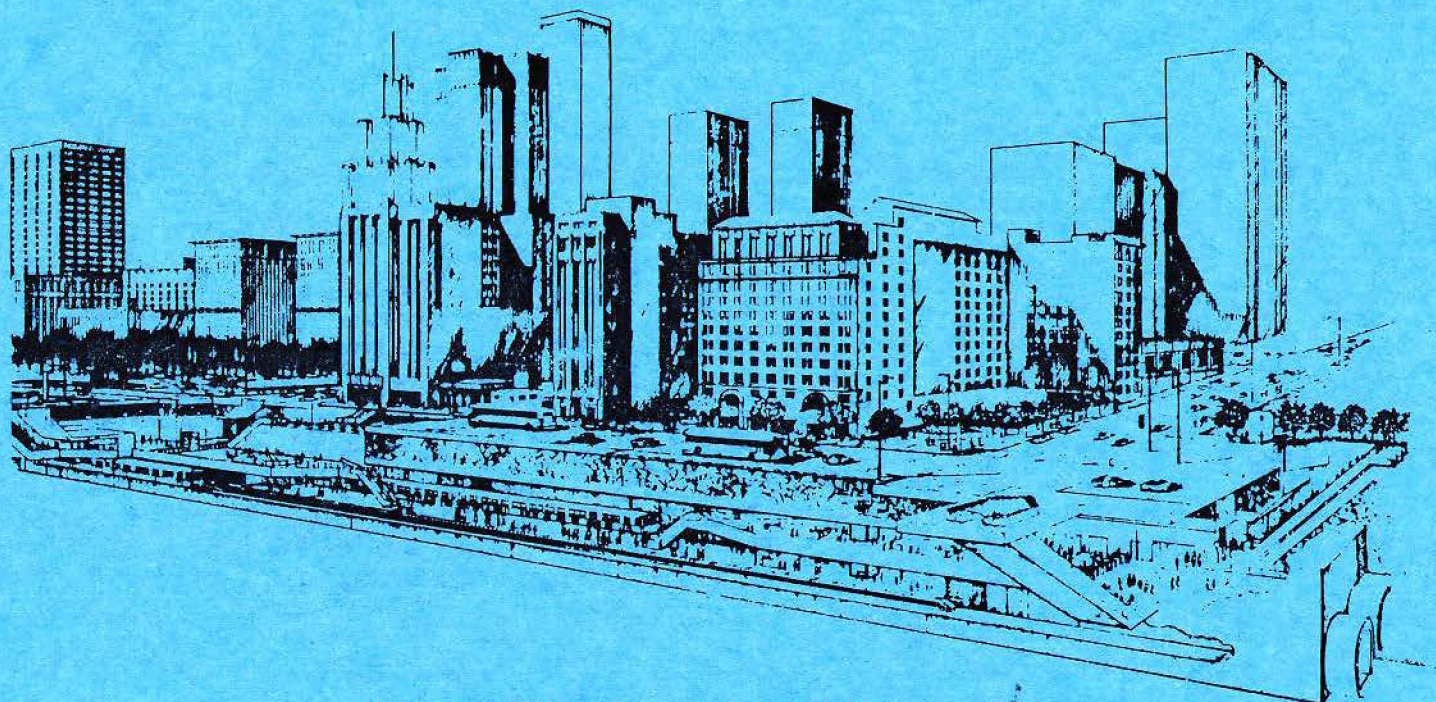

**REPORT NUMBER 64
OCTOBER 1989**

PDCC

A Joint Venture of The Ralph M. Parsons Co., Dillingham Construction N. A. Inc., and De Leuw, Cather & Co.,



**MONTHLY CONTRACT
PERFORMANCE REPORT**

for the

LOS ANGELES METRO RED LINE PROJECT

OCTOBER 1989

presented to

Southern California Rapid Transit District

CONTRACT NO. 3369

"The preparation of this Document has been financed in part through grants from the State of California, the City of Los Angeles, the Los Angeles County Transportation Commission and the U. S. Department of Transportation, Urban Mass Transportation Administration, under the Urban Mass Transportation Act of 1964, as amended."

Month OCTOBER Year 1989

14412

SCRTD
1985-
.M46
R46
no. 64

MAR 19 '93



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

TABLE OF CONTENTS

	Page
I. Construction Manager's Summary Statement	1
II. Manpower Performance	8
III. Equal Opportunity Performance	15
IV. Schedule Performance	17
V. Cost Performance	20
VI. Additional Activities Performed in October	26
VII. Summary of Activities Planned for November	38
VIII. Subcontractor/Consultant Status	43
IX. Construction Progress Photos	

100

100



SECTION I

CONSTRUCTION MANAGER'S

SUMMARY STATEMENT

MTA LIBRARY



LOS ANGELES METRO RED LINE

CONTRACT PERFORMANCE REPORT

PDCD

PERIOD OCTOBER 1989

I. CONSTRUCTION MANAGER'S SUMMARY STATEMENT

MAJOR CM ACTIVITIES

This Contract Performance Report (CPR) for the month of October 1989 is the fourth CPR in the Sixth Annual Work Plan (6th AWP) and covers the period September 30 to October 27, 1989. The following is a summary, by functional organization, of major CM activities during this period:

CONSTRUCTION OPERATIONS: Continued construction management (CM) services for 16 Facility Contracts and 11 Systems Contracts, monitoring of utilities relocations, and performance of submittal reviews. Continued conducting QC inspections of work for compliance to plans and specifications. Monitored contractor progress to approved project schedules. Assisted contractors in coordination with local public agencies in areas of community impact, permits and traffic access. Continued to conduct safety inspections of all contractor activities. Responded to contractor document clarification requests as appropriate.

Environmental Activities: Continued monitoring for groundwater and construction water discharges at 7 construction sites. Continued monitoring of Discharge Monitoring Stations at Ballona Creek and Los Angeles River. Prepared and submitted September Discharge Monitoring Report (DMR) to the California Regional Water Quality Control Board (CRWQCB). Prepared and submitted September LA River Dissolved Solids Report to Central and West Basin Water Replenishment District (CWBWRD). Prepared and submitted water quality reports for new dewatering flows from A130 and A135 to CRWQCB.

Utilities and Traffic Activities: Continued coordination of traffic control plans and street closures with city agencies for 5 contracts. Continued coordination of MOS-1 Traffic Control/Traffic Safety inspections with LADOT. Processed a total of 17 Traffic and Utilities related submittals.

Surveying Activities: Continued checking contractor's control points and layout at various construction sites. Continued monitoring instrumentation, building and ground settlement points on A135, A141, A145, A146, A165, A171 and A175. Continued location surveys at yards and shops contracts. Checked layout and excavation for A135 station. Continued walkway as-builts survey for AR and AL tunnels (A171). Checked as-built escalator wellways in Home Savings for A167. Completed review of high utilities claims (A165).

PROJECTS CONTROLS: Processed 28 Change Requests as follows: 2 for A112; 5 for A141; 2 for A145; 1 for A146; 2 for A165, 1 for A167; 1 for A171; 8 for A175; 4 for A610/A115; and 2 for A620. Processed 5 Change Notices as



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

follows: 1 for A130; 1 for A141; 1 for A146; 1 for A175; and 1 for A610/A115. Processed 45 Change Orders as follows: 2 for A112; 1 for A130; 7 for A135; 4 for A145; 6 for A146; 4 for A165; 5 for A167; 4 for A175; 4 for A610/A115; 1 for A615; 2 for A620; 3 for A640; and 1 for A755; Processed 36 executed Change Orders through TRACS as follows: 3 for A112, 3 for A130; 5 for A135; 1 for A141; 11 for A146; 8 for A165; 1 for A175; 1 for A610/A115; and 2 for A710. Processed 4 Potential Claims as follows: 2 for A112; 1 for A130; and 1 for A610. Processed 4 Change - Technical Evaluations as follows: 3 for A145 and 1 for A175. Processed 5 Force Account Change Packages as follows: 5 for A146. Completed Close-out Reconciliations on 4 Force Account Change Orders as follows: 4 for A146. Processed 20 Monthly Payment Estimates. Reviewed Contractor Monthly Progress Reports. Prepared Scheduling inputs to RTD Monthly Status Report. Approved-as-noted Part II Schedule Submittals for A167. Reviews in progress for Part II Schedule revisions from A145, A165 and A175. Review in progress for A167 Part II Schedule. Completed review of A130 Part II Schedule. Prepared quarterly update for the Level III Schedule.

Cost Estimates for Changes/Proposals: A-130-CR-026A: Reviewed contractors proposal and prepared estimate comparison. A-135-CR-004, CR-032 Continued to review changes and proposals related to LAUPT Baggage Handling Facilities and Police Room. A-135-CR-047 Reviewed Contractors proposals, prepared comparison, negotiated settlement for revised work, elevator hydraulic lines. A-135-CR-059 Completed estimate for enlarged wall opening, Door 7B. A-135-CR-051, A141-CR-120, A145-CR-147, A165-CR-083 and A175-CR-051 Completed revised estimates for emergency telephone blockouts. A-136 Began review of Stage II contract documents and MRTC estimate for support in preparation of contract schedule. A-141-CR-092 Completed estimate on relocated Emergency Exit Stair No. 21. A-141-CR-095 Completed review and estimate on increased escalator wellway openings. A-141-CR-097 Reviewed contractors proposal for additional strain gages and monitoring. A-141-CR-100 Completed estimate for revisions to Elevator equipment room. A-141-CR-104 Began estimate on revisions to water service and corrosion control. A-141-CR-011 Access delay to Union Station, reviewed contractor (subcontractors) proposals, prepared estimates and evaluations, participated in negotiations. A-145-CR-124 Reviewed contractors proposal for additional cost to negotiated change. A-145-CR-132, 133 Prepared preliminary estimate for plumbing and piping changes not included with hydraulic changes. A-145-CR-148 Prepared estimate for changes due to added drawing E-145. A-146-CR-038 Reviewed scope of work in preparation for walkway and wet standpipe change estimate. A-165-CR-075 Clarified scope of work and material takeoff for wet standpipe and sprinkler system change. A-165 Reviewed decking quantities, prepared comparison and met with contractor. A-167-CR-002 Reviewed contractors proposal for change to structural openings, BRS wall. A-175-CR-035 Reviewed contractors revised proposal for incoming Electrical Service Room. A-175-CR-047 Prepared estimate for additional embedded drainlines in crossover. A-175-CR-053 Prepared estimate for revisions to plumbing and fire protection systems and structural



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

openings. A-175-CR-075, CR-076, CR-077 Prepared ROM estimate for miscellaneous structural changes. A-620-CR-030 Prepared ROM estimate for access delay to tunnels. A-732 Began preparation of ROM estimate for installation of wheel press and wheel boring machine. Prepared estimate for tunnel bulkheads at Civic Center and 7th Flower Stations. Reviewed contractors proposed Force Account labor rate submittals.

CONTRACT/PROCUREMENTS: Issued three Purchase Orders for five Personal Computers and related software upon District approval. Issued Subcontract with E. D. Greenawalt for estimating services upon District approval. Requested District approval to issue Amendment to consulting agreement with F. E. Endacott & Associates for funds increase to cover remaining AWP-6 work requirements.

ENGINEERING SERVICES: Reviewed RTD consultant J. P. Gould's preliminary evaluation of the A141 tunnel hard rock claim. Assembled A145 construction/instrumentation data and transmitted to MRTC and RTD consultant J. P. Gould. Monitored two test case alternative methods of destressing struts at A141 Civic Center Station. Transmitted A141 Contractor's excavation support design calculations to RTD consultant, J. P. Gould for use in analyzing the Civic Center Station strut overload claim. Completed and distributed draft report on A145 Design Verification Study Task B, for use in evaluating the A141 Civic Center Station strut overload claim. Completed geologic observations in the A146 AR tunnel. Collected, tabulated and transmitted data to J. P. Gould on the A141 Station excavation history plotted against ground movements and strut load build-ups. Processed 14 field inquiries with MRTC to obtain clarification of design requirements. Responded to 160 requests for information or documentation clarification from various Contractors.

During this period 350 Contractor submittals were processed as follows:

For Contract 112	- Approved - 5; Approved-as-Noted - 3;	
For Contract A130	- Approved - 16; Approved-as-Noted - 11; Rejected - 13.	
For Contract A135	- Approved - 3; Approved-as-Noted - 22; Rejected - 7; For Record Only - 1.	
For Contract A135BH	- Approved - 3.	
For Contract A141	- Approved - 6; Approved-as-Noted - 17; Rejected - 3; For Record Only - 1.	
For Contract A145	- Approved - 12; Approved-as-Noted - 36; Rejected - 5; For Record Only - 5.	
For Contract A146	Approved-as-Noted - 4.	



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

For Contract A165	- Approved - 29;	Approved-as-Noted - 37;	Rejected - 4;	For Record Only - 1.
For Contract A167	- Approved - 6;	Approved-as-Noted - 7;	Rejected - 8.	
For Contract A171	- Approved - 2;	Approved-as-Noted - 2.		
For Contract A175	- Approved - 6;	Approved-as-Noted - 7;	Rejected - 5.	
For Contract A610/A115	- Approved - 13;	Approved-as-Noted - 2;	Rejected - 10.	
For Contract A612	- Approved - 1.			
For Contract A615	- Approved - 1.			
For Contract A616	- Approved - 3;	Approved-as-Noted - 1.		
For Contract A620	- Approved - 15;	Approved-as-Noted - 3;	Rejected - 1.	
For Contract A630	- Approved - 1;	Approved-as-Noted - 1.		
For Contract A631	- Approved - 2;	Approved-as-Noted - 1.		
For Contract A640	- Approved - 1;	Approved-as-Noted - 3.		
For Contract A710	- Approved - 1.			
For Contract A740	- Approved - 2.			
For Contract A745	- Approved - 1.			

TOTAL	<u>129</u>	<u>157</u>	<u>56</u>	<u>8</u> = 350
-------	------------	------------	-----------	----------------

SAFETY/SECURITY: Performed daily site safety, health and security surveillances and prepared written reports for the 11 construction contracts. Coordinated activities of the Systemwide Security Guard Service and the Systemwide Clean-up Service Subcontractors. Reviewed and approved the A631 Safety Representative candidate. Continued work on revisions/modifications to specifications on CSSM for Phase II. Began video-still safety site surveys with DIA's Director of Safety.

COMMUNITY RELATIONS - Coordinated community notifications for A130, A141, A145, A146, A165 and A175 tenants affected by lane restrictions and/or street closures. Coordinated and resolved traffic mitigation concerns for tenants along Hill St. affected by A141, and A146 traffic access plans, and for tenants in the 7th/Flower area affected by A165 and A146 (under 7th St.) traffic plans. Provided assistance to A130, A141, A145, A146 and A165 for problems caused by blocked access, noise, dust, accidents, security, rodent control and general construction activities. Provided assistance to RTD in responding to media requests and coordinating 10 site visits. Processed 28 inquiries/complaints. Provided assistance to RTD/LGCA in coordination and implementation of October 25 Community Awareness Meeting for Union Station/Yards & Shops area tenants.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

QUALITY ASSURANCE/QUALITY CONTROL - Continued to review welding activities and conducted fabrication inspections as required to support facilities and system procurement contracts as follows: Site Inspection at: A130, A145 - Inspection of welds on starpacks, kneebrace supports, walers and struts during excavation; - A145 - Inspection of bulkhead strut welds for tunnel supports and rebar column fabrication; A141 - Evaluation and inspection of welds during strut support modification; A145, A165, A175 - Inspection of welds during installation of permanent structures; A145 - Inspection of welds for deck beams for south blast relief shaft area and escalator entrance. Shop Inspection at: Paramount Metals - Inspection of embedded supports for slurry walls, rails, escalator beam supports, tunnel rings, and heavy frames for permanent structures (A130, A141, A145, A165, A175); Cowelco - Inspection of handrails, stairways and miscellaneous embedded frames for A135 Baggage Handling Facility; Angeles Steel - Inspection and monitoring of stud welding subcontracted from Paramount Metals; Scott Company - Inspection of Wet Standpipe and Hydraulic piping system spool pieces (A135, A145, A165). Continued to monitor on-site testing and Smith-Emery test laboratory activities. Witnessed system pressure tests for: A141 Wet Standpipe pipe spool; A171 Fire Lines; and A610/A115 Fire Lines, and Domestic Water and Natural Gas Lines. Inspected welded joints on A145 Deluge Lines. Monitored Smith-Emery testing of elastomeric pad samples for A171 and Batch Plant Inspection at Calmat and TMC. Inspected installation and monitored testing of HDPE for A135. Participated in A112 contract close-out activities. Participated in Safety Certification Review Team Audit of Contract A112. Conducted QA review of approximately 142 contractor submittals for various contracts. Issued Quality Assurance audit for Flakt, Inc. and National Metals Inc. for contracts A740 and A745. Supported audit of PDCD/QA Program by Hill International for UMTA. Monitored Smith-Emery concrete test reports.

EQUAL OPPORTUNITY - Monitored Equal Opportunity reporting requirements (i.e. SSA&P Report, Monthly Employment Utilization Reports, Certified Payroll) for 27 Contracts. Conducted project site interviews for 6 contracts. Processed penalty assessments for the late submittal of the Monthly Employment Utilization Reports for 7 Contracts.

MANPOWER PERFORMANCE

The manpower performance for October is measured against the approved planned staffing for this period from the 6th AWP. During October the actual staff level was 193 vs. the planned staff level of 175. Therefore, the actual staff count for October was 18 over the planned staffing level. The staff breakdown by company was 130 for the Joint Venture firms and 63 for the Associate Subcontractors. The increased staff was required for the processing of excessive field submittals and correspondence, requests for information, and for multishift inspection of construction work at various job sites.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

the 6th AWP. During October the actual staff level was 193 vs. the planned staff level of 175. Therefore, the actual staff count for October was 18 over the planned staffing level. The staff breakdown by company was 130 for the Joint Venture firms and 63 for the Associate Subcontractors. The increased staff was required for the processing of excessive field submittals and correspondence, requests for information, and for multishift inspection of construction work at various job sites.

The October period had 160 available workhours/person. The plan provided for expenditure of 28,000 hours, including "as-required" manhours which would have generated a projected equivalent head count of 175.0 personnel at 160 hours/person. Actual hours expended were 29,514 which translates into a 184.46 equivalent head count at 160 hours/person including temporary personnel, resulting in the equivalent of 9.46 personnel over the plan.

Cumulative total hours incurred through October were 118,154 against a plan of 117,584 resulting in an over plan variance of 570 hours.

EQUAL OPPORTUNITY (EO) PERFORMANCE

EO performance for PDCD in October measured on a cost accrual basis for the category of DBE, and on a percentage basis for the category of Minority and Women Affirmative Action were as follows:

- o Cumulative DBE participation for the Sixth Annual Work Plan through the month, measured against a total cost basis was 21.8%, 1.8% over the goal of 20%. Cumulative DBE participation since contract inception is 22.8%, 2.8% above the 20% goal.
- o Minority and Women Affirmative Action performance for the month exceeded the established goal of 17% for minorities by 23% and was below the goal of 8% for women by 1%.

SCHEDULE PERFORMANCE

- o **Contractor Submittals** - During this period, 274 submittals were received per contract number as follows: A112 (6), A130 (15), A135 (30), A135BH (2), A141 (27), A145 (56), A146 (4), A165 (56), A167 (17), A171 (2), A175 (7), A610/A115 (14), A612 (1), A615 (0), A616 (3), A620 (20), A630 (0), A630 (0), A631 (6), A640 (3), A710 (1), A732 (0), A740 (3), and A745 (1); of the 274 received this period plus the 265 carryover from September, 350 packages were processed and returned to the contractors; the balance of 189 remain in review.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

COST PERFORMANCE - Sixth Annual Work Plan

- o Total incurred costs of \$1,355,528 for CM Direct Services (excluding General Condition Items) for the period were under the plan of \$1,369,817 by \$14,289. This variance results from the net effect of Other Direct Costs (ODCs) being under the plan by \$21,627 and labor expenditures (total PDCD and subcontractors) being over the plan by \$7,338.
- o The cumulative costs for total CM Services (including General Condition Items) incurred through October were \$5,605,152 against a plan of \$5,947,526 resulting in an under plan of \$342,374.
- o The October CPR indicates an Estimate at Completion as of the 6th AWP (including General Condition Items) of \$16,865,101 versus a plan of \$16,872,967 for an underexpenditure of \$7,866.

GENERAL CONDITION ITEMS

General Condition Items (GCI's) expenditure of \$46,207 for the period were under the plan of \$64,692 for the period by \$18,485. This report forecasts an Estimate At Completion (EAC) as of the 6th AWP period for GCI's of \$793,686 which is over the plan of \$791,300 by \$2386.

GENERAL

- o This "Monthly Contract Performance Report" covers progress relative to PDCD's CM Services contract with the RTD. For information on the status of construction/procurement contracts, see the "Monthly Status Report" produced by the District. A copy of the RTD report is distributed to previous recipients of the no longer produced PDCD "Monthly Construction Performance Report", as required.


Melvin L. Polacek
Construction Manager





SECTION II

MANPOWER PERFORMANCE



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

II. MANPOWER PERFORMANCE

This CPR for the month of October compares actual manpower to the planned manpower in the approved 6th AWP. Table II-1, Page 10, illustrates planned staff vs. actual staff and variances for October.

During October, personnel assignments/deletions included the addition of 1 Senior Change Specialist, 2 Inspectors, 1 Secretary (Administration), and 1 Data Technician (Temp); and the deletion of 1 Senior Accountant, 1 Chief Inspector, 1 QA/QC Engineer (A/R), and 1 Estimating Consultant (A/R).

For the October period, under the approved 6th AWP, the total planned staffing level (including regular and as-required classifications) is 175. The actual staff (including regular, as-required and temporary classifications) was 193 resulting in 18 over the plan. The current actual staff by company for the October period is as follows:

<u>Company</u>	<u>Staff Level</u>	<u>Company</u>	<u>Staff Level</u>
The Ralph M. Parsons Company	56	Jenkins, Gales & Martinez, Inc.	10
Dillingham Construction, Inc.	55	Kal Krishnan Consulting	2
De Leuw, Cather & Company	19	Martin & Huang International	4
Better Personnel Employment Services	9	North Pacific Construction Management	6
Construction Control Services Corporation	16	Ochoa & Sillas	-
Dames & Moore	1	Randolph & Tate Associates	-
D'Leon Consulting	1	Transmetrics	1
Engineering-Science, Inc.	2	Manpower	4
Jacobs Associates	7		

The PDCD Manpower Chart on Page 11 illustrates planned manpower for Construction Services for the Sixth Annual Work Plan period. Actual equivalent manpower is shown for the months of July through October.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

The October period had 160 available workhours/person. The plan provided for an expenditure of 28,000 hours, including "as-required" manhours, which would have generated a projected equivalent head count of 175.0 personnel @ 160 hrs./person. Actual hours expended were 29,514 which translates into an equivalent head count of 184.46 @ 160 hrs./person including temporary personnel, resulting in the equivalent of 9.46 personnel over the plan.

The hours expended for the period were 29,514 versus a plan of 28,000. The 1,514 manhours variance for the period is calculated as follows:

9.46 equivalent staff over plan @ 160
hours/period in plan =

1,514 hours

OCTOBER MANHOUR VARIANCE TO PLAN

1,514 hours

Cumulative total hours for the 6th AWP incurred through October were 118,154 against a plan of 117,584 resulting in an over plan variance of 570 hours (Page 23).



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

TABLE II-1 CONSTRUCTION MANAGEMENT STAFF COUNT - OCTOBER
SIXTH ANNUAL WORK PLAN

<u>Phase II</u> <u>Construction</u> <u>Services</u>			
<u>Regular/As-required/Temporary</u>			
<u>Position</u>	<u>Planned</u>	<u>Actual</u>	<u>Variance</u>
Construction Manager	1	1	0
Manager, Safety and Security	1	1	0
Safety Inspectors	1	1	0
Manager, Quality Assurance(3)	1	0	(1)
Lead Quality Assurance Engineer(3)	0	1	1
QA/QC Engineers/Inspectors	1	2	1
Manager, Project Administration/Accounting(5)	1	0	(1)
Lead Accountant(5)	0	1	1
Senior Accountant	1	0	(1)
Senior Accounting Clerks	2	2	0
Manager, Community Relations	1	1	0
Community Relations Coordinator	1	1	0
Manager, EO Administration	1	1	0
EO Administrator	1	0	(1)
Labor Relations Advisor	0	0	0
Legal Counsel	0	0	0
Subtotal	<u>13</u>	<u>12</u>	<u>(1)</u>
DCM, Eng'r Serv./Proj. Controls(4)	0	0	0
Manager, Eng'r Serv./Proj. Contr.(4)	0	1	1
Manager, Administration and Staff Support(4)	1	0	(1)
Manager, Project Controls	1	1	0
Technical Data Coordinator	1	1	0
Lead Cost Engineer	1	1	0
Cost Engineers	4	4	0
Lead Change Control	1	1	0
Change Control Specialist	2	1	(1)
Claims Proc. Spec.	1	1	0
Data Technicians	1	1	0
Lead Planner/Scheduler	1	1	0
Planner/Schedulers	9	7	(2)
Lead Estimator	1	1	0
Estimators	3	3	0
Sr. Data Technician	1	1	0
Computer Support	0	0	0
Lead Document Control Specialist	1	1	0
Document Control Specialist	1	1	0
Shop Drawing Coordinator	1	2	1
Data Technician	1	2	1
File Clerk	1	2	1
Manager, Contracts/Procurement(5)	1	1	0
Sr. Contract Administrator	1	1	0
Office Services Manager	1	1	0
Secretarial/Word Processing/Clerical/ Drafting/ Courier	1	1	0
Subtotal	<u>50</u>	<u>52</u>	<u>2</u>

<u>Phase II</u> <u>Construction</u> <u>Services</u>			
<u>Regular/As-required/Temporary</u>			
<u>Position</u>	<u>Planned⁽¹⁾</u>	<u>Actual⁽²⁾</u>	<u>Variance</u>
Manager, Engineering Services/ Systems Integration	1	1	0
Drafting Technicians	2	1	(1)
Lead Architect	1	2	1
Architect	0	1	1
Lead Electrical Engineer	1	1	0
Electrical Engineer	1	7	6
Lead Engineer, Geotech. Section	1	1	0
Engineers, Geotech. Section	4	3	(1)
Lead Mechanical Engineer	1	1	0
Mechanical Engineer	0	3	3
Lead Structural Engineer	1	1	0
Sr. Struct./Struct. Engineers	2	4	2
Lead Systems Engineer	1	1	0
Systems Engineer	2	1	(1)
Office Engineer	0	1	1
Subtotal	<u>18</u>	<u>29</u>	<u>11</u>
DCM, Operations	1	1	0
Manager, General Services	1	1	0
Lead Utilities Engineer	1	0	(1)
Party Chief	1	1	0
Instrument Person	1	2	1
Rod Person	2	1	(1)
Lead Environmental Engineer	1	1	0
Environmental Specialists	3	2	(1)
Engineering Technician/Coordinator	0	1	1
Resident Engineers	9	8	(1)
Chief Inspectors	8	9	1
Sr. Inspectors/Inspectors	34	37	3
Office Engineers	9	11	2
Field Secretaries/Clerical	10	12	2
Manager, Systemwide Construction	1	1	0
Office Engineer	3	3	0
Resident Engineers	4	4	0
Secretaries/Clerical	4	4	0
Inspector	0	0	0
Data Technicians	1	1	0
Subtotal	<u>94</u>	<u>100</u>	<u>6</u>
Totals	<u>175</u>	<u>193</u>	<u>18</u>

NOTES:

- (1) The "Planned" staff count is taken directly from the RTD approved PDCD 6th AMP. It is the planned staff count for the reported month and includes both "Regular" and "As-required" classifications.
- (2) The "Actual" staff count is the total actual staff count by Job Position. Included are regular, as-required and temporary staff.
- (3) Effective July 1, 1989, the duties of the Manager, Quality Assurance have been reassigned to the Lead QA/QC Engineer.
- (4) Effective July 1, 1989, the Manager of Administration and Staff Support assumed the position of DCM, Project Engineering/Controls Services and the position title was changed to Manager, Engineering Services/Project Controls.
- (5) Effective July 1, 1989, the Manager, Contracts/Procurement assumed the administrative duties previously handled by the Manager, Project Administration/Accounting. Effective August 1, 1989, the Lead Accountant assumed the accounting duties previously handled by the Manager, Project Administration/Accounting and the title "Manager, Project Administration/Accounting" was eliminated.




LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT SIXTH ANNUAL WORK PLAN

PERIOD OCTOBER 1989

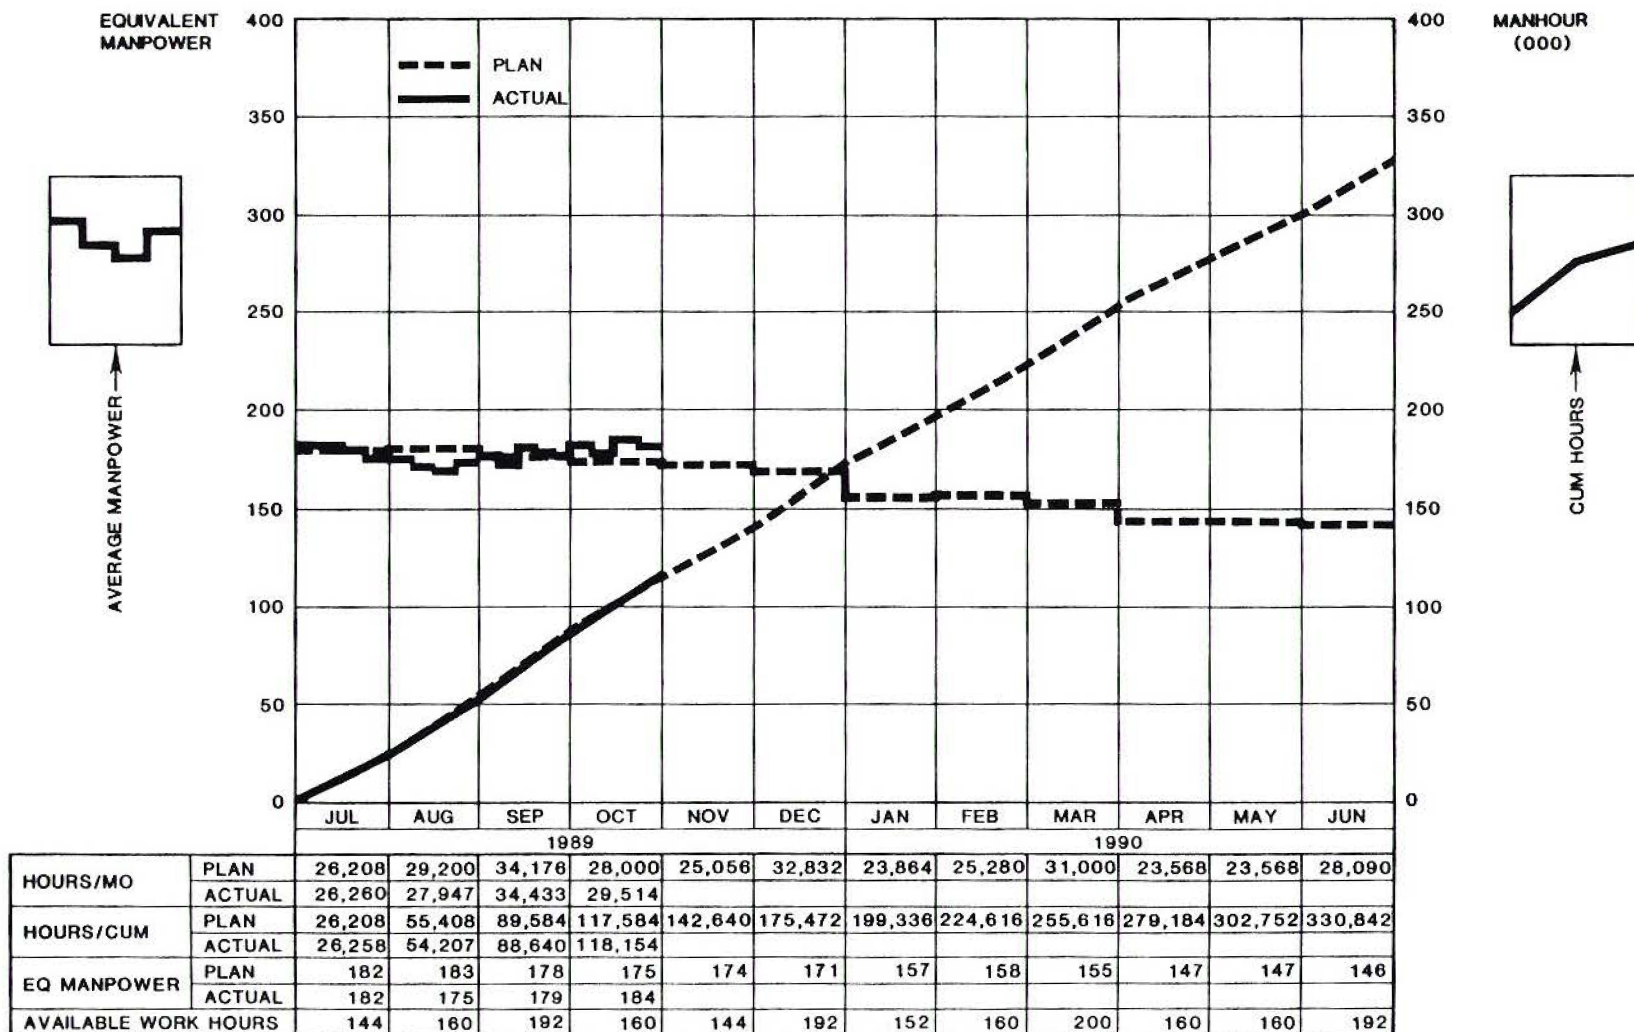

PDCD MANPOWER

Parsons-Dillingham-De Leuw, Cather



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

SIXTH ANNUAL WORK PLAN PDCD MANHOURS BY FUNCTIONAL DEPARTMENT

PAGE 1 OF 3

			1989						1990						
DESCRIPTION (MHRS)			JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	TOTALS
MANHOURS BY FUNCTIONAL DEPARTMENT															
A PROJECT MANAGEMENT	PLAN	current	2,448	2,720	3,264	2,720	2,448	3,264	2,417	2,544	2,980	2,384	2,224	2,669	32,082
		cumulative	2,448	5,168	8,432	11,152	13,600	16,864	19,281	21,825	24,805	27,189	29,413	32,082	
	ACTUAL	current	2,729	2,602	3,280	3,066	0	0	0	0	0	0	0	0	11,677
		cumulative	2,729	5,331	8,611	11,677	11,677	11,677	11,677	11,677	11,677	11,677	11,677	11,677	
C. FAC. CONSTRUCTION	PLAN	current	10,800	11,920	13,440	11,200	9,792	12,672	8,968	9,440	11,800	8,960	9,120	10,944	129,056
		cumulative	10,800	22,720	36,160	47,360	57,152	69,824	78,792	88,232	100,032	108,992	118,112	129,056	
	ACTUAL	current	11,255	11,876	14,473	11,745	0	0	0	0	0	0	0	0	49,349
		cumulative	11,255	23,131	37,604	49,349	49,349	49,349	49,349	49,349	49,349	49,349	49,349	49,349	
E SYSTEMWIDE CONST	PLAN	current	1,872	2,080	2,496	2,080	2,016	2,688	2,417	2,544	3,180	2,704	2,704	3,245	30,026
		cumulative	1,872	3,952	6,448	8,528	10,544	13,232	15,649	18,193	21,373	24,077	26,781	30,026	
	ACTUAL	current	1,559	1,659	2,210	1,981	0	0	0	0	0	0	0	0	7,409
		cumulative	1,559	3,218	5,428	7,409	7,409	7,409	7,409	7,409	7,409	7,409	7,409	7,409	
F GENERAL SERVICES	PLAN	current	1,440	1,600	1,920	1,600	1,440	1,920	1,094	1,152	1,440	1,024	1,024	1,229	16,883
		cumulative	1,440	3,040	4,960	6,560	8,000	9,920	11,014	12,166	13,606	14,630	15,654	16,883	
	ACTUAL	current	1,486	1,549	1,600	1,406	0	0	0	0	0	0	0	0	6,041
		cumulative	1,486	3,035	4,635	6,041	6,041	6,041	6,041	6,041	6,041	6,041	6,041	6,041	
K PROJECT CONTROLS	PLAN	current	3,960	4,400	5,280	4,400	4,104	5,472	3,739	3,936	4,720	3,392	3,392	4,070	50,865
		cumulative	3,960	8,360	13,640	18,040	22,144	27,616	31,355	35,291	40,011	43,403	46,795	50,865	
	ACTUAL	current	3,457	3,887	4,067	3,687	0	0	0	0	0	0	0	0	15,098
		cumulative	3,457	7,344	11,411	15,098	15,098	15,098	15,098	15,098	15,098	15,098	15,098	15,098	



LOS ANGELES METRO RED LINE

CONTRACT PERFORMANCE REPORT

PDCD

PERIOD OCTOBER 1989

SIXTH ANNUAL WORK PLAN PDCD MANHOURS BY FUNCTIONAL DEPARTMENT

PAGE 2 OF 3

			1989						1990						
DESCRIPTION (MHRS)			JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	TOTALS
MANHOURS BY FUNCTIONAL DEPARTMENT															
L PROCUREMENT	PLAN	current	432	480	576	320	288	384	274	288	360	256	256	307	4,221
		cumulative	432	912	1,488	1,808	2,096	2,480	2,754	3,042	3,402	3,658	3,914	4,221	
	ACTUAL	current	249	309	352	295	0	0	0	0	0	0	0	0	1,205
		cumulative	249	558	910	1,205	1,205	1,205	1,205	1,205	1,205	1,205	1,205	1,205	1,205
M ENG. SVCS./SYST. INTEGR.	PLAN	current	2,520	2,960	3,360	2,800	2,232	2,976	2,842	2,832	3,540	2,608	2,448	3,130	34,248
		cumulative	2,520	5,480	8,840	11,640	13,872	16,848	19,690	22,522	26,062	28,670	31,118	34,248	
	ACTUAL	current	2,913	2,950	5,135	4,762	0	0	0	0	0	0	0	0	15,760
		cumulative	2,913	5,863	10,998	15,760	15,760	15,760	15,760	15,760	15,760	15,760	15,760	15,760	15,760
N COMMUNITY RELATIONS	PLAN	current	288	320	384	320	288	384	152	160	200	160	160	192	3,008
		cumulative	288	608	992	1,312	1,600	1,984	2,136	2,296	2,496	2,656	2,816	3,008	
	ACTUAL	current	248	265	272	156	0	0	0	0	0	0	0	0	941
		cumulative	248	513	785	941	941	941	941	941	941	941	941	941	941
P SAFETY	PLAN	current	288	320	384	320	288	384	304	320	400	256	256	307	3,827
		cumulative	288	608	992	1,312	1,600	1,984	2,288	2,608	3,008	3,264	3,520	3,827	
	ACTUAL	current	200	320	340	280	0	0	0	0	0	0	0	0	1,140
		cumulative	200	520	860	1,140	1,140	1,140	1,140	1,140	1,140	1,140	1,140	1,140	1,140
Q QUALITY ASSURANCE	PLAN	current	432	480	576	320	288	384	274	288	360	288	288	346	4,324
		cumulative	432	912	1,488	1,808	2,096	2,480	2,754	3,042	3,402	3,690	3,978	4,324	
	ACTUAL	current	338	402	520	438	0	0	0	0	0	0	0	0	1,698
		cumulative	338	740	1,260	1,698	1,698	1,698	1,698	1,698	1,698	1,698	1,698	1,698	1,698



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

SIXTH ANNUAL WORK PLAN PDCD MANHOURS BY FUNCTIONAL DEPARTMENT

PAGE 3 OF 3

			1989						1990						
DESCRIPTION (MHRs)			JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	TOTALS
MANHOURS BY FUNCTIONAL DEPARTMENT															
R PROJECT ADMIN.	PLAN	current	1,440	1,600	1,920	1,600	1,440	1,920	1,383	1,616	1,820	1,536	1,376	1,651	19,302
		cumulative	1,440	3,040	4,960	6,560	8,000	9,920	11,303	12,919	14,739	16,275	17,651	19,302	
	ACTUAL	current	1,581	1,856	1,914	1,554	0	0	0	0	0	0	0	0	6,905
		cumulative	1,581	3,437	5,351	6,905	6,905	6,905	6,905	6,905	6,905	6,905	6,905	6,905	
S EQUAL OPPORTUNITY	PLAN	current	288	320	384	320	288	384	0	0	0	0	0	0	1,984
		cumulative	288	608	992	1,312	1,600	1,984	1,984	1,984	1,984	1,984	1,984	1,984	
	ACTUAL	current	245	272	270	144	0	0	0	0	0	0	0	0	931
		cumulative	245	517	787	931	931	931	931	931	931	931	931	931	
T LABOR RELATIONS	PLAN	current	0	0	0	0	144	0	0	0	200	0	160	0	504
		cumulative	0	0	0	0	144	144	144	144	344	344	504	504	
	ACTUAL	current	0	0	0	0	0	0	0	0	0	0	0	0	0
		cumulative	0	0	0	0	0	0	0	0	0	0	0	0	
U LEGAL	PLAN	current	0	0	192	0	0	0	0	160	0	0	160	0	512
		cumulative	0	0	192	192	192	192	192	352	352	352	512	512	
	ACTUAL	current	0	0	0	0	0	0	0	0	0	0	0	0	0
		cumulative	0	0	0	0	0	0	0	0	0	0	0	0	
TOTAL (HOURS)	PLAN	current	26,208	29,200	34,176	28,000	25,056	32,832	23,864	25,280	31,000	23,568	23,568	28,090	330,842
		cumulative	26,208	55,408	89,584	117,584	142,640	175,472	199,336	224,616	255,616	279,184	302,752	330,842	
	ACTUAL	current	26,260	27,947	34,433	29,514	0	0	0	0	0	0	0	0	118,154
		cumulative	26,260	54,207	88,640	118,154	118,154	118,154	118,154	118,154	118,154	118,154	118,154	118,154	



SECTION III

EQUAL OPPORTUNITY

PERFORMANCE





LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

III. EQUAL OPPORTUNITY PERFORMANCE

DBE Participation

The monthly DBE participation for the Sixth Annual Work Plan for October measured on the basis of accrued total cost was 21.8%, 1.8% above the 20% goal. The cumulative percentage for the Sixth Annual Work Plan was 23.5%, 3.5% above the 20% goal (Figure 1 on Page 16). The cumulative percentage for the total contract from its inception in July 1984 is 22.8%, 2.8% above the 20% goal.

Affirmative Action Analysis

The Affirmative Action Analysis, as indicated in Figure 2 on Page 16, shows the established goal of 17% for minorities was exceeded by 23%. The Affirmative Action Analysis for women, as indicated in Figure 3 on Page 16, shows 7%, which is below the goal of 8% by 1.0%.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

SIXTH ANNUAL WORK PLAN

PERIOD OCTOBER 1989

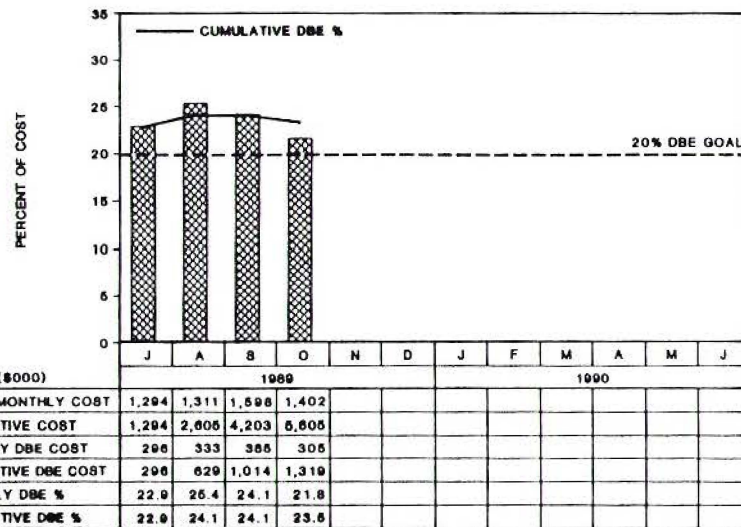


FIGURE 1 - DBE ANALYSIS

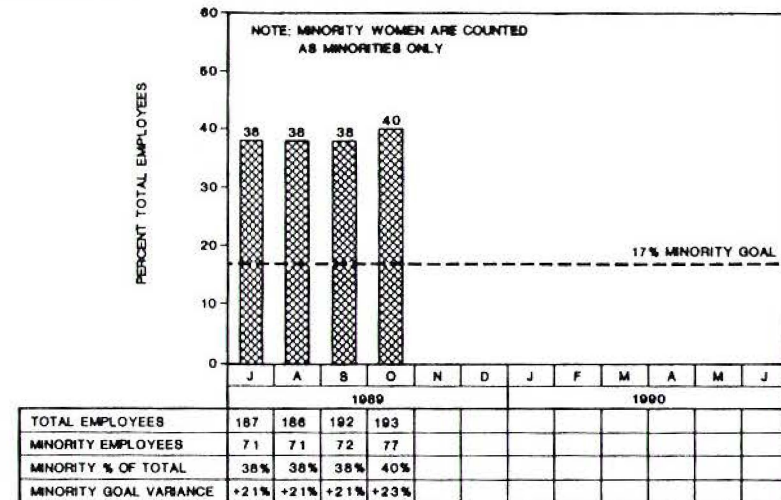


FIGURE 2 - MINORITY AFFIRMATIVE ACTION ANALYSIS

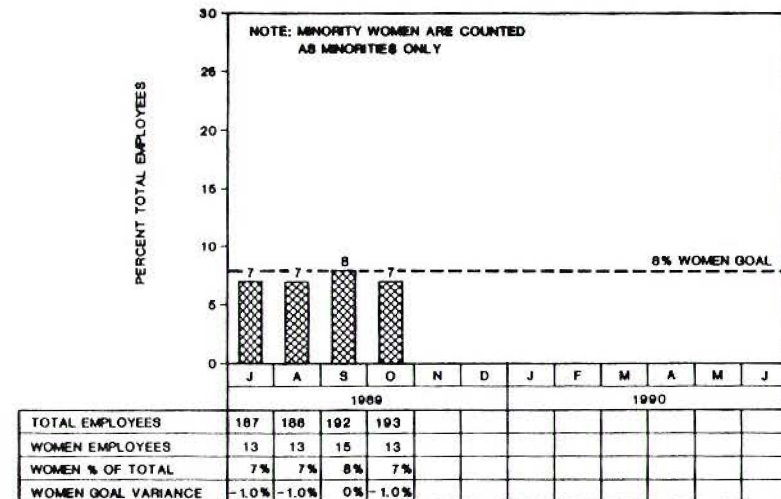


FIGURE 3 - WOMEN AFFIRMATIVE ACTION ANALYSIS

SECTION IV
SCHEDULE PERFORMANCE

MTA LIBRARY



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

IV. SCHEDULE PERFORMANCE

CONTRACTOR SUBMITTALS - During this period, 274 submittals were received from the Construction Contractors and 265 were carried over from September. 350 packages were processed (approved, approved-as-noted, rejected and reviewed for record only) and returned to the Contractors as shown in the following tabulation. The balance of 189 are still under review.

<u>Contracts</u>	<u>Carryover From Sept.</u>	<u>No. Of Submittals Received in Oct.</u>	<u>Submittals Processed Within 30 Days</u>	<u>Submittal Processed In Over 30 Days</u>	<u>Carryover To November</u>
A112✓	7	6✓	5	3	5✓
A130	34	15	30	10	9
A135	30	30	24	9	27
A135BH	9	2	3	0	8
141	19	27	22	5	19
A145/A145A	39	56	49	9	37
A146	4	4	2	2	4
A165	41	56	55	16	26
A167	18	17	20	1	14
A171	2	2	4	0	0
A175	18	7	13	5	7
A610/A115	19	14	23	2	8
A612	0	1	1	0	0
A615	1	0	1	0	0
A616	10	3	4	0	9
A620	9	20	19	0	10
A630	2	0	2	0	0
A631	1	6	3	0	4
A640	1	3	1	3	0
A710	0	1	1	0	0
A732✓	1	0	0	0	1
A740	0	3	2	0	1
A745	0	1	1	0	0
TOTAL	265	274	285	65	189

Parsons-Dillingham-De Leuw, Cather



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

Construction Package Reviews - Analysis of the activities on the "Design Packages Status Window Report, Current Period", (Page 19), shows the following document review:

- o Constructibility Reviews Completed Constructibility Review of A760/100%, Signing and Edgelights.
- o Claims Avoidance Review - Completed Claims Avoidance Review (CAR) of A760/100%, Signing and Edgelights. Continue CAR of A147, Civic Center Station, Stage II and A157, 5th/Hill Station, Stage II.

Training Programs - The following training programs were underway during the October period:

- o Provided specialized underground safety training/indoctrination for PDCD staff, MRTC and visitors.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

DESIGN PACKAGE STATUS WINDOW REPORT - CURRENT PERIOD 9-30-89 TO 10-27-89

Contract #	Description	Pkg Type	Review Code	Schedule Receipt	Received	Schedule Complete	Actual Complete	SC	Remarks
A-147	CIVIC CENTER STATION (STAGE II)	DWGS	CAR	08-16-89	08-17-89	10-27-89			*RESCHEDULED TO 11-10-89 BY PDCD
A-147	CIVIC CENTER STATION (STAGE II)	SPEC	CAR	08-16-89	08-30-89	10-27-89			*RESCHEDULED TO 11-10-89 BY PDCD
**									
A-157	5TH/HILL STATION (STAGE II)	DWGS	CAR	08-14-89	08-16-89	10-06-89			*RESCHEDULED TO 11-3-89 BY PDCD
A-157	5TH/HILL STATION (STAGE II)	SPEC	CAR	08-14-89	08-22-89	10-06-89			*RESCHEDULED TO 11-3-89 BY PDCD
**									
A-760	SIGNING AND EDGELIGHTS	DWGS	CAR	09-08-89	09-19-89	09-29-89	10-17-89		*RESCHEDULED TO 10-13-89 BY PDCD
			DC100	09-08-89	09-19-89	09-13-89	10-17-89		*RESCHEDULED TO 10-13-89 BY PDCD
A-760	SIGNING AND EDGELIGHTS	SPEC	CAR	09-08-89	09-19-89	09-29-89	10-17-89		*RESCHEDULED TO 10-13-89 BY PDCD
			DC100	09-08-89	09-19-89	09-29-89	10-17-89		*RESCHEDULED TO 10-13-89 BY PDCD
**									

6 records listed. 8 values listed.

Review Codes : LT60 - Less than 60% IP60 - In progress 60% PF85 - Prefinal 85%
PF90 - Prefinal 90% FS100 - Final submittal 100% DC100 - Final design complete 100%
CAR- Claims Avoidance Review CE - Check Estimate

NOTE : Based on 10-03-89, MRTD Design Review Schedule

Parsons-Dillingham-De Leuw, Cather





SECTION V

COST PERFORMANCE



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

V. COST PERFORMANCE

SIXTH ANNUAL WORK PLAN

Total incurred costs of \$1,355,528 (Page 25) for CM Direct Services (without General Condition Items) for the period were under the plan of \$1,369,817 by \$14,289. This variance results from the net effect of Other Direct Costs (ODCs) being under the plan by \$21,627 and Labor expenditures (total PDCD and subcontractors) being over the plan by \$7,338.

The cumulative costs for total CM Services (including General Condition Items) incurred through October were \$5,605,152 against a plan of \$5,947,526 resulting in an under plan expenditure of \$342,374 (Page 25).

The October CPR forecasts (Page 25) a total CM Services Estimate At Completion of \$16,865,101 versus a plan of \$16,872,967 for an underexpenditure of \$7,866. Extracting the General Condition Items for separate reporting, the October CPR forecasts a CM Direct Services Estimate At Completion of \$16,071,415 versus a plan of \$16,081,667 for an under plan expenditure of \$10,252.

GENERAL CONDITION ITEMS

General Condition Items (GCI's) expenditure of \$46,207 were under the plan of \$64,692 for the period by \$18,485. This report forecasts an Estimate At Completion (EAC) as of the 6th AWP period for GCI's of \$793,686 versus a plan of \$791,300, for a projected overplan expenditure of \$2,386. (Page 24)

LABOR COSTS

The average hourly labor rate, including burdens and fees, experienced for the period was \$43.00/hr. compared to a plan rate of \$45.06 (-)/hr., resulted in a difference of \$2.06 per hour.

The variances can be summarized into two categories:

STAFFING VARIANCE

9.4625 equivalent staff over plan @ 160
hours at \$45.0589/hour =

IMPACT ON OCTOBER COSTS

\$ 68,219



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

RATE VARIANCE

184.4625 actual staff equivalent @ 160 hours
@ \$2.06278931/hour =

(60,881)

OCTOBER COST VARIANCE TO PLAN

\$ 7,338

OTHER DIRECT COSTS

Other Direct Costs (ODCs) were under the plan for the period by a net of \$21,627 as follows:

DESCRIPTION	CURRENT PERIOD DOLLARS			CUMULATIVE DOLLARS		
	BUDGET	ACTUAL	VARIANCE	BUDGET	ACTUAL	VARIANCE
(1)Field Office Expenses	55,300	44,540	-10,760	221,200	179,882	-41,318
(2)Office Equipment	3,725	573	-3,152	14,900	6,744	-8,156
(3)Travel & Relocation	18,142	7,257	-10,885	72,567	33,663	-38,904
(4)Vehicles & Maintenance	4,900	7,522	2,622	19,600	18,259	-1,341
(5)Reproduction	6,050	4,624	-1,426	24,200	18,654	-5,546
(6)Telephone & Telex	5,950	5,627	-323	23,800	20,961	-2,839
(7)Computer Operation Support	2,292	2,361	69	9,167	10,396	1,229
(8)Gross Receipt Tax	7,834	6,951	- 883	31,334	30,151	-1,183
(9)Field Equipment	3,975	7,086	-3,111	15,900	13,665	-2,235
S/T ODC's	108,168	86,541	-21,627	432,668	332,375	-100,293

NOTES

- (1) Field Office Expenses - underexpenditure due to less than planned purchase of supplies and parking.
- (2) Office Equipment - underexpenditure due to lower than planned expenditures.
- (3) Travel and Relocation - underexpenditure due to planned travel not materializing.
- (4) Vehicles & Maintenance - overexpenditure due to higher than planned vehicle maintenance costs.
- (5) Reproduction - underexpenditure due to lower than planned reproduction.
- (6) Telephone and Telex - underexpenditure due to lower communications cost.
- (7) Computer Operation Support - overexpenditure due to higher than normal DMCS costs.
- (8) Gross Receipt Tax - varies directly with the actual cumulative rate of expenditure per period.
- (9) Field Equipment - overexpenditure due to higher than planned environmental expenditures in the current period.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

CM COST PERFORMANCE - OCTOBER 1989 SIXTH ANNUAL WORK PLAN CONSTRUCTION (\$000)

	PLANNED	ACTUAL	VARIANCE	%
PDCD				
LABOR, BURDENS, FEE				
CUMULATIVE THROUGH SEPTEMBER	\$ 2598	\$ 2541	\$ (57)	-2.19%
CURRENT MONTH	820	851	31	3.78%
CUMULATIVE THROUGH OCTOBER	\$ 3418	\$ 3392	\$ (26)	-0.76%
TRAVEL AND ODC'S				
CUMULATIVE THROUGH SEPTEMBER	\$ 325	\$ 245	\$ (80)	-24.62%
CURRENT MONTH	108	87	(21)*	-19.44%
CUMULATIVE THROUGH OCTOBER	\$ 433	\$ 332	\$ (101)	-23.33%
SUBCONTRACTORS				
CUMULATIVE THROUGH SEPTEMBER	\$ 1,396	\$ 1,289	\$ (107)	-7.66%
CURRENT MONTH	442	418	(24)	-5.43%
CUMULATIVE THROUGH OCTOBER	\$ 1,838	\$ 1,707	\$ (131)	-7.13%
SUBTOTAL CM DIRECT SERVICES				
CUMULATIVE THROUGH SEPTEMBER	\$ 4,319	\$ 4,075	\$ (244)	-5.65%
CURRENT MONTH	1,370	1,356	(14)	-1.02%
CUMULATIVE THROUGH OCTOBER	\$ 5,689	\$ 5,431	\$ (258)	-4.54%
GENERAL CONDITION ITEMS				
CUMULATIVE THROUGH SEPTEMBER	\$ 194	\$ 128	\$ (66)	-34.02%
CURRENT MONTH	65	46	(19)*	-29.23%
CUMULATIVE THROUGH OCTOBER	\$ 259	\$ 174	\$ (85)	-32.82%
TOTAL CM SERVICES				
CUMULATIVE THROUGH SEPTEMBER	\$ 4,513	\$ 4,203	\$ (310)	-6.87%
CURRENT MONTH	1,435	1,402	(33)	-2.30%
CUMULATIVE THROUGH OCTOBER	\$ 5,948	\$ 5,605	\$ (343)	-5.77%
HOURS				
CUMULATIVE THROUGH SEPTEMBER	89,584 hrs	88,640 hrs	(944) hrs	-1.05%
CURRENT MONTH	28,000	29,514	1,514	5.41%
CUMULATIVE THROUGH OCTOBER	117,584 hrs	118,154 hrs	570 hrs	0.48%

* OFF BY ONE DUE TO ROUNDING



LOS ANGELES METRO RED LINE


PDOD

CONTRACT PERFORMANCE


REPORT

SIXTH ANNUAL WORK PLAN


PERIOD OCTOBER 1989

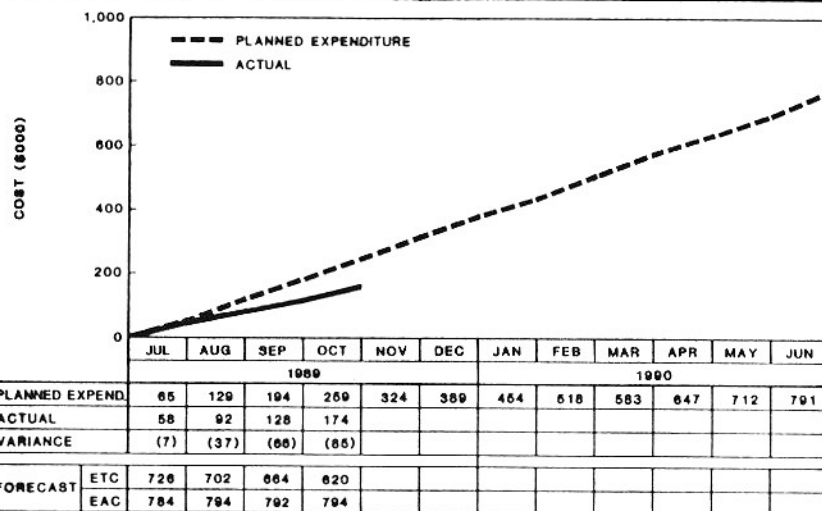

GENERAL CONDITION ITEMS CUMULATIVE COST PERFORMANCE

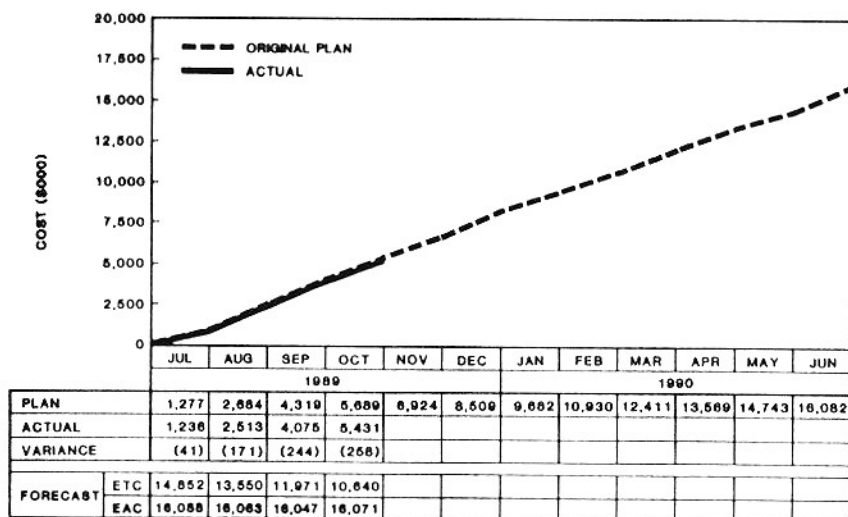

CM DIRECT SERVICES CUMULATIVE COST PERFORMANCE

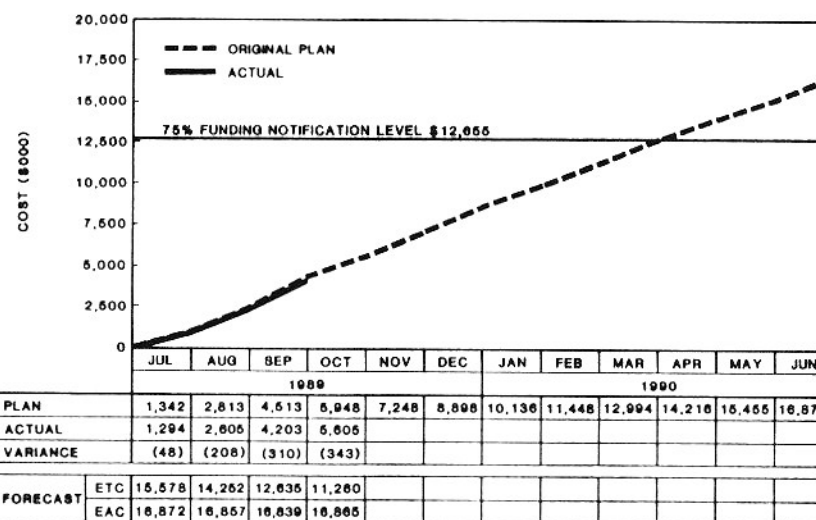

TOTAL CM SERVICES (INCLUDING G.C.I.'s) CUMULATIVE COST PERFORMANCE



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

**PDCD CM SERVICES - 6TH ANNUAL WORK PLAN
COST REPORT FOR MONTH ENDING OCT 27, 1989
REPORT SUMMARIZED BY RESPONSIBILITY
CONSTRUCTION
GENERAL CONDITION ITEMS**

RESPONSIBILITY CD-DESCRIPTION	CURRENT PERIOD DOLLARS			CUMULATIVE DOLLARS			ESTIMATE TO COMPL	AT COMPLETION DOLLARS		
	BUDGET	ACTUAL	VAR.	BUDGET	ACTUAL	VARIANCE		BUDGET	ESTIMATE	VARIANCE
A RODENT & PEST CONTROL	0	0	0	0	0	0	5,000	5,000	5,000	0
B GUARD SERVICES	6,000	9,344	3,344	24,000	28,830	4,830	48,000	72,000	76,830	4,830
E CLEAN-UP OF FIELD SITES	2,000	2,500	500	8,000	5,720	-2,280	16,000	24,000	21,720	-2,280
G SIGNS AND BARRICADES	0	0	0	0	0	0	10,000	10,000	10,000	0
X CONSTRUCTION PHOTO	4,000	4,346	346	16,000	19,346	3,346	32,000	48,000	51,346	3,346
Y TESTING PROGRAM	52,692	30,017	-22,675	210,767	120,257	-90,510	508,533	632,300	628,790	-3,510
S/T GEN. COND. ITEMS	64,692	46,207	-18,485	258,767	174,153	-84,614	619,533	791,300	793,686	2,386



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

PDCD CM SERVICES - 6TH ANNUAL WORK PLAN COST REPORT FOR MONTH ENDING OCT 27, 1989 REPORT SUMMARIZED BY RESPONSIBILITY CONSTRUCTION

RESPONSIBILITY CD-DESCRIPTION	CURRENT PERIOD DOLLARS BUDGET	ACTUAL	VAR.	CUMULATIVE DOLLARS BUDGET	ACTUAL	VARIANCE	ESTIMATE TO COMPL	AT COMPLETION DOLLARS BUDGET	ESTIMATE	VARIANCE
A PROJECT MANAGEMENT	80,378	82,041	1,663	329,548	330,298	750	652,073	968,491	982,371	13,880
C FAC. CONSTRUCTION	450,333	441,580	-8,753	1,896,547	1,873,524	-23,023	3,480,898	5,113,259	5,354,422	241,163
E SYSTEMWIDE CONST	78,840	76,210	-2,630	323,244	291,060	-32,184	846,277	1,147,194	1,137,337	-9,857
F GENERAL SERVICES	70,514	62,948	-7,566	289,106	271,029	-18,077	430,101	772,363	701,130	-71,233
K PROJECT CONTROLS	213,139	165,745	-47,394	873,871	716,474	-157,397	1,577,010	2,471,628	2,293,484	-178,144
L PROCUREMENT	16,118	14,573	-1,545	86,952	59,093	-27,859	122,763	208,485	181,856	-26,629
M ENG. SVCS./SYST. INTEGR.	154,620	253,360	98,740	610,920	831,986	221,066	1,181,494	1,823,139	2,013,480	190,341
N COMMUNITY RELATIONS	13,770	7,505	-6,265	56,455	39,104	-17,351	84,161	140,616	123,265	-17,351
P SAFETY	16,150	13,622	-2,528	66,217	56,419	-9,798	126,942	193,159	183,361	-9,798
Q QUALITY ASSURANCE	20,221	19,493	-728	101,228	75,926	-25,302	159,501	260,163	235,427	-24,736
R PROJECT ADMIN.	44,547	42,577	-1,970	182,644	177,626	-5,018	364,065	549,161	541,691	-7,470
S EQUAL OPPORTUNITY	13,435	6,457	-6,978	55,084	38,657	-16,427	15,516	83,298	54,173	-29,125
T LABOR RELATIONS	0	0	0	0	0	0	33,713	33,713	33,713	0
U LEGAL	0	0	0	24,000	0	-24,000	40,000	64,000	40,000	-24,000
S/T LABOR-BRDN & OH	1,172,065	1,186,111	14,046	4,895,816	4,761,196	-134,620	9,114,514	13,828,669	13,875,710	47,041
1 FIELD OFFICE EXPENSES	55,300	44,540	-10,760	221,200	179,882	-41,318	465,400	663,600	645,282	-18,318
2 OFFICE EQUIPMENT	3,725	573	-3,152	14,900	6,744	-8,156	29,800	44,700	36,544	-8,156
3 TRAVEL & RELOCATION	18,142	7,257	-10,885	72,567	33,663	-38,904	165,133	217,700	198,796	-18,904
4 VEHICLES & MAINT.	4,900	7,522	2,622	19,600	18,259	-1,341	63,200	82,800	81,459	-1,341
5 REPRODUCTION	6,050	4,624	-1,426	24,200	18,654	-5,546	48,400	72,600	67,054	-5,546
7 TELEPHONE & TELEX	5,950	5,627	-323	23,800	20,961	-2,839	47,600	71,400	68,561	-2,839
B COMPUTER OPERATION SUPPT.	2,292	2,361	69	9,167	10,396	1,229	18,333	27,500	28,729	1,229
9 GROSS RECEIPT TAX	7,834	6,951	-883	31,334	30,151	-1,183	62,666	94,000	92,817	-1,183
A FIELD EQUIPMENT	3,975	7,086	3,111	15,900	13,665	-2,235	31,800	47,700	45,465	-2,235
S/T ODC'S	108,168	86,541	-21,627	432,668	332,375	-100,293	932,332	1,322,000	1,264,707	-57,293
W PDCD FEE	57,500	57,500	0	230,000	230,000	0	345,000	575,000	575,000	0
X S/C FEE	32,084	29,376	-2,708	130,275	107,428	-22,847	248,570	355,998	355,998	0
S/T FEES	89,584	86,876	-2,708	360,275	337,428	-22,847	593,570	930,998	930,998	0
S/T CM DIRECT SVCS	1,369,817	1,355,528	-14,289	5,688,759	5,430,999	-257,760	10,640,416	16,081,667	16,071,415	-10,252
S/T GEN. COND. ITEMS	64,692	46,207	-18,485	258,767	174,153	-84,614	619,533	791,300	793,686	2,386
TOTAL CM SERVICES	1,434,509	1,401,735	-32,774	5,947,526	5,605,152	-342,374	11,259,949	16,872,967	16,865,101	-7,866

PERCENT OF BUDGET EXPENDED = 33%

NEGATIVE VARIANCE INDICATES UNDERRUN

SECTION VI

ADDITIONAL ACTIVITIES

PERFORMED IN OCTOBER





LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

VI. ADDITIONAL ACTIVITIES PERFORMED IN OCTOBER

The following activities performed by the CM functional organization are in addition to the activities presented in other sections of this report.

A. Administration And Accounting

- (1) Continued to assist the Resident Engineers in the supply of administrative material and the assignment/orientation of new field personnel at the field offices.
- (2) Continued processing of personnel (acquisition and termination).
- (3) Coordinated audit responses from Associate Subcontractors to RTD Audit Department.

B. Quality Assurance

- (1) Continued to review welding activities and conduct fabrication inspections as required to support facilities and system procurement contracts A130, A135, A141, A145, A165, and A175.

Site Inspection:

- o A130, A145 - Inspection of welds on starpacks, kneebrace supports, walers and struts during excavation.
- o A145 - Inspection of bulkhead strut welds for tunnel supports and rebar column fabrication.
- o A141 - Evaluation and inspection of welds during strut support modification.
- o A145, A165, A175 - Inspection of welds during installation of permanent structures.
- o A145 - Inspection of welds for deck beams for south blast relief shaft area and escalator entrance.

Shop Inspection:

- o Paramount Metals - Inspection of embedded supports for slurry walls, rails, escalator beam supports, tunnel rings, and heavy frames for permanent structures (A130, A141, A145, A165, A175).
- o Cowelco - Inspection of handrails, stairways and miscellaneous embedded frames for A135 Baggage Handling Facility.
- o Angeles Steel - Inspection and monitoring of stud welding subcontracted from Paramount Metals.
- o Scott Company - Inspection of Wet Standpipe and Hydraulic piping system spool pieces (A135, A145, A165).



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

- (2) Continued to monitor on-site testing and Smith-Emery test laboratory activities.
- (3) Witnessed system pressure tests for A141 Hydraulic Oil Lines.
- (4) Witnessed pressure test for A141 Wet Standpipe spool.
- (5) Witnessed system pressure test for A171 Fire Lanes.
- (6) Monitored Smith-Emery Batch Plant Inspection at Calmat and TMC.
- (7) Witnessed pressure test for A610/115 Fire Lines, Domestic Water and Natural Gas Lines.
- (8) Inspected welded joints on A145 Deluge Lines.
- (9) Monitored Smith-Emery testing of elastomeric pad samples for A171.
- (10) Participated in A112 contract close-out activities.✓
- (11) Participated in Safety Certification Review Team Audit of Contract A112.✓
- (12) Conducted QA review of approximately 142 contractor submittals for various contracts.
- (13) Issued report for audit of Flakt, Inc. and National Metals Inc. for Contracts A740 and A745.
- (14) Supported audit of PDCD/QA Program by Hill International for UMTA.
- (15) Monitored Smith-Emery concrete test reports.
- (16) Inspected installation and monitored testing of HDPE on Contract A135.

C. Equal Opportunity Administration

- (1) Monitored Equal Opportunity reporting requirements (i.e. SSA&P Report, Monthly Employment Utilization Reports, Certified Payroll) for Contract Nos. A112,✓ A130, A135, A141, A145, A146, A165, A167, A171, A610/A115, A612, A615, A616, A620, A640, A710, A740, and A745.
- (2) Conducted project site visits/employee interviews at A141, A145, A146, A165, A171, and A175.
- (3) Processed penalty assessments for the late submittal of the Monthly Employment Utilization Reports for Contracts A112,✓ A130, A135, A141, A145, A165 and A167.

D. Contracts and Procurement

- (1) Issued three Purchase Orders for five Personal Computers and related software upon District approval.
- (2) Issued Subcontract with E. D. Greenawalt for estimating services upon District approval.
- (3) Requested District approval to issue Amendment to consulting agreement with F. E. Endacott & Associates for funds increase to cover remaining AWP-6 work requirements.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

E. Community Relations

- (1) Coordinated community notifications for A130, A141, A145, A146, A165 and A175 tenants affected by lane restrictions and/or street closures.
- (2) Coordinated and resolved traffic mitigation concerns for tenants along Hill St. affected by A141, and A146 traffic access plans, and for tenants in the 7th/Flower area affected by A165 and A146 (under 7th St.) traffic plans.
- (3) Provided assistance to A130, A141, A145, A146 and A165 for problems caused by blocked access, noise, dust, lack of visibility, accidents, security and general construction activities.
- (4) Provided assistance to PDCD/RTD in responding to media requests and coordinating 10 site visits.
- (5) Processed 28 inquiries/complaints.
- (6) Provided assistance to RTD/LGCA in coordination/presentation of the October 25 Community Awareness Meeting for Union Station/Yards & Shops.
- (7) Provided assistance to 7th Street/Metro Center Station tenants regarding rodent control.
- (8) Coordinated and resolved traffic mitigation concerns for tenants adjacent to Lebanon Street affected by A631 traffic access plan.

F. Safety and Security

- (1) Continued to monitor safety, health and security activities on all active construction sites.
- (2) Continued to monitor activities of the Security Guard Service and the Site Clean-up Service subcontractors.
- (3) Continued work on revisions/modifications to specifications on CSSM for Phase II.
- (4) Began video still safety site surveys with DIA'S Director of Safety.
- (5) Reviewed second submission of A631 candidates and approved a Safety Representative.

G. Construction Operations

- (1) Continued construction management (CM) services for Contracts A112, A130, A135, A141, A143, A144, A145/A145A, A146, A165, A167, A171, A175, A610/A115, A612, A615, A616, A620, A630, A640, A710, and A732, A740, A745, A750 (4984, 4986, 4988) and A795; monitoring of Master Agreement Work and submittal reviews.
- (2) Continued coordination of traffic control plans and street closures with city agencies for A130, A141, A145, A146, and A165.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

- (3) Continued coordination of MOS-1 Inspection with LADOT.
- (4) Processed a total of 17 Traffic and Utilities related submittals.
- (5) Continued monitoring of ground water and construction water discharges at A141, A144, A145, A146; A165, A171 and A175.
- (6) Continued monitoring of Discharge Monitoring Stations at Ballona Creek and Los Angeles River.
- (7) Prepared and submitted September Discharge Monitoring Report (DMR) to the California Regional Water Quality Control Board (CRWQCB).
- (8) Prepared and submitted September LA River Dissolved Solids Report to Central and West Basin Water Replenishment District (CWBWRD).
- (9) Prepared and submitted water quality reports for new dewatering flows from A130 and A135 to CRWQB.
- (10) Checked as-built escalator wellways in Home Savings (A167).
- (11) Continued checking contractor's control points and layout at various construction sites.
- (12) Continued monitoring instrumentation, building and ground settlement points on A135, A141, A145, A146, A165, A171, and A175.
- (13) Continued location survey at shop and yards contracts.
- (14) Checked layout and excavation elevation for A135 station.
- (15) Continued walkway as-builts survey for AR and AL tunnels (A171).
- (16) Completed review of high utilities claims (A165).

H. Engineering Services

- (1) Reviewed RTD consultant J.P. Gould's preliminary evaluation of the A141 tunnel hard rock claim.
- (2) Assembled A145 construction/instrumentation data and transmitted to MRTC and RTD consultant J. P. Gould.
- (3) Monitored two test case alternative methods of destressing struts at A141 Civic Center Station.
- (4) Transmitted A141 Contractor's excavation support design calculations to RTD consultant J. P. Gould for to be used in analyzing the Civic Center Station strut overload claim.
- (5) Completed and distributed draft report on A165 Design Verification Study Task B, for use in evaluating the A141 Civic Center Station strut overload claim.
- (6) Completed geologic observations in the A146 AR Tunnel.
- (7) Collected, tabulated and transmitted data to J. P. Gould on the A141 Station excavation history plotted against ground movements and strut load build-ups.
- (8) Processed 14 field inquiries with MRTC to obtain clarification of design requirements.
- (9) Responded to 160 requests for information or documentation clarification from various contractors.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

- (10) Completed final design and claims avoidance review of Contract A760 Signing and Edgelight Procurement.
- (11) Continued claims avoidance review of Contract A157 5th/Hill Station Stage II, final design.
- (12) Continued claims avoidance review of Contract A147 Civic Center Station Stage II, final design.
- (13) Completed comprehensive review of electrical embedments on Contract A145.
- (14) For Contract A112 - Approved 5 Contractor submittals for O & M Training Program, Car Hoist Supports, Water Sealer, Electrical Test Procedures, and Paving Joint Sealant.
Approved-as-Noted 3 Contract submittals for O and M Manuals, Steel Doors, and Instrumentation Booklets.
- (15) For Contract A130 - Approved 16 Contractor submittals for Monthly Narrative & Schedule Updates, Cathodic Protection, Underpinning Concrete Piles, Rebar Details, Traffic Control Plan, Mix Design, Welder Certification, Rebar Mill Certifications and Ground Rod Penetration of HDPE Membrane. Approved-as-noted 11 Contractor submittals for Car Wash System, Mech. Embeds, Lift Drawings, Electrical Embeds, Rebar Details, Welding Procedure and Certification, Wall Form Dwgs. & Calcs., Metal Embeds, Tunnel and Excavation Equipment.
Rejected 13 Contractor submittals for Monthly Schedule Status Reports, Revised Part II Schedule, Car Washing Systems, Plumbing Data and Typical Tunnel Installation.
- (16) For Contract A135 - Approved 3 Contractor submittals for Rebar Mill Certificates.
Approved-as-Noted 22 Contractor submittals for Precast Concrete Walkway, Metal Embeds, Lift Drawings Hydraulic Lines, Refrigeration Piping, Wall Form Dwgs. & Calcs., Shoring Layout & Calcs., Passage Walkway Wood Canopy, Rebar Details, Mill Test Report and Mechanical Sleeve Coupler.
Rejected 7 Contractor submittals for Mechanical Embeds, Lift Dwgs., Wall at Passenger Tunnel and Shoring Layout.
Reviewed for Record Only 1 Contractor submittal for Installation of Inclinator.
- (17) For Contract A135BH (Baggage Handling) - Approved 3 Contractor submittals for Basement Piping, 2" Fireline and 750 KVA Transformer.
- (18) For Contract A141 - Approved 6 Contractor submittals for Pipe Sleeves, Support & Guides, Concrete Lift Dwgs., Controlling Traffic and Mechanical Qualification Test & Welding Procedures.
Approved-as-Noted 17 Contractor submittals for Shoring for Ancillary Level, Concrete Lift Dwgs., Reinforcement, Tunnel & Shaft Groundwater Procedure Plan, Mix Design, Reinforcement Mill Test Report, Catalog Cuts and Magnetometer Probe Hole.
Rejected 3 Contractor submittals for Excavation Support System Bracing Removals, Welding Procedures/Certifications and Lift Dwgs.
Reviewed For Record Only 1 Contractor submittal for Monthly Progress Schedule Update.
- (19) For Contract A145 - Approved 12 Contractor submittals for Welder Certification and Qualification Tests,



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

Concrete Inserts, Construction Joints, Lift Dwgs., Rebar Dwgs., and Electrical Junction Box.

Approved-as-Noted 36 Contractor submittals for Monthly Schedule Update, Lift Dwgs., So. Entrance Bracing, Decking over So. Blast Relief Shaft, Water Main Supports, Rebar Dwgs., Electrical Junction Boxes, Conduit Tagging Method and Non-Skid Coating for Deck Mats.

Rejected 5 Contractor submittals for Stair Nosings, Restrutting Column Lines, Welder's Qualifications and Monthly Reports.

Reviewed for Record Only 5 Contractor submittals for Monthly Progress Status Reports and Revised Schedule.

- (20) For Contract A146 - Approved-as-noted 4 Contractor submittals for Traffic Plan, Catalog Data, Sump Pump Control Data and Monthly Schedule Update and Narrative.

- (21) For Contract A165 - Approved 29 Contractor submittals for Shoring Traveler System, Re-shoring Details, Rebar Dwgs., Lift Dwgs. for Base Slabs, Walls, Platforms, Roof Slabs, and Columns.

Approved-as-Noted 37 Contractor submittals for Calculations, Lift Drawings for Base Slabs, Walls and roof Slabs, and Rebar drawings for Slabs, Walls, Platform, Mezzanine and Exhaust Duct.

Rejected 4 Contractor submittals for Light Fixtures, Wall Lift Drawing and Rebar.

Review for Record Only 1 Contractor submittal for Roosevelt Building Footing Lift Drawing.

- (22) For Contract A167 - Approved 6 Contractor submittals for Hardware Schedule, Engineered Glass Walls, Base, Waterproofing Membrane, Dry Set Mortar, Grout, Quarry Tile, Custom Concrete & Latex Mortar Admix and Type RHH/RHW Wire, Cable & Insulation.

Approved-as-Noted 7 Contractor submittals for Monthly Progress Status Report, NAS Part II Narrative, Precast Moulding, Concrete Mix Design, Hilti Anchoring System, Erection Dwgs., Welded Bracket for Standpipe and HVAC @ Home Savings.

Rejected 8 Contractor submittals for Monthly Schedule Update, Ven-Chem Certification, Granite for Home Savings, Italian Marble Tile, Rolling Grilles & Fire Doors, Hose Rack Angle Valves, HVAC Equipment, and Cable Tray Support Layout.

- (23) For Contract A171 - Approved 2 Contractor submittals for Elasto-Pad and Miscellaneous Metal.

Approved-as-Noted 2 Contractor submittals for Part II Schedule Update and Sump Discharge Piping.

- (24) For Contract A175 - Approved 6 Contractor submittals for Recalculations for Formed Walls, Mix Design, Rebar Drawings, Outlet Boxes and Invert Slab.

Approved-as-Noted 7 Contractor submittals for Pedestrian Crosswalk, Resume and Qualifications, Rebar Dwgs., Cast-In-Place Floating Slab Pans, Walls and Mezzanine Slab, Calcs. for Shoring & Soffit Forms and High Wall Forms.

Rejected 5 Contractor submittals for Monthly Progress Status Report Crosswalk at Westlake, Data Type H Sleeves for Wet Standpipe & Sprinkler Lines, Roofing Shoring, and Detour-Westlake Ave.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

- (25) For Contract A610 - Approved 13 Contractor submittals for CWR Destressing Procedure; YD. Rail Flow Diagram & Mechanical Vibrators, Plumbing Fixtures, Stock Rails #10 Turnouts, Special Plate Details, Stock Rails 21'-0" Switch, Manganese Steel Center Xing, Manganese Steel End Xing, and Rust Proof Compound L.
Approved-as-Noted 2 Contractor submittals for Valves, Ceiling Plates & Pipe Insulation and Closure & Buffer Rails.
Rejected 10 Contractor's submittals for Cathodic Protection Test Station, Gas Fired Domestic Water Heaters, Ventilation Fans, Gas Pressure Regulators, Fire Dept. Valves & Hose Rack Assembly, Roof Drains & Fl./Ceiling Plates, Fl. Drains & Cleanouts, #10 turnout, Details for Electrified T.O., Rail Clamp Assembly.
- (26) For Contract A612 - Approved 1 Contractor submittals for Smoke Emission Optical Density.
- (27) For Contract A615 - Approved 1 Contractor submittal for Qualification Test Results.
- (28) For Contract A616 - Approved 3 Contractor submittals for Production Fastener Test Results.
Approved-as-Noted 1 Contractor submittal for Production Elastomer Test Results.
- (29) For Contract A620 - Approved 15 Contractor submittals for Maintainability Analysis, Maintainability Demonstration Test, Civic Center FDR Corrections, 5th/Hill FDR Corrections, 7th/flower FDR Corrections, Junction Box Installation, Impedance Bond Installation, Wayside Signal Installation, Switch Machine Layout, Exterior Cable, Construction Safety and Security Manual, Factory Inspection Test Procedure,
Approved-as-Noted 3 Contractor submittals for Yard Track and Cable Plans, QA Program and Train Stop Installation.
Rejected 1 Contractor submittal for ATC Vehicle Equipment Qualification Test.
- (30) For Contract A630 - Approved 1 Contractor submittal for Bus Duct.
Approved-as-Noted 1 Contractor submittal for Auxiliary Power Transformer.
- (31) For Contract A631 - Approved 2 Contractor submittals for Electrical Insulated Flooring and Paint Products.
Approved-as-Noted 1 Contractor submittal for DC Control Power Supply.
- (32) For Contract A640 - Approved 1 Contractor submittal for CTS Telephone Subsystem Diagnostic Test Equipment.
Approved-as-Noted 3 Contractor submittals for Radio Frequency Power Documentation, Telephone & Cable Circuit Board, and Telephone Subsystem Special Tools.
- (33) For Contract A710 - Approved 1 Contractor submittal for Monthly Progress Status Report and Schedule Update.
- (34) For Contract A740 - Approved 2 Contractor submittals for Test Report EF/SVF Impeller Spin and Monthly Progress Report and Schedule Update.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

(35) For Contract A745 - Approved 1 Contractor submittal for Monthly Progress Report and Schedule Update.

I. PROJECT CONTROLS

- (1) Processed Change Requests: A112-CR-142, A112-CR-144, A141-CR-126, A141-CR-127, A141-CR-128, A141-CR-129, A141-CR-132, A145-CR-153, A145-CR-155, A146-CR-040, A165-CR-093, A165-CR-097, A167-CR-011, A171-CR-030, A175-CR-060, A175-CR-061, A175-CR-062, A175-CR-075, A175-CR-076, A175-CR-077, A175-CR-078, A175-CR-079, A610-CR-081, A610-CR-083, A610-CR-084, A610-CR-085, A620-CR-029, and A620-CR-030.
- (2) Processed Change Notices: A130-CN-021, A141-CN-075, A146-CN-013, A175-CN-035A, and A610-CN-037.
- (3) Processed Change Orders: A112-CO-040, A112-CO-060, A130-CO-021, A135-CO-0022G, A135-CO-0022H, A135-CO-0022I, A135-CO-0022J, A135-CO-0022K, A135-CO-0022M, A135-CO-031, A145-CO-031A, A145-CO-067A, A145-CO-095, A145-CO-098, A146-CO-021, A146-CO-021Q, A146-CO-021S, A146-CO-021W, A146-CO-021X, A146-CO-021Y, A146-CO-021Z, A146-CO-035A, A165-CO-052B, A165-CO-053, A165-CO-054, A167-CO-002, A167-CO-002A, A167-CO-003, A167-CO-004, A167-CO-005, A175-CO-036, A175-CO-037, A175-CO-045, A175-CO-046, A610-CO-011, A610-CO-056PTI, A610-CO-061, A610-CO-064, A615-CO-002, A620-CO-029, A620-CO-030, A640-CO-005A, A640-CO-007, A640-CO-009, and A755-CO-003.
- (4) Processed through TRACS, 36 executed Change Orders: A130-CO-004B, A130-CO-028, A130-CO-030, A135-CO-031, A146-CO-021N, A146-CO-021Q, A146-CO-021S, A146-CO-030, A165-CO-048, A165-CO-049, A165-CO-050, A165-CO-051, A165-CO-052, A165-CO-052A, A165-CO-052B, A165-CO-053, A610-CO-060, A710-CO-004, A710-CO-007, A112-CO-059, A112-CO-060, A112-CO-062, A112-CO-059A, A135-CO-0022G, A135-CO-0022H, A135-CO-0022J, A135-CO-0022K, A141-CO-059, A146-CO-021T, A146-CO-021U, A146-CO-021V, A146-CO-021W, A146-CO-021X, A146-CO-021Y, A146-CO-021Z, and A175-CO-046.
- (5) Processed Potential Claims: A112-PC-049, A112-PC-070, A130-PC-016, and A610-PC-037.
- (6) Processed Change - Technical Evaluations: A145-CR-142, A145-CR-150, A145-CR-152, and A175-CR-060.
- (7) Processed Force Account Change Packages: A146-CO-021B, A146-CO-021C, A146-CO-021CL, A146-CO-021E, and A146-CO-026.
- (8) Processed Monthly Payment Estimates for 20 Estimates For 20 Contracts: A112, A130, A135, A141, A144, A145, A146, A165, A167, A171, A175, A610/115, A612, A616, A620, A640, A710, A740, A745, and A755.
- (9) Completed a close-out reconciliation on 4 Force Account Change Orders: A146-CO-021B, A146-CO-021C, A146-CO-026, and A146-CO-021E.
- (10) Reviewed Contractor Monthly Progress Reports.
- (11) Prepared Scheduling inputs to RTD Monthly Status Report.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

- (12) Prepared Quarterly Update for the Level III Schedule.
- (13) Approved as noted A167 Part II Schedule submittal.
- (14) Review in progress for A167 Part II Schedule.
- (15) Review in progress for Part II Schedule revisions from A145 and A165.
- (16) A175 Part II Revised Schedule under review.
- (17) Completed review of A130 Part II Schedule.
- (18) A-130-CR-026A Reviewed Contractor's proposal and prepared estimate comparison.
- (19) A-135-CR-004, CR-032 Continued to review changes and proposals related to LAUPT Baggage Handling Facilities and Police Room.
- (20) A-135-CR-047 Reviewed Contractor's proposal, prepared comparison, negotiated settlement for revised work, elevator hydraulic lines.
- (21) A-135-CR-059 Completed estimate for enlarged wall opening, door 7B.
- (22) A-135-CR-051, A141-CR-120, A145-CR-147, A165-CR-083 and A175-CR-051 Completed revised estimates for emergency telephone blockouts.
- (23) A-136 Began review of Stage II Contract documents and MRTC estimate for support in preparation of contract schedule.
- (24) A-141-CR-092 Completed estimate on relocated Emergency Exit Stair No. 21.
- (25) A-141-CR-095 Completed review and estimate on increased escalator wellway openings.
- (26) A-141-CR-097 Reviewed contractors proposal for additional strain gages and monitoring.
- (27) A-141-CR-100 Completed estimate for revisions to Elevator equipment room.
- (28) A-141-CR-104 Began estimate on revisions to water service and corrosion.
- (29) A-141-CR-011 Access delay to Union Station, reviewed Contractor (subcontractors) proposals, prepared estimates and evaluations, participated in negotiations.
- (30) A-145-CR-124 Reviewed contractors proposal for additional costs to negotiated change.
- (31) A-145-CR-132, 133 Prepared preliminary estimate for plumbing and piping changes not included with hydraulic changes.
- (32) A-145-CR-148 Prepared estimate for changes due to added drawing E-145.
- (33) A-146-CR-038 Reviewed scope of work in preparation for walkway and wet standpipe change estimate.
- (34) A-165-CR-075 Clarified scope of work and material takeoff for wet standpipe and sprinkler system change.



LOS ANGELES METRO RED LINE

CONTRACT PERFORMANCE REPORT

PDCD

PERIOD OCTOBER 1989

- (35) A-165 Reviewed decking quantities, prepare comparison and met with contractor.
- (36) A-167-CR-002 Reviewed contractor's proposal for change to structural openings, BRS wall.
- (37) A-175-CR-035 Reviewed contractor's revised proposal for incoming Electrical Service Room.
- (38) A-175-CR-047 Prepared estimate for additional embedded drainlines in crossover.
- (39) A-175-CR-053 Prepared estimate for revisions to plumbing and fire protection systems and structural openings.
- (40) A-175-CR-075, CR-076, CR-077 Prepared ROM estimate for miscellaneous structural changes.
- (41) A-620-CR-030 Prepared ROM estimate for access delay to tunnels.
- (42) A-732 ✓ Began preparation of ROM estimate for installation of wheel press and wheel boring machine.✓
- (43) Systemwide Prepared estimate for tunnel bulkheads at Civic Center and 7th Flower Stations.
- (44) General Reviewed contractors proposed Force Account labor rate submittals.

J. CM Meetings in October 1989

Date	Agency/Company	General Subject
October 2	TSG/Wagner	A141 Strut Removal
October 2	MRTC	A141 Strut Removal
October 2	RTD/S&SA	DOT/IG Audit Plan
October 4	RTD/Southern California Gas	Briefing tour of A165
October 4	RTD/A112/PE✓	Close out Planning✓
October 4	RTD	A141-CR-011 Access delay review, subcontractor proposals and auditor report
October 4	MRTC, BAH, LAPD, RTD Police, LACOSD, RTD, Coroner.	Project Security and Operational Security Requirements.
October 4	MRTC, BAH, LAFD, LACOFD, RTD	System Safety and Operational Requirements
October 5	RTD/MRTC	A141 Strut Removal
October 5	MRTC	A145 Instrumentation Data
October 5	LAUPT	Status summary of hazardous waste encountered on Metro Red Line Sites.
October 5	Contractos, LADWP, Ins. Cos., Ins. Brokers, CM's AGCC	Pending Legislation on Safety, Health and Environmental Issues General Safety.
October 5	PMOC/Hill International	PMOC Audit of PDCD



LOS ANGELES METRO RED LINE

POCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

October 5	RTD/TSG & Subs	A141-CR-011 Access delay reviewed GKN, Valverde, and Felix proposals. Met with RPS (resteel) and Comstock (electrical) for review, to be resubmitted.
October 5	RTD/TSP	A135-CR-047 Hydraulic lines. Negotiated agreed price for revised work.
October 6	TSG	A141 Strut Removal
October 6	MRTC	A130 Shield Design
October 6	RTDD/IG	A141-CR-011 Access delay. Reviewed auditors report on Geofon proposal.
October 9	Roosevelt Building	Security, Construction Activities, Insurance
October 9	RTD/A112/PE✓	Safety Cert. Review ✓
October 11	Substructure Committee	Monthly Utilities Meeting
October 11	RTD	A141-CR-011 Access delay. Reviewed final auditor report on Geofon, RTD position.
October 11	LADOT, Granite	Wilshire Boulevard detour
October 11	RTD/LGCA	Roosevelt Building
October 12	Atkinson	A145 Strut Removal Sequence
October 12	G. List, West Germany Engineer	Tour of A141
October 12	A640/RE/Bechtel	A640 Audits
October 18	MRTC	A141 Strut Removal Alternatives
October 18	MRTC/RTD	A136 Design/Review
October 18	A740/745/RE/Flakt	A740/745 QA Program
October 18	RTD/Granite	A165-CR-070 Negotiations for increased elevator hoistway door rough opening.
October 19	S. Diaz, UMTA	Tour of A165
October 19	RTD/Granite	A165 Decking quantities. Reviewed detailed area by area takeoff and comparison.
October 20	MRTC	A145 Rebar Alternative
October 20	RTD/MRTC	Electrical Junction Boxes



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

October 20	MRTC/RTD	A760 Design Review
October 20	LA City Sanitation Division	Contamination delineation around the Union Station area.
October 23	MRTC	A141 Magnetometer Probe Holes
October 23	PMOC/Hill International	PMOC Audit of PDCD
October 24	RTD/TSG	A141-CR-011 Access delay. Offer made to RPS, Geofon and Comstock to resubmit.
October 25	Geofon, RPS & Comstock RTD	A141-CR-011 Access delay. Review status subcontractor negotiations.
October 25	MRTC	A141 Strut Removal Test Program
October 25	RTD/Public	Community Awareness Meeting for Yards & Shops and Union Station tenants
October 26	RTD/TSG, Comstock & Felix	A141-CR-011 Access delay. Comstock to review materials escalation etc. Review TSG, G & A and profit.
October 27	Shank-Ohbayashi	A146 Geotechnical Instrumentation

SECTION VII

SUMMARY OF ACTIVITIES

PLANNED FOR NOVEMBER



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

VII. SUMMARY OF ACTIVITIES PLANNED FOR NOVEMBER 1989

A. Administration and Accounting

- (1) Continue to provide priority administrative and accounting assistance to construction field operations.
- (2) Continue the recruitment and termination of personnel as required.
- (3) Continue to coordinate RTD's auditing process with Associate Subcontractors.

B. Quality Assurance

- (1) Continue to review welding activities and conduct fabrication inspections as required in support of facilities and systems contracts.
- (2) Continue to monitor on-site testing activities and Smith-Emery laboratory activities.
- (3) Continue to support Factory Acceptance Testing activities in support of systems contracts.
- (4) Continue review of Project Quality Manuals.
- (5) Continue review of contractor submittals.
- (6) Continue audits of systems contracts.
- (7) Continue participation in contract closeout activities for Contract A112.
- (8) Begin preparations for close-out activities for Contract A171.
- (9) Witness off-site pressure testing for Wet Standpipe System components for Contract A146.

C. Equal Opportunity Administration

- (1) Conduct contract compliance site visits, employee interviews and monitor reporting requirements for Contract Nos. A112, A130, A135, A141, A145, A146, A165, A167, A171, A175, A610/115, A612, A615, A616, A620, A640, A710, A740 and A745.
- (2) Evaluate Contractor EO performance with respect to approved specifications and apply penalty assessments as required.

D. Contracts and Procurements

- (1) Issue Requests for Quotations for estimated annual requirements for office supplies and paper products.



LOS ANGELES METRO RED LINE

CONTRACT PERFORMANCE REPORT

PDCD

PERIOD OCTOBER 1989

- (2) Upon receipt of District approval, issue Amendment to Consulting Agreement with F. E. Endacott & Associates for an increase in AWP-6 funding.

E. Community Relations

- (1) Continue tenant notifications on traffic access issues for A141, A145, A146, A165 and A175.
- (2) Continue expanded communication activities with A130, A145, A146, A165 and A175 tenants regarding ongoing and pending construction activities.
- (3) Assist RTD/Local Government and Community Affairs in planning and executing community outreach to Building Managers in the downtown area, including extending promotional activities for the Project Streetwise Hotline and the Information Centers.
- (4) Continue implementing CR Work Plan; conduct community presentations; the dissemination of construction information; and responding to complaints and inquiries.
- (5) Assist RTD/LGCA in coordinating noon hour construction briefings for the community.
- (6) Coordinate traffic access plans for the Holiday Season with LADOT and the Traffic Management Department.
- (7) Update CR tenant mailing list, emergency contact information and CR merchant files.
- (8) Continue to assist PDCD/RTD with site visits and media requests.

F. Safety and Security

- (1) Performed daily site safety, health and security surveillance and prepared written reports for the A112, A130, A135, A141, A145, A146, A165, A167, A175 and A610/A115 construction contracts.
- (2) Coordinated activities of the Systemwide Security Guard Service and the Systemwide Clean-up Service subcontractors.
- (3) Revise and Distribute the Emergency Response Plan.
- (4) Continue video still safety surveys with DIA Director of Safety.

G. Construction Operations

- (1) Continue construction management (CM) services at Contracts A112, A130, A135, A141, A143, A144, A145/A145A, A146, A165, A167, A171, A175, A610/A115, A612, A615, A616, A620, A630, A640, A710, A732, A740, A745, A750 (4984, 4986, 4988) and A795; monitoring of Master Agreement work and submittal reviews.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

- (2) Continue coordination with governmental agencies and MOS-1 inspection with LADOT.
- (3) Continue to process submittals and Master Agreement invoices on as-needed basis.
- (4) Continue monitoring of groundwater and construction water discharges at A130, A135, A141, A144, A145, A146, A165, A171 and A175.
- (5) Continue monitoring Discharge Monitoring Stations at Ballona Creek and Los Angeles River.
- (6) Prepare and submit October Discharge Monitoring Report (DMR) to the California Regional Water Quality Control Board (CRWQCB).
- (7) Prepare and submit October Discharge Monitoring Report (DMR) to the California Regional Water Quality Control Board (CRWQCB).
- (8) Continue to monitor instrumentation, building and ground settlement marks, and various contracts.
- (9) Continue to check Contractor's control points and layout.
- (10) Continue to perform survey tasks as requested by REs.
- (11) Continue to perform as-built survey of tunnels for Contracts A141 and A146.
- (12) Continue location surveys in shop and yards contracts.
- (13) Continue to check slab pours for Contracts A141, A145, A165 and A175.
- (14) Continue control survey through AR and AL's Tunnels (A171).

H. Engineering Services

- (1) Continue inspecting instrumentation and analyzing data in Contracts A130, A135, A141, A145, A146, A165 and A175.
- (2) Update report on A145 geology and instrumentation for the A141 Design Criteria Verification Study, Task B.
- (3) Review RTD Consultant, J. P. Gould's preliminary report on A141 Station strut overload claim.
- (4) Continue to process Contractor's submittals for Contracts A112, A130, A135, A135BH, A141, A145, A146, A165, A167, A171, A175, A610/A115, A612 A615, A616, A620, A630, A631, A640, A710, A732, A740, A745, A750, and A795.
- (5) Continue production of A161 as-built drawings.
- * (6) Complete claims avoidance reviews for Contract A147, Civic Center Station, Stage II and Contract A157, 5th/Hill Station Stage II.

* See Page 42.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

I. Project Controls

- (1) Process Monthly Payment Estimates for all active contracts.
- (2) Process through TRACS all the executed Change Orders.
- (3) Continue close-out reconciliations for Force Account Change Orders.
- (4) Review Contractor Monthly Progress Reports.
- (5) Prepare Scheduling inputs to RTD Monthly Progress Report.
- (6) Complete reviews of Part II Schedule revisions for A165 and A145.
- (7) Review initial A631 Part II Schedule Submittal.
- (8) Complete review of Part II A167 Schedule.



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

DESIGN PACKAGE STATUS WINDOW REPORT - NEXT 30 DAYS 10-28-89 TO 11-24-89

Contract #	Description	Pkg Type	Review Code	Schedule Receipt	Received	Schedule Complete	Actual Complete	SC	Remarks
A-147	CIVIC CENTER STATION (STAGE II)	DWGS	CAR	08-16-89	08-17-89	11-10-89			*RESCHEDULED TO 11-10-89 BY PDCD
A-147	CIVIC CENTER STATION (STAGE II)	SPEC	CAR	08-16-89	08-30-89	11-10-89			*RESCHEDULED TO 11-10-89 BY PDCD
**									
A-157	5TH/HILL STATION (STAGE II)	DWGS	CAR	08-14-89	08-16-89	11-03-89			*RESCHEDULED TO 11-3-89 BY PDCD
A-157	5TH/HILL STATION (STAGE II)	SPEC	CAR	08-14-89	08-22-89	11-03-89			*RESCHEDULED TO 11-3-89 BY PDCD

**

4 records listed. 4 values listed .

Review Codes : LT60 - Less than 60%
PF90 - Prefinal 90%
CAR- Claims Avoidance Review

IP60 - In progress 60%
FS100 - Final submittal 100%
CE - Check Estimate

PF85 - Prefinal 85%
DC100 - Final design complete 100%

NOTE : Based on 10-3-89, MRTC Design Review Schedule

700 2000



SECTION VIII
SUBCONTRACTOR/CONSULTANT
STATUS

MTA LIBRARY





LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

VIII. SUBCONTRACTOR/CONSULTANT STATUS

The following 6th AWP Subcontract Status Report provides a current status of subcontracts awarded to the twelve associate and four consultant subcontractors. The Report shows major milestones for each subcontractor action from receipt of the requisition, execution of the document and includes an abbreviated description of the subcontract amendment issued.

SIXTH ANNUAL WORK PLAN SUBCONTRACT STATUS REPORT

OCTOBER 27, 1989

SUBCONTRACT NUMBER	SUBCONTRACTOR	REQUI- SITION	REQ FOR PROPOSAL	NEGOTIATION COMPLETE	JV APPROVAL	DATE TO SC	RETURNED FROM SC	CONSENT REQUESTED	CONSENT RECEIVED	NTE AMOUNT	DATE EXECUTED	REMARKS
1-SC-3369-1	BETTER PERSONNEL EMPLOYMENT SERVICES											
	AMEND. NO. 12	08/07/89	04/12/89	06/13/89	07/20/89	06/16/89	06/16/89	06/21/89	07/27/89	\$415,724	07/27/89	SIXTH AWP
2-SC-3369-1	CONSTRUCTION CONTROL SERVICES CORP.											
	AMEND. NO. 13	08/07/89	04/12/89	06/14/89	07/20/89	06/22/89	06/27/89	06/28/89	07/27/89	\$1,569,347	07/27/89	SIXTH AWP
3-SC-3369-1	DAMES & MOORE											
	AMEND. NO. 11	08/07/89	04/12/89	06/12/89	07/20/89	06/22/89	06/26/89	06/26/89	07/27/89	\$138,215	07/27/89	SIXTH AWP
4-SC-3369-1	ENGINEERING-SCIENCE											
	AMEND. NO. 12	08/07/89	04/12/89	06/12/89	07/20/89	06/22/89	06/27/89	06/28/89	07/27/89	\$214,364	07/27/89	SIXTH AWP
6-SC-3369-1	JACOBS ASSOCIATES											
	AMEND. NO. 14	08/07/89	04/12/89	06/09/89	07/20/89	06/23/89	06/27/89	06/28/89	07/27/89	\$856,565	07/27/89	SIXTH AWP
7-SC-3369-1	JENKINS, GALES & MARTINEZ, INC.											
	AMEND. NO. 14	08/07/89	04/12/89	06/12/89	07/20/89	06/26/89	06/26/89	06/26/89	07/27/89	\$656,763	07/27/89	SIXTH AWP
8-SC-3369-1	MARTIN & HUANG INTERNATIONAL											
	AMEND. NO. 13	08/07/89	04/12/89	06/30/89	07/20/89	06/30/89	07/06/89	07/10/89	07/27/89	\$388,110	07/27/89	SIXTH AWP



LOS ANGELES METRO RED LINE

CONTRACT PERFORMANCE REPORT

PDCDPERIOD OCTOBER 1989**SIXTH ANNUAL WORK PLAN SUBCONTRACT STATUS REPORT (Cont'd)**

OCTOBER 27, 1989

SUBCONTRACT NUMBER	SUBCONTRACTOR	REQUI- SITION	REQ FOR PROPOSAL	NEGOTIATION COMPLETE	JV APPROVAL	DATE TO SC	RETURNED FROM SC	CONSENT REQUESTED	CONSENT RECEIVED	NTF AMOUNT	DATE EXECUTED	REMARKS
9-SC-3369-1	NORTH PACIFIC CONSTRUCTION MANAGEMENT											
	AMEND. NO. 14	08/07/89	04/12/89	06/13/89	07/20/89	06/23/89	06/27/89	06/28/89	07/27/89	\$248,172	07/27/89	SIXTH AWP
10-SC-3369-1	OCHOA & SILLAS											
	AMEND. NO. 8	08/07/89	N/A	N/A	N/A	06/23/89	06/23/89	06/27/89	09/06/89	\$64,000	09/06/89	SIXTH AWP
11-SC-3369-1	RANDOLPH & TATE ASSOCIATES											
	AMEND. NO. 8	08/07/89	04/12/89	06/15/89	N/A	06/30/89	07/24/89	07/24/89	08/04/89	\$20,000	08/08/89	SIXTH AWP
15-SC-3369-1	MUESER RUTLEDGE CONSULTING ENGINEERS (JAMES GOULD, Ph.D)											
	AMEND. NO. 7	08/07/89	N/A	07/14/89	N/A	07/17/89	07/28/89	07/28/89	09/18/89	\$10,000	09/20/89	SIXTH AWP
18-SC-3369-1	GEO GRAY/ PHOTOGRAPHY											
	AMEND. NO. 5	09/08/89	N/A	06/21/89	N/A	08/31/89	09/06/89	07/20/89	09/06/89	\$48,000	09/06/89	SIXTH AWP
21-SC-3369-1	SMITH EMERY CO.											
	AMEND. NO. 6	09/08/89	N/A	N/A	07/20/89	08/31/89	09/22/89	07/19/89	09/22/89	\$632,300	09/22/89	SIXTH AWP
22-SC-3369-1	COLEMAN SECURITY SERVICES INC.											
	AMEND. NO. 4	07/12/89	N/A	07/14/89	N/A	08/08/89	08/31/89	07/14/89	08/04/89	\$72,000	08/31/89	SIXTH AWP
	AMEND. NO. 5	08/25/89	N/A	09/13/89	N/A	09/22/89	09/27/89	N/A	N/A	\$76,000	09/27/89	ADDED SERVICES
29-SC-3369-1	SUBWAY TERMINAL BLDG (A145/146 SITE OFFICE LEASE)											
	AMEND. NO. 2	N/A	N/A	N/A	N/A	06/30/89	06/30/89	05/25/89	05/30/89	\$58,000	06/30/89	1 YR EXTEN



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

SIXTH ANNUAL WORK PLAN SUBCONTRACT STATUS REPORT (Cont'd)

OCTOBER 27, 1989

SUBCONTRACT NUMBER	SUBCONTRACTOR	REQU- SITION	REQ FOR PROPOSAL	NEGOTIATION COMPLETE	JV APPROVAL	DATE TO SC	RETURNED FROM SC	CONSENT REQUESTED	CONSENT RECEIVED	NTE AMOUNT	DATE EXECUTED	REMARKS
35-SC-3369-1	MARY & SON MAINTENANCE (SITE CLEAN-UP)											
	AMEND. NO. 1	09/08/89	N/A	N/A	N/A	08/08/89	08/18/89	07/14/89	08/04/89	\$24,000	08/18/89	SIXTH AWP
37-SC-3369-1	KAL KRISHNAN											
	AMEND. NO. 2	08/07/89	N/A	N/A	N/A	07/14/89	07/19/89	07/19/89	08/04/89	\$93,279	08/08/89	SIXTH AWP
39-SC-3369-1	D'LEON CONSULTING ENGINEERS CO.											
	AMEND. NO. 1	08/07/89	N/A	N/A	07/20/89	07/20/89	07/20/89	07/21/89	09/06/89	\$170,554	06/09/89	SIXTH AWP
40-SC-3369-1	TRANSMETRICS											
	AMEND. NO. 1	08/07/89	N/A	N/A	N/A	07/25/89	07/25/89	07/27/89	09/06/89	\$74,591	06/09/89	SIXTH AWP
41-SC-3369-1	W. B. EVANS & ASSOCIATES (CONSULTING AGREEMENT)	06/27/89	N/A	N/A	N/A	09/07/89	09/14/89	06/27/89	09/06/89	\$13,500	08/22/89	
	AMEND. NO. 1	08/21/89	N/A	08/24/89	N/A	09/07/89	09/14/89	08/24/89		\$40,750		FUNDS INCREASE
42-SC-6669-1	MANPOWER	07/11/89	06/09/89	06/30/89	N/A	08/08/89	08/17/89	07/07/89	08/04/89	\$92,000	08/17/89	SIXTH AWP
43-SC-3369-1	F. E. ENDACOTT & ASSOCIATES (CONSULTING AGREEMENT)	07/07/89	N/A	N/A	N/A	07/18/89	08/07/89	08/07/89	09/18/89	\$7,500	09/20/89	SIXTH AWP
	AMEND. NO. 1		N/A	N/A	N/A			10/26/89		\$18,500		FUNDS INCREASE
44-SC-3369-1	E. D. GREENAWALT (CONSULTING AGREEMENT)	09/19/89	N/A	N/A	N/A	10/03/89	10/03/89	10/03/89	10/24/89	\$18,000	10/26/89	



SECTION IX

CONSTRUCTION PROGRESS

PHOTOS






LOS ANGELES METRO RED LINE

CONTRACT PERFORMANCE REPORT


PDCD

PERIOD OCTOBER 1989


MAIN SHOP BUILDING CONTRACT A112

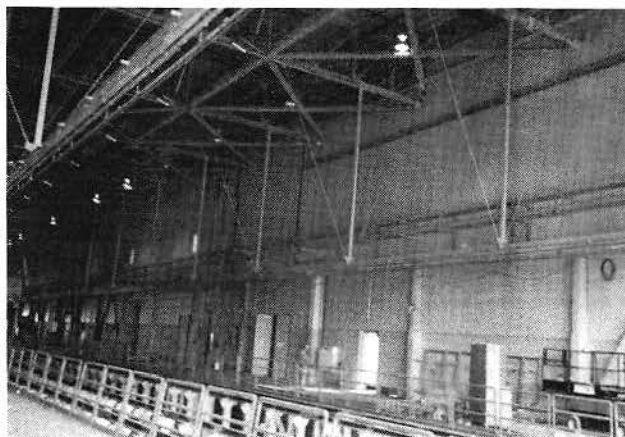


INTERIOR PANELING & HANDRAIL COMPLETE
IN THE S & I AREA

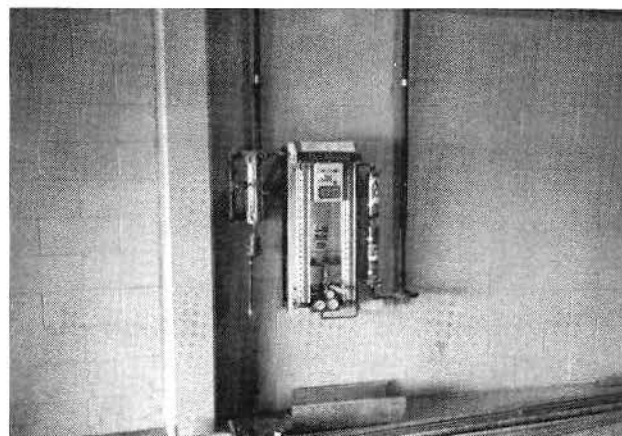

BREATHING AIR STATION INSTALLED
IN BLOWDOWN FACILITY

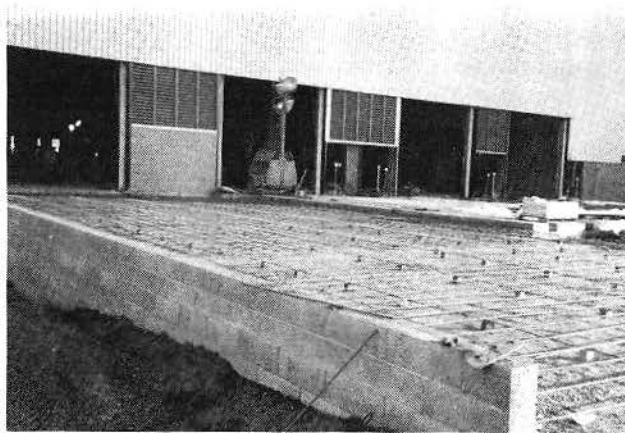

RETAINING WALL, APRON & TRACK FOUNDATION IN
PROCESS, AT THE SOUTH END OF THE MAIN REPAIR AREA

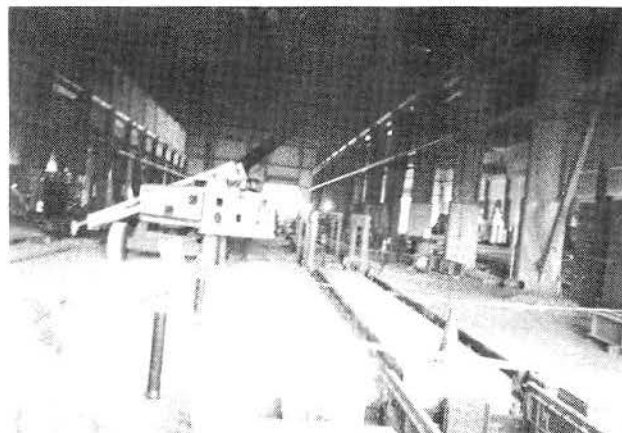

MAIN REPAIR AREA, WITH CAR HOISTS BEING INSTALLED

Parsons-Dillingham-De Leuw, Cather

MTA LIBRARY




LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989


MAIN SHOP BUILDING CONTRACT A112 (Cont'd)✓

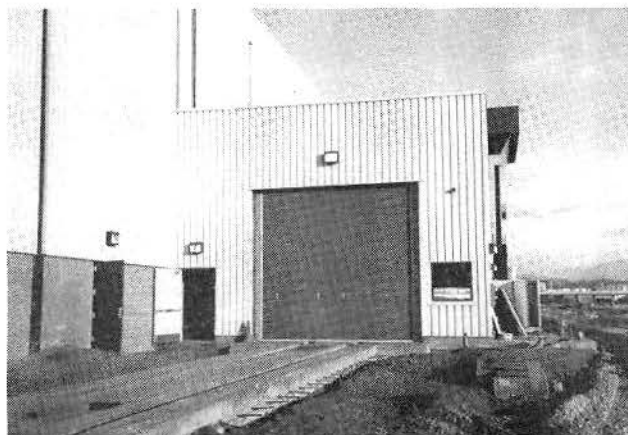

**SOUTH END OF BLOWDOWN FACILITY, WITH
TELESCOPING DOOR & RAIL FOUNDATION IN PLACE**



COMPLETED BLOWDOWN FACILITY

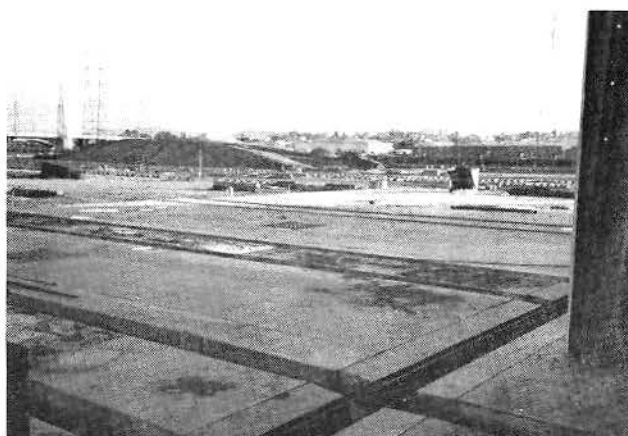

**COMPLETED RAIL FOUNDATIONS & APRON AT
THE NORTH END OF THE MAIN REPAIR AREA**



**REBAR PLACED FOR APRON AT SOUTH END
OF MAIN REPAIR AREA**

Parsons-Dillingham-De Leuw, Cather




LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

YARD LEADS & TRANSFER ZONE CONTRACT A130

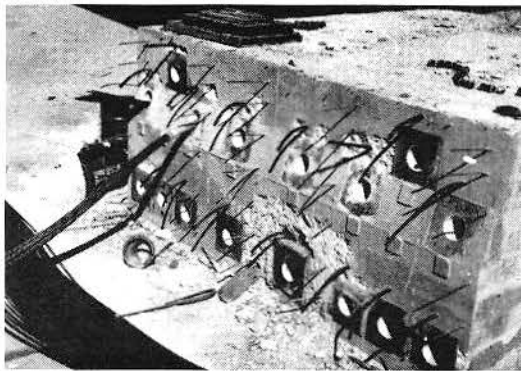


DUCTS IN TRANSFER BEAM FOR
POST TENSIONING



SEISMIC BRACE BEING INSTALLED ON
TRANSFER BEAM



EXISTING BENT SUPPORT BEING REMOVED
FROM TRANSFER BEAM

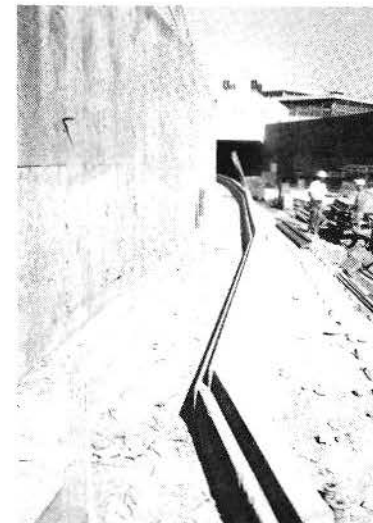

CABLE TRENCH AND ELEVATED
WALKWAY IN "U" WALL AREA




LOS ANGELES METRO RED LINE

CONTRACT PERFORMANCE REPORT


PDCD

PERIOD OCTOBER 1989

UNION STATION CONTRACT A135

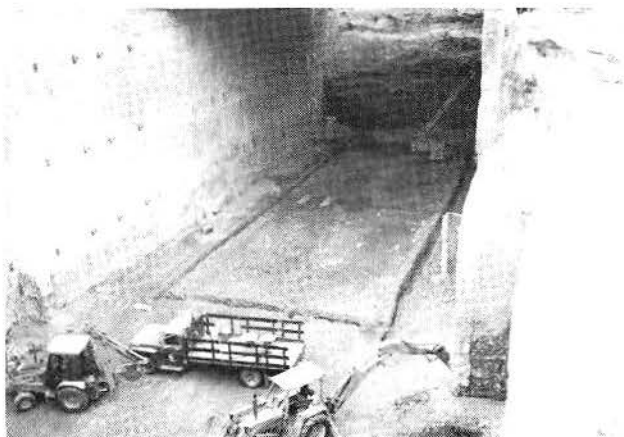


INVERT PREPARED FOR INSTALLATION OF GROUNDING
GRID AND THE SLURRY WALL BEING PREPARED FOR
HDPE, LOOKING SOUTHWEST FROM STA 102+00

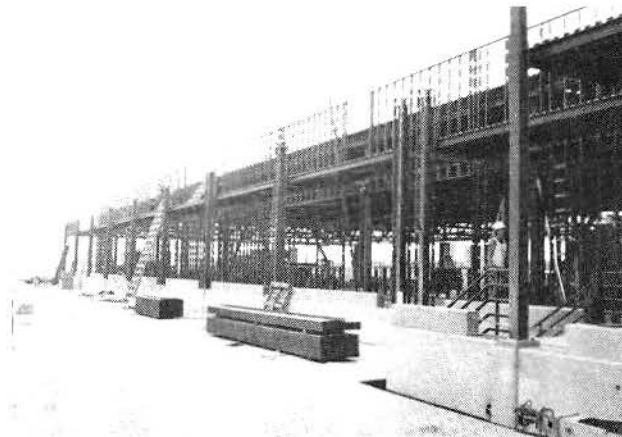

LOOKING AT THE NEW BAGGAGE HANDLING
FACILITY AT TRACK LEVEL, VIEW FROM
N.E. CORNER LOOKING SOUTH



HDPE BEING ROLLED ALONG THE FACE OF THE
NORTH SLURRY WALL, VIEW FACING NORTH WALL

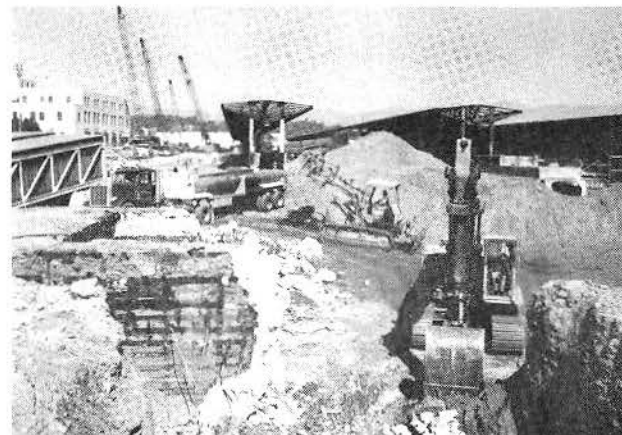

DEMOLITION OF THE MAIN PASSENGER TUNNEL,
LOOKING NORTH FROM PLATFORM #3

Parsons-Dillingham-De Leuw, Cather



LOS ANGELES METRO RED LINE

CONTRACT PERFORMANCE REPORT


PDCD

PERIOD OCTOBER 1989


CIVIC CENTER STATION AND TUNNEL CONTRACT A141



REAPPLYING NON-SKID COATING TO DECKING
AT INTERSECTION OF FIRST & HILL STREETS

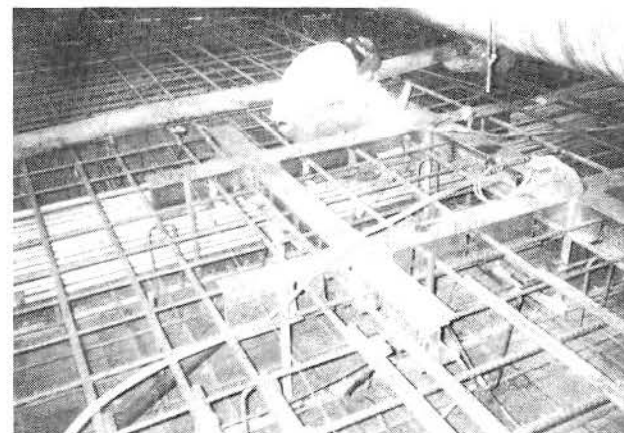

INSTALLING TRANSFORMER SUPPORT BASE IN
ANCILLARY DECK PRIOR TO CONCRETING

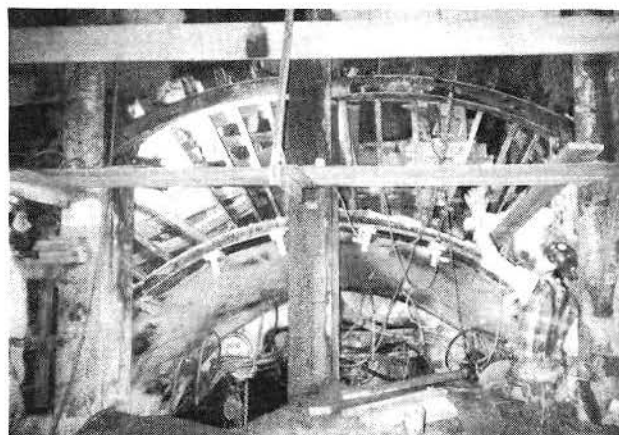

INSTALLING CROWN BARS AT AR TUNNEL PORTAL
AT 5TH/HILL STATION PRIOR TO REMOVAL OF
TUNNEL SHIELD HEAD THRU 5TH/HILL STATION



LOS ANGELES METRO RED LINE

CONTRACT PERFORMANCE REPORT

PDCD

PERIOD OCTOBER 1989

CIVIC CENTER STATION AND TUNNEL CONTRACT A141 (Cont'd)



CROSS PASSAGE #4 AFTER COMPLETING
60% OF EXCAVATION FROM AR SIDE



CUTTING "C" LEVEL WALER DURING TESTING
OF STRUT REMOVAL PROCEDURE




LOS ANGELES METRO RED LINE

CONTRACT PERFORMANCE REPORT


PD CD

PERIOD OCTOBER 1989


CIVIC CENTER STATION AND TUNNEL CONTRACT A141

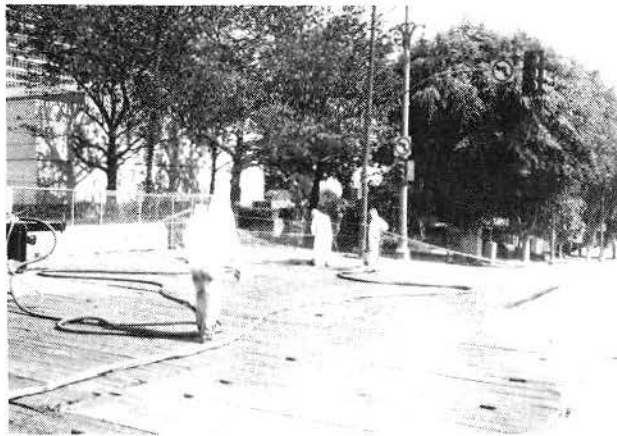

REAPPLYING NON-SKID COATING TO DECKING
AT INTERSECTION OF FIRST & HILL STREETS

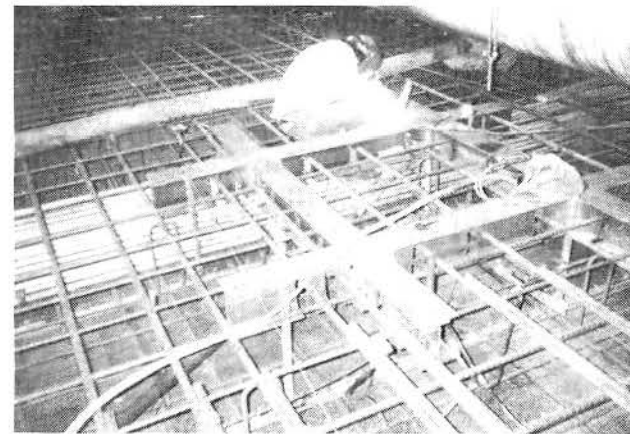

INSTALLING TRANSFORMER SUPPORT BASE IN
ANCILLARY DECK PRIOR TO CONCRETING

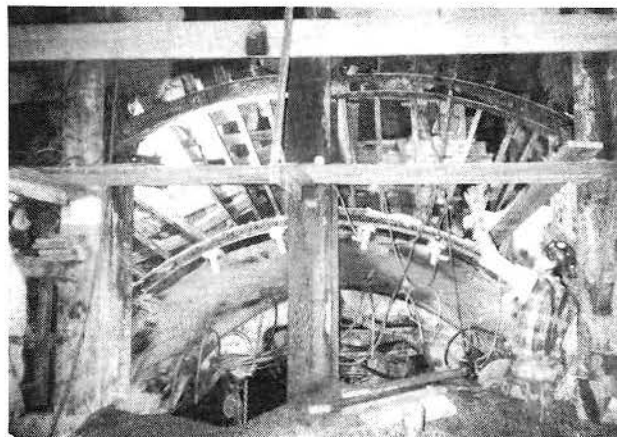

INSTALLING CROWN BARS AT AR TUNNEL PORTAL
AT 5TH/HILL STATION PRIOR TO REMOVAL OF
TUNNEL SHIELD HEAD THRU 5TH/HILL STATION




LOS ANGELES METRO RED LINE

CONTRACT PERFORMANCE REPORT

PDCD

PERIOD OCTOBER 1989

CIVIC CENTER STATION AND TUNNEL CONTRACT A141 (Cont'd)

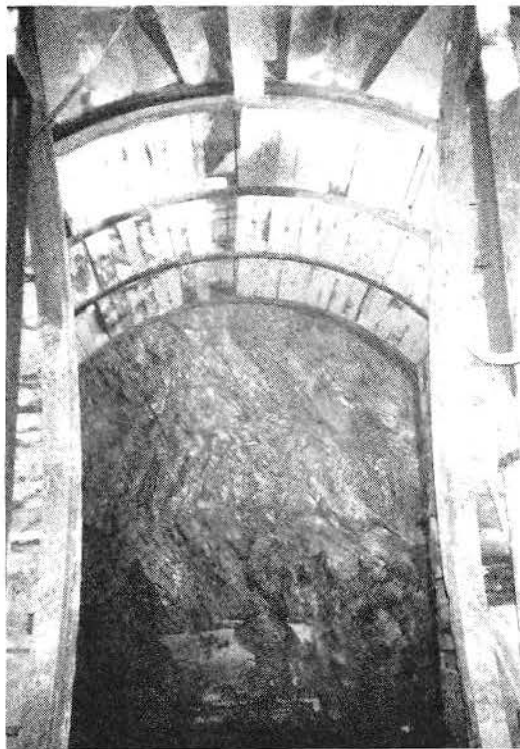

CROSS PASSAGE #4 AFTER COMPLETING
60% OF EXCAVATION FROM AR SIDE



CUTTING "C" LEVEL WALER DURING TESTING
OF STRUT REMOVAL PROCEDURE

Parsons-Dillingham-De Leuw, Cather



LOS ANGELES METRO RED LINE

PDCD

CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989


5TH/HILL UTILITY RELOCATION AND 5TH/HILL STATION STAGE I CONTRACT A145/A145A




POURED STATION'S COLUMNS INVERT 13



SOUTHEAST ENTRANCE EXCAVATION.
EXCAVATION SUPPORT SYSTEM INSTALLATION

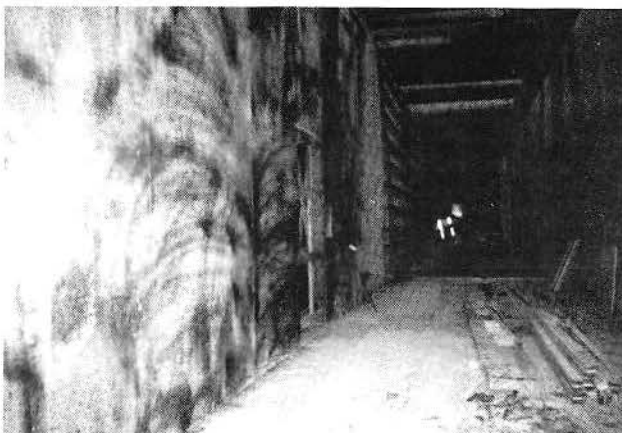

STATION'S INTERIOR AND EXTERIOR WALLS,
INVERT 14

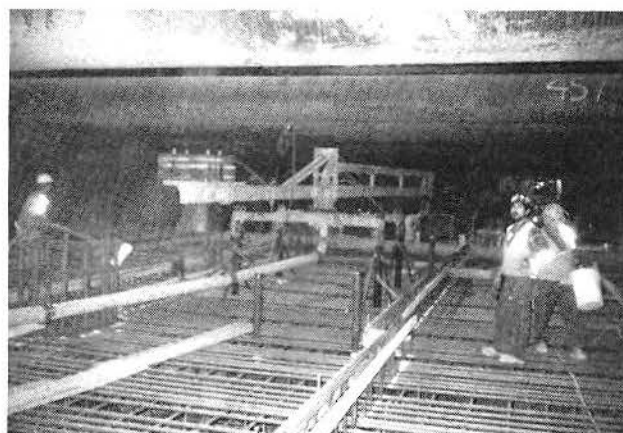

PREPARATION FOR INVERT 4 CONCRETE POUR




LOS ANGELES METRO RED LINE

PDCD


CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989


TUNNELS FROM 5TH/HILL TO 7TH/FLOWER CONTRACT A146

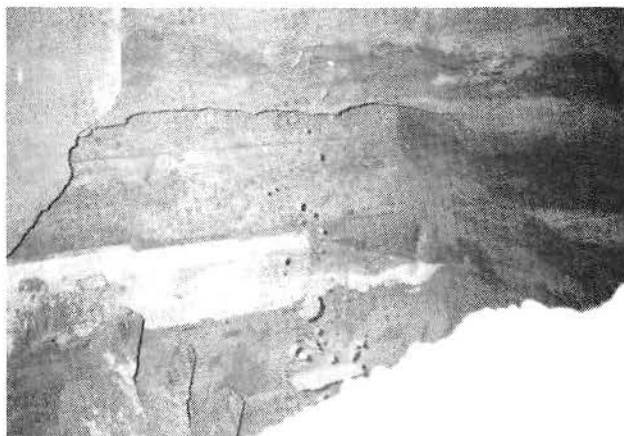

SHOWS TIMBER LAGGING OF A165 EAST WALL
AS IT WAS ENCOUNTERED IN A146 AR TUNNEL.
EXCAVATOR BUCKET SHOWN IN LOWER LEFT

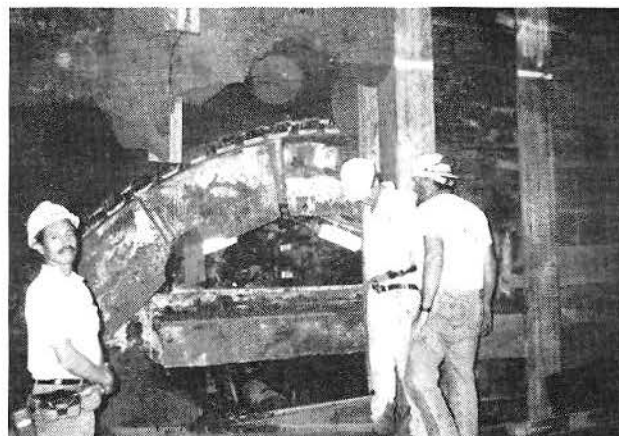

VIEW OF FRONT END OF TUNNELING MACHINE
FROM THE EAST WALL OF A165 STATION

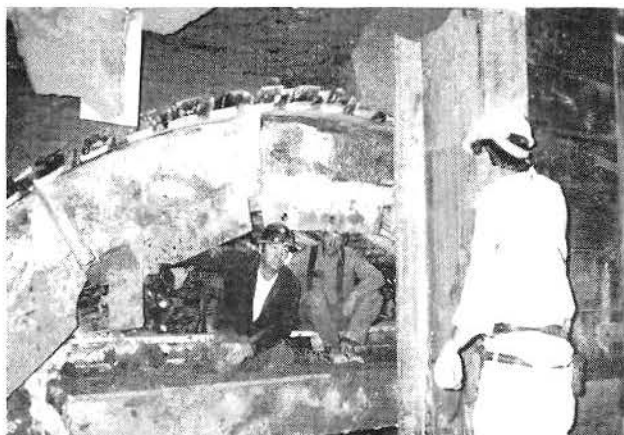

SHOWS WORKMEN CLIMBING INTO A165 STATION
FROM AR TUNNEL BREAK THROUGH ON 10/25/89



WORKMEN REMOVING SOLDIER PILES AND LAGGING AT
BREAK THROUGH INTO EAST WALL OF A165 STATION

Parsons-Dillingham-De Leuw, Cather




LOS ANGELES METRO RED LINE

PDCD


CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989


7TH/FLOWER STATION STAGE I CONTRACT A165

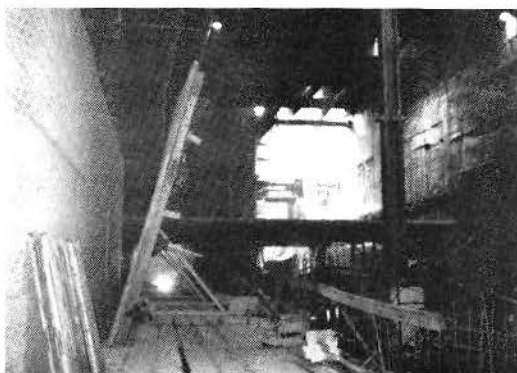


RED LINE TRACK LEVEL, FACING WEST

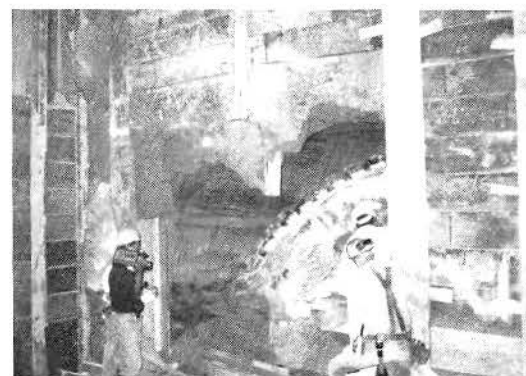

EXPOSING AR TUNNEL AT EAST BULKHEAD

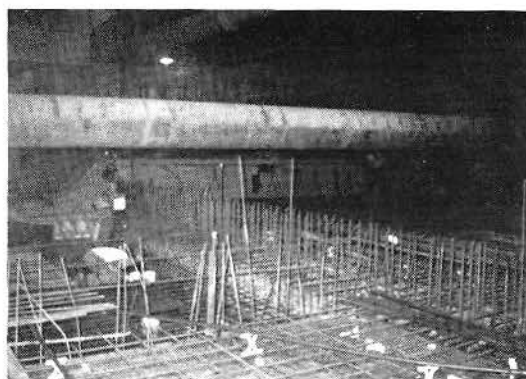

INSTALLING REBAR & EMBEDS FOR BLUE
LINE ROOF SLAB, NORTH OF FLOWER ST.

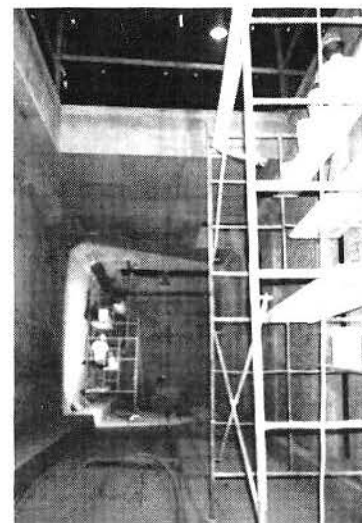

BLUE LINE TRACK LEVEL,
NORTH OF FLOWER ST.,
MEZZANINE LEVEL ABOVE

Parsons-Dillingham-De Leuw, Cather




LOS ANGELES METRO RED LINE

CONTRACT PERFORMANCE REPORT


PDCD

PERIOD OCTOBER 1989


7TH/FLOWER STATION STAGE II CONTRACT A167

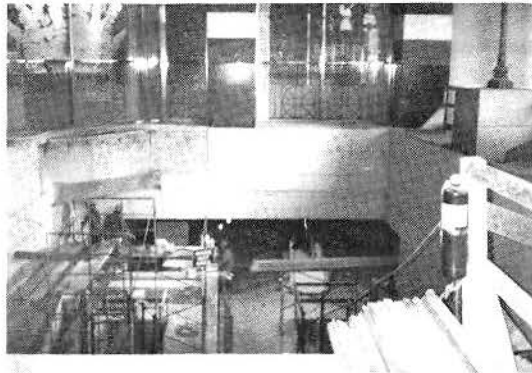

GRANITE CLADDING INSTALLATION, MRT WEST
ENTRANCE AT THE HOME SAVINGS BLDG.

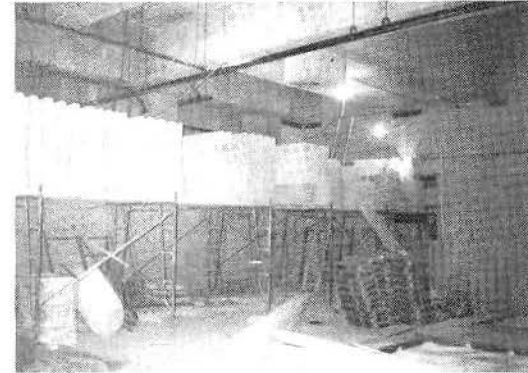

C.M.U. BLOCK AND SCAFFOLDING -
PREPARATION FOR INSTALLATION OF
CONCRETE MASONRY UNIT WALL -
FAN ROOM #61 - RTD SPACE
AT HOME SAVINGS BLDG.

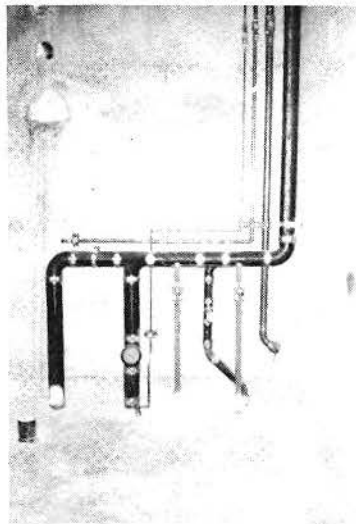

PLUMBING LINES - TOILET
ROOM #35 - RTD SPACE AT
THE HOME SAVINGS BLDG.



INSTALLATION OF CABLE TRAY SUPPORT,
CORRIDOR #62 - RTD SPACE AT
THE HOME SAVINGS BLDG.

Parsons-Dillingham-De Leuw, Cather




LOS ANGELES METRO RED LINE

PDCD


CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

LINE SECTION - 7TH/FLOWER TO WILSHIRE/ALVARADO CONTRACT A171

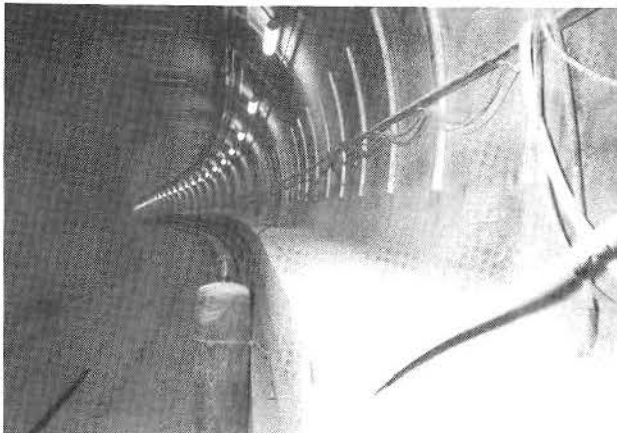

INSTALLATION COMPLETED FOR LIGHTING
AND WALKWAY IN THE AL TUNNEL

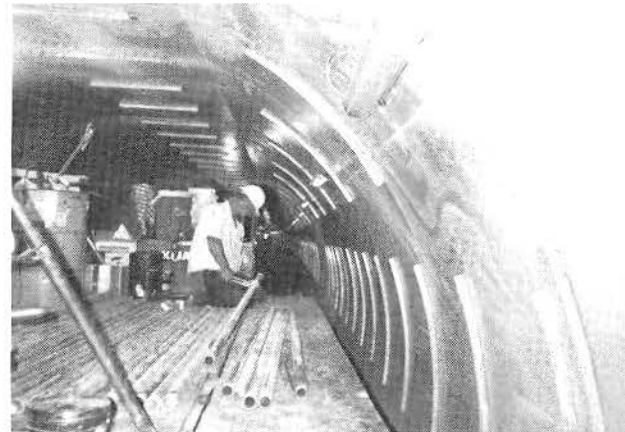

INSTALLATION OF CONDUITS IN AR TUNNEL



FABRICATION/INSTALLATION OF SUMP
DISCHARGE PIPING



WET STAND PIPE SUPPLY LINE IN
CROSSPASSAGE 12




LOS ANGELES METRO RED LINE

CONTRACT PERFORMANCE REPORT



PDCD

PERIOD OCTOBER 1989


WILSHIRE/ALVARADO STATION - STAGE I CONTRACT A175

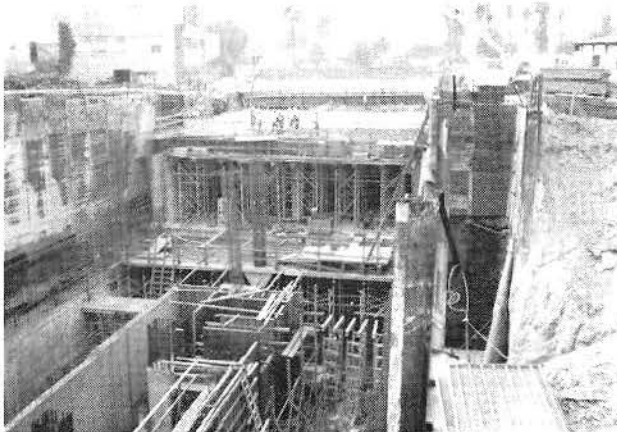

PLACEMENT OF CONCRETE FOR FIRST ROOF SLAB 10/13/89,
EAST OF WESTLAKE AVE.

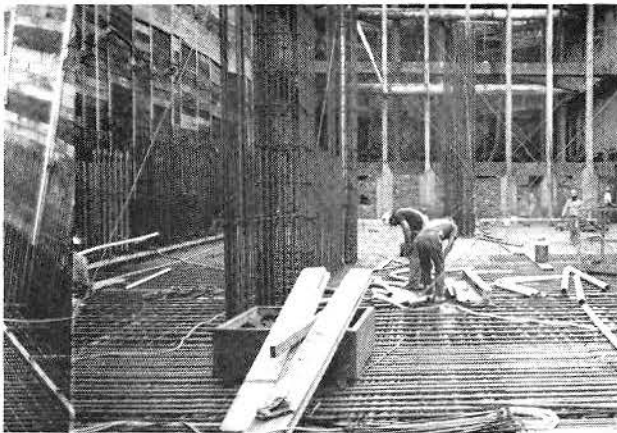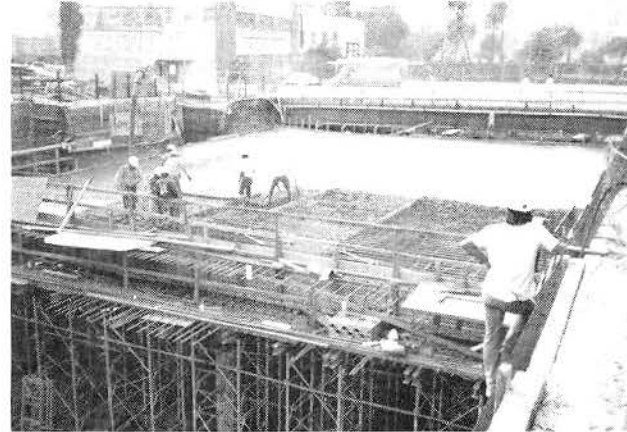

PLACEMENT OF RESTEEL AND EMBEDDED ITEMS
FOR BASE SLAB, AT THE A171/A175 SHAFT
INTERFACE, BLOCKS 12 & 13

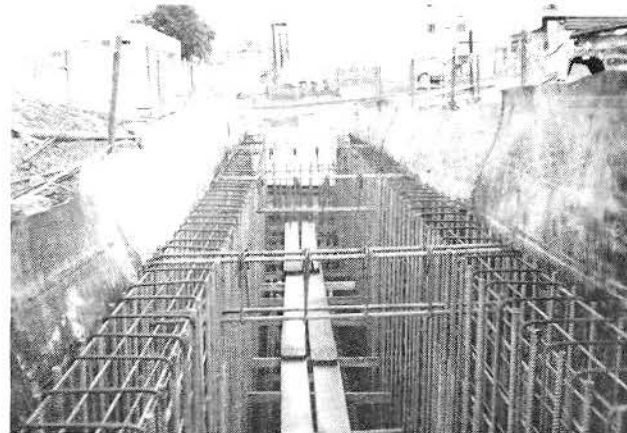

RESTEEL INSTALLATION FOR FRESH AIR INTAKE,
EAST OF WESTLAKE AVE.

Parsons-Dillingham-De Leuw, Cather




LOS ANGELES METRO RED LINE

CONTRACT PERFORMANCE REPORT

PDCD

PERIOD OCTOBER 1989


TRACKWORK INSTALLATION/YARD STORAGE AREA CONTRACT A610/A115

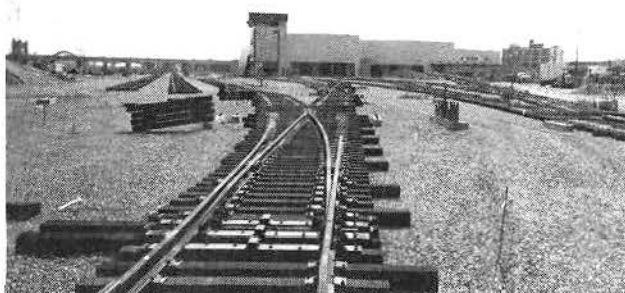


ASSEMBLING PRE-FABRICATED YARD ELECTRIFIED
TURNOUTS NORTH OF MAIN SHOP BLDG.
(LOOKING SOUTH TOWARDS MAIN SHOP BLDG.)



GRADING WORK FOR NON-ELECTRIFIED
MAINTENANCE-OF-WAY AND OUTDOOR STORAGE
TRACKS, EAST OF M.O.W. BLDG.
(LOOKING SW TOWARDS M.O.W. BLDG.)

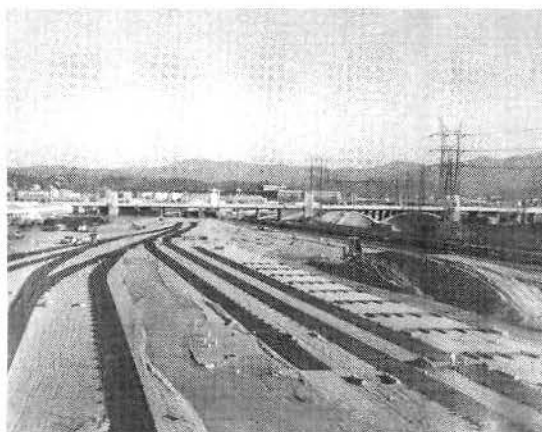

PRE-PLATED TIES, PRE-ASSEMBLED TURNOUTS AND
BALLASTED FUTURE TRACK 8 FOR STORAGE OF CWR
STRINGS. (LOOKING NORTH FROM MAIN SHOP BLDG.
TOWARDS NORTH END OF YARD & 1ST. ST. BRIDGE)

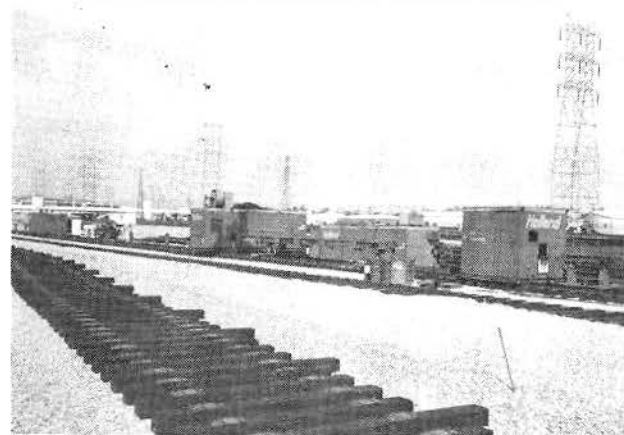

COMPLETED SET-UP OF WELDING PLANT ON
TRACK 9, WELDING OPERATIONS STARTED 11/26/89.
(LOOKING NE FROM CAR WASH TRACK)

Parsons-Dillingham-De Leuw, Cather




LOS ANGELES METRO RED LINE

CONTRACT PERFORMANCE REPORT

PDCD

PERIOD OCTOBER 1989

DIRECT FIXATION FASTENERS CONTRACT A616

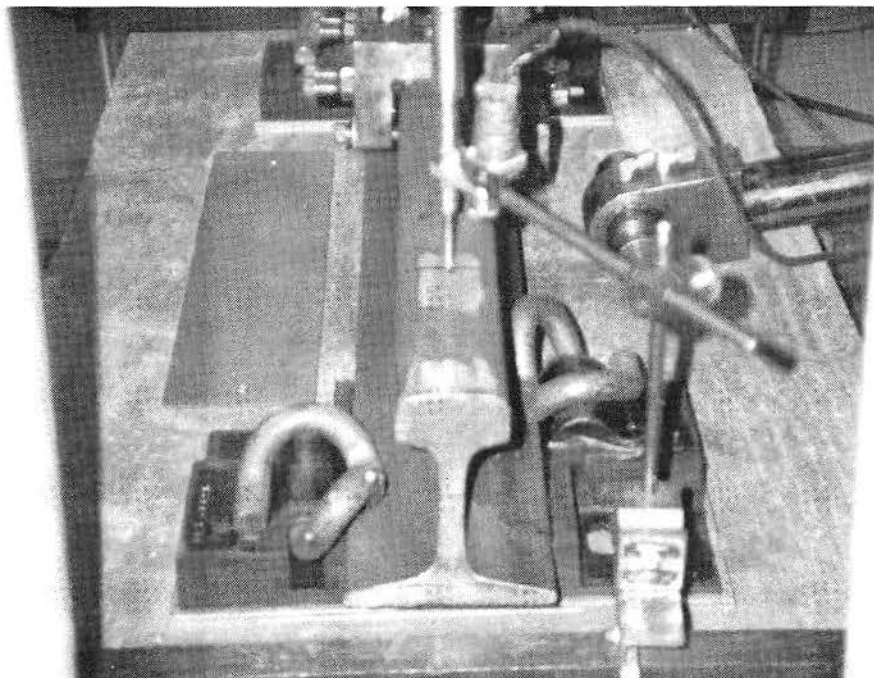

PRODUCTION TESTING OF FASTENER

Parsons-Dillingham-De Leuw, Cather




LOS ANGELES METRO RED LINE

PDCD


CONTRACT PERFORMANCE REPORT

PERIOD OCTOBER 1989

AUTOMATIC TRAIN CONTROL CONTRACT A620

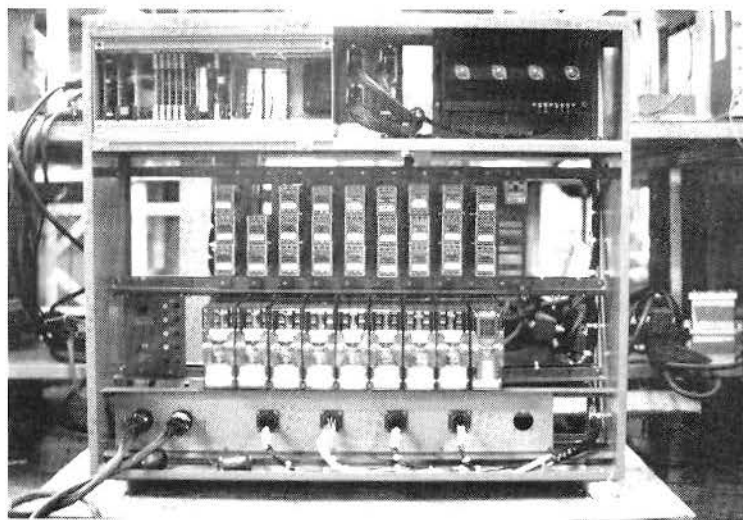

VEHICLE AUTOMATIC TRAIN PROTECTION
RACK PROTOTYPE UNIT

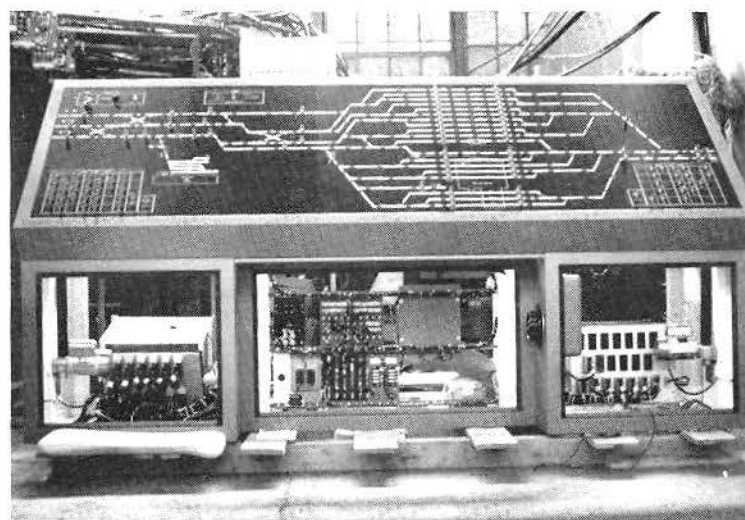

YARD CONTROL CONSOLE, FACTORY
TEST WEEK OF 9/18/89

Parsons-Dillingham-De Leuw, Cather

MTA LIBRARY



LOS ANGELES METRO RED LINE

CONTRACT PERFORMANCE REPORT

PDCD

PERIOD OCTOBER 1989

WHEEL TRUING MACHINE CONTRACT A732



WHEEL TRUING MACHINE CONTROL UNIT

Parsons-Dillingham-De Leuw, Cather



LOS ANGELES METRO RED LINE

CONTRACT PERFORMANCE REPORT

PDCD

PERIOD OCTOBER 1989

VENTILATION EQUIPMENT CONTRACT A740



SUBWAY VENT FAN & DAMPER BEING
TESTED FOR TRANSIENT PRESSURE
CHARACTERISTICS



PARALLEL RUN-IN TEST OF EMERGENCY FAN





