

**From:** Boudreau, Brian  
**Sent:** Wednesday, January 16, 2013 10:35 AM  
**To:** Yu, Kimberly  
**Cc:** Taylor, Paul  
**Subject:** Questions from 1/10/13 Board Staff Briefing

Here are my proposed responses to the questions raised at the January 10, 2013 Board Staff briefing:

**Question:** What are the schedules for the Westside Extension and Regional Connector Construction Management Support Services Contracts and Design/Build Contracts?

**Answer:** See attached schedules

**Question:** What is the reason for the Regional Connector forecast completion date slipping from December 2019 to May 2020?

**Answer:** There are a number of factors which have lead to the revised forecasted completion date, including additional efforts to mitigate the construction impacts of the project and additional time required for peer review and outreach to the contracting community during the procurement process.

**Question:** Will the Regional Connector open in phases?


**Answer:** Yes, the first phase is forecast to open to Eastside in January 2020 and the second phase is forecast to open to Pasadena in May 2020.

**Question:** Did the PMO notify the Board of issues related the Patsaouras Plaza contract bids coming in higher than budgeted?

**Answer:** Yes the Program Management monthly report has been addressing these issues beginning with the October 2012 report.

The other comments received regarding enhanced content of the report will be addressed in next month's report.

### DESIGN / BUILD CONTRACT PROCUREMENT SCHEDULE

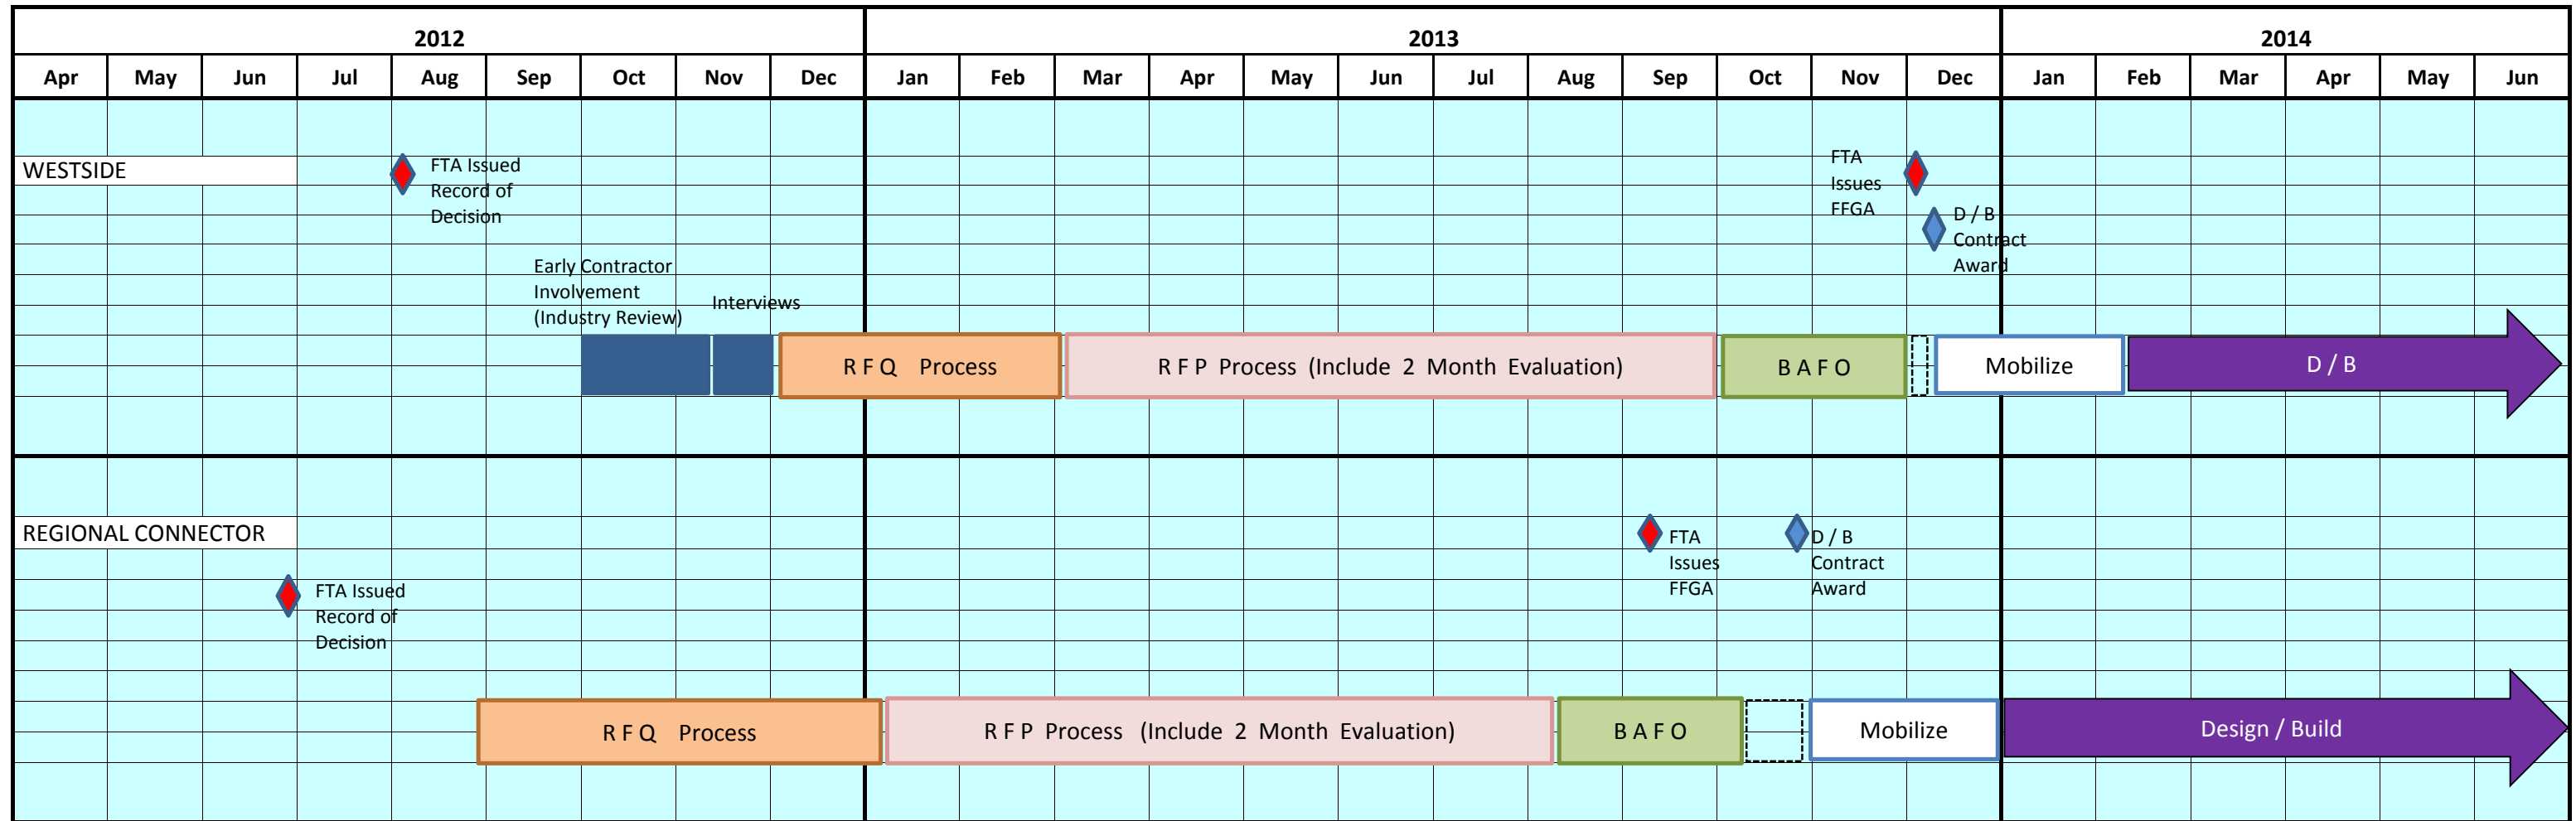

CONTRACT MANAGEMENT SUPPORT SERVICES PROCUREMENT SCHEDULE

