




I-405 Sepulveda Pass Improvements Project

MONTHLY PROJECT STATUS REPORT

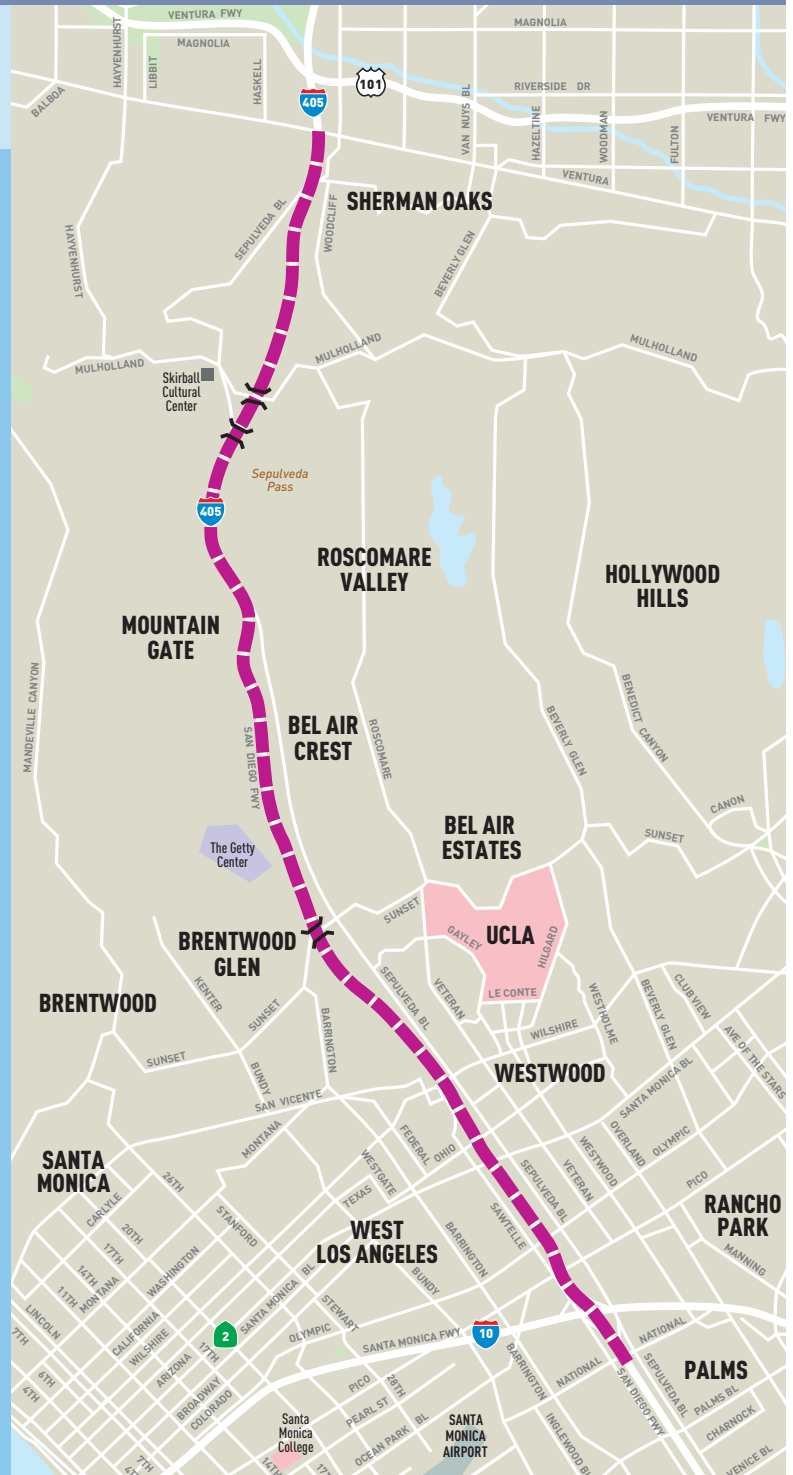

Metro®



11-00623P1 © 2010 LACMTA

INTERSTATE 405 SEPULVEDA PASS IMPROVEMENTS PROJECT

MONTHLY PROJECT STATUS REPORT

THE PREPARATION OF THIS DOCUMENT HAS BEEN FINANCED IN PART THROUGH GRANTS FROM THE FEDERAL HIGHWAY ADMINISTRATION (FHWA) AND THE AMERICAN RECOVERY AND REINVESTMENT ACT (AARA) AND FUNDS FROM THE STATE OF CALIFORNIA.

OCTOBER 2012

TABLE OF CONTENTS

	Page No.
Project Overview & Status.....	1-2
Management Issues.....	2-5
Project Status	
• Project Scope.....	6-7
• Schedule	
○ Key Milestones Six-Month Lookahead	8-9
○ Project Summary Schedule	10
○ Critical Path Narrative.....	11
• Project Cost Status.....	12
• Financial/Grant Status.....	13
• Staffing.....	14-15
• Real Estate.....	16
• Environmental.....	17
• Community Relations.....	18
• Quality Assurance.....	19
• Safety and Security Status.....	20-21
• Third Party.....	22
Contract C0882 Status.....	23
Chronology of Events.....	24-34
Construction Photographs.....	35-40
Appendices.....	41-44

PROJECT OVERVIEW & STATUS

The I-405 Sepulveda Pass Improvements Project will add a 10-mile HOV lane and improve supporting infrastructure such as ramps, bridges, and soundwalls on the San Diego Freeway (I-405); while widening lanes from the Santa Monica Freeway (I-10) to Ventura Freeway (U.S. 101). This project will reduce existing and forecasted traffic congestion on the I-405 and enhance traffic operations by adding freeway capacity in an area that experiences heavy congestion. In addition to these modifications, the project will improve both existing and future mobility and enhance safety throughout the corridor. Project benefits include a decrease in commuter time, reduce air pollution, and promote ridesharing. The I-405 Sepulveda Pass Improvements Project features include:

- *Add a 10-mile HOV lane on the northbound I-405 between the I-10 and US-101 freeways*
- *Remove and replace the Skirball Center, Sunset Blvd. and Mulholland Dr. Bridges*
- *Realign 20 on and off ramps*
- *Widen 20 existing overpasses and structures*
- *Construct approximately 18 miles of retaining walls and soundwalls*

Interstate 405 (I-405), also known as the San Diego Freeway, is a north/south route classified as an interstate/interregional loop freeway. It is part of the National Highway System (NHS), originating at the I-5 in Orange County in the City of Irvine and terminating at the I-5 in Los Angeles County, in the City of Los Angeles near the community of Mission Hills.

The design-build contract Notice to Proceed (NTP) was given on 6/2/2009, with commencement of contract time (1550 calendar days) on August 31, 2009. Substantial completion is currently expected to occur in May 2013, with final acceptance of the project required by November 27, 2013.

Reconstruction of the Mechanically Stabilized Earth (MSE) walls has started on the walls which were deconstructed.

Kiewit submitted a Revised Schedule which showed a Substantial Completion date way beyond the contractual completion date. Project reviewed the schedule and sent Kiewit over-the-shoulder (OTS) comments. As discussed during the Executive Partnering Meeting, Metro will write a letter to Kiewit accepting the schedule for planning purposes only. Kiewit is currently reviewing the comments, and Project will conduct joint comments resolution sessions with Kiewit, in turn Kiewit will incorporate comments and update the schedule. This schedule will become the basis of the monthly progress and status reporting.

Key project activities for October 2012 include:

- Mulholland Bridge north side construction started in October 2012.
- Executive Partnering started in August – September 2012 and has dictated the Project to work with the Contractor to establish a realistic schedule, irrespective of contractual responsibility for schedule delay. While this appears to be reasonable, the Contractor submitted a new schedule which added significant amount of time to the schedule compared to the one which was developed during the April-May 2012 timeframe. Project reviewed the schedule and sent OTS comments to Kiewit. The contractor is currently reviewing the comments, and Project will conduct joint comments resolution sessions with Kiewit, upon which Kiewit will incorporate comments and update the schedule.

PROJECT OVERVIEW & STATUS (Cont'd)

- The work at GSA was going well, but the recent newly found utility lines will affect work and schedule in the GSA area.
- Bridge construction activities in Segment 1 has increased.
- Level of Kiewit activity has increased significantly. MSE walls which were deconstructed because of wall failure have been removed and Kiewit is expending significant project resources to catch up. Note that while the Project applauds this effort, it comes at the expenses of other Project activities.

MANAGEMENT ISSUES

Concern No. 1: Align I-405 Closer to the Getty Parking Structure (96" MWD Waterline)

Status/Action In December 2011, Metro issued Kiewit a unilateral change order for the construction in the amount justified by Metro's Independent Cost Estimate. Work has progressed and is being compensated based on this change order as part of the monthly Pay Application process. Metro and Kiewit have been negotiating this change for several months and only a few outstanding issues remain to be negotiated, namely direct costs for traffic handling, subcontractor direct costs for Retaining Wall 1827, supervision, and escalation. Project anticipates reaching a mutually agreed price by the end of November 2012. Negotiation of the design costs are also in progress with an anticipated completion by the end of November 2012. However, Metro has agreed to issue an interim change for the amount of Metro's current estimate based on negotiations to date.

Concern No. 2: Provisional Sums

Status/Action There will be a significant cost increase in Provisional Sums caused by unknown utility conflicts at bid time. Currently, Project is reviewing Utility scopes to verify their accuracy and identify other issues, such as future changes, that could impact the project later. In addition, the Project is actively pushing Kiewit to forward price all relocations and stop Time and Material (T&M) pricing, except in emergency type situations. Kiewit is fighting this.

Concern No. 3: Reversible Lane Project on Sepulveda

Status/Action Project has received approval from Metro Board and commitment from City for \$2.6 million in Reversible Lane work and will implement the work where feasible.

MANAGEMENT ISSUES (Cont'd)

Concern No. 4: Review Support from COLA

Status/Action Project understands that LABOE is in the process of hiring additional staff to support Larry Hsu on Metro projects. LADOT is also working on a plan to hire new staff to support Metro projects. At this point, LABOE has added staff and we are waiting and expecting to see benefits.

Concern No. 5: Kiewit and Metro Estimating Approaches

Status/Action Metro and Kiewit have found it difficult to reconcile estimates. While Metro implemented staff changes and refocused efforts on estimates to try and resolve issues with Kiewit, the Project still continues to have problems. At the Executive Partnering Meeting, Kiewit mentioned that they would like to reconcile the estimates and finalize the associated payments. In the past several months, Kiewit has quoted the outstanding numbers to be in the range of \$45 to \$70 million. These numbers were checked against Project records and the result was not close to Kiewit's figures. It is obvious that Kiewit is asking for reimbursement of disputed items which are documented as non-payable. Project is meeting with Kiewit staff weekly to identify a complete list, prioritize, and resolve issues. As noted in Concern No. 1 above, Metro and Kiewit have met for several months attempting to reconcile the estimating process. It should be noted that Kiewit's additional supervision (not allowed by contract) quantities and inefficiencies are the cause of most of the discrepancies.

Concern No. 6: Mulholland Bridge Realignment

Status/Action Demolition of the second half of the Mulholland Bridge was completed in September 2012 and construction of the north side of the bridge has begun.

Concern No. 7: Recovery Schedule

Status/Action Kiewit is having problems with the MSE walls which may impact the schedule. The Project is working with Kiewit and Caltrans to determine means and methods to achieve Substantial completion of May 31, 2013, although the latest impacts may make it harder to achieve this date. Project requested Kiewit to submit a revised Recovery Schedule in March 2012 but have not received this schedule yet. The current assessed completion date is December 2013 which puts the project at a potential 6 months delay. Based on the Executive Partnering discussions to prepare a more realistic schedule, the Contractor submitted a new schedule which added significant amount of time to the schedule compared to the one which was developed during the April-May 2012 timeframe. Project reviewed the schedule and sent OTS comments to Kiewit. Also, based on the Executive Partnering

MANAGEMENT ISSUES (Cont'd)

Meeting discussions. Metro will write a letter to Kiewit accepting the schedule for planning purposes only. The contractor is currently reviewing the comments, and Project will conduct joint comments resolution sessions with Kiewit, upon which Kiewit will incorporate comments and update the schedule.

Concern No. 8: Project Cost and Schedule Reassessment

Status/Action The Project has developed a total project cost forecast which has identified a significant potential cost overrun due to increased labor cost, Provisional Sums, and Utilities. Project believes that this overrun would be offset by the Betterments and cost recovery potential from other Agencies, if the cost is recovered. Metro is currently developing the report for the Board that identifies trends noted above and potential solutions.

Concern No. 9: Real Estate Cost Reassessment

Status/Action Caltrans completed an updated report of the Real Estate capital cost requirements which showed no cost overruns at this time. This will be used as a tracking and measurement tool against Project cost forecast.

Concern No. 10: Widening of Sepulveda between Montana and Church

Status/Action This is part of the Westwood Hills lawsuit settlement and resolution of issues with the LADOT regarding the width of Sepulveda. The Project is behind in fact-finding and cost resolution.

Concern No. 11: Retaining Walls 1720 and 1730

Status/Action The changes to these walls are related to the potential Westwood Hills lawsuit settlement, LADOT requests for widening of Sepulveda, and reduced work for Kiewit at this location. Metro has been fact-finding with Kiewit for quite some time to get closer to resolving cost estimate differences. Area 5 (Getty) is taking priority so the resolution of this issue may be delayed. Metro Board approved the initial change and the Project is working under the assumption that this work is a credit to the project.

Concern No. 12: Giro Lawsuit


Status/Action Metro and Caltrans are reviewing options and alternatives for the ramp design of the north side of Sepulveda due to the Giro issue. The project is also looking into closing the northbound Getty on-ramp, based on construction requirements, to help reduce construction impacts.

MANAGEMENT ISSUES (Cont'd)

Concern No. 13: MSE Walls Failure

Status/Action All walls have been deconstructed and new wall designs are nearing completion, reconstructing walls is continuing.

PROJECT SCOPE

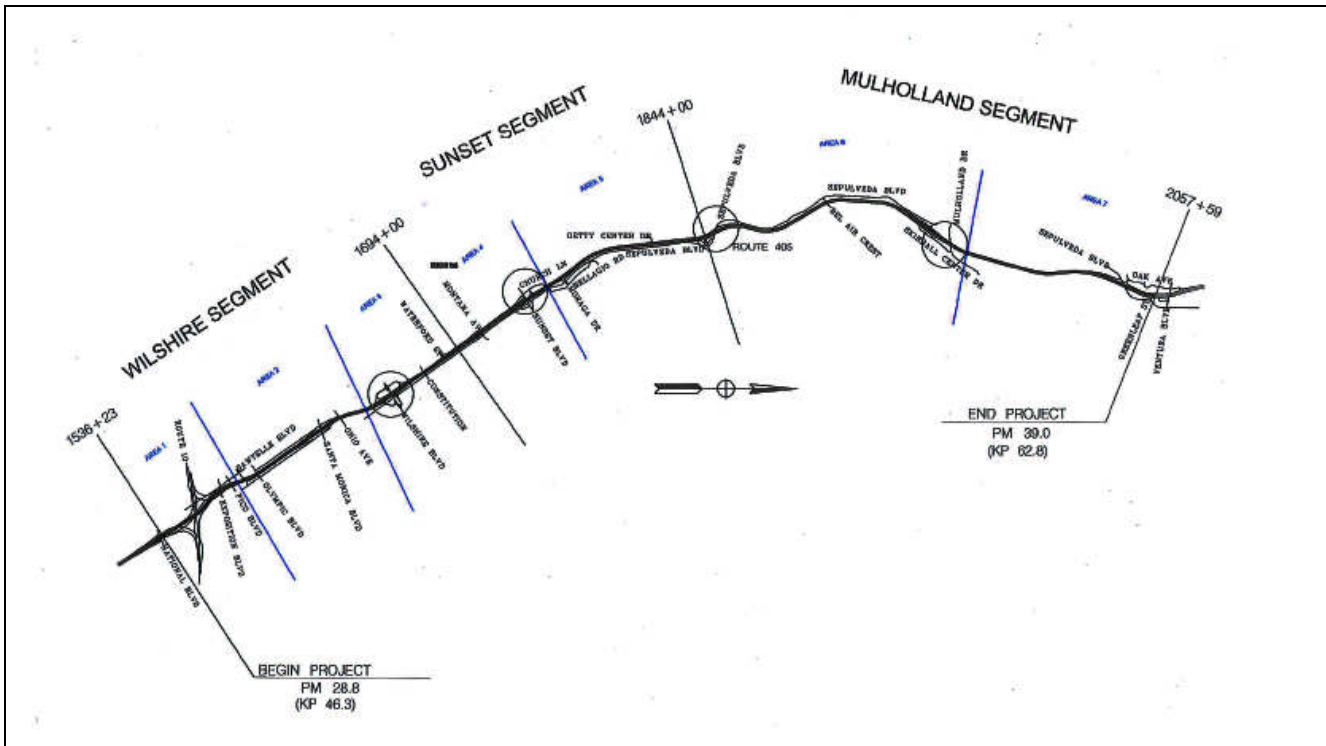

The I-405 Sepulveda Pass Improvements Project is a Design-Build contract to add a 10-mile High Occupancy Vehicle (HOV) lane on the northbound San Diego Freeway (I-405) between the Santa Monica (I-10) and Ventura (US 101) Freeways. The purpose of the project is to reduce congestion by adding the HOV lane and closing the HOV gap, which will provide a continuous HOV lane from the Orange County Line to the I-405/US-101 interchange. The scope entails an 11-foot half median, one 12-foot HOV lane, a 1-foot HOV buffer, five 12-foot mixed-flow lanes (six 12-foot mixed-flow lanes between Mulholland Bridge and Valley Vista), and a 10-foot outside shoulder.

Most of the freeway widening required for this project occurs along the east side of I-405 along Sepulveda Blvd. between Montana Ave. and Moraga Dr. and between Getty Center Drive and the northbound Getty Center off-ramp. Sepulveda Blvd. is going to be slightly realigned at the relocated southbound I-405 Skirball Center Drive on/off-ramps in order to add a dual-left-turn lane to the on-ramp.

Some freeway widening also occurs along the west side of the freeway between Olympic Blvd. and Waterford Street, and between Bel Air Crest to just north of Ventura Blvd. This entails NB and SB lanes and shoulder standardization.

In order to reduce accidents associated with traffic on the ramps, project scope includes several interchange improvements as detailed below:

PROJECT SCOPE






- Wilshire Blvd. interchange in both directions
The northbound on-ramp from eastbound Wilshire Blvd. is grade-separated from the northbound off-ramp to westbound Wilshire Blvd. and from Sepulveda Blvd. The southbound off-ramp to eastbound Wilshire Blvd. is grade-separated from the southbound off-ramp to westbound Wilshire Blvd.
- Northbound I-405 Sunset Blvd. interchange
The northbound I-405 off-ramp to eastbound Sunset Blvd. is widened to include one more lane. Two exclusive 12-foot lanes on the reconstructed Sunset Blvd. overcrossing and two 12-foot lanes on the on-ramp are provided for the northbound I-405 on-ramp from eastbound Sunset Blvd. In the eastbound direction three 12-foot lanes and in the westbound direction three 11-foot lanes are provided which solves the existing reduction from three lanes to two lanes in the eastbound direction. In both directions, 4-foot shoulders and 5-foot sidewalks as well as a 13-foot median are provided on the Sunset Blvd. overcrossing.
- The irregular northbound I-405 on/off-hook ramps at the Getty Center interchange are reconfigured to a standard diamond interchange to increase stopping sight distances in order to improve safety.
- The southbound I-405 Skirball Center Drive interchange is relocated to form a “T” intersection with Sepulveda Blvd. This eliminates the existing intersection at Skirball Off-Ramp and Skirball Center Drive.
- The southbound Valley Vista On and Off Ramps are realigned due to freeway widening and freeway mainline realignment between SB Valley Vista On/Off Ramps. The realignment will improve the stopping sight distance for the SB Valley Vista Off Ramp. A third lane will be added to the SB Valley Vista On-Ramp to increase the ramp capacity.
- A second NB lane will be added on Skirball Center Drive between the Skirball Bridge and NB Skirball ramps.
- A NB auxiliary lane and bike lanes will be added on Sepulveda Blvd. on each direction, between the new SB Skirball ramps and Skirball Bridge.

A total of 12 soundwalls and 54 retaining walls within the project limits are constructed at embankments where right-of-way is constrained.


A total of 12 undercrossings within the project limits are widened. Three overcrossings at Sunset Boulevard, Skirball Center Drive, and Mulholland Drive are replaced.

KEY MILESTONE SCHEDULE SIX-MONTH LOOKAHEAD


	Milestone Date	Oct-12	Nov-12	Dec-12	Jan-13	Feb-13	Mar-13
Bridge 17 - Church Lane UC - Construction Begins - Drilling CIDH Piles	10/1/12A	○					
Bridge 22 - Mulholland OC - Begin Construction Work for the North Side Bridge - Phase 2 SOE	10/1/12A	○					
Bridge 20 - Belair Crest UC - Begin Work to Correct Grade Deficiency on Girders	10/2/12A	○					
Bridge 21 - Skirball OC - Pour Bent 2 South Column	10/10/12A	○					
Bridge 15 - Sunset NB On-Ramp - Pour Top Deck	10/19/12A	○					
Bridge 18 - Getty Center UC - Pour Deck of Span 2 East Side of Bridge (NB)	10/23/12A	○					
Bridge 8 - EB Wilshire to NB On-ramp - Complete Driving Piles at Bents 2 & 3	10/23/12A	○					
Bridge 2 - Exposition UC - Complete Pour Bent 3 Column	10/24/12A	○					
Bridge 2 - Exposition UC - Complete Pour Bent 4 Cap	10/24/12A	○					
Bridge 6A - SB Off-Ramp to EB Wilshire - Pour Abutment 1	10/26/12A	○					
Bridge 17 - Church Lane UC - Complete Drilling and Pouring 21 CIDH Piles	10/26/12A	○					
Bridge 18 - Getty Center UC - Pour Deck of Span 2 West Side of Bridge (SB)	10/30/12A	○					
Bridge 14 - NB On-Ramp to Sunset Blvd. - Begin Construction Work	11/2/12		○				
Bridge 5 - Ohio UC - Pour Deck SB Side	11/6/12		○				
Bridge 6A - SB Off-ramp to EB Wilshire - Complete Pouring Abutment 2	11/8/12		○				
Bridge 6B - SB Off-ramp to EB Wilshire - Complete Pouring Abutments 1 & 2	11/8/12		○				
Bridge 22 - Mulholland OC - Begin F/PS of Abutment 1 - North Side	11/13/12*		○				
Bridge 5 - Ohio UC - Pour Approach Slabs NB Side	11/15/12		○				
Bridge 2 - Exposition UC - Complete PC & Steel Girder Top Deck & Diaphragms (Span 1-3)	12/4/12			○			
Bridge 21 - Skirball OC - Complete Installation of Precast Concrete Girders-South Side.	12/12/12*			○			
Bridge 7 - NB405 to EB Wilshire Off-ramp - Complete Installation of CIP Box Girder (Stem Spans 4-3) - PH 2	12/13/12*			○			

 Metro Milestone	 Design/Build	 Third Parties Approval
 Caltrans Milestone	* New Date	 FHWA Federal Highway Administration Approval

KEY MILESTONE SCHEDULE SIX-MONTH LOOKAHEAD

	Milestone Date	Oct-12	Nov-12	Dec-12	Jan-13	Feb-13	Mar-13
Bridge 7 - NB Wilshire Off-ramp CIP Box Girder (Stem Spans 2-1) - PH 1 Begin Installation	12/14/12*			○			
Bridge 8 - NB Wilshire On-ramp CIP Box Girder (Top Deck Phase 1 & Phase 2) Begin Installation.	12/27/12*			○			
Bridge 22 - Mulholland OC - Begin Erecting Falsework (PH1 North Side)	12/27/12*			○			
Bridge 7 - NB Wilshire Off-ramp CIP Box Girder (Stem Spans 2-1) - PH 2 Begin Installation	1/10/13*				○		
Bridge 2 - Exposition UC - Begin Demolition of Existing Bridge Spans 4 - Abutment 9.	1/16/13*				○		
Bridge 2 - Exposition UC - Complete Demolition of Existing Bridge Spans 4 - Abutment 9.	1/23/13				○		
Bridge 8 - NB Wilshire On-ramp CIP Box Girder (Top Deck Phase 1 & Phase 2) Complete Installation.	1/24/13*				○		
Bridge 7 - NB Wilshire Off-ramp CIP Box Girder (Stem Spans 2-1) - PH 2 Complete Installation	1/30/13*				○		
Bridge 7 - NB Wilshire Off-ramp CIP Box Girder (Top Deck Spans 4-31) - PH 1 Begin Installation	2/4/13					○	
Bridge 22 - Mulholland OC. Begin forming bottom deck.	2/20/13					○	
Bridge 14 - NB 405 Sunset Blvd. Off-ramp. Begin closure window (120 day maximum closure)	2/26/13*					○	
Bridge 14 - NB 405 Sunset Blvd. Off-ramp. Begin bridge demolition.	2/26/13*					○	
Bridge 8 - NB Wilshire On-ramp - Begin Installation of CIP Box Girder Top Deck - (abut #9, bent 6-8) - PH 3	2/28/13*					○	
Bridge 7 - NB Wilshire Off-ramp CIP Box Girder (Top Deck Spans 4-31) - PH 1 Complete Installation	3/6/13						○
Bridge 14 - NB 405 Sunset Blvd. Off-ramp. Complete bridge demolition.	3/6/13						○
Bridge 2 - Exposition UC - Begin Installation of CIP Box Girder Stems, Stage 2 (Span 4-8)	3/7/13						○
Bridge 7 - NB Wilshire Off-ramp - Begin Installation of CIP Box Girder Top Deck (Spans 4-3) - PH 2.	3/7/13*						○
Bridge 2 - Exposition -Complete CIP Box Girder (Stems) Stage 2 (Span 4-8)	3/14/13*						○
Bridge 6 SB Wilshire Off-ramp - Begin Installation of Structural Steel Girder-6B	3/14/13*						○
Bridge 23 - Sepulveda - Begin Installation of CIP T-Griders - PH 1	3/14/13*						○
							

PROJECT SUMMARY SCHEDULE

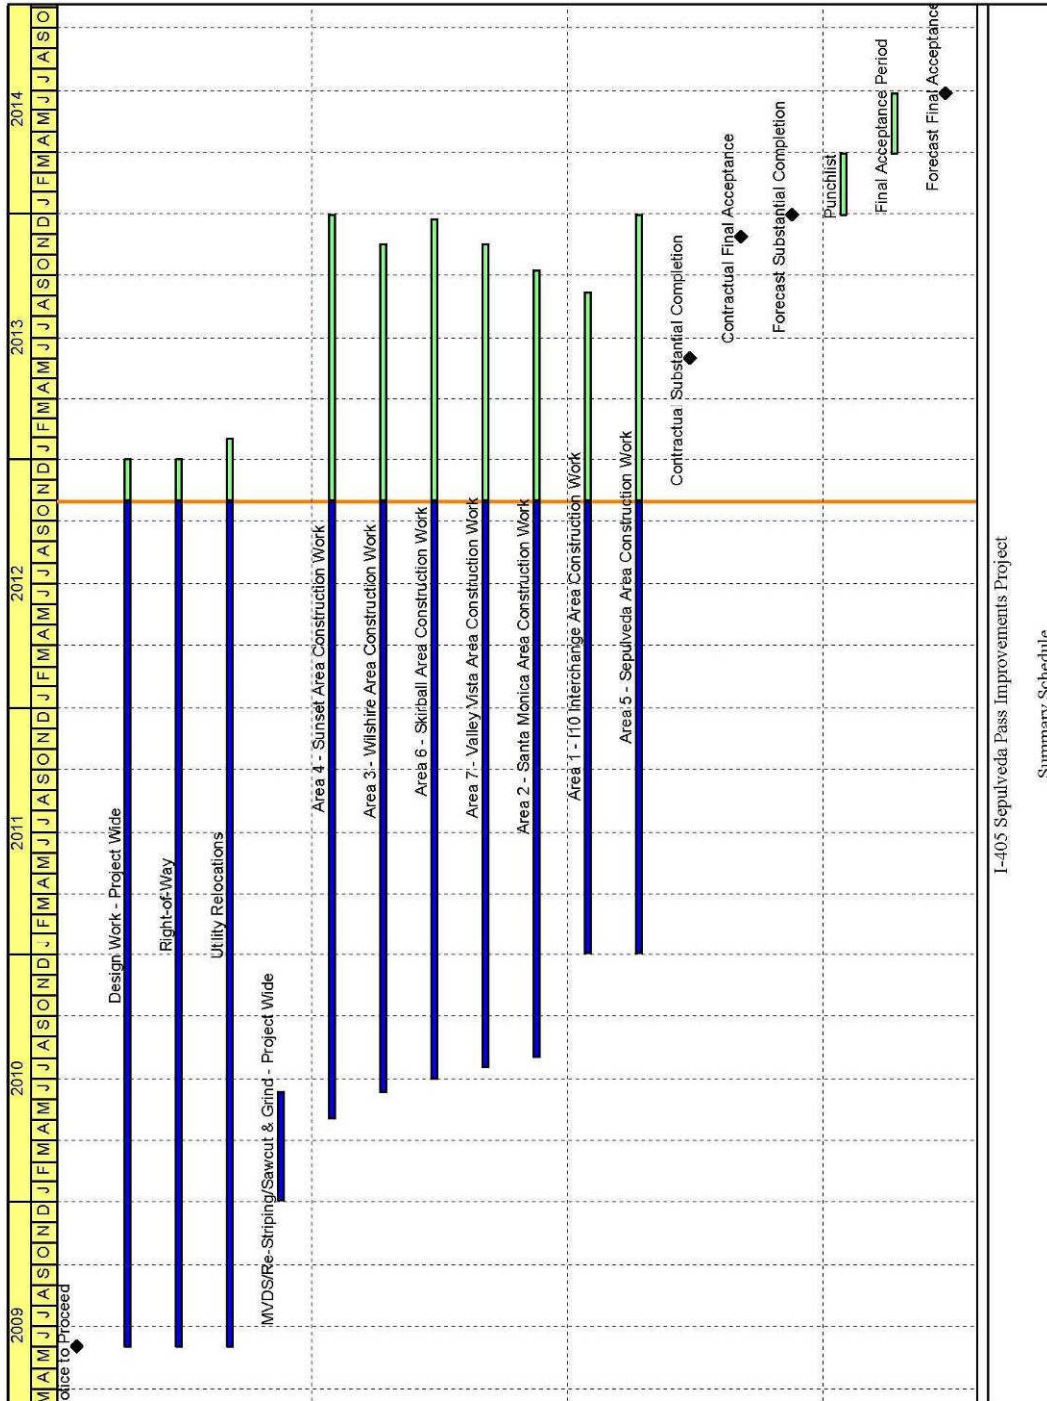

I-405 Sepulveda Pass Improvements Project

Summary Schedule

CRITICAL PATH NARRATIVE

The project has several critical paths which may potentially change as the work progresses. Based on the current project update, the primary critical path runs through the relocation of the Southern California Gas Line Utility 189 and continues through Sepulveda Widening at Area 4. The path then continues with construction of MSE Wall 1718 and Sunset Area NB widening. The path ends with Area 4 median work.

PROJECT COST STATUS

I-405 SEPULVEDA PASS IMPROVEMENTS PROJECT
 FEDERAL PROJECT #: SARRA-405-3(015)N, METRO PRIME CONTRACT# C0882
 METRO CONSTRUCTION MANAGEMENT DIVISION / CALTRANS
 COMBINED COST REPORT BY PHASE
 PERIOD ENDING: OCTOBER 2012
 DOLLARS IN THOUSANDS

PHASE #	PHASE CODE	DESCRIPTION	ORIGINAL BUDGET	CURRENT BUDGET		COMMITMENTS		EXPENDITURES		CURRENT FORECAST		BUDGET / FORECAST VARIANCE
				PERIOD	TO DATE	PERIOD	TO DATE	PERIOD	TO DATE	PERIOD	TO DATE	
0	PA&ED	PROJECT APPROVAL & ENVIRO DOCS	22,000	-	21,457	(379)	21,078	(379)	21,078	-	21,457	-
1	PSE	PLANS, SPECS, & ENGINEERING	63,100	-	25,560	103	25,613	103	25,677	-	25,632	72
2	RS	RIGHT-OF-WAY SUPPORT	14,000	-	9,543	132	5,991	132	5,991	-	8,076	(1,467)
3	CS	CONSTRUCTION SUPPORT	28,000	-	67,813	9,448	54,248	(169)	51,407	-	71,971	4,158
4	C	CONSTRUCTION	823,900	-	810,441	-	801,339	-	461,137	-	863,919	53,478
9	RC	RIGHT-OF-WAY CAPITAL	83,000	-	99,186	3,588	47,300	1,772	34,824	-	42,945	(56,241)
SUBTOTAL PROJECT			1,034,000	-	1,034,000	12,893	955,569	1,460	600,114	-	1,034,000	-
4	C	CONSTRUCTION OF CITY OF L.A.'S REVERSIBLE LANES PROJECT	-	-	6,000	-	-	-	-	-	6,000	-
4	C	CONSTRUCTION OF CALTRANS DRAINAGE SYSTEM REPAIRS	-	-	8,000	-	-	-	-	-	8,000	-
TOTAL PROJECT			1,034,000	-	1,048,000	12,893	955,569	1,460	600,114	-	1,048,000	-

NOTE: EXPENDITURES ARE CUMULATIVE THROUGH SEPTEMBER 30, 2012.
 KIEWIT EXPENDITURES ARE ONLY THROUGH JUNE 30, 2012 DUE TO INVOICING LAG.

PROJECT COST ANALYSIS

Original and Current Budgets

The Original Budget reflects the Metro Board adopted Life-of-Project (LOP) Budget which was approved in April 2009 in the amount of \$1,034.0 million. An additional \$6.0 million was approved by the Metro Board to add the City of LA's Reversible Lanes Project Scope funded by the City of Los Angeles, along with another \$8.0 million approved by the Metro Board to add Caltrans drainage system repairs to be funded by Caltrans. This brings the Total Current Budget to \$1,048 million.

Current Budget and Current Forecast

The Current Budget is \$1,048.0 million. Trends 1 through 119 have been approved and are included in the Current Forecast of \$1,048.0. Project Budget Change Requests 1 through 5 (PBCR) have been approved and included in the Current Budget.

Commitments

The Commitments increased by \$12.9 million this period primarily for purchase orders associated with DWP utility relocations, Caltrans real estate acquisitions, consulting services and Metro/Caltrans staff charges.

Expenditures

Expenditures are cumulative through September 2012. The expenditures increased by a total of \$1.5M this period. Expenditures for this period within the construction support phase included Metro and Caltrans project staff and miscellaneous consultant contract services. Costs in the right-of-way categories were for 3rd party Metro staff costs and for third party and utility relocation expenditures. Caltrans right-of-way expenditures for the period included staff charges for right-of-way support and real estate acquisitions. No invoices for Kiewit were processed by Metro Accounting this period. The \$600.1 million in Project Expenditures to date represents 57.3% of the Current Budget.

FINANCIAL/GRANT STATUS – ORIGINAL SCOPE ACTIVITIES

OCTOBER 2012		STATUS OF FUNDS BY SOURCE							
SOURCE	(A)	(B)	(C)	(D)	(D/B)	(E)	(E/B)	(F)	(F/B)
	APPROVED BUDGET	TOTAL FUNDS ANTICIPATED	TOTAL FUNDS AVAILABLE	COMMITMENTS		EXPENDITURES		BILLED TO FUNDING SOURCE *	
				\$	%	\$	%	\$	%
FEDERAL SAFETEA-LU	\$117.000	\$117.000	\$117.000	\$117.000	100%	\$47.035	40%	\$47.035	40%
FEDERAL ARRA	\$189.900	\$189.900	\$189.900	\$189.900	100%	\$189.900	100%	\$189.900	100%
STATE CMIA	\$614.000	\$614.000	\$614.000	\$546.444	89%	\$319.439	52%	\$309.858	50%
STATE TCRP	\$90.000	\$90.000	\$90.000	\$90.000	100%	\$31.515	35%	\$31.515	35%
STATE RSTP	\$10.100	\$10.100	\$10.100	\$10.100	100%	\$10.100	100%	\$10.100	100%
PROPOSITION C 25%	\$13.000	\$13.000	\$13.000	\$2.125	16%	\$2.125	16%	\$2.125	16%
SUB TOTAL FUNDS	\$1,034.000	\$1,034.000	\$1,034.000	\$955.569	92%	\$600.114	58%	\$590.533	57%
CITY OF LA **	\$6.000	\$6.000	\$0.000	\$0.000		\$0.000		\$0.000	
CALTRANS	\$8.000	\$8.000							
TOTAL FUNDS	\$1,048.000	\$1,048.000	\$1,034.000	\$955.569		\$600.114		\$590.533	

NOTE: EXPENDITURES ARE CUMULATIVE THROUGH SEPTEMBER 2012.
 * BILLING AMOUNT IS LESS THAN EXPENDITURES AMOUNT DUE TO SYSTEM LAG IN SUBMITTING INVOICES TO CALTRANS.
 ** CONSTRUCTION OF CITY OF LA REVERSIBLE LANES PROJECT.
 *** CONSTRUCTION OF CALTRANS DRAINAGE SYSTEM REPAIRS.

STATUS OF FUNDS ANTICIPATED

FEDERAL SAFETEA-LU: \$117M is available for drawdown for specific phases of the Project as agreed upon in the Cooperative Agreement between Caltrans and Metro.

FEDERAL ARRA: \$189.9M is available for drawdown for specific phases of the Project as agreed upon in the Cooperative Agreement between Caltrans and Metro with consultation with FHWA.

STATE CMIA: State Proposition 1B Bond sales provided \$254.7M to the project. Funds are available for drawdown. The remaining balance of \$359.3M has been allocated and are available for drawdown.


STATE TCRP: \$42M is available for drawdown for specific phases of the Project as agreed upon in the Cooperative Agreement between Caltrans and Metro. The remaining balance of \$48M has been made available by the CTC and is available for drawdown.

STATE RSTP: \$10.1M is available for drawdown for specific phases of the Project as agreed upon in the Cooperative Agreement between Caltrans and Metro.

PROPOSITION C 25%: The Metro Board approved the allocation of \$13M to the Project.

STAFFING STATUS

Total Project Staffing - FTEs

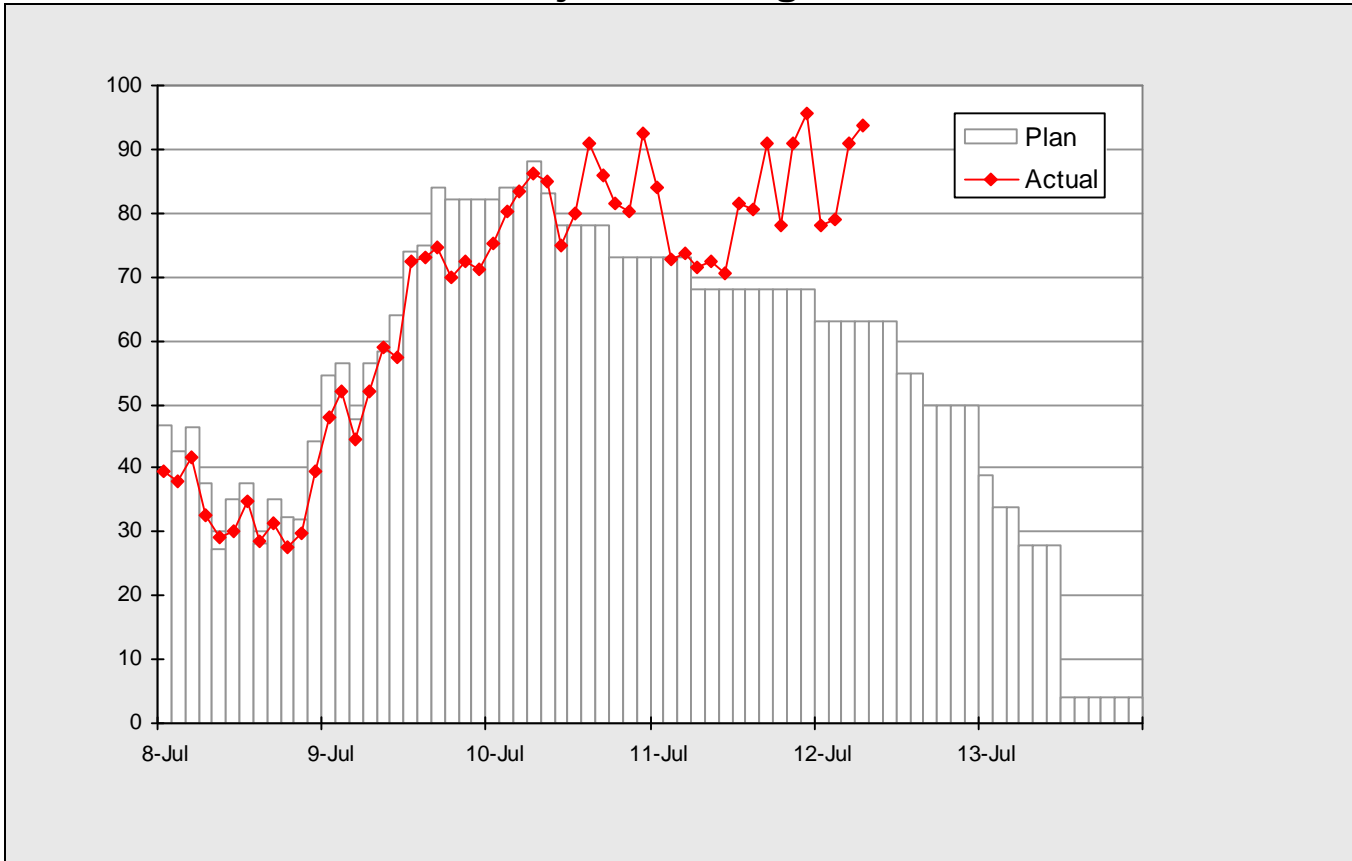


Total Project Staffing


Project Staffing Plan is presently being reassessed as a component of the Cost Schedule Reassessment.

STAFFING STATUS


MTA - FTEs

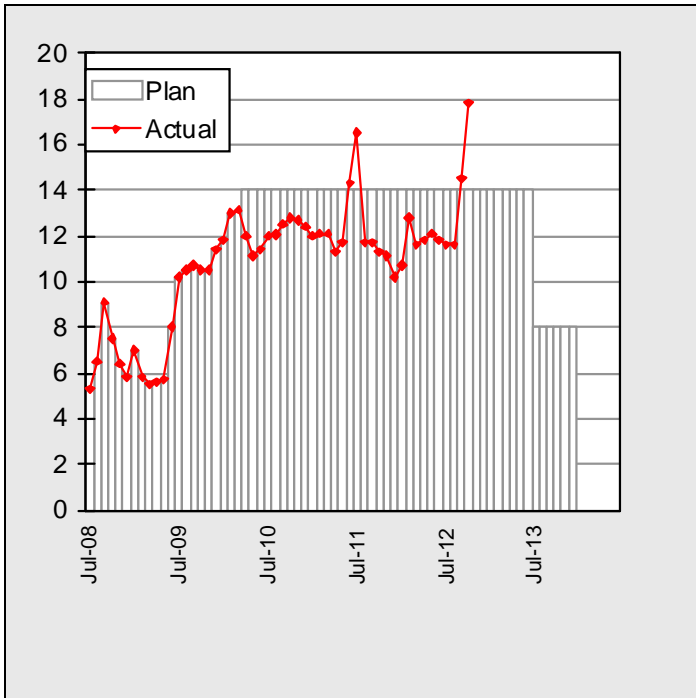

CALTRANS- FTEs

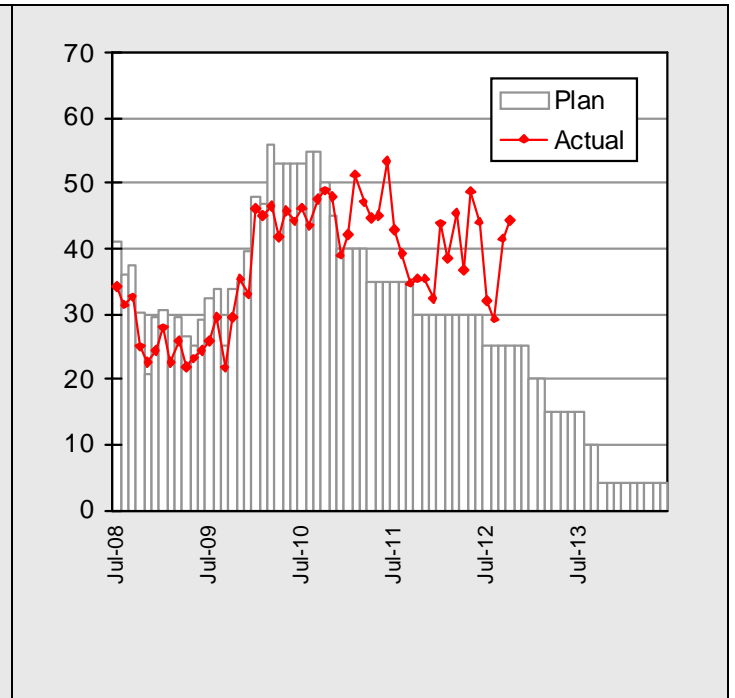

STANTEC - FTES

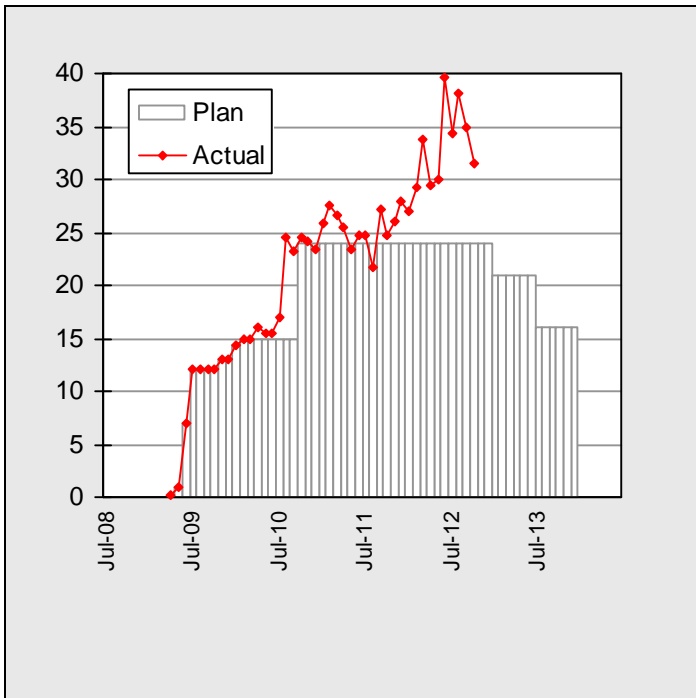

REAL ESTATE STATUS

The Real Estate acquisition process is proceeding and the Project is working on obtaining and releasing the past due parcels to the Contractor.

- Parcel 79619 (LACMTA) – Access has been provided but parcel has not been acquired yet. Acquisition will take place after the completion of project. This parcel has no apparent schedule impact.
- Parcel 79585 (Rodeo Realty) – Right-of-Entry has been acquired that will allow construction to proceed. This parcel has no apparent schedule impact. Final Order of Condemnation (FOC) was September 12, 2012.
- Parcel 79692 (Skirball) – Right-of-Entry has been provided for the additional ROW but the parcel has not been acquired yet. This parcel has no apparent schedule impact.
- Temporary Construction Easements with the 22 parcels in the Westwood Hills Area have been extended until December 31, 2012 to facilitate completion of the work.
- Parcel 80330 (Easement at Retaining Wall 1882) – Offer was made on September 27, 2012.
- Soundwall on EB I-10 to SB I-405 Connector – Full take will be required for the construction of a soundwall at the I-10 to SB I-405 Connector. Process for acquisition has started.
- Parcel 79612 – Additional right-of-way requirements are needed for drainage system.
- Parcel 79629/79630 – Additional right-of-way requirements are needed for grading and drainage.

ENVIRONMENTAL STATUS

- Ongoing coordination with Santa Monica Mountains Conservancy (SMMC) and National Park Service on wildlife crossings and the redesign of NB Getty on-ramp and the associated wildlife culvert.
- Ongoing preparation of an Environmental Addendum for changes associated with the N/B Getty on-ramp.
- Ongoing coordination regarding landscaping along Sepulveda Blvd. between Constitution and Sunset and required mitigation associated with tree removal from City and State R/W. Caltrans, Metro and LABSS continue to discuss outstanding tree removal permits and tree replacement plans.
- The Regional Water Quality Control Board requested additional information regarding the fire on September 14, 2012 and responsibility for additional protective measures on 10/1/12. It was determined that the hillside that was burned is within the property of the Santa Monica Mountains Conservancy and the Project is not responsible for any additional BMP measures outside the project limits.
- Preparing an amendment to the Natural Environment Study (NES) to address impacts associated with additional grading behind retaining wall 1921.

COMMUNITY RELATIONS STATUS

- Distributed construction notices for the following construction activities: Chevron utility work weekend lane reduction on Sepulveda Blvd. at Bronwood Avenue, Bellagio Road curb and gutter replacement, excavation of Wall 1718, Sunset Blvd. cul-de-sac pothole and pre-wall operations, Sunset Blvd. Bridge pile testing, Sepulveda Blvd. drainage system between Montana Avenue and Homedale Avenue, full Sepulveda Blvd. weekend closure from Church Lane to Montana Avenue for roadway utility work, Bronwood Avenue paving closure extended by one week, full Sepulveda Blvd. weekend closure from Montana Avenue to Church Lane for paving work Church Lane Bridge CIDH (Cast in Drill Hole), storm drain improvements at Homedale/Sepulveda, pile drilling at north end of Wall 1730 Sunset Bridge weekend reconfiguration and opening, tree removal at north west corner of Montana/Sepulveda, beam removal and backfill operations at Wall 1746, removal of Wall 1718, utility weekend tie-in on Sepulveda Blvd., Sunset cul-de-sac and Sepulveda Blvd. utility backfill work, storm drain inlet improvements at Wall 1730, utility box improvements at Bronwood alleyway, soundwall removal between Church Lane and Sunset Bridge, roadway paving along Wall 1730, southbound 405 mainline paving between Bel Air Crest Bridge and southbound Getty on-ramp, Mulholland Bridge Falsework-southbound, Mulholland Bridge Falsework-northbound, Mulholland Drive weekend closure, Mulholland Bridge Demo/Freeway Closure, Valley Vista wall removal, Sherman Oaks Bridge demo and early prep work and southbound Getty on-ramp traffic reconfiguration.
- Participated in the following meetings: Global Traffic Management Meeting, City landscape review, webinar mobile outreach, West Los Angeles Traffic Committee Meeting, meeting with Delgado residents and Valley Vista property owners.
- Coordinated the following work activities: weekly distribution of Sepulveda activities to residents of Walls 1720/1730 and nighttime Sepulveda activities to Village Bel Air, addressed adverse impacts in the Valley Vista and Sherman Oaks area, Mulholland Drive nightly closures, Sepulveda Blvd. utility relocation, Sherman Oaks Bridge column pour, Sherman Oaks wall-early prep work, wall removal and retaining wall construction, Valley Vista utility work on Sutton, Valley Vista drainage work and Bel Air Crest work activities.
- 4,768 followers on Twitter.
- 19,381 likes on Facebook.
- 318 subscribers on Nixle.
- 43,769 page views on Website.

QUALITY ASSURANCE STATUS

- Metro Quality participated in:
 - Eleven Pre-Activity Meetings.
 - Two Project Quality Meetings.
 - Joint Project Partnering Meeting
 - Project Quality Council Meeting
 - Training /Oversight presentation on the LIDAR System.
- Eleven Nonconformance Reports (NCRs) were issued this month.
- Twelve Deficiency Reports (DRs) were issued this month.

SAFETY AND SECURITY STATUS

- The contractor experienced three recordable injuries during the month of October. These included an insect sting which became infected, a knee sprain and a fatal head trauma (see Special Safety Report on following page for details).
- Safety Staff participated in pre-activity (readiness review) meetings to ensure compliance with approved Work Plans and contract specifications.
- Construction activities are monitored during day and night shifts to ensure contractor compliance with contract specifications. A special investigation into the fatal injury has begun.
- Safety staff attended weekly Progress Meeting, Foreman's Weekly Safety Meetings and other project meetings to evaluate Contractors Safety Program compliance with contract requirements.
- October Contractor Work Hours (Design & Construction): 181,029
- Contractor – Project to Date Work Hours (Design & Construction): 4,565,681
- Total Project to Date Work Hours (Contractor & the IPO Staff): 5,060,691
- Project to Date Recordable Injury Rate: 0.7 (Seventeen Recordable Injuries) (each rate is per 200,00 work hours)
- Project to Date Total Time Away Injury Rate: 0.4 (Eight Time Away From Work Injuries)
- Project to Date Total Days Away Rate: 18.2 (463 Days Away From Work)
- Metro night shift staff reassigned at the end of August. The vacant position is currently being recruited.

SAFETY AND SECURITY STATUS (Cont'd)

OCTOBER 11th 2012 FATAL WORKER INJURY

The following information is preliminary.

At approximately 0220 hours on Thursday October 11th, 2012 a three worker Kiewit crew was loading shoring beams (steel 'H' or 'I' beams) onto a flatbed trailer and semi-tractor combination at the Southbound Santa Monica Blvd. off ramp. The ramp was closed to traffic at the time. A Kiewit Structural Crew was also working in the immediate area but was not directly involved in the beam loading operation.

The crew was composed of an equipment operator in a tracked back hoe and two laborers assisting the operator. The crew had just placed a beam on the trailer and released the rigging from the beam. The operator began to track backwards while the laborer climbed down from the trailer to the ground in between the trailer and a string of barrier (type 'K') rail. As the operator tracked backwards he turned the body of the excavator around 180° in order to be facing the direction he was moving.

As the body of the excavator swung around, it made light contact with one of the beams already on the trailer. This beam was pushed into another which was pushed into the beam closest to the edge of the trailer, knocking that beam off the trailer and onto the ground. The operator did not even realize that he had made the contact. The beam did not fall in a manner level to the ground but rather fell with one end dropping to the ground as it slid off the trailer, elevating the opposite end of the beam well above the level of the trailer.

As the end of the beam toward the front of the trailer came down from its elevated height, it fell onto and trapped beneath it the laborer who was walking between the trailer and the barrier rail (where he was retrieving the tag line they had been using), trapping him beneath it and killing him. The laborer was in the process of walking from the trailer ladder toward the excavator in order to follow the excavator back up the ramp to rig the next beam to be moved.

CHP and the LA County Coroner responded and began investigations. The scene was cleared and the ramp opened to the public at approximately 0711 hours.

For the safety of all workers due to the level of distraction that an event of this type creates, all work on the Project was suspended on October 11th (day and night shift). The workers family was notified by Kiewit Management and counselors were made available for any and all employees who wished to take advantage of the services. Work was also curtailed on Friday, October 12th 2012.

A Cal/OSHA representative responded and is conducting their investigation. Metro Construction Safety Staff will continue their investigation in parallel with the California Highway Patrol, OSHA and Kiewit investigations.

THIRD PARTY AGREEMENT STATUS

Third Party	Type of Agreement	Forecast Execution Date	Required Need Date	Status/ Comments
City of Los Angeles	MCA	3/13	6/09	A stand-alone Master Cooperative Agreement (MCA) between the City of Los Angeles and LACMTA is currently being drafted for the I-405 Project.
Los Angeles County Department of Public Works/Los Angeles Flood Control District	MCA	Cancelled	Cancelled	On advice of County Counsel, LACMTA is not required to enter into a Master Cooperative Agreement with the Los Angeles County Department of Public Works/Los Angeles Flood Control District since the I-405 Project is a State Project, not a LACMTA Project.
Utility Owners	Utility Agreements	Various	Various	Caltrans style Utility Agreements (similar to MTA Work Order Authorizations) will be completed as relocation plans are approved for each location.

CONTRACT STATUS

I-405 Sepulveda Pass Improvements Project Design/Build Contractor: Kiewit		Contract No.: C0882 Status as of: November 2, 2012				
Progress/Work Completed: Major work started/completed this period: - Bridge 17 Church Lane - Construction is started. - Bridge 22 Mulholland - Construction of north side of bridge is started. - Bridge 20 Bel Air Crest - Repair work to correct grade deficiency is started. - Bridge 15 Sunset NB on-ramp - Top deck is poured. - Bridge 18 Getty Center - NB & SB sides of bridge span 2 top decks are poured. - Bridge 16A SB off-ramp to EB Wilshire - Abutment 1 is poured. - Maintenance during construction - SWPPP cleanout and repairs, graffiti removal from k-rails, trash and debris removal.		Major Activities (In Progress): • Grading and paving. • Construction of Retaining Walls and sound walls. • Utility Relocations. • Bridge 1 and 2 construction. • Bridge 3 construction. • Bridge 4a/4b construction. • Bridge 5a/5b construction. • Bridge 7 and Bridge 8 construction. • Bridge 9 construction. • Bridge 12 and Bridge 13 construction. • Bridge 15 and Bridge 16 construction. • Bridge 17 and Bridge 18 construction. • Bridge 19 and Bridge 20 construction. • Bridge 21 and Bridge 22 construction. • Bridge 23 construction. • Maintenance during construction.				
Areas of Concern: • Redesign of NB Getty on-ramp due to Giro Property ROW. • DSC at Wall 1921 Sepulveda Blvd. at Mission Dump. • Area 4 utilities.		Major Activities Next Period: • Bridge 14 NB Off-ramp to Sunset - Begin construction. • Bridge 5 Ohio - SB top deck pour, NB approach slabs pour. • Bridge 6A & 6B SB off-ramp to Wilshire - Abutments are poured. • Bridge 22 Mulholland - North side Abutment 1 begin construction.				
		Original Baseline	Time Extension	Current Contract	Forecast Completion	Variance Cur-Fcast
Commencement		08/31/09	0	08/31/09	08/31/09	0
Completion		05/31/13	0	05/31/13	12/28/13	-211
Punchlist Complete		08/29/13	0	08/29/13	03/28/14	-211
Final Acceptance		11/27/13	0	11/27/13	06/26/14	-211
Schedule Summary:		Cost Summary: \$ In 000's				
Notice of Award	04/29/09	1. Award Value:		720,922		
Notice to Proceed	06/02/09	2. Executed Modifications:		67,047		
Original Contract Duration (CD)	1640	3. Approved Change Orders:		14,859		
Approved Time Extensions (CD)	0	4. Current Contract Value (1 + 2 + 3):		802,828		
Current Contract Duration (CD)	1640	5. Incurred Cost:		497,766		
Elapsed Time from NTP (CD)	1,250	6. Percent Incurred Cost:		62.0%		
Contract Elapsed Time Percent	76.2%					

CHRONOLOGY OF EVENTS

May 18, 2007	The Draft Environmental Impact Report (EIR)/Environmental Impact Statement (EIS) is issued.
May 22, 2007 to October 1, 2007	Public review of draft EIS.
February 29, 2008	The Final Environmental Impact Report (EIR)/Environmental Impact Statement (EIS) is issued.
March 10, 2008	The Final Environmental Impact Report (EIR)/Environmental Impact Statement (EIS) errata with U. S. General Services Administration (GSA) comments is issued.
March 14, 2008 to April 14, 2008	Public review of Final EIS.
April 25, 2008	Record of Decision (ROD) approved.
October 10, 2008	LACMTA issued Invitation For Bid (IFB) for the project.
February 20, 2009	Project bids opened.
April 23, 2009	LACMTA Board authorized the Chief Executive Officer to award Design-Build Contract C0882 to Kiewit Pacific Co.
April 23, 2009	LACMTA Board approved establishing a budget of \$1.034 billion for project 405523.
April 23, 2009	LACMTA awarded Contract C0882 to Kiewit Pacific in the amount \$694,156,000 to include Schedules A, C, and H (Option 4).
April 29, 2009	LACMTA issued a revised NOA to Kiewit Pacific in the amount \$720,922,000 to include Schedules A, C, E (Option 1), F (Option 2), G (Option 3), and H (Option 4).
June 2, 2009	LACMTA issued Notice to Proceed to Kiewit Pacific for the Design-Build Contract C0882.
August 31, 2009	Contract Commencement Date.
September 24, 2009	Kiewit Pacific submitted the Project Baseline Schedule.
October 14, 2009	Project Design Quality Management Plan approved.

CHRONOLOGY OF EVENTS (Cont'd)

December 14, 2009	Project Quality Management System approved.
January 20, 2010	Project Baseline Schedule was approved.
January 27, 2010	Roadway Restriping commenced.
March 12, 2010	Major Project Permits were obtained; Permit 401 – Water Quality Control Board, Permit 404 – U.S. Army Corps of Engineers, and Permit 1600 – California Department of Fish & Game.
May 31, 2010	The Project completed one year without a Recordable Injury.
July 23, 2010	Sunset Bridge major demolition of the south side top deck and center column.
August 2, 2010	Commenced construction on Bridge 4a/b.
August 16, 2010	Commenced ExxonMobil 16" utility relocation at Bridge 16.
August 20, 2010	Operating Engineers Local 12 initiate labor action by striking.
August 24, 2010	Completed ductbank work on Sepulveda for DWP utility undergrounding.
August 24, 2010	Commenced construction of Walls 1720/1730.
August 24, 2010	ITS Backbone is cut.
September 7, 2010	DWP started pulling wires for utility undergrounding on Sepulveda.
September 9, 2010	Operating Engineers Local 12 Labor action is settled and strike ends.
September 13, 2010	Completed the excavation of Roadway at 1685/1691.
September 15, 2010	Completed the removal of Wall 1665.
September 18, 2010	Completed installation of Temporary walkway at Skirball Bridge.
September 28, 2010	Pioneer access to Sunset on-ramp, Bridge 15 Abutment 1.

CHRONOLOGY OF EVENTS (Cont'd)

October 12, 2010	Began excavation of Sunset Bridge 16 Abutment 1 Footing.
October 12, 2010	Began demolition of Skirball Bridge 21.
October 15, 2010	Completed demolition Skirball Bridge 21.
October 15, 2010	Began driving piles at Santa Monica Bridge 4.
October 15, 2010	Installed Beams at Sunset Bridge 16, Bent #2.
October 15, 2010	Began driving piles on Santa Monica Bridge 4.
October 19, 2010	Completed demolition of Sunset Bridge 16, Abutment 4.
October 21, 2010	Installed beams at Sunset Bridge 15 On Ramp, Abutment 1.
October 22, 2010	Began Demolition of Sunset Bridge 16, Abutment 1.
October 22, 2010	Installed Piles at Wall 1720.
October 25, 2010	Began Excavation at Walls 1685/1691.
October 28, 2010	Began the relocation of overhead power lines at Ohio Ave Bridge 5.
October 28, 2010	Clear and grub area at Wall 1746.
November 12, 2010	Completed demolition of soundwall, barrier rail, and overhang at Bridge 13.
November 15, 2010	Completed installation of SOE at Abutment 1 NB at Bridge 4 Santa Monica.
November 15, 2010	Completed demolition of existing ExxonMobil 16" Oil Pipeline.
November 17, 2010	Completed excavation of CIP at Wall 1640.
November 18, 2010	Began excavation at Wall 1635.
November 29, 2010	Began Excavation at Bridge 13.
November 30, 2010	Began relocation of SCE underground vault.

CHRONOLOGY OF EVENTS (Cont'd)

December 7, 2010	Began driving piles at Bridge 13 - Montana Avenue UC.
December 14, 2010	Completed Pile driving at Abutment 1 Bridge 16 Sunset OC.
December 15, 2010	Completed the installation of new power poles and raised the utility wires at Bridge 5 - Ohio Avenue.
December 16, 2010	Completed piles at abutments 1 and 2 for Bridge 13 Montana Ave UC.
December 17, 2010	Began installation of SOE beams at Bridge 15 Sunset on-ramp.
January 3, 2011	Began Construction of Piers and Columns at Bridge 16.
January 11, 2011	Began Construction Activities at Bridge 5.
January 13, 2011	Began Construction Activities at Bridge 12.
January 17, 2011	Began Installation of Footings and Pile Caps at Bridge 16.
February 1, 2011	Began Construction Activities at Bridge 21 – Skirball Center Drive.
February 14, 2011	Began Field Work relocating Storm Drain at Veterans Administration (VA).
February 21, 2011	Began Field Work relocating Chevron Oil Pipeline at Bridge 23 – Sepulveda UC.
February 23, 2011	Began Construction Activities at Bridge 15 – Sunset On-Ramp.
February 25, 2011	Completed Drilling and Placing Beams at NB Abutments 1 & 2 at Bridge 12 – Constitution UC.
February 28, 2011	Completed Pouring Columns at Bent 3, Bridge 16 – Sunset OC.
March 2, 2011	Began Field Work relocating LADWP 4" Waterline at Valley Vista.
March 2, 2011	Completed Driving 14" Square Piles at Bridge 3 Abutment 1.
March 15, 2011	Began Field Work relocating So Cal Gas Line at Wall 1746.

CHRONOLOGY OF EVENTS (Cont'd)

March 18, 2011	Completed Setting Soldier Beams at Bridge 15 Bent 2 & 3 Mainline.
March 23, 2011	Began Field Work Encasing Sewer Lines 401-403 at Walls 1720, 1730 and 1746.
March 31, 2011	Completed Setting and Backfilling Wall Panels at Wall 1942B.
April 4, 2011	Began Installation of Bent 2 & Bent 3 Columns at Bridge 21 Skirball Center Drive OC.
April 5, 2011	Began Installation of Storm Drain at Walls 1720 and 1730.
April 10, 2011	Completed Installation of Girders at Bridge 13 Montana Ave UC.
April 22, 2011	Completed Bridge 9 Wilshire Blvd. UC demolition for widening.
April 25, 2011	Began Work Relocating Shell Oil Line at Bridge 23 Sepulveda UC.
May 2, 2011	Began Relocation of Area 2 Sewer Lines # 201-203.
May 6, 2011	Completed Setting Girders at Southside of Bridge 16 Sunset OC.
May 11, 2011	Began Construction Work on Bridge 3 Olympic Blvd.
May 25, 2011	Completed Tie Back Installation at Walls 1720 and 1730.
June 3, 2011	Completed Girder Installation on the North Side of Bridge 21 Skirball OC.
June 13, 2011	Began Installation of Precast Deck Panels on Bridge 16 Sunset OC.
June 24, 2011	Began Demolition of Existing Walls 1720 and 1730 along Sepulveda Blvd.
June 30, 2011	Completed Installation of Precast Deck Panels on Bridge 16 Sunset OC.

CHRONOLOGY OF EVENTS (Cont'd)

July 6, 2011	Began Relocation of LADWP Overhead Power Lines at Mulholland Bridge.
July 13, 2011	Completed installation of Void Slab Deck at Bridge 12 Constitution UC.
July 14, 2011	Completed Pouring Diaphragms 1, 2, and 3 at Bridge 21 Skirball OC.
July 16, 2011	Began Demolition of South Side of Bridge 22 Mulholland OC.
July 17, 2011	Completed Demolition of South Side of Bridge 22 Mulholland OC.
July 20, 2011	Completed Installation of Pre-cast Girders at Bridge 4SB Santa Monica UC.
July 26, 2011	Began Driving Piling at Bridge 8 NB from EB Wilshire, Bent 8.
August 1, 2011	Began installation of forms and rebar for Top Deck at Bridge 21, Skirball Center Drive.
August 3, 2011	Began work on the Interchange Ramp from Westbound I-10 to Northbound I-405.
August 6, 2011	Began work installing Top Deck at Bridge 4 Santa Monica Blvd.
August 24, 2011	Completed pouring the Top Deck at Bridge 13, Montana Ave.
August 26, 2011	Completed installation of Footing & Pile Cap/Abutment-Wingwalls/Bridge Bearing Bridge 3 Olympic Blvd.
August 31, 2011	Completed pouring the Top Deck at South Side of Bridge 16, Sunset Blvd.
September 15, 2011	Completed installation of Top Deck and Diaphragm on Bridge 16, Sunset Blvd.
September 16, 2011	Completed pouring the Top Deck at Bridge 21, Skirball Center Drive.
September 23, 2011	Began construction of LADWP Power Utilities undergrounding ductbank between Stations 1740 and 1760.

CHRONOLOGY OF EVENTS (Cont'd)

September 27, 2011	Completed pouring curb and gutter on west side of Bridge 16, Sunset Blvd.
September 29, 2011	Completed pouring Lateral Retaining Walls #6, #7, and #8 at Retaining Wall 1720.
October 14, 2011	Completed pouring footing for Bent 2 at Bridge 22, Mulholland Drive.
October 17, 2011	Began installation of Bent 2 Forms at Bridge 22, Mulholland Drive.
October 18, 2011	Began construction activities at Bridge 18, Bel Air Crest.
October 22, 2011	New Bridge 16, Sunset Blvd. South Side opened to vehicle traffic.
October 27, 2011	Completed pouring Abutment 1 at Bridge 22, Mulholland Drive.
November 1, 2011	Began demolition of Bridge 16 Sunset Blvd. north side.
November 7, 2011	Began installation of CIDH Piles for I-10 Connector.
November 9, 2011	Completed demolition of Bridge 16 Sunset Blvd. north side.
November 22, 2011	Received the VA License to Enter agreement.
November 22, 2011	Completed pouring Bridge 22 Mulholland OC Bent 2 Columns.
November 22, 2011	Completed pouring Bridge 5 Ohio NB Abutments 1 & 2.
December 1, 2011	MSE Wall 1897 along NB Sepulveda Blvd. south of Skirball Center Drive ruptures. Kiewit stops work on all MSE Walls throughout the project and begins investigation into MSE Wall deficiencies.
December 1, 2011	Began 2 nd pouring of Bridge 22 Mulholland Abutment 1.
December 8, 2011	Completed subgrade for NM Connector.
December 17, 2011	Began installation of Precast Girders at Bridge 5A Ohio Ave.
December 19, 2011	Began installation of falsework beams for Bridge 15 Sunset on-ramp.

CHRONOLOGY OF EVENTS (Cont'd)

December 19, 2011	Began driving piles for Bridge 16 Sunset Blvd. Bent 3.
January 4, 2012	Began De-construction of MSE Wall 1738A.
January 9, 2012	Began De-construction of MSE Wall 1665.
January 16, 2012	Completed demolition of the I-405 median barrier at Mulholland Bridge and began erection of Falsework.
January 19, 2012	Began pouring footings for Soundwalls at Retaining Walls 1720 and 1730.
January 20, 2012	Completed pouring column # 1 @ Sunset Blvd. Bridge.
January 25, 2012	Began De-construction of MSE Wall 1634.
January 27, 2012	Kiewit stopped work on all Soil Nail Walls due to developing cracks, pending investigation.
January 31, 2012	Poured columns at Bel Air Crest Bridge.
February 13, 2012	Construction activities are started in Area 5 at Bridge 18 Getty Center UC and Bridge 19 Sepulveda UC.
February 15, 2012	De-construction of MSE Wall 1738A at Sunset NB Off-Ramp is completed.
February 18, 2012	Piers and Columns are poured for Bridge 16 Sunset Blvd.
February 18, 2012	LADWP completes installation of new underground cabling in ductbank along Sepulveda Blvd and Wilshire Ave. Final paving of Sepulveda trench is completed.
February 28, 2012	Kiewit submits notification to LACMTA that all remaining MSE Walls, with the exceptions of completed MSE Walls 1619 and 1942B will be de-constructed.
March 2, 2012	Full NB Freeway Closure at Mulholland Bridge to install Falsework Girders.
March 6, 2012	Caltrans identifies a potential Safety Concern during Mulholland Bridge Falsework Girder Installation on the SB Side and orders girders to be removed. Caltrans issues Stop Work Order pending review of Girder Installation Process.

CHRONOLOGY OF EVENTS (Cont'd)

March 8, 2012	Caltrans completes review of Girder Installation Process and authorizes resumption of installation of Falsework Girders at Mulholland Bridge. SB Side Falsework Girders are installed.
March 22, 2012	Concrete Girders are installed at Bridge 5B Ohio UC SB side.
April 7, 2012	Kiewit completes installation of Mulholland Bridge (South Side) Sheet Decking and begins installation of structural rebar.
April 10, 2012	Kiewit resumes construction of MSE Walls. Construction of Wall 1672 new leveling pad is started.
April 14, 2012	Kiewit begins installation of top deck and diaphragm structural rebar at Bridge 4 Santa Monica UC.
April 20, 2012	Kiewit pours concrete top deck, curb, and gutter at Bridge 9 Wilshire UC.
May 1, 2012	Begin installation of Concrete girders at Bridge 16 Sunset OC North Side.
May 4, 2012	Kiewit resumes construction of MSE Walls using an approved new Wall Panel Vendor and Construction Plan. Construction begins at MSE Wall 1672 along Sepulveda Blvd. north of Wilshire Blvd.
May 4, 2012	Completion of installation of Concrete Girders at Bridge 16 Sunset OC North Side.
May 18, 2012	Construction of MSE Wall 1808 along Sepulveda Blvd. north of Getty Center Drive is started using new Wall Panels and Construction Plan.
May 24, 2012	Structural construction is started within the GSA Property. Construction of Bridge 7 Bent 3 is started.
May 31, 2012	Construction of MSE Wall 1686 along Sepulveda Blvd. north of Constitution Drive is started using new Wall Panels and Construction Plan.

CHRONOLOGY OF EVENTS (Cont'd)

June 2, 2012	NW1 Ramp from WB I-10 to NB I-405 is opened for traffic.
June 6, 2012	GSA Microwave Security System is installed.
June 7, 2012	Bridge 7 NB I-405 to EB Wilshire Off-ramp Columns for Bents 3 and 4 are constructed on GSA Property.
June 22, 2012	90-Day Shutdown of Bridges 10 & 11 NB I-405 to WB Wilshire and WB Wilshire to NB I-405 commenced.
June 27, 2012	Demolition of existing Bridges 10 & 11 is completed.
July 15, 2012	Bridge 21 Skirball Center Drive, North side, is opened to traffic.
July 20, 2012	Bridge 22 Mulholland Drive, Top Deck is poured.
July 21, 2012	Bridges 10 & 11 Pre-cast Girders are installed.
July 30, 2012	Bridge 21 Skirball Center Drive, South Side, Demolition is started.
August 3, 2012	Bridge 21 Skirball Center Drive, South Side, Demolition is Completed.
August 10, 2012	Bridges 10 & 11 Top Deck is Poured.
August 23, 2012	Bridge 16 Sunset Blvd. Top Deck is Poured.
August 31, 2012	Bridges 10 & 11 are Opened for Traffic.
September 4, 2012	Bridge 7 Falsework installation begins.
September 24, 2012	Bridge 16 is fully opened for traffic.
September 24, 2012	Bridge 22 South Side is opened for traffic.
September 28, 2012	Began demolition of the north side of Mulholland Bridge 22.
September 30, 2012	Complete demolition of the north side of Mulholland Bridge 22.
October 1, 2012	Began construction activities for Bridge 17, Church Lane UC.

CHRONOLOGY OF EVENTS (Cont'd)

October 1, 2012	Began construction activities for Bridge 22, Mulholland OC north side.
October 15, 2012	MSE Wall 1897 reconstruction is completed.
October 19, 2012	Bridge 15 Sunset NB On-ramp, top deck is poured.
October 23, 2012	RW 1720 punch list work begins.

CONSTRUCTION PHOTOGRAPHS



CONSTRUCTION PHOTOGRAPHS



CONSTRUCTION PHOTOGRAPHS




Progress Photos October 2012 - Bridge 7 NB/EB Wilshire Off Falsework




Progress Photos October 2012 - Bridge 8 NB/EB Wilshire On Falsework

CONSTRUCTION PHOTOGRAPHS

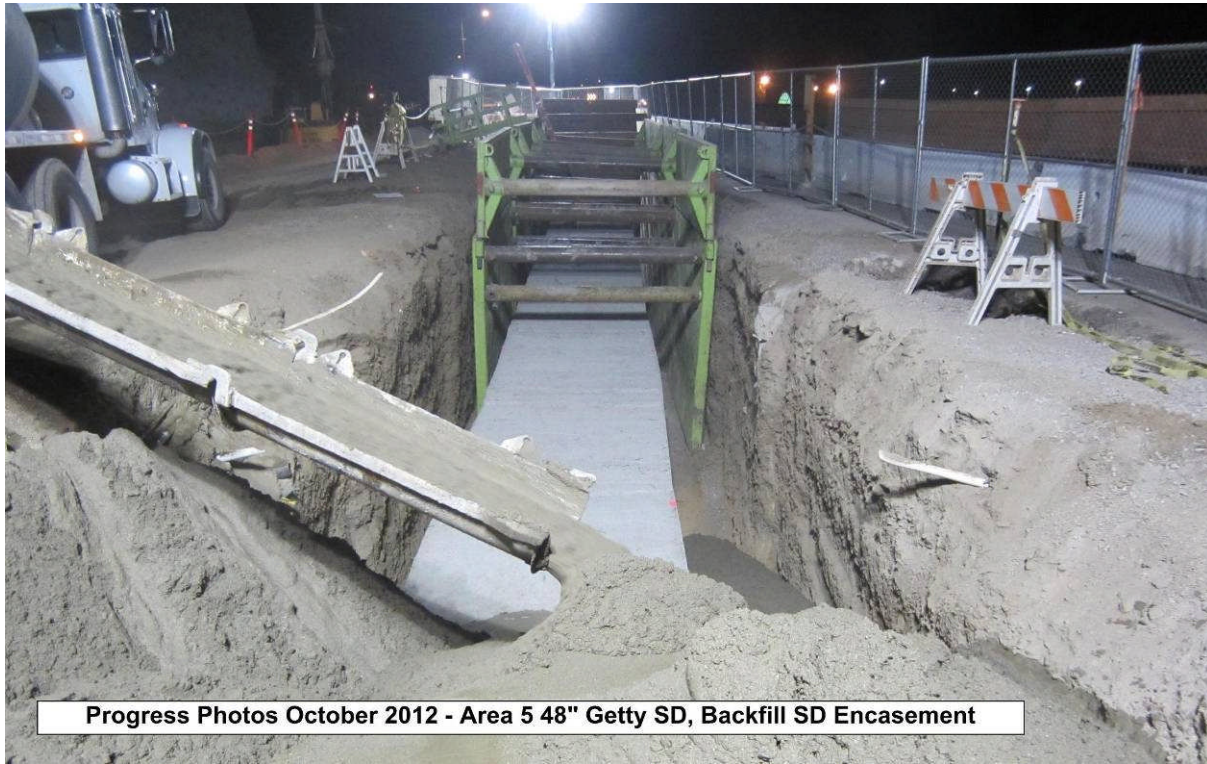

CONSTRUCTION PHOTOGRAPHS

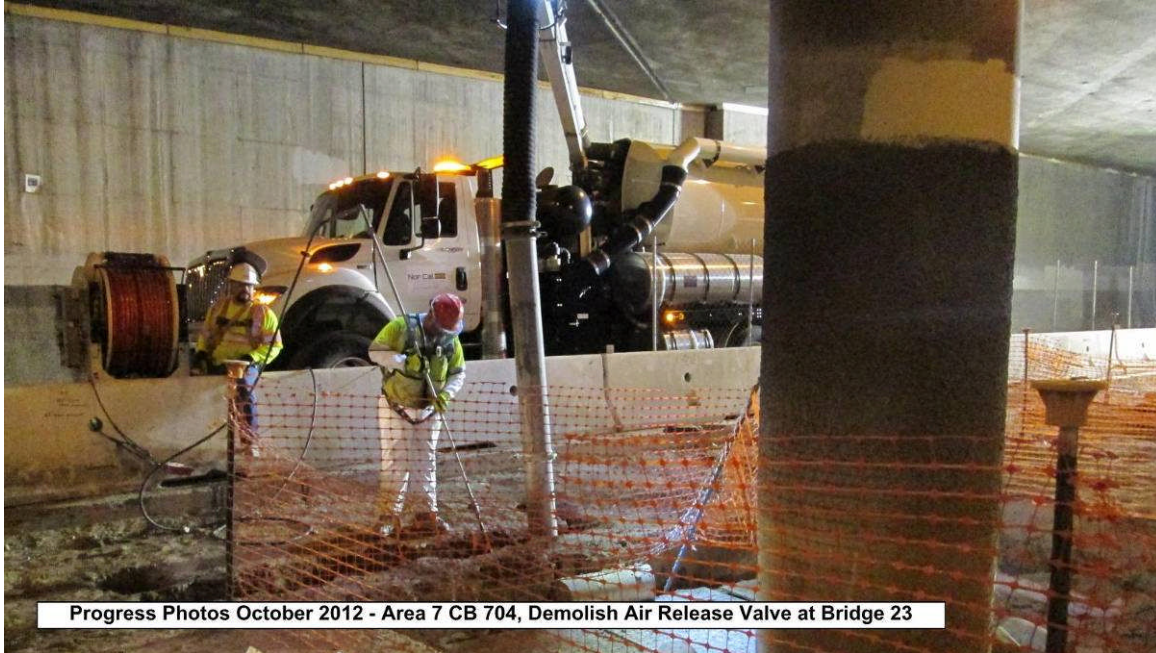

Progress Photos October 2012 - Area 7 CB 704, Demolish Air Release Valve at Bridge 23



Progress Photos October 2012 - CoLA Drainage Line 601 Form, Pour & Finish South of CB 601B

CONSTRUCTION PHOTOGRAPHS



Progress Photos October 2012 - UID 248 LADWP, Remove Beams and Backfill

APPENDICES

COST AND BUDGET TERMINOLOGY

APPROVED BUDGET: The Approved Project Budget as established by Metro Board of Directors at the time it authorizes Construction Project Management Division to commence full design and construction of the project (Project Adoption).

CURRENT BUDGET: The Original Budget plus all budget amendments approved by formal Metro action. Also referred to as Approved Budget.

CURRENT FORECAST: Evaluation of costs to go combined with actual expenditures.

COMMITMENTS: The total of actual contract awards, executed change orders or amendments, approved work orders of Master Cooperative Agreements, offers accepted for purchase of real estate, and other Metro actions which have been spent or result in the obligation of specific expenditures at a future time.

EXPENDITURES: The total dollar amount of funds expended by Metro for contractor or consultant invoices, third party invoices, staff salaries, real estate and other expenses that is reported in Metro's Financial Information System (FIS).

PROJECT APPROVAL & ENVIRONMENTAL DOCUMENTS: Costs for agency staff and consulting contracts leading to project approval and environmental clearances.

PLANS, SPECS. & ENGINEERING: Agency staff and consulting contract costs between the initial project approval and environmental clearances but prior to start of construction.

RIGHT-OF-WAY SUPPORT: Costs for agency staff involved in real estate appraisal and parcel purchase activities and agency staff costs involved in utility relocations and third party agreements. Includes real estate appraisal costs.

CONSTRUCTION SUPPORT: Agency staff and consulting contract costs occurring during the construction phase of the project.

CONSTRUCTION: Costs for highway construction, bridge and on/off ramp construction and modifications, retaining wall and sound wall construction. Includes final design costs by Design/Build Contractor.

RIGHT-OF-WAY CAPITAL: Costs for real estate parcel purchases and utility relocations costs after approval of utility company agreements. Includes costs for Master Cooperative Agreements after approval by agencies.

**APPENDIX
LIST OF ACRONYMS**

ARRA	American Recovery & Reinvestment Act
AWIS	Automated Work Zone Information Systems
CADD	Computer Aided Drafting and Design
CALTRANS	California Department of Transportation
CCTV	Closed Circuit Television
CD	Calendar Day
CDFG	California Department of Fish and Game
CEQA	California Environmental Quality Act
CM	Construction Manager
CMAC	Congestion Mitigation Air Quality
CMIA	Cash Management Improvement Act
CMS	Changeable Message Signs
CN	Change Notice
CO	Change Order
COE	Corps of Engineers
COLA	City Of Los Angeles
CPM	Critical Path Method
CPUC	California Public Utilities Commission
CR	Camera Ready
CTC	California Transportation Commission
D-B	Design-Build
D-B-B	Design-Bid-Build
DD	Design Development
DEIR	Draft Environmental Impact Report
DR	Deficiency Report
DWP	Department of Water and Power
EIR	Environmental Impact Report
EIS	Environmental Impact Statement
FD	Final Design
FEIR	Final Environmental Impact Report
FHWA	Federal Highway Administration
FIS	Financial Information System
FOCT	Fiber Optics Cable Transmission System
FTE	Full Time Equivalent
GDSR	Geotechnical Design Summary Report
GSA	General Services Administration
GSRD	Gross Solids Removal Devices
HAR	Highway Advisory Radio
HOV	High Occupancy Vehicle
IFB	Invitation for Bid
IPO	Integrated Project Office
ITS	Intelligent Transportation Systems

**APPENDIX
LIST OF ACRONYMS (Continued)**

LA	Los Angeles
LABOE	Los Angeles Bureau of Engineering
LACFCD	Los Angeles County Flood Control District
LADOT	Los Angeles Department of Transportation
LADPW	Los Angeles Department of Public Works
LADWP	Los Angeles Department of Water and Power
LARTMC	Los Angeles Regional Transportation Management Center
LFAT	Local Field Acceptance Test
LNTP	Limited Notice To Proceed
LONP	Letter Of No Prejudice
LOP	Life of Project
MCA	Master Cooperative Agreement
METRO	Los Angeles County Metropolitan Transportation Authority
MIS	Major Investment Study
MOT	Maintenance of Traffic
MPSR	Monthly Project Status Report
MSE	Mechanically Stabilized Earth
MVDS	Microwave Vehicle Detection System
MVP	Maintenance Vehicle Pullouts
MWD	Metropolitan Water District
N/A	Not Applicable
NCR	Non-Conformance Report
NEPA	National Environmental Quality Act
NHS	National Highway System
NOA	Notice of Award
NTE	Not to Exceed
NTP	Notice To Proceed
NTSC	National Television System Committee
P6	Primavera Project Planner® (scheduling software)
PC	Project Control
PE	Preliminary Engineering
PIP	Project Implementation Plan
PM	Project Manager
PMA	Project Management Assistance
PMP	Project Management Plan
P&P	Policies & Procedures
PR	Project Report
PS&E	Plans, Specs & Engineering
PSR	Project Study Report
QA	Quality Assurance
QAR	Quality Assurance Report

**APPENDIX
LIST OF ACRONYMS (Continued)**

QC	Quality Control
QPSR	Quarterly Project Status Report
RFC	Request For Change or Released for Construction (based on context)
RFP	Request For Proposal
RMS	Ramp Metering Systems
ROM	Rough Order of Magnitude
ROW	Right-Of-Way
SIT	System Integration Testing
RSTP	Regional Surface Transportation Program
RWQCB	Regional Water Quality Control Board
SAFETEA-LU	Safe, Accountable, Flexible, Efficient Transportation Equity Act: A Legacy for Users
SCE	Southern California Edison
SONET	Synchronous Optical Network
SOV	Schedule Of Value
SOW	Statement Of Work
SP	Special Provision
TBD	To Be Determined
TCRP	Traffic Congestion Relief Program
TMS/CS	Traffic Monitoring Stations/Count Stations
TPM	Transportation Management Plan
VE	Value Engineering
WBS	Work Breakdown Structure
WP	Work Package
