

Crenshaw/LAX Transit Project



Metro[®]

CRENSHAW/LAX TRANSIT PROJECT

MONTHLY PROJECT STATUS REPORT

THE PREPARATION OF THIS DOCUMENT HAS BEEN FINANCED IN PART THROUGH A GRANT FROM THE U. S. DEPARTMENT OF TRANSPORTATION, FEDERAL TRANSIT ADMINISTRATION (FTA).

MAY 2019

TABLE OF CONTENTS

	Page No.
Project Overview	1-5
Executive Summary.....	6-9
Project Update	
• Project Schedule	
○ Project Summary Schedule.....	10
○ Progress Summary.....	11
○ Planned vs. Actual Progress.....	11
○ Key Milestones Six-Month Look Ahead.....	12
○ Major Equipment Delivery Status.....	13
○ Critical Path	14
○ Project Schedule Contingency Drawdown.....	15
○ Risk Management Narrative.....	16
• Project Cost	
○ Project Cost Status & Analysis.....	17-18
○ Cost Contingency Drawdown and Analysis.....	19
○ Summary of Contract Modifications.....	20
Disadvantaged Business Enterprise (DBE)	21-22
Project Labor Agreement.....	23-24
Financial/Grant.....	25
Project Staffing	26-27
Real Estate	28
Quality Assurance.....	28
Environmental	28
Construction and Community Relations	29
Creative Services	29
Safety and Security.....	30
Appendices	
• Chronology of Events.....	31-32
• Project Cost Status – Southwestern Yard.....	33-34

PROJECT OVERVIEW

Project Background


The Crenshaw/LAX Transit Project is a north/south corridor that serves the cities of Los Angeles, Inglewood, Hawthorne and El Segundo as well as portions of unincorporated Los Angeles County. The alignment extends 8.5 miles, from the intersection of Crenshaw and Exposition boulevards to a connection with the Metro Green Line at the Aviation/LAX Station. The project provides major connections with the Los Angeles International Airport (LAX) as well as links to the Metro Green Line, the Exposition Line and countywide bus network.

Two additional stations, Leimert Park and Westchester/Veterans were funded by the City of Los Angeles and by Metro and were approved to be part of the project by the Metro Board in May 2013. The Metro Board in July 2014 and again in May 2015, approved a revision to the project alignment to include accommodations to the alignment at 96th street to not preclude a future light rail Metro Rail station being developed as part of the Airport Metro Connector (AMC) project. The accommodations included shifting the ultimate track configuration to the west side of the alignment to confine the revised track-work on Metro right-of-way to mitigate potential cost exposure. These accommodations are not funded by the Crenshaw/LAX Transit Project but are paid for by the AMC project.

The alignment is comprised of a double-tracked right-of-way consisting of sections of at-grade in-street, at-grade within railroad right-of-way, aerial, and below-grade guideway sections, eight stations, park and ride facilities at two locations, utilities, landscaping, roadway improvements required by the project and a maintenance & storage facility (Southwestern Yard).

The Project configuration is based on years of planning and environmental work that is reflected in the following milestones:

- Major Investment Study – 2003
- Metro Board approval of Alternative Analysis – December 2009
- Initiation of Preliminary Engineering – September 2010
- Metro Board certification of Final EIS/EIR – September 2011
- FTA issuance of Record of Decision – December 2011
- TIFIA and TIGER II Grants approved September 2012

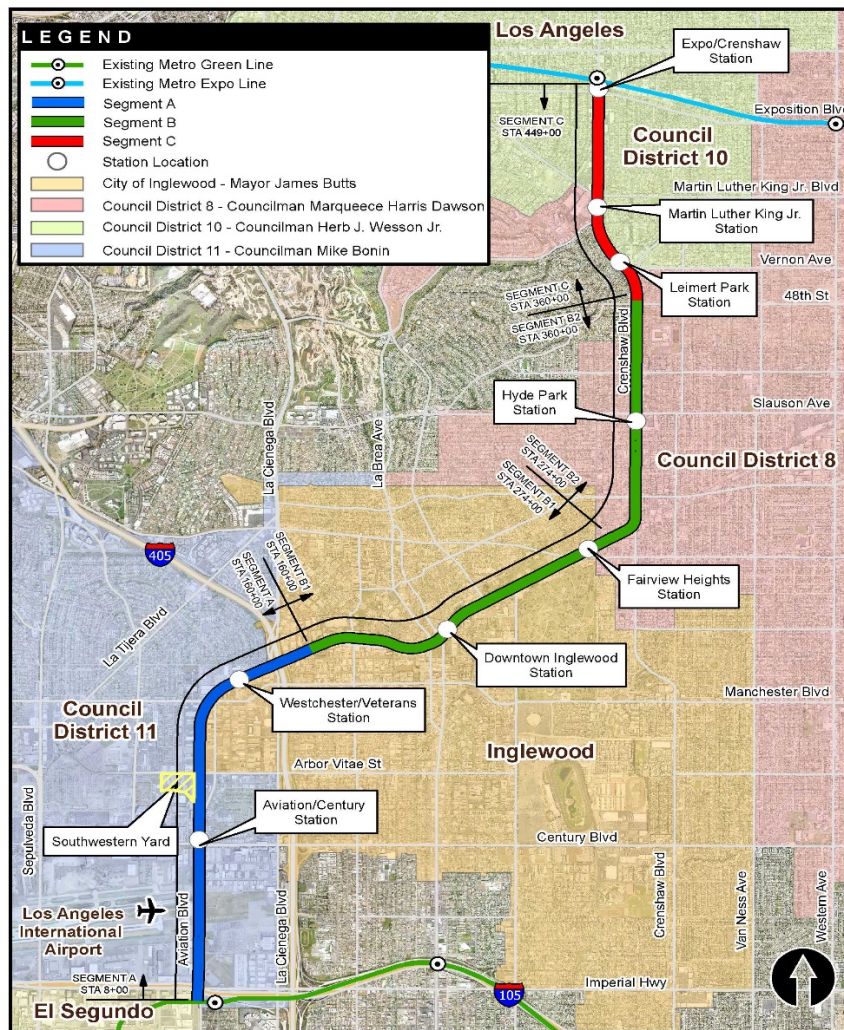

Major Procurements

Contract C0990 Crenshaw/LAX Advanced Utility Relocations

The design of several early utility relocations was advanced sufficiently into final design to allow for bidding of critical early utility relocations. This contract includes relocating three (3) existing duct banks that feed various NAVAIDS on the south airfield complex. New ductbank infrastructure will be built by Metro with the fiber replacement work and cut-over by FAA/LAWA. These ductbanks contain fiber lines and power lines which belong to both LAWA and FAA. Since the track alignment is below grade at these crossings, the ductbanks have to be relocated in advance to allow for the construction of the track alignment. In addition, other wet utilities along the Harbor Branch and Crenshaw Boulevard segments of the corridor that can be relocated in advance are included as part of this contract.

Design-Build Contract C0988 Crenshaw/LAX Transit Corridor

This is the largest project contract which completes final design and construction of the infrastructure required along the corridor alignment. The structures required to be constructed are eight stations, grade separations including flyover structures, cut and cover trenching, tunneling and three park-n-ride facilities. The scope of work will include all the necessary systems work including train control, traction power supply substations and distribution, overhead catenary, communications, and systems tie-in to the existing Metro Green Line. The project delivery method for this contract was design-build utilizing a two-step best value procurement approach with submittal of qualification statements through a RFQ process, prequalification of qualified proposers followed by release of a RFP soliciting technical and price proposals with an option at Metro's discretion for best and final offers (BAFO).

Design-Build Contract C0991 Southwestern Yard

The Board-adopted 2009 Long Range Transportation Plan (LRTP) for Los Angeles County envisioned one new central Light Rail Transit (LRT) Maintenance facility to be used by all projects. Since the LRTP adoption, substantial progress on light rail system planning and development, including more accurate vehicle assignments, cost estimates, and functional requirements, has led Metro to conclude that two new LRT yards, an Eastern Yard and a Southwestern Yard, are necessary. This contract will construct the Southwestern Yard which will consolidate maintenance facility requirements for this project as well as the operating Metro Green Line, proposed South Bay Metro Green Line Extension and proposed Metro Green Line to LAX.

Contract C0992 Crenshaw/LAX Concrete Ties and Assembly Items

Metro added a contract for procuring owner-supplied equipment for the Design-Build Contract C0988 Crenshaw/LAX Transit Corridor Contractor. The equipment within the contract scope of work includes concrete ties and assembly items.

Contract C0992A Crenshaw/LAX Rail and Bumping Posts Procurement

Metro added a contract for rebidding the procurement of running rail and bumping posts for the Design-Build Contract C0988 Crenshaw/LAX Transit Corridor Contractor including a bumping post for the Design-Build Contract C0991 Southwestern Yard.

Light Rail Vehicles

The Board approved exercising Option 1 of Contract P3010 with Kinkisharyo International (KI) to provide light rail vehicles (LRV) for the Crenshaw/LAX project. The total number of vehicles in the option is 28 which include 20 LRVs for the Crenshaw/LAX project and two additional cars for spares. The first Option 1 P3010 car was delivered in May 2017. The final P3010 car (22nd car) was delivered in September 2017, completing the Option delivery for the Crenshaw Project. All twenty-two Crenshaw cars are currently in revenue service on the Green and Blue Lines. KinkiSharyo/ASTS to work on the Cutover (revenue service) software development to include Crenshaw's final alignment, track profiles, and berthing locations. Once completed, a series of software validation tests will need to be performed prior to implementation on the P3010s.

Rail Operations Center (ROC)

The existing functional operations at the ROC are being expanded to accommodate the central control functions associated with five new rail lines including Crenshaw/LAX Project. The Project is contributing \$3.5 million towards this expansion which is scheduled to be completed in time for Crenshaw/LAX Project System Integration phase 2 testing (SIT-2), pre-revenue, safety drills and revenue service.

Fare Collection

A notice-to-proceed was issued on January 30, 2018 to the existing Metro Universal Fare System (UFS) contractor, Cubic Transportation Systems, to procure UFS equipment for the Crenshaw/LAX Project eight stations. The contractor commenced manufacturing of the equipment in February 2018 and completed manufacturing of the equipment and shipped to a local storage area where it is being stored until the Crenshaw/LAX Project stations become ready for its installation. UFS contractor and C0988 mainline contractor are coordinating access to stations.

Program Management

The WSCC contract is being managed by a team of Metro and consultant personnel jointly located at the Integrated Project Management Office (IPMO). Mott MacDonald provides engineering and design support services while Stantec, Inc., provides construction management support services. An overview of staffing is provided under the Staffing section of this report. The on-site program management team is also supported by Metro Headquarters resources to include, but not limited to, engineering, risk management, environmental, quality management, operations, and creative services departments.

Project Schedule and Budget:

The Revenue Service Date (RSD) is forecast for summer 2020.

In May 2013, the Metro Board approved a Motion that amended the fiscal year 2014 Proposed Metro Budget to include funding for an underground station at Leimert Park Village and an at-grade station at Hindry as part of the baseline project. This Motion added \$135 million to the LOP budget which included \$80 million in uncommitted fiscal year 2014 funding and \$55 million from the City of Los Angeles. Metro reached agreement with the City of Los Angeles to cover the incremental cost of the stations above the \$80 million identified in fiscal year 2014 funding which the Metro Board approved in May 2013.

With Metro Board approval on June 27, 2013, the additional \$135 million is included in the sources of funds chart as well as the additional \$160.1 million for the increased cost of the base work. All recommendations were approved by the Metro Board on June 27, 2013 except that change order authority was maintained at \$500,000. This board action amended the life of project budget to \$2,058 million.

The Metro Board approved on May 28, 2015, an increase in the amount of funding that the Crenshaw/LAX Project is contributing toward the total cost of the Southwestern Yard Project. An additional \$10.8 million is required to be funded by drawdown from the Unallocated Contingency Current Budget SCC 90 and added to the Southwestern Yard Current Budget SCC 30. The current budget includes the 49% cost allocation share that the project is responsible for paying which includes funding of the design and construction for the Southwestern Yard. This amount is revised to \$150.2 million out of a new total of \$307.2 million adopted by the Metro Board.

The amount of funding available for the Crenshaw/LAX Transit Corridor Project, excluding the Southwestern Yard \$150.2 million allocation and Environmental/Planning budget of \$26.0 million is \$1,881.8 million. Although there is no change to the Total LOP Current Budget there was a reallocation for changes to the SCC elements within the Current Budget in April 2017. The reallocation was required due to the drawdown to date of the SCC 90 Allocated Contingency for changes issued to the design-build contractor, additional relocations of utilities by third parties, additional legal services, and special service as well as an increase in professional services for construction and project management oversight.

Construction and Community Relations: The Construction and Community Relations team is tasked with promoting the Project and performing public outreach within the community to keep stakeholders informed of construction activities occurring along the Project alignment. To facilitate the communication, community leadership councils have been formed which represent geographic-based constituent groups along the Project.

The Project is also engaged in social media outreach and various marketing and advertising efforts designed keep the public informed and excited about the Project. These efforts are aimed at promoting businesses that are affected by construction.

System Integration:

The Project's integration of three separate lines, each possessing distinct system technologies, presents significant challenges for both the Project and Metro. The Project is coordinating the systems interface design, construction, testing, and commissioning while the Agency maintains revenue service on the operating lines.

Rail Activation:

The Project and Metro Operations recognize the extensive planning required in preparation for rail activation of the new regional light rail service the Project will enable through the south Los Angeles area. Associated detailed planning and scheduling efforts to optimize the extensive efforts are underway.

EXECUTIVE SUMMARY

As of the end of May 2019, the Project has achieved 92.6% completion based on earned value measurements for design and construction. The focus of the Project continues with facilitating critical path construction activities. Work is trending behind schedule due to the alignment contractor's progress. The following is an overview of current design and construction activities.

Design Status

Design - Build Contract C0988 (Mainline Contractor) – Walsh-Shea Corridor Constructors (WSCC) final design is complete except for designs required for changes. WSCC continues design and engineering in support of construction.

Design - Build Contract C0991 Southwestern Yard Contractor (Division 16) - Hensel Phelps/Herzog JV (HPH) has substantially completed final design. HPH continues design and engineering in support of Contract closeout.

Construction Status

Mainline Contractor - WSCC continues construction along all areas of the alignment. The four at-grade stations structure concrete placements are substantially complete and finish work continues for these stations. All six bridge superstructures are substantially complete and continuing with finishes, systems installations and testing. The aerial station structure concrete placement is substantially complete. The three underground stations remain at various levels of completion with emphasis on electrical, mechanical, systems and finish work inside the stations and entrance structures.

Trackwork is nearing completion with wayside and OCS/OCR work continuing along the alignment. System work continues in the stations for traction power, communication and train control. WSCC and Metro continue to coordinate with DWP and SCE for power energization and other utilities (water, gas, phone) at various locations.

Construction continues within the roadway section through Park Mesa Heights.

Southwestern Yard (Division 16) – HPH has achieved Substantial Completion as of January 30, 2019 and temporary certification of occupancy was issued on February 15, 2019. The contractor continues working on final punch list items required for completion of the contract. Metro continues the closeout process for this contract.

Cost and Schedule Summary

Metro issued in August 2018 a non-compensable unilateral change order to WSCC to extend their substantial completion milestone to December 11, 2019. Metro is evaluating a potential 2020 date for revenue service based on the revised substantial completion milestone date.

WSCC in late May 2019, submitted a schedule update for the February 2019 period of performance. This update indicated the contractor has forecast no change to the Substantial Completion date since the January 2019 schedule update. No schedule updates by WSCC have been submitted for the March 2019 thru May 2019 periods of performance. Metro is accessing the effect of delays on the Project’s schedule critical path.

The critical path of the Project remains completing construction activities, then systems wiring and commissioning of communications, train control, OCS/OCR installations and field acceptance testing. The critical path then flows through Systems Integration Testing (SIT), Phase I (by WSCC) and then SIT Phase II (by Metro), leading to pre-revenue services and revenue service.

WSCC Schedule Metrics – Mainline Contractor

	Original Contract Date/Duration	Time Extension (CD)	Current Contract Schedule	Forecast (Metro PMS Contractor)	Variance CD (Trending)
NTP	09/10/13				
Substantial Completion	09/08/18	459	12/11/19	1/31/20	51 days

HPH Schedule Metrics – Southwestern Yard Contractor

	Original Contract Date/Duration	Time Extension (CD)	Current Contract Schedule	Forecast (Metro PMS)	Variance CD (Trending)
NTP	06/29/15				
Substantial Completion	10/31/18	91	01/30/19	01/30/19 (Actual)	Completed

Project costs continue to track within budget and projected contingency limits. To date, the design and construction changes for WSCC related to base scope represent approximately 13% of the contract value with a potential to increase to 13.5%. For HPH, the changes represent 1.1% of the contract value with a potential to increase to 1.2%. Detailed cost and budget information is provided later in this report.

Key Management Concerns

No. 1: WSCC Construction Schedule Progress

Status/Action

Metro is evaluating a potential 2020 date for revenue service based on the revised WSCC Contract Substantial Completion Milestone date of December 11, 2019. The contractor's latest schedule submittal, February 2019, continues to reflect a 51-calendar's day slippage. No schedule updates by WSCC have been submitted for the March 2019 thru May 2019 periods of performance. Metro's assessment is that progress thru May 2019 is at least eight (8) weeks behind schedule.

Progress on construction activities continue to slip based on WSCC's weekly six-week look ahead schedule. Efforts to stop the continuous schedule slippage may include additional resources, selective overtime and weekend work. Coordination of field work needs to be strengthened in all areas of construction, including electrical, finishes, systems, motor control centers/communication interface cabinets, overhead catenary systems, overhead conductor rail, traction power, distributed power, train control installation, and testing.

No 2: Remaining Contingency is less than 2% of Total Project Budget.

Status/Action

Metro monitors and reports on the drawdown of contingency monthly. In May 2019 there was a drawdown of contingency of \$1.6 million which reduced remaining contingency to \$14.8 million. The remaining contingency is 0.7% of total project current forecast and 7.2% of total project cost-to-go.

Metro has identified funding available in fiscal year 2019 for specific scope of work that is eligible to be reallocated to a non-Crenshaw/LAX Project local funding source. Metro initiated in July 2018 reallocating the associated expenditures to date for this specific scope of work. This allows Metro to replenish a portion of the Crenshaw/LAX Project contingency. Through the end of May 2019, there has been \$67.9 million reallocated which allows the Project to use these funds for additional contractor modifications, increased third party requirements and professional services modifications to support a revised forecast completion schedule.


Project Construction Photos



AVIATION/CENTURY STATION - tactile paver installation along platform.



TUNNEL – Installation of emergency lighting at Southbound tunnel.

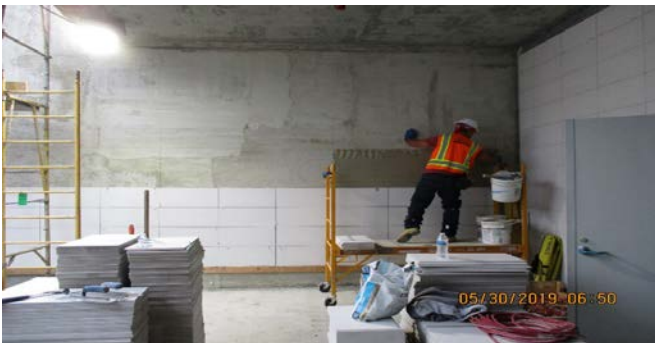

LEIMERT PARK STATION – Installation of ceramic tile at entrance stairs #1.



EXPOSITION/CRENSHAW STATION – Finishing coat at plaza walls.

PROJECT UPDATE

PROJECT SCHEDULE


Project Summary Schedule

Crenshaw/LAX Transit Corridor - Master Schedule May 2019		Crenshaw/LAX Level 1 Schedule		MASTER SCHEDULE MAY 2019														
Activity ID	Activity Name	Finish	Finish	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
Crenshaw/LAX Transit Corridor - Master Schedule May 2019				14-Jul-20														
Milestones & Key Dates				14-Jul-20														
Program Elements				12-Aug-19														
865512	Crenshaw/LAX	14-Jul-20																
C0990	Advanced Utility Relocation																	
C0992	Concrete Ties and Assembly Items																	
C0992A	Running Rail & Bumping Post																	
C0988	Pre-Construction Crenshaw/LAX	16-Mar-18																
C0988	Construction & Installation	14-Jul-20																
Sitework																		
	Stations	13-Dec-19																
	Guideway & Track	13-Sep-19																
	System-Wide Components	05-Nov-19																
	Systems	10-Dec-19																
	Testing	31-Jan-20																
	Substantial Completion	31-Jan-20																
	Start Up	14-Jul-20																
Pre - Revenue Operations																		
Revenue Service Summer of 2020																		
RSD	Revenue Service Summer of 2020																	
860003	Southwestern Yard and Paint Body Shop	30-Jan-19																
	Milestone	30-Jan-19																
	Preliminary Engineering	18-Dec-12																
	Right of Way	31-Oct-17																
	Design Build Procurement	29-Jun-15																
	Final Design	11-Jan-17																
	Construction & Installation	30-Jan-19																
◆	Milestone																	
▶	Remaining Work																	

Progress Summary



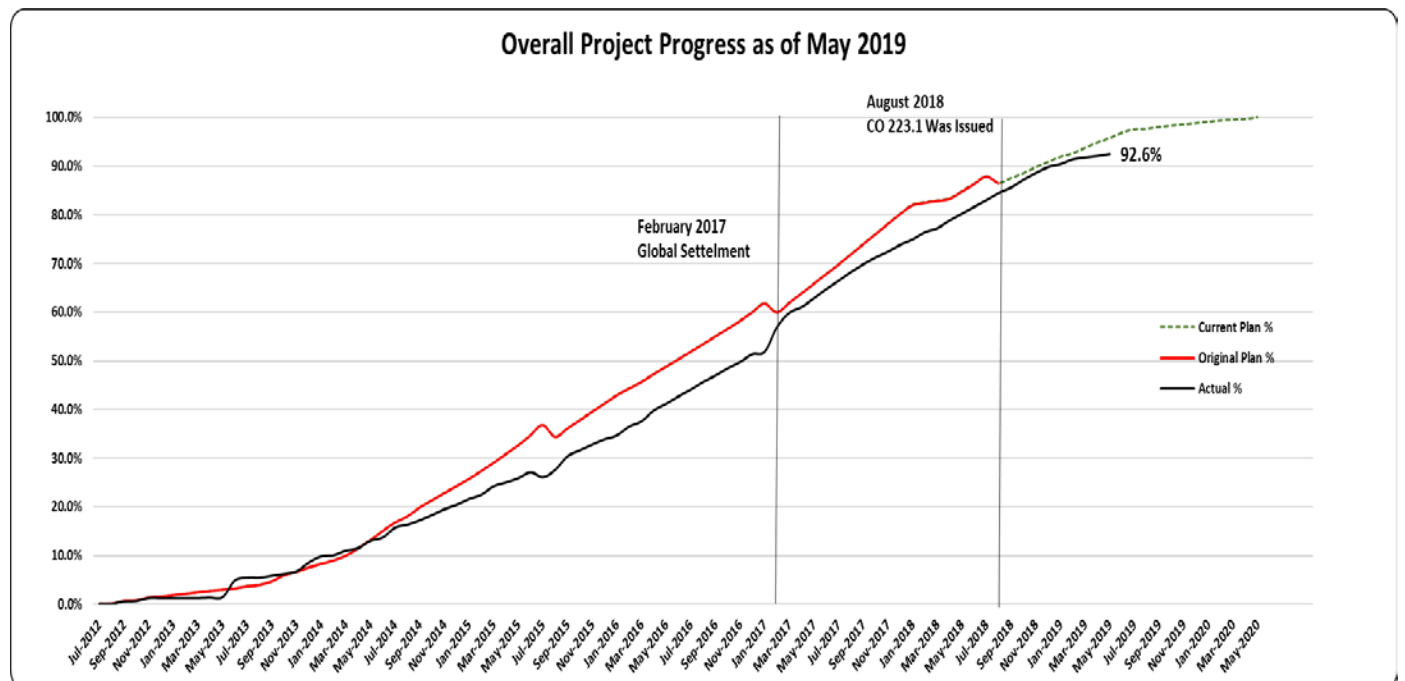





	Status	Change from Last Period	Comment
Current Revenue Service:	10/30/2019	0	
Forecast Revenue Service:	-	0	Revenue Service Summer of 2020
TIFIA Revenue Service:	10/30/2019	0	
Final Design Progress:			
Contract C0988	99.7%	0.0%	Design Services During Construction Behind Schedule
Contract C0990	100%	None	Design Completed
Contract C0991	100%	None	Design Services During Construction Completed
Contract C0992	100%	None	Design Completed
Contract C0992A	100%	None	Design Completed
Construction Contracts Progress:			
Contract C0988	88.2%	0.6%	Behind Schedule
Contract C0990	100%	None	Completed
Contract C0991	100%	None	Completed
Contract C0992	100%	None	Completed
Contract C0992A	100%	None	Completed

Planned vs. Actual Progress



Key Milestones Six Month Look Ahead

	Milestone Date	May-19	Jun-19	Jul-19	Aug-19	Sep-19	Oct-19
TPSS-01 Permanent Power Drop - SCE - Install Equipment, Cable, Energize & Monitor	5/1/19 A	▽					
Field Acceptance Testing & Start-up @ TPSS-01	5/13/19 A	⬡					
Milestone No. 2, Fare Collection System (FCS) Substantial Completion	5/31/19 A	⬡					
TPSS-03 Permanent Power Drop - SCE - Install Equipment, Cable, Energize & Monitor	06/30/19		▽				
TPSS-05 & 06 Permanent Power Drop - SCE - Install Equipment, Cable, Energize & Monitor	06/30/19		▽				
OCS Vehicle Required for Pre-Energization Tests PRE-SIT	07/11/19			⬡			
TPSS-08 Permanent Power Drop - SCE - Install Equipment, Cable, Energize & Monitor	07/15/19			▽			
Ventilation Equipment - UG #4 Installation and Testing	08/05/19				⬡		
Aux Power at 104th St - Permanent Power Drop - LADWP - Install Equipment, Cable, Energize & Monitor	09/09/19					⬡	
Complete Green Line Cut-Over (Weekend Closures)	09/23/19					⬡	
Radio Sytem LFAT UG4 and underground Stations	10/18/19						⬡
Ventilation Equipment - UG #3 Installation and Testing	10/30/19						⬡

 MTA Staff	 MTA Board Action	 FTA (Federal Transit Administration)	 Utility Company
 Other Agencies	 C0991 D/B Contractor	 Design Consultant	 C0988 D/B Contractor

"A" following date is actual and completed * New

**Crenshaw/LAX Transit Project
Monthly Project Status Report**

May 2019

Major Equipment Delivery


Metro Supplied Equipment

Equipment	Initial Procurement	Scheduled Delivery	Scheduled Installation
LRT Vehicles	(NTP) 8/20/12	Option 1 9/1/17	N/A
Ticket Vending Machines and Equipment	1/30/18	2/28/19 (Warehoused)	5/1/2020 (Prior to RSD)

Design - Builder Equipment Delivery Requirements


Activity Name	Early Finish	Need Date
Fab/Procure & Deliver Fans - UG #3	March 2019 A	April 2019
Fab/Procure & Deliver Fans - UG#4	March 2019 A	July 2019
Fab/Procure & Deliver Fans - UG #1	March 2019 A	August 2019
Fab/Procure & Deliver Emergency Ventilation Fans – Leimert Station	April 2019 A	June 2019
Fab/Procure & Deliver Emergency Ventilation Fans - MLK Station	May 2019 A	July 2019
Fab/Procure & Deliver Emergency Ventilation Fans - Expo. Station	July 2019	August 2019
Fabricate & Deliver Elevators - Aviation/Century Elevated Station	June 2019	June 2019
Fabricate & Deliver Elevators - Leimert Station	June 2019	June 2019
Fabricate & Deliver Elevators - MLK Station	July 2019	July 2019
Fabricate & Deliver Elevators - Expo. Station	July 2019	August 2019
Fabricate, Test & Deliver MCC's - Leimert Station	March 2019 A	June 2019
Fabricate, Test & Deliver MCC's - MLK Station	March 2019 A	June 2019
Fabricate, Test & Deliver MCC's - Expo Station	June 2019	July 2019
Fabricate, Test & Deliver MCC's - 104 th Street	August 2019*	April 2019*
Fabricate, Test & Deliver MCC's - Victoria/60 th Street	August 2019*	May 2019*
*Requires schedule mitigation by Mainline Contractor		

Critical Path

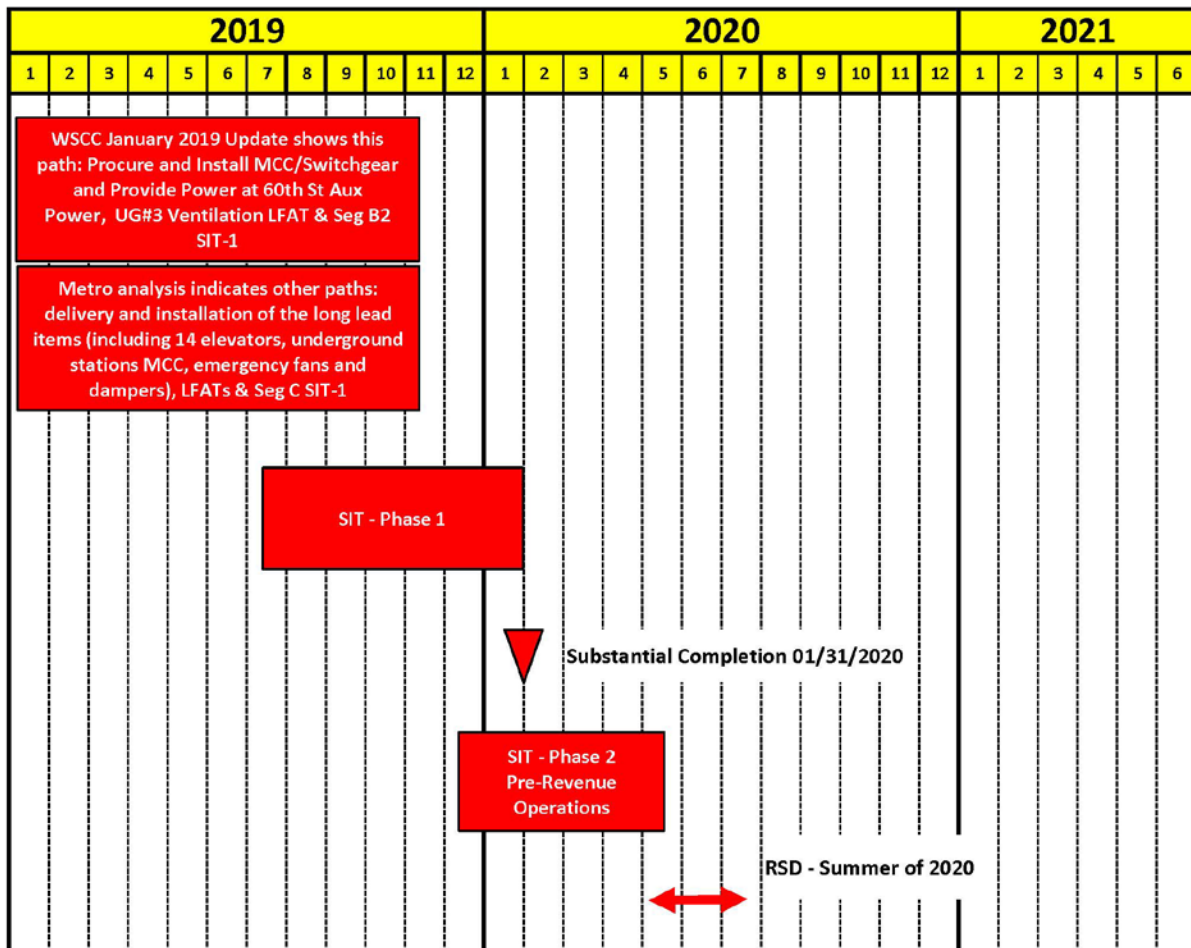

The critical path of the Project remains completing construction activities, then systems wiring and commissioning of communications, train control, OCS/OCR installations and field acceptance testing. The critical path then flows through Systems Integration Testing (SIT), Phase I (by WSCC) and then SIT Phase II (by Metro), leading to pre-revenue services and revenue service.

Project Schedule Contingency Drawdown

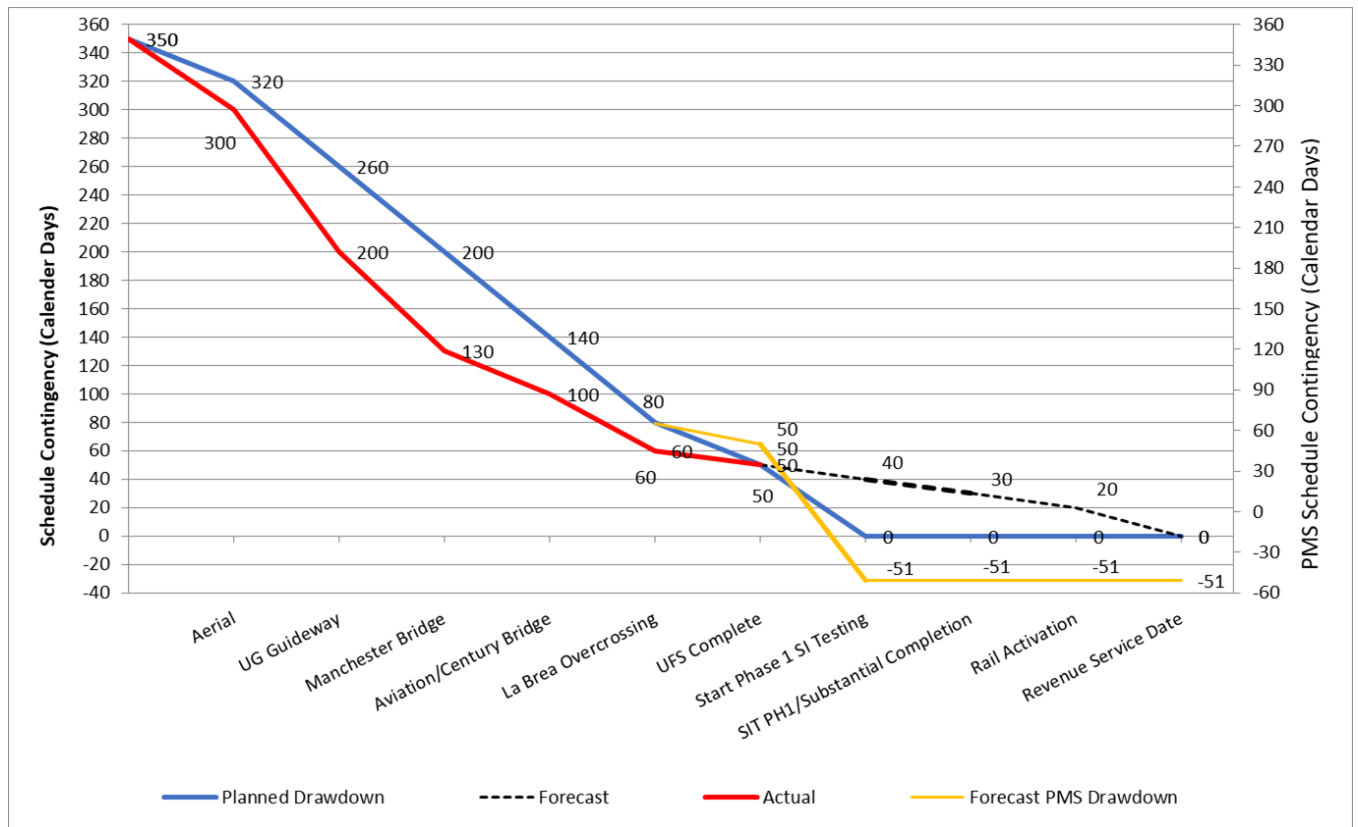

Metro issued in August 2018 a non-compensable unilateral change order to WSCC to extend their substantial completion milestone to December 11, 2019. Thus, performance measurement is now tracked against this new date.

The contractor last schedule update submitted was for period as of February 2019. They reported they are behind schedule, but more delays reported in this period. Metro assessment is that WSCC is behind schedule by at least 51 calendar days.

Metro is evaluating a potential 2020 date for revenue service based on the revised substantial completion milestone date.

Risk Management Narrative

Summary of Risks

Within this reporting two risks were closed, and no new risks were identified. There is a total of thirty-five (33) risks to be managed in the next reporting period.

Of the thirty-five (35) risks, seven (7) are scored as high (10 to 25 risk rating), ten (10) as medium (4 to 9 risk rating), and eighteen (18) as low (Less than 4 risk rating).

Top 7 Risks

The table below shows the top project risks:

Risk ID	SCC	Risk Description	Risk Rating
369	50	Continued delay of fire rated conduit/cable installation. WSCC is falling behind in completing work as scheduled and potential cost and claim.	25
124	50	Main Line testing prior to pre-revenue operations may take longer than expected, resulting in increased Main Line Metro and Consultant costs and potential delay to December 11, 2019 - Substantial Completion.	18
359	40	Extended Overhead or productivity loss claims exposure not covered by cost impacts in individual risks.	18
362	30	Schedule activities that are critical to completion (Trackwork, OCR/OCS, TPSS Energization, Emergency Fans installation, Train Control wiring/testing and Communications equipment installation/wiring/testing).	16
355	50	Issues with long lead delivery or improper planning for integration, testing and startup of Communication systems.	12
277	50	SCADA interface between ROC & field installations could impact Metro's SIT2. Workforce issue to perform testing.	11
354	50	Issues with energization of traction power. DWP and Edison Issues	11

Newly Identified Risks

- No new risks were added to the risk register.

Closed Risks

- Two risks were closed in this period.

Risk Score Changes

- No risks score were changed in this period.

Actions in Next Reporting Cycle

Continuous efforts in Risk Management will be made through the following actions:

- Update the project risk register.

PROJECT COST

Project Cost Analysis

SCC CODE	DESCRIPTION	ORIGINAL BUDGET	CURRENT BUDGET		COMMITMENTS		EXPENDITURES		CURRENT FORECAST		CURRENT BUDGET/ FORECAST VARIANCE
			PERIOD	TO DATE	PERIOD	TO DATE	PERIOD	TO DATE	PERIOD	TO DATE	
10	GUIDEWAYS	471,335,000	-	450,354,375	(5,918,151)	440,747,649	(3,646,713)	428,095,678	(5,921,172)	440,747,649	(9,606,726)
20	STATIONS	153,906,000	-	315,050,000	-	310,284,580	2,677,567	263,267,414	-	310,284,580	(4,765,420)
30	SUPPORT FACILITIES SOUTHWEST YARD	66,673,000	-	71,164,000	-	67,338,361	116,687	65,480,521	(795,639)	67,338,361	(3,825,639)
40	SITWORK/SPECIAL CONDITIONS	235,576,000	-	395,798,361	618,191	401,801,377	(4,718,838)	343,705,604	(6,039,817)	401,801,377	6,003,016
50	SYSTEMS	125,132,000	-	169,436,000	3,849,946	174,831,167	4,403,067	119,734,161	-	174,831,167	5,395,167
	CONSTRUCTION SUBTOTAL (10-50)	1,052,622,000	-	1,401,802,736	(1,450,015)	1,395,003,135	(1,168,230)	1,220,283,378	(12,756,627)	1,395,003,135	(6,799,601)
60	RIGHT-OF-WAY	132,294,000	-	127,490,000	83,840	132,045,286	16,275	131,794,629	68,081	132,045,286	4,555,286
70	LRT VEHICLES	87,780,000	-	83,571,544	1,413,483	83,571,544	-	78,832,400	-	83,571,544	-
80	PROFESSIONAL SERVICES	273,147,000	-	368,734,466	22,572,674	406,604,497	4,474,160	356,811,252	14,312,351	406,604,518	37,870,053
	SUBTOTAL (10-80)	1,545,843,000	-	1,981,598,746	22,619,982	2,017,224,462	3,322,206	1,787,721,660	1,623,805	2,017,224,484	35,625,737
90	UNALLOCATED CONTINGENCY	177,157,000	-	50,401,254	-	-	-	-	(1,623,805)	14,775,516	(35,625,737)
	TOTAL PROJECT 865512 (10-100)	1,723,000,000	-	2,032,000,000	22,619,982	2,017,224,462	3,322,206	1,787,721,660	-	2,032,000,000	-
	ENVIRONMENTAL/PLANNING - 405512	5,526,150	-	5,526,150	-	5,526,150	-	5,526,150	-	5,526,150	-
	ENVIRONMENTAL/PLANNING - 465512	20,473,850	-	20,473,850	-	20,022,881	-	20,022,881	-	20,473,850	-
	TOTAL PROJECTS 405512 & 465512 (ENV / PLAN'G)	26,000,000	-	26,000,000	-	25,549,031	-	25,549,031	-	26,000,000	-
	TOTAL PROJECTS 405512, 465512 & 865512	1,749,000,000	-	2,058,000,000	22,619,982	2,042,773,493	3,322,206	1,813,270,691	-	2,058,000,000	-

1. Expenditures are Cumulative through May 31, 2019.

2. Expenditures exclude \$6.6 million for State Board of Equalization (SBOE) decision to tax LRT Vehicle deliveries since August 2016. Metro is appealing the decision by the SBOE but paid tax so as not to incur any late fees.

3. Expenditures exclude \$5.5 million for various right-of-way and professional services costs that are being reallocated to other local funding.

The project numbers 405512, 465512, 865512 and 860003 are internal to Metro and are used to differentiate between environmental/planning and construction components of the project.

Original Budget:

The Board in October 2011 established the Life-of-Project (LOP) Original Budget of \$1,749 million for the Crenshaw/LAX Transit Project.

Current Budget:

There have been two increases in the total LOP Current Budget to date:

- The Board in December 2012 approved an increase of \$13.9 million for a new LOP Current Budget total of \$1,762.9 million. The Unallocated Contingency Standard Cost Category (SCC) 90 budget line item was increased by the \$13.9 million for a new total of \$191.1 million.
- The Board in June 2013 approved an increase of \$295.1 million for a new LOP total of \$2,058.0 million. The total increase was based on two actions:
 - Increase LOP base project scope in the amount of \$160.1 million, and
 - Increase LOP to include the options for Crenshaw/Vernon Station (Leimert Park Village) and Florence/Hindry Station in the amount of \$135.0 million.
- The Board in May 2015 approved an increase in the amount of funding that the Crenshaw/LAX project is contributing toward the total cost of the Southwestern Yard Project. An additional \$10.8 million was drawdown from the Unallocated Contingency Current Budget SCC 90 and added to the Southwestern Yard Current Budget SCC 30. The Current Budget includes the 49% cost allocation share that the project is responsible for paying which includes funding of the design and construction for the Southwestern Yard. This amount was revised to \$150.2 million.

The \$150.2 million is spread among the SCC 30, 40, 60, 80 and 90 in the Cost Report by Element table above. A project cost status chart depicting the LOP Current Budget for the Southwestern Yard Project is included in the appendix section of this report. The Current Budget allocation for Crenshaw/LAX Transit Project only, excluding the Southwestern Yard Project \$150.2 million 49% allocation and the Environmental/Planning Current Budget of \$26.0 million, is \$1,881.8 million.

Although there is no change to the Total LOP Current Budget there was a reallocation for changes to the SCC elements within the Current Budget in April 2017.

Commitments:

Commitments increased by \$22.6 million this period to \$2,042.8 million which represents 99.3% of the current budget. The total increase is related to design-build Contract C0988 Crenshaw/LAX Transit Corridor, real estate relocation and professional services. The total commitments include \$150.2 million for the Southwestern Yard 49% allocation.

Expenditures:

Expenditures increased by \$3.3 million this period to \$1,813.3 million which represents 88.1% of the current budget. The increase is for costs associated with design-build Contract C0988 Crenshaw/LAX Transit Corridor, Contract C0991 Division 16: Southwestern Yard, real estate relocation and professional services. The cumulative expenditures to date include \$144.6 million for the Southwestern Yard 49% allocation. In addition, \$8.3 million in expenditures were reallocated to another project thus reducing the actual expenditures for the period.

Current Forecast:


The total current forecast remains the same as the total current budget.

Non-Crenshaw/LAX Transit Project Funded Scope of Work

The costs shown in the table below are not part of Crenshaw/LAX Transit Project costs but are funded by other Metro projects using the services of the alignment design-builder (Contract C0988).

C0988 NON-CRENSHAW/LAX TRANSIT PROJECT FUNDED SCOPE OF WORK									
DESCRIPTION	CURRENT BUDGET		COMMITMENTS		EXPENDITURES		CURRENT FORECAST		FORECAST VARIANCE
	PERIOD	TO DATE	PERIOD	TO DATE	PERIOD	TO DATE	PERIOD	TO DATE	
405556 SYSTEMWIDE TRANSIT PLANNING	-	320,035	-	320,035	-	320,035	-	320,035	-
210090/93 FARE GATE PROJECT	-	2,566,226	-	2,566,226	-	2,081,126	-	2,566,226	-
210152 CRENSHAW/LAX BUS TRANSFER FACILITY	-	2,200,000	-	2,200,000	-	403,334	-	2,200,000	-
460303 AIRPORT METRO CONNECTOR	-	37,914,465	-	37,047,674	-	36,935,066	-	37,914,465	-
500013 C/LAX LAWA SCOPE OF WORK	-	1,575,362	-	1,114,613	-	545,439	-	1,575,362	-
405522 HIGHWAY PLANNING	-	1,935,000	-	1,935,000	-	719,503	-	1,935,000	-
TOTAL	-	46,511,088	-	45,183,548	-	41,004,503	-	46,511,088	-

Cost Contingency Drawdown

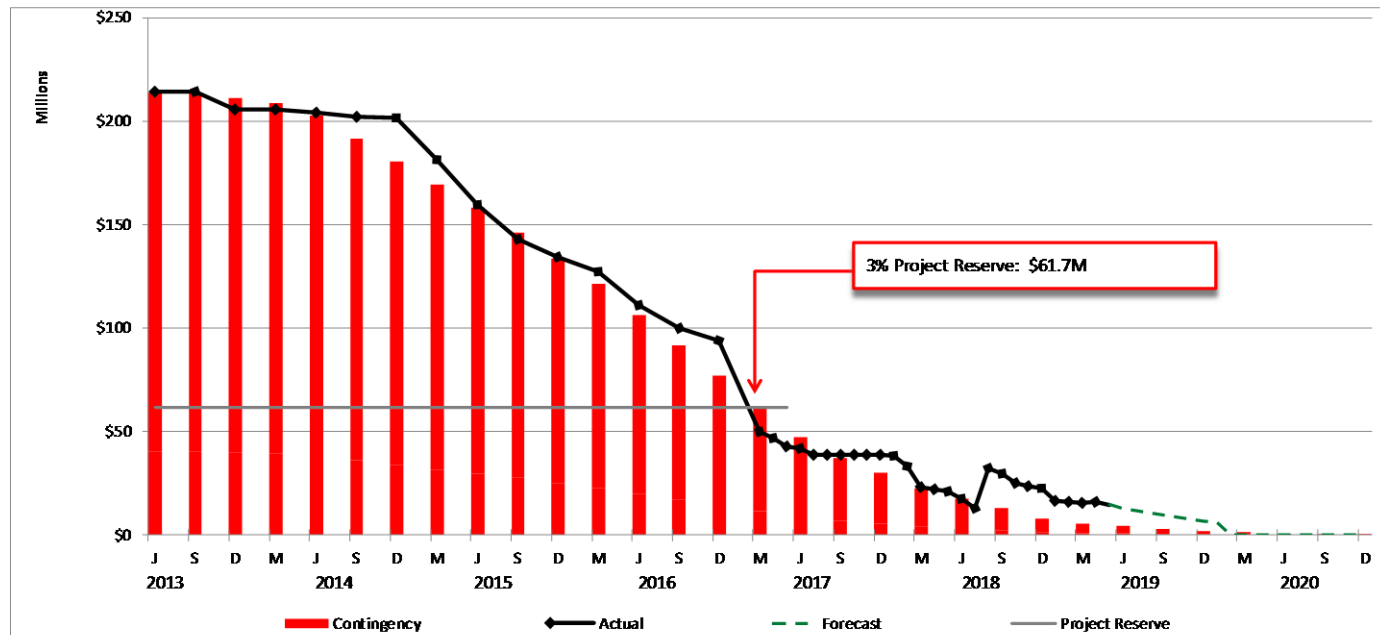

Cost Contingency Drawdown Analysis

The project current budget of \$2,058,000,000 includes a contingency amount of \$213,866,792. The drawdown plan is correlated to anticipate risk trends and measures drawdowns moving forward.


Included in the project contingency drawdown is a 3% project reserve threshold. The Board is to be notified when it becomes necessary to drawdown contingency below the project reserve line to cover project costs. This notification request was adopted by the Metro Board of Directors in September 2012. In February 2017, the project contingency drawdown curve went below the 3% project reserve level and the Board was notified.

This month, \$1,623,805 was drawn down from contingency. The remaining total project contingency (allocated and unallocated) is \$14,775,515.

PROJECT COST CONTINGENCY (through 31-May-2019)					
UNITS IN DOLLARS					
	Original Contingency	Previous Period	Current Period	To-Date	Remaining Contingency (Forecast)
Unallocated Contingency	173,500,000	(157,100,680)	(1,623,805)	(158,724,485)	14,775,515
Allocated Contingency	40,366,792	(40,366,792)	-	(40,366,792)	-
Total Contingency	213,866,792	(197,467,472)	(1,623,805)	(199,091,276)	14,775,515

SUMMARY OF CONTRACT MODIFICATIONS

Contract Modifications (MODs) by Cost Level

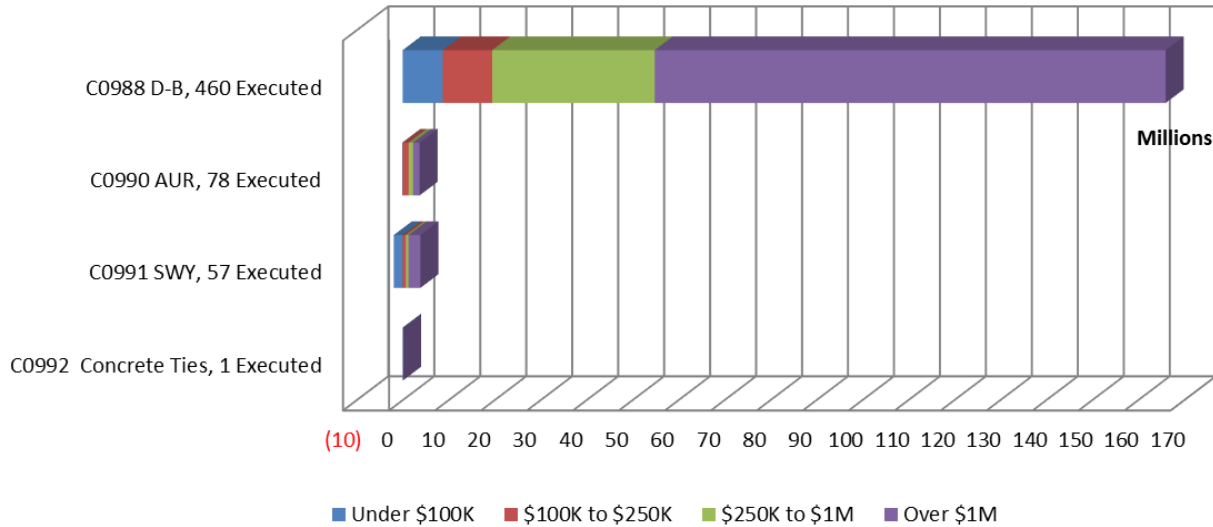

	C0988	C0990	C0991	C0992	Total
	460 Executed	78 Executed	57 Executed	1 Executed	
Under \$100K	\$ 8,724,541	\$ (70,251)	\$ (1,918,854)	\$ 81,738	\$ 6,817,174
\$100k to \$250K	\$ 10,747,534	\$ 1,280,184	\$ 674,625	\$ -	\$ 12,702,342
\$250K to \$1M	\$ 35,365,777	\$ 984,662	\$ 590,334	\$ -	\$ 36,940,773
Over \$1M	\$ 111,145,950	\$ 1,417,202	\$ 2,590,000	\$ -	\$ 115,153,152
Total Contract MODs	\$ 165,983,801	\$ 3,611,797	\$ 1,936,105	\$ 81,738	\$ 171,613,441
Contract Award Amount	\$ 1,272,632,356	\$ 7,827,500	\$ 172,312,695	\$ 2,161,297	\$ 1,454,933,848
% of Contract MODs	13.04%	46.14%	1.12%	3.78%	11.80%

Four hundred and sixty (460) changes with a total value of \$165.98 million have been executed since award of Contract C0988. There are an additional thirty-six (36) changes with a total value of \$0.50 million pending the administrative approval process.

Seventy-eight (78) changes with a total value of \$3.61 million have been executed for completed Contract C0990.

Fifty-seven (57) changes with a total value of \$1.94 million have been executed since award of Contract C0991. There are an additional two (2) changes with a total value of \$0.20 million pending the administrative approval process.

One (1) change with a value of \$81,738 was executed for completed Contract C0992.

Percent of Contract modifications equals the total Change modifications divided by the Contract Award amount

DISADVANTAGED BUSINESS ENTERPRISE (DBE)

Contract C0988 Crenshaw/LAX Transit Corridor Design-Build

(Reported Data as of May 2019)

- **DBE Goal (Design)** – A numerically expressed percentage of funds apportioned to Design Contracts and is calculated based upon the relative availability of DBE firms as compared to all firms in the relevant geographic market area. **20.00%**
- **Current DBE Commitment** – Total DBE Committed Dollars divided by Total Contract Value for Design or Construction. **\$25,157,579 (20.00%)**
- **Current DBE Participation** – Total amount paid to date to DBEs divided by the amount paid to date to Prime. **\$29,434,375 (23.97%)**

Twenty-Six (26) Design subcontractors have been identified to-date

- **DBE Goal (Construction)** - A numerically expressed percentage of funds apportioned to Construction Contracts and is calculated based upon the relative availability of DBE firms as compared to all firms in the relevant geographic market area. **20.00%**
- **DBE Commitment** - Contract commitment divided by current contract value for Construction **\$259,865,769 (20.00%)**
- **Current DBE Commitment** - Actual commitments as Construction work is awarded **\$279,102,905 (21.48%)**
- **Current DBE Participation** - Total amount paid to date to DBEs divided by the amount paid to date to Prime **\$292,847,324 (26.19%)**

309 Construction subcontractors have been identified to-date.

DISADVANTAGED BUSINESS ENTERPRISE (DBE)

Contract C0991 Division 16: Southwestern Yard Design-Build

(Reported Data as of April 2019)

- **DBE Goal (Design)** – A numerically expressed percentage of funds apportioned to Design Contracts and is calculated based upon the relative availability of DBE firms as compared to all firms in the relevant geographic market area. **20.00%**
- **Current DBE Commitment** – Total DBE Committed Dollars divided by Total Contract Value for Design or Construction. **\$2,467,837 (20.93%)**
- **Current DBE Participation** – Total amount paid to date to DBEs divided by the amount paid to date to Prime. **\$2,438,118 (21.17%)**

Ten (10) Design subcontractors have been identified to-date

- **DBE Goal (Construction)** - A numerically expressed percentage of funds apportioned to Construction Contracts and is calculated based upon the relative availability of DBE firms as compared to all firms in the relevant geographic market area. **16.00%**
- **DBE Commitment** - Contract commitment divided by current contract value for Construction. **\$25,930,837 (16.00%)**
- **Current DBE Commitment** - Actual commitments as Construction work is awarded **\$32,838,720 (20.26%)**
- **Current DBE Participation** - Total amount paid to date to DBEs divided by the amount paid to date to Prime **\$31,177,629 (20.55%)**

Ninety-six (96) Construction subcontractors have been identified to-date

PROJECT LABOR AGREEMENTS (PLA)
Contract C0988 Crenshaw/LAX Transit Corridor Design-Build

(Reported Data as of April 2019)

- | | |
|--|---------------|
| • Targeted Worker Goal – Construction work to be performed by residents from Economically Disadvantaged Area of LA County | 40.00% |
| • Targeted Worker Current Attainment | 60.09% |
| • Apprentice Worker Goal – Construction work to be performed by Apprentices | 20.00% |
| • Apprentice Worker Current Attainment | 23.37% |
| • Disadvantaged Worker Goal – Construction work to be performed by Disadvantaged Workers whose primary place of residence is within LA County | 10.00% |
| • Disadvantaged Worker Current Attainment | 12.07% |

PROJECT LABOR AGREEMENTS (PLA) STATUS

Contract C0991 Division 16: Southwestern Yard Design-Build

(Reported Data as of April 2019)

- **Targeted Worker Goal** – Construction work to be performed by residents from Economically Disadvantaged Area of LA County **40.00%**
- **Targeted Worker Current Attainment** **49.51%**
- **Apprentice Worker Goal** – Construction work to be performed by Apprentices **20.00%**
- **Apprentice Worker Current Attainment** **29.89%**
- **Disadvantaged Worker Goal** – Construction work to be performed by Disadvantaged Workers whose primary place of residence is within LA County **10.00%**
- **Disadvantaged Worker Current Attainment** **10.23%**


FINANCIAL/GRANT

SOURCE	(A)	(B)	(C)	(D)	(D/B)	(E)	(E/B)	(F)	(F/B)
	ORIGINAL BUDGET	TOTAL FUNDS ANTICIPATED	TOTAL FUNDS AVAILABLE	COMMITMENTS \$	%	EXPENDITURES \$	%	BILLED to \$	FUNDING SOURCE %
FEDERAL - CMAQ	68.2	104.0	54.0	104.0	100%	54.0	52%	54.0	52%
FEDERAL - SECTION 5309 BUS CAPT	8.6	8.6	8.6	8.6	100%	8.6	100%	8.6	100%
FEDERAL - REGIONAL STP	20.0	99.9	99.9	99.9	100%	91.2	91%	91.2	91%
FEDERAL - ALTERNATIVE ANALYSIS	1.2	1.2	1.2	1.2	100%	1.2	100%	1.2	100%
FEDERAL - TIGER II	0.0	13.9	13.9	13.9	100%	13.9	100%	13.9	100%
STATE REGIONAL IMPROVEMENT PROG	36.5	36.6	26.3	36.6	100%	26.3	72%	26.3	72%
STATE PPM	0.178	0.178	0.178	0.178	100%	0.178	100%	0.178	100%
STATE PROP 1B PTMISEA	201.2	129.0	129.0	129.0	100%	129.0	100%	129.0	100%
STATE PROP 1 B LOCAL PARTNER PROG	0.0	49.5	49.5	49.5	100%	49.5	100%	49.5	100%
MEASURE R - TIFIA LOAN	545.9	545.9	545.9	545.9	100%	545.9	100%	545.9	100%
MEASURE R	661.1	529.3	529.3	529.3	100%	449.5	85%	449.3	85%
CITY CONTRIBUTION	52.4	101.7	101.7	86.5	85%	44.3	44%	44.3	44%
GENERAL FUNDS	0.0	54.3	54.3	54.3	100%	54.3	100%	54.3	100%
PROP C 25% HIGHWAY	148.9	379.1	379.1	379.1	100%	340.5	90%	340.2	90%
PROP C 40% DISCRETIONARY	0.0	0.0	0.0	0.0	0%	0.0	0%	0.0	0%
PROP A 35% RAIL CAPITAL	4.8	4.9	4.9	4.9	100%	4.9	100%	4.9	100%
TOTAL	1,749.0	2,058.0	1,997.7	2,042.8	99.0%	1,813.3	88.0%	1,812.7	88.0%

NOTE: Expenditures are cumulative through May 31, 2019
 Original Budget based on Board approved October 2011 Funding/Expenditure Plan
 Expenditures exclude \$6.6 Million for State Board of Equalization decision to tax LRT vehicle deliveries since August 2016.
 Metro is appealing decision but paid taxes to not include late fees.
 Expenditures exclude \$5.5 Million for various right-of-way and professional services cost being reallocated to other funding.


PROJECT ORGANIZATION AND STAFFING

The design-build contract is being managed by joint team of Metro and consultant personnel jointly located at the Integrated Project Management Office (IPMO).

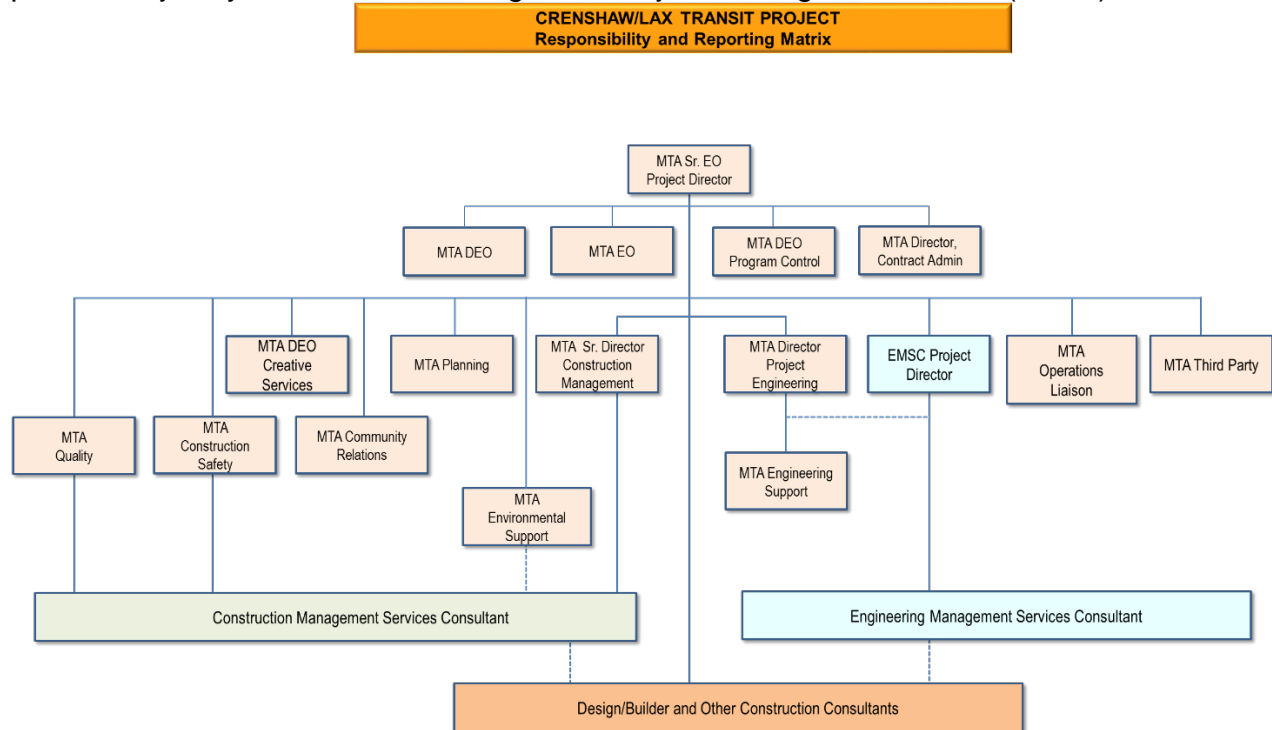


The overall FY19 Total Project Staffing Plan averages 106.5 Full Time Equivalent (FTEs) per month consisting of 53.5 for Metro Agency staff, 45.5 for Construction Management Support Services Consultant and 7.6 for Design and Engineering Support Services Consulting staff.


For May 2019, total project staffing were 109.3 FTEs for the month consisting of 49.2 FTEs for Metro’s project administration staff, 50.7 FTEs for Construction Management Support Services Consultant and 9.4 FTEs for Design and Engineering Support Services Consulting staff.

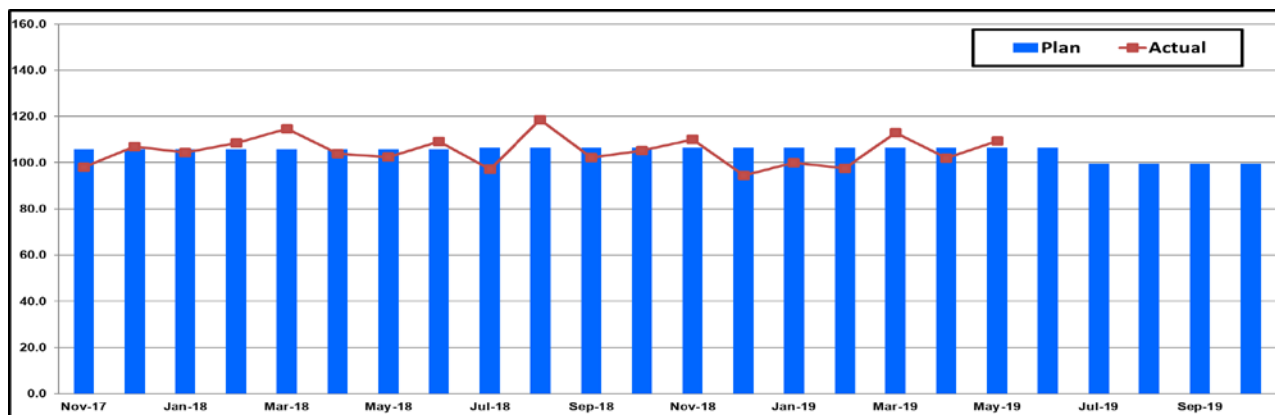


Metro Staff

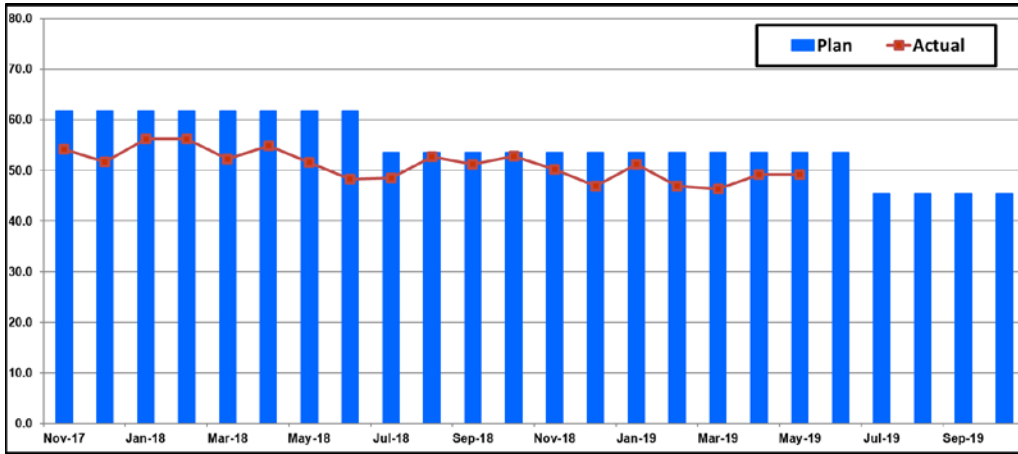

CM Support Services Staff (Consultant)

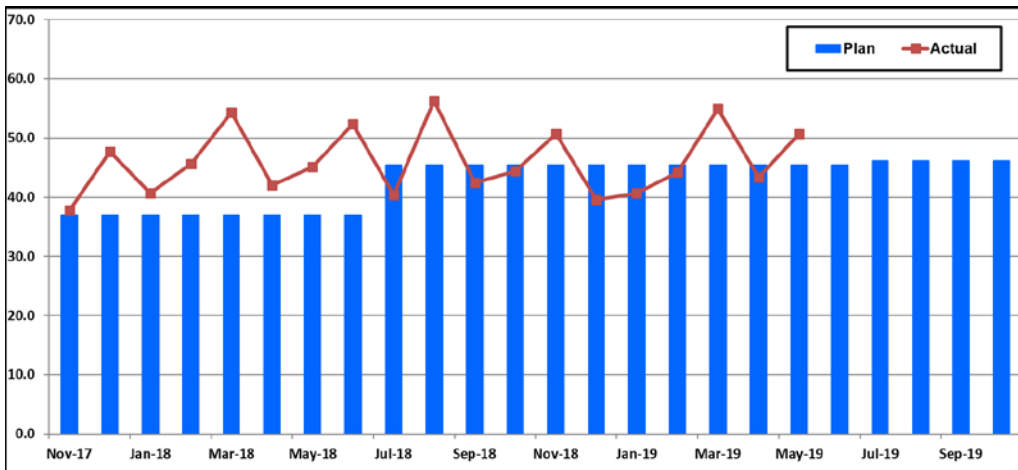

Engineering Services Staff (Consultant)

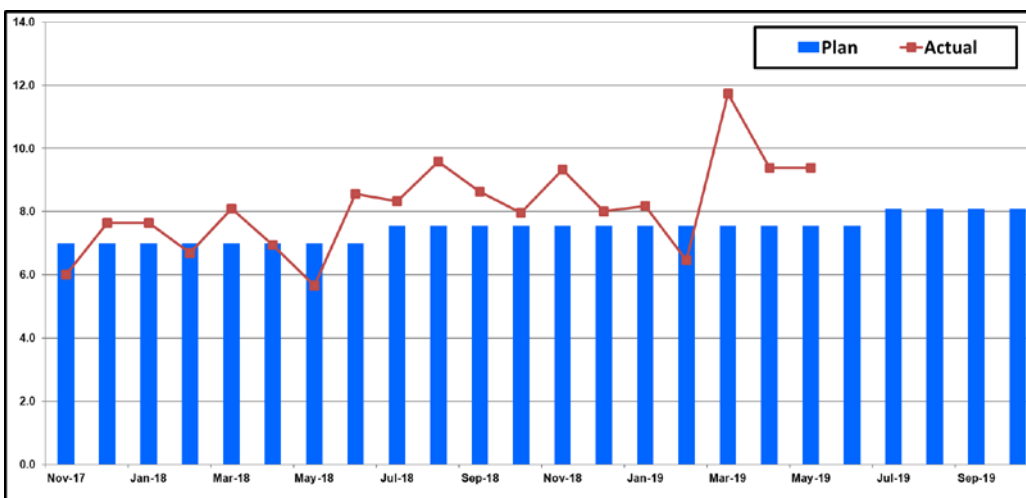

Staffing by Group

The opposing graphs represent planned vs. actual staffing levels by group.

Metro staffing includes full time staff located in the IPMO as well as part-time support located at Gateway Headquarters.

Staffing plans are developed for each fiscal year based on project needs.

REAL ESTATE

- Metro is working on extending some temporary construction easements due to revised construction schedule.
- Work requiring the last remaining parcel does not fall under WSCC's scope of work and will be constructed under a separate contract. *Relocations for this parcel should be complete by end of June 2019.*

QUALITY ASSURANCE

C0988 Crenshaw/LAX Transit Corridor Design Build

- *WSCC issued six Non-Conformance Reports (NCR'S) during the month.*
- Attended weekly Quality Team Meetings with WSCC Lead Quality personnel and City of Los Angeles Bureau of Contract Administration (ConAd).
- Participated in Readiness Review Meeting for Installation of Oil Water Separator and UG Stations Elevator Steel.
- Participated in Underground Structures Weekly Construction Performance, Systems Meeting and Technical Meetings.
- No Inspections scheduled for Metro's Independent Testing Lab (ITL).
- *Visited EW Shop (Total Industries Yard) for the elevator frame structure welding work.*

ENVIRONMENTAL

C0988 Crenshaw/LAX Transit Corridor Design Build

- Noise and vibration spot checks continue to be conducted weekly at multiple sensitive locations and at locations of new activities along the project alignment.
- SWPPP inspections of all project areas are conducted weekly by WSCC and spot checks by Metro to observe site conditions and report on performance of stormwater protection Best Management Practices and overall housekeeping.
- *Conducted an EMS and Environmental Compliance Progress Meeting on 5/8/19 and 5/22/19.*
- *There were no encounters with contaminated or hazardous materials this month.*

CONSTRUCTION RELATIONS

- Continued working with WSCC to minimize the impacts of lane and street closures along the Crenshaw/LAX alignment.
- Circulated public notice for project construction activities. The notices are distributed via-email, social media networks and hand delivered to key stakeholders.
- Continue to provide directional signage for businesses impacted by ongoing construction activities.
- Ongoing coordination with WCSS and Metro Bus Operations to plan for bus detour routes to accommodate lane reductions and closures.
- Continued outreach to stakeholders in the LAX area regarding ongoing construction activities.
- Continued face to face outreach to key stakeholders and community organizations along the alignment.

CREATIVE SERVICES

- Facilitated artist reviews of fabrication submittals by contractor for porcelain enamel steel artworks.
- *Reviewed fabricator shop drawings for porcelain enamel steel art panels.*
- *Completed site inspections of artwork locations for glass mosaic murals at underground stations.*
- *Attended comment resolution meetings for the Platform Edge Light Mock-up.*
- *Reviewed and provided comments for C/LAX lighting submittals.*

SAFETY AND SECURITY

- Conducted Monthly All Hands Safety and Security Meetings with WSCC to discuss narratives for Cal/OSHA ventilation for all three station boxes and tunnels, security /vandalism and ROW protection, track allocation, Teamwork and Partnering and Access and Egress.
- Monitored construction activities daily including weekends to ensure compliance with contract specifications.
- Participated in Safety Briefings/Safety Huddles at EXPO, MLK and Vernon Stations.
- Contract C0991 Hensel Phelps Project to date completed 518,946 work hours with 3 recordable injuries. Hensel Phelps and their subcontractors completed 14,113 work hours and zero (0) recordable injuries for the month of January 2019.
- Hensel Phelps submitted a Notice of Substantial Completion to Metro on January 30, 2019. They continued to work on punch list items.
- Total Days Away (DART) Injury Rate: Six (6) Days Away from Work (DART) Injuries is 0.1. The National Ave is 1.7.
- Project to Date – Total Days Away Rate (561 Days Away from Work) is 17.1. No National Published Rate.
- *Contract C0988 (WSCC) completed 126,648 work hours with one recordable injury for the month of May 2019. Total Project to Date work hours is 8,241,865 with a total of ninety-three (93) recordable incidents. The Project Recordable Rate is 2.25. The Bureau of Labor Statistics (BLS) average recordable rate per 200,000 work hours is 2.8.*

CHRONOLOGY OF EVENTS

October 2011	Board approved the Life-of-Project Budget of \$1.749 billion.
December 30, 2011	Received Record of Decision from FTA.
March 12, 2012	Received Statement of Qualifications for Contract C0988 C/LAX Transit Corridor.
May 30, 2012	Awarded Contract No. C0990 C/LAX Advanced Utility Relocations to Metro Builders and Engineers Group LTD.
May 23, 2013	Board amended the Agency's FY14 Proposed Budget to include funding of \$80 million for an underground station at Leimert Park Village as part of the baseline project.
June 27, 2013	The Board awarded Contract C0988 Crenshaw/LAX Transit Corridor to Walsh-Shea Corridor Constructors.
September 10, 2013	Issued Notice to Proceed to Walsh-Shea Corridor Constructors, Contract C0988 Crenshaw/LAX Transit Project.
December 5, 2013	The Board approved Memorandum of Understanding with the Los Angeles World Airports for a parallel design and possible construction modifications near Aviation/Century Station to accommodate elements of LAWA's SPAS.
December 5, 2013	The Board awarded Contract C0992 with Rocla Concrete Tie, Inc; for the procurement of concrete ties and assembly items.
January 21, 2014	A Groundbreaking Ceremony was held at the Crenshaw/Exposition Station.
January 23, 2014	The Board awarded Contract C0992A Rail and Bumping Posts to LB Foster Rail Technologies Corp.
August 21, 2014	Substantial Completion issued for Advanced Utility Relocations Contract C0990.

CHRONOLOGY OF EVENTS (Continued)

May 28, 2015	The Board awarded Contract C0991 Division 16: Southwestern Yard to Hensel Phelps/Herzog JV. Also increased by \$22.0 million the Life of Project Budget for the Southwestern Yard Project to a new amount of \$307.2 million.
May 28, 2015	The Board approved Design Option 3 for the track alignment to accommodate the future Metro Connector Transit Station (96 th St. Station).
June 29, 2015	Issued Notice to Proceed to Hensel Phelps/Herzog JV, Contract C0991 Division 16: SouthwesternYard.
April 27, 2016	The Tunnel Boring Machine was launched and drilling from north to south of the alignment started.
May 7, 2016	Held Halfway There Community Celebration at Leimert Park marking the halfway point of the project.
May 27, 2016	Held Groundbreaking Ceremony for the Southwestern Yard (Division 16).
April 6, 2017	The northbound tunnel boring machine completed mining with the hole thru at Leimert Park Station.
June 15, 2018	Restoration of the road over the three underground stations along Crenshaw Blvd. commenced at Leimert Park Station area and the at-grade transition section.
January 30, 2019	Substantial completion was achieved by the Southwestern Yard (Division 16) Contract C0991 Contractor, Hensel/Phelps/Herzog JV.

PROJECT COST STATUS – SOUTHWESTERN YARD

SCC CODE	DESCRIPTION	ORIGINAL BUDGET	CURRENT BUDGET		COMMITMENTS		EXPENDITURES		CURRENT FORECAST		FORECAST VARIANCE
			PERIOD	TO DATE	PERIOD	TO DATE	PERIOD	TO DATE	PERIOD	TO DATE	
10	GUIDEWAYS	0	0	0	0	21,997	0	21,997	0	21,997	21,997
20	STATIONS	0	0	0	0	0	0	0	0	0	0
30	SUPPORT FACILITIES (Y & S)	85,546,835	0	85,189,999	0	85,691,329	(49,000)	85,664,357	0	85,691,329	501,330
40	SITWORK/SPECIAL CONDITIONS	35,932,000	0	38,273,000	200,577	40,009,941	422,144	37,070,576	(595,062)	40,009,941	1,736,941
50	SYSTEMS	25,784,616	0	32,991,000	58,462	34,392,804	300,582	32,714,541	58,462	34,392,804	1,401,804
	(10-50) CONSTRUCTION	147,263,451	0	156,453,999	259,039	160,116,071	673,726	155,471,470	(536,600)	160,116,071	3,662,072
60	RIGHT-OF-WAY	99,910,000	0	100,000,000	0	102,420,623	(1,395)	102,417,215	0	102,420,623	2,420,623
70	VEHICLES	0	0	0	0	0	0	0	0	0	0
80	PROFESSIONAL SERVICES	35,601,095	0	33,639,631	4,192,489	42,646,822	572,142	36,141,309	2,329,678	42,646,822	9,007,191
90	PROJECT CONTINGENCY	13,659,732	0	17,106,370	0	0	0	0	(1,793,078)	2,016,483	(15,089,887)
TOTAL		296,434,278	0	307,200,000	4,451,528	305,183,517	1,244,473	294,029,994	0	307,200,000	0

C0991 PAINT & BODY SHOP PROJECT											
DESCRIPTION	ORIGINAL BUDGET	CURRENT BUDGET		COMMITMENTS		EXPENDITURES		CURRENT FORECAST		FORECAST VARIANCE	
		PERIOD	TO DATE	PERIOD	TO DATE	PERIOD	TO DATE	PERIOD	TO DATE		
861301 DIV 22 PAINT & BODY SHOP	11,000,000	0	11,000,000	0	11,000,000	0	10,321,826	0	11,000,000	0	
GRAND TOTAL	307,434,278	0	318,200,000	4,451,528	316,183,517	1,244,473	304,351,820	0	318,200,000	0	

NOTE: EXPENDITURES ARE CUMULATIVE THROUGH MAY 31, 2019.

The project number 865512, 860003 and 861301 are internal to Metro and are used to differentiate between various components of the project.

Original Budget:

The Board in May 2015 established the Life-of-Project (LOP) budget of \$307.2 million for the Southwestern Yard Project.

Current Budget:

The Board in May 2015 approved an increase for the funding for the Southwestern Yard by \$22.0 million to increase the LOP budget to \$307.2 million to allow for the award of design-build Contract C0991 Southwestern Yard Project. Of the total \$307.2 million, \$150.2 million is funded in the Crenshaw/LAX Transit Project LOP budget which includes the original 49% allocation amount of \$139.4 million plus a new \$10.8 million reduction from the Crenshaw/LAX Transit Project contingency line item in the budget. There is no increase in the LOP for the Crenshaw/LAX Transit Project. The original 51% share associated with future Green Line related extensions in an amount of \$145.8 million was increased by \$11.2 million for a new total of \$157.0 million.

In addition to the \$307.2 million there is another \$11.0 million that is the budget for the paint and body shop, under another Metro internal cost project number, which funding was approved by a prior agreement for a paint and body shop to support the Green Line shops and was required for the award of the design-build Contract C0991 Southwestern Yard Project.

The grand total of the combined budget is \$318.2 million.

Current Forecast:

The current project forecast is \$318.20 million and remain the same as total current budget.

Commitments:

The commitments are cumulative through May 31, 2019. The total commitments increased by \$4.45 million to \$316.18 million to date represents 99.37% of the current budget. The increase is for commitments associated with change order issued to design-build contractor and FIS adjustment to professional services.

Expenditures:

The expenditures are cumulative through May 31, 2019. The total expenditures increased by \$1.24 million to \$304.35 million which represents 95.65% of the current budget. The increase is for cost associated with design-build contract C0991 Division 16: Southwestern Yard and project administration, construction management support and labor compliance.
