



Metro

Metropolitan Transportation Authority

One Gateway Plaza
Los Angeles, CA 90012-2952

213.922.2000 Tel
metro.net

November 22, 2021

TO: Distribution

FROM: Mat Antonelli *MA 11/22/21*
Project Manager

SUBJECT: Regional Connector Transit Project
October 2021 Monthly Project Status Report

Enclosed is the Monthly Project Status Report for the Regional Connector Transit Project. This report contains the Los Angeles County Metropolitan Transportation Authority's (LACMTA) representation of the Regional Connector Transit Project status for the period ending October 29, 2021.

If you have any questions regarding this report or its supporting information, please contact Dan Estrada, Deputy Executive Officer of Program Control at (213) 893-7130.

Enclosure

Los Angeles County
Metropolitan Transportation Authority

Regional Connector Transit Project

MONTHLY PROJECT STATUS REPORT

October 2021



Metro[®]

REGIONAL CONNECTOR TRANSIT PROJECT

MONTHLY PROJECT STATUS REPORT

THE PREPARATION OF THIS DOCUMENT HAS BEEN FINANCED IN PART THROUGH A GRANT FROM THE U. S. DEPARTMENT OF TRANSPORTATION, FEDERAL TRANSIT ADMINISTRATION (FTA).

October 2021

TABLE OF CONTENTS

Project Overview	1
Executive Summary	5
Project Update	10
Project Schedule.....	10
Progress Summary.....	11
Planned vs. Actual Progress.....	11
Key Milestones Six-Month Look Ahead	12
Major Equipment Delivery.....	12
Project Cost	13
Project Cost Analysis.....	13
Cost Contingency Drawdown and Analysis	15
Summary of Contract Modifications.....	16
Disadvantaged Business Enterprise (DBE)	17
Project Labor Agreement	17
Financial/Grant	18
Project Staffing.....	19
Real Estate	21
Quality Assurance.....	22
Environmental	23
Construction and Community Relations.....	24
Creative Services	25
Safety and Security	26
Appendix.....	27
Chronology of Events	

PROJECT OVERVIEW

Project Background

The Regional Connector Transit Project (Project) will link the terminus of the Blue and Expo Lines at 7th/Metro Center to the Gold Line near the current Little Tokyo/Arts District Station through a new 1.9-mile underground alignment in downtown Los Angeles. The alignment includes three underground stations: Grand Av Arts/Bunker Hill; Historic Broadway; and Little Tokyo/Arts District.

From the existing 7th Street/Metro Center Station, the Project alignment will extend north under Flower Street to 2nd Street. It will then proceed east underneath 2nd Street to just west of Central Avenue where the alignment will veer northeast under privately held property to the new Little Tokyo/Arts District Station at 1st and Central. The alignment continues briefly eastward through a Wye Junction (Wye) constructed beneath the 1st and Alameda intersection. To the north of the Wye at Temple and Alameda, and to the east of the Wye at 1st and Vignes, trains will connect with the Gold Line by rising to the surface through two new transition portals heading north to Pasadena, and east to East Los Angeles.



Upon completion, the Project will in effect facilitate regional light rail service along a 49-mile north-south route – Azusa to Long Beach, and a 23-mile east-west route – East LA to Santa Monica.

Passenger forecasts in 2035, as a result of the improved service, indicate 90,000 daily transit trips will occur through the 1.9-mile downtown trunk, including 17,000 new riders.

The above Project configuration is based on years of planning and environmental work that is reflected in the following milestones:

- Metro Board approval of Alternative Analysis – January 2009
- Initiation of Draft EIS/EIR – February 2009
- Initiation of Preliminary Engineering (PE) – January 2011
- Metro Board certification of Final EIS/EIR – April 2012
- FTA issuance of Record of Decision – June 2012
- PE and Advanced PE complete – March 2013
- FTA award of Full Funding Grant Agreement – February 2014.

Major Procurements

Utility Relocation: Advanced Utility Relocation Contract C0981R was awarded to Pulice Construction, Inc. in January 2014, and the Notice to Proceed (NTP) issued on February 18, 2014. Contract C0981R was terminated for convenience on April 14, 2015, and remaining AUR work was transferred to the C0980 Design/Build (D/B) Contractor.

Guideway & Systems Contract: The Board authorized to solicit a major D/B contract, C0980, in August 2011. A contract was awarded on April 24, 2014, to Regional Connector Constructors (RCC), a joint venture of Skanska USA Civil West California District, Inc. and Traylor Brothers, Inc. in the amount of \$927,226,995. NTP was issued July 7, 2014. The final engineering and design for the joint venture was performed by Mott McDonald.

Vehicles: Metro procured four (4) Light Rail Vehicles (LRVs) for the Project. The vehicles were built and delivered by Kinkisharyo International, LLC under Option 2 of Contract P3010. Delivery and acceptance of four LRVs occurred late 2020.

Rail Operations Center (ROC): The existing functional operations at the ROC are being expanded to accommodate the central control functions associated with five new rail lines to include Regional Connector. The Project is contributing \$4.4M towards this expansion (representing a \$400k forecast increase in May 2021). The ROC expansion is scheduled to be complete by December 2021.

Fare Collection: Procurement of Universal Fare System and Ticket Vending Machine equipment was completed in January 2018 with award to Cubic Corporation. Metro is coordinating with RCC for installation and testing schedules, which are now expected to begin in 4th Quarter 2021.

Program Management

The RCC contract is being managed by a team of Metro and consultant personnel jointly located at the Integrated Project Management Office (IPMO). The consultant component is comprised of The Connector Partnership, a joint venture between AECOM, Inc. and WSP (CPJV) which provides engineering and design support services while Arcadis, Inc., provides construction management support services. An overview of management staffing of these consultants is provided under the Staffing Section of this report. The on-site program management team is also supported by Metro Headquarters resources to include, but not limited to, engineering, risk management, environmental, quality management, operations, and creative services departments.

Project Schedule and Budget: The Revenue Service Date (RSD) is planned for Fall 2022.

In January 2017, the Metro Board revised the Life of Project (LOP) Budget for Regional Connector Transit Project 860228 to \$1.756 billion. The LOP budget for Concurrent Non-FFGA activities related to Project 861228 was increased to \$59.4 million in January 2021. Financing costs are estimated at \$14M. Cost forecasts remain consistent with budgets. A detailed FFGA budget forecast is included under the Project Cost Section of this report.

Funding has been secured from a variety of sources, detailed in the Financial/Grant Section on Page 18, to include:

- Federal New Starts Grant
- Federal Congestion Management Air Quality and RIP Programs
- State Proposition 1A/1B and Capital Project Loan proceeds
- City of Los Angeles
- Lease revenues.

Construction and Community Relations: The Construction and Community Relations Team is tasked with promoting the Project and performing public outreach within the communities to keep stakeholders informed of construction activities occurring along the Project alignment. To facilitate the communication, community leadership councils have been formed which represent geographic-based constituent groups along the alignment.

The Project is also engaged in social media outreach and various marketing and advertising efforts designed to keep the public informed and supportive of the Project. These efforts are aimed at promoting businesses that are affected by construction. An overview of monthly activities is presented in the Construction and Community Relations Section on Page 24.

System Integration: The Project's integration of three separate lines, each possessing distinct system technologies, presents significant challenges for both the Project and Metro at-large. Extensive planning continues to be performed to define logistics of the systems' cut overs that will be required. The Project continues to coordinate the completed systems interface design, with active installation of devices and systems, as well as testing as Metro maintains revenue service on the three operating lines.

Rail Activation: The Project and Metro Operations recognize the extensive planning required in preparation for rail activation of the new regional light rail service the Project will enable through downtown Los Angeles. The training of 400+ operators and supervisors across the regions has surfaced as a key component to rail activation. This training will require dedicated time during rail activation to ensure safety.

Planning efforts have outlined a sequence of dependent testing, training, simulation, and safety certification. Detailed review of each element leading to start-up is underway. These reviews include recent developments related to bifurcating the substantial completion and the procurement related to modifications at the ROC. Interface between Project Management, Operations and Fire Life Safety representatives will intensify to ensure an integrated and timely approach is realized.

EXECUTIVE SUMMARY

In *October*, the Project achieved 87.1% completion based on earned value measurements for design and construction. The focus of the Project is to continue with systems, mechanical and electrical installations, station finishes, and planning and installation of artwork at stations while the last of structural concrete and trackwork are active over the next several months. The following is an overview of current design and construction activities.

Design Status

Miscellaneous design changes to approved design packages continue to be managed as Engineering Change Instructions (ECI). ECIs enable required changes to be promptly addressed while the balance of the scope is built.

Construction Status

1st Street Cut & Cover Tunnel & U-Channel: Completed *LVT track installation at the Right tunnel and U-Channel*. Continued *emergency walkway installation*. Started LVT track installation at the *Left U-Channel*.

Wye Structure: Completed *Wye Fan Plant exterior and interior walls, roof deck and delivery of emergency ventilation fans*. Continued installation of the Right Hand #5 turnout, diamond special track, and curved rail installation at Alameda Left Track. Continued installation of Load Break and Motorized Disconnect Switches at the Wye Disconnect Room. Started *backfill* at the Wye Fan Plant.

Alameda Street Cut & Cover Tunnel & U-Channel: Completed *stem walls*. Continued MSE wall installation, storm drain and sewer installations at Mangrove. *Continued* wet standpipe, and *lighting* installation. Started *#10 double crossover track*.

Future Little Tokyo/Arts District Station: In the station box, continued metal ceiling panels, fire protection installation, mechanical/electrical/plumbing installations, and elevator installations at PL1 and PL2. Started *the edge light support installation*. In the lower ancillary, started *service stair #1 CMU walls*. Continued mechanical/electrical/plumbing installation. In the mid-vent ancillary, continued the CMU walls. In the upper ancillary, continued mechanical/electrical/plumbing. Continued the installation of Train Control racks & equipment in the TC&C Room. In the west vent shaft, completed the *acoustic placement*. In the Plaza area, started *the canopy steel installation*.

Reach 1 Tunnels Section (Future Little Tokyo/Arts District Station to Crossover Cavern): Completed installation of fiber optic cables and impedance bonds. Continued *mechanical/electrical/plumbing installations at Cross Passage #1 and Cross Passage #2*, and walkway handrail installation in both tunnels.

Crossover Cavern: *Completed* tunnel lighting installation.

Historic Broadway Station: At the platform level, *completed edge pavers and platform lighting installation. Continued* the mechanical/electrical/plumbing installations, and metal ceiling panel installation. At the concourse level, continued CMU walls, metal ceiling panels, and the mechanical/electrical/plumbing installations. At the Ancillary level, continued the CMU walls, and mechanical/electrical/plumbing installations. At the Roof Level, *completed Public Stair #1 stair treads. Continued station entrance area backfill, and* the installation of the *East Tunnel Vent Plenum walls. Started Public Stair #1 roof deck.* In the station box area, continued Emergency Exit #2 structure, utility relocations and street restoration.

Reach 2 Tunnel Section (Historic Broadway Station to Grand Av Arts/Bunker Hill Station): Completed the installation of *fiber optic cable. Continued* the emergency walkway handrail in the Right and Left Track Tunnels. *Started wayside sign installations.*

Grand Av Arts/Bunker Hill Station: At the platform level, continued the metal panel ceiling, mechanical/electrical/plumbing and the PL7|PL8 elevator installation. At the concourse level, *completed* elevator hoist way enclosure steel for the concourse level PL1-6 elevators. *continued the metal panel ceiling, and mechanical/electrical/plumbing.* At the lower and upper ancillary levels, *completed LADWP equipment installation. Continued* the installation of mechanical/electrical/plumbing. *Started the installation of hollow metal doors.* At the roof level, continued the installation of mechanical/electrical/ plumbing. At the upper roof level, continued the installation of mechanical/electrical/ plumbing. At the Plaza, *continued* elevator steel hoist way enclosure installation, *and* mechanical/electrical/ plumbing. *Started the metal panel ceiling installation.* At the Upper Plaza, continued the installation of steel shoes (barrier glazing). *Started the canopy steel installation.* At Northbound Flower Street, continued the storm drain installation *and* street restoration. At Hope Street, continued street restoration. At 2nd Place, *completed the storm drain installation. Started the street restoration.* At Southbound Flower Street, *completed* telecommunications conduits.

Reach 3 Tunnel Section (Grand Av Arts/Bunker Hill Station to Flower): Continued the installation of handrail. *Completed the fiber optic cable installation.*

Flower Cut & Cover Tunnel: Completed *mechanical/electrical/plumbing installations and* remedial work of portions of OCR rail in both tunnels where tolerances were not in conformance. Continued the installation of *hollow metal doors* at the Mechanical Room and Disconnect Room, and *street restoration. Started handrail, wayside signs, and disconnect conduit installations. Bus Bridge 2.7 was carried-out successfully at 7th/Metro Station; work to advance systems cut-overs in January were the focus of efforts over the weekend of October 20th.*

Schedule Summary

Divergence between Metro's Project Master Schedule and RCC's Contract Schedule had manifest over several months.

That dynamic has reversed with RCC's portrayal of schedule slippages over two consecutive cycles. Inefficiencies continue to impact RCC progress rates due in large part to lagging completion of predecessor activities at interfaces between operations, e.g., trackwork completion to train control device installations, or trackwork completion to OCR installation, etc.

Forecasts for substantial completion milestones are threatened. *RCC is refining mitigation plans to stem schedule loses and minimize impacts of material and equipment delays that are owed to COVID-19 disruptions (per RCC assertions).*

Costs Summary

Project costs continue to track within budget. To date, the design and construction changes related to base scope represent 10.7% of the contract value. There is one notice of intent to claim by RCC. The notice relates to Historic Broadway Station SOE stability issues. Detailed cost and budget information begins on Page 13.

Coronavirus Impacts

It remains unclear as to what extent the Coronavirus (COVID-19) has impacted construction operations. RCC has notified Metro of work inefficiencies and impacts to material supply chains, especially related to stainless steel, special trackwork, conduit deliveries, and electrical equipment. These reports highlight direct schedule impacts of equipment and materials – leading to subsequent delays with testing.

There has been a total of 117 positive cases through September 2021; all cases have been closed with sufficient negative testing. RCC continues to follow local, state, and federal regulations related to COVID-19 to maintain operations.

Key Management Concerns


Item 1: Rail Activation for integrating three transit lines is complex. Schedule and cost challenges are likely to continue to manifest. New challenges are expected with the bifurcated substantial completion. *Cut-over logistics at Union Station has raised concerns about disruptions to Rail Operations on the Gold Line at/and north of Union Station. Single-track allocations designed to minimize operational disruption are under review with Operations to determine the appropriate path-forward.*

Status/Action: *Seven (7) weekend bus bridges have been successfully completed as of the data date. Continued planning and incorporation of lessons-learned are underway for the remaining scheduled weekend outage in December 2021 and January 2022.*

Item 2: RCC has indicated that COVID-19 has impacted performance on the Project through the late delivery of several MCC units, as well as elements where stainless steel is prominent (i.e., dampers and attenuators). *RCC has updated their list of materials/commodities adversely impacted by COVID-19.*

Status/Action: RCC has initiated mitigation measures in anticipation of delayed equipment deliveries. Metro continues to monitor the situation to determine the extent of actual impact to schedule or will likely occur in the coming months; MCC units now all installed.

Project Construction Photos

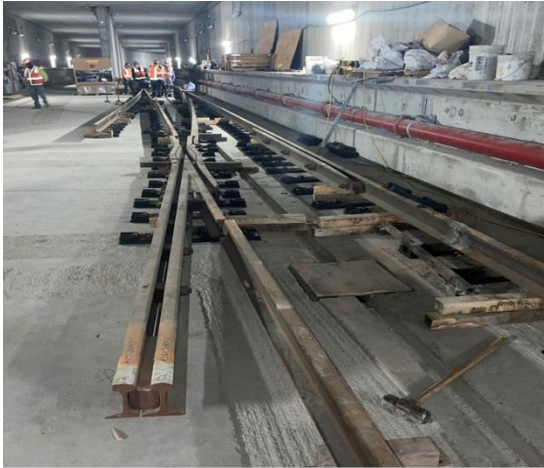

Alameda No. 10 rail distribution



1st/Central decorative paving restoration




Historic Broadway Station LTS1 slurry backfill



Welding for hoist way frames at PL3-6
at Grand Av Arts/Bunker Hill Station



Removing soldier piles on Flower St

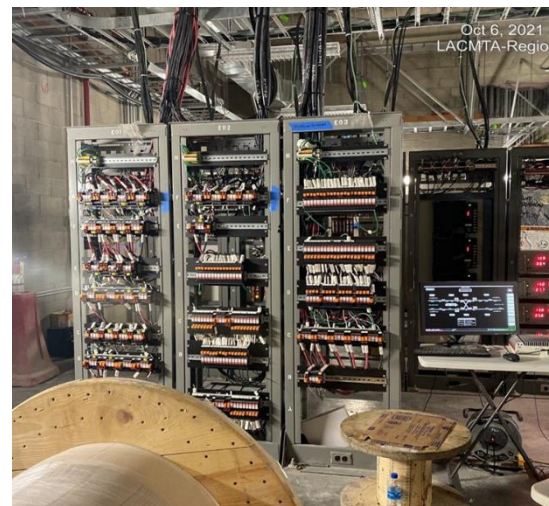


Energized Train Control racks in TC and Comm Room

PROJECT UPDATE

PROJECT SCHEDULE

Project Summary Schedule

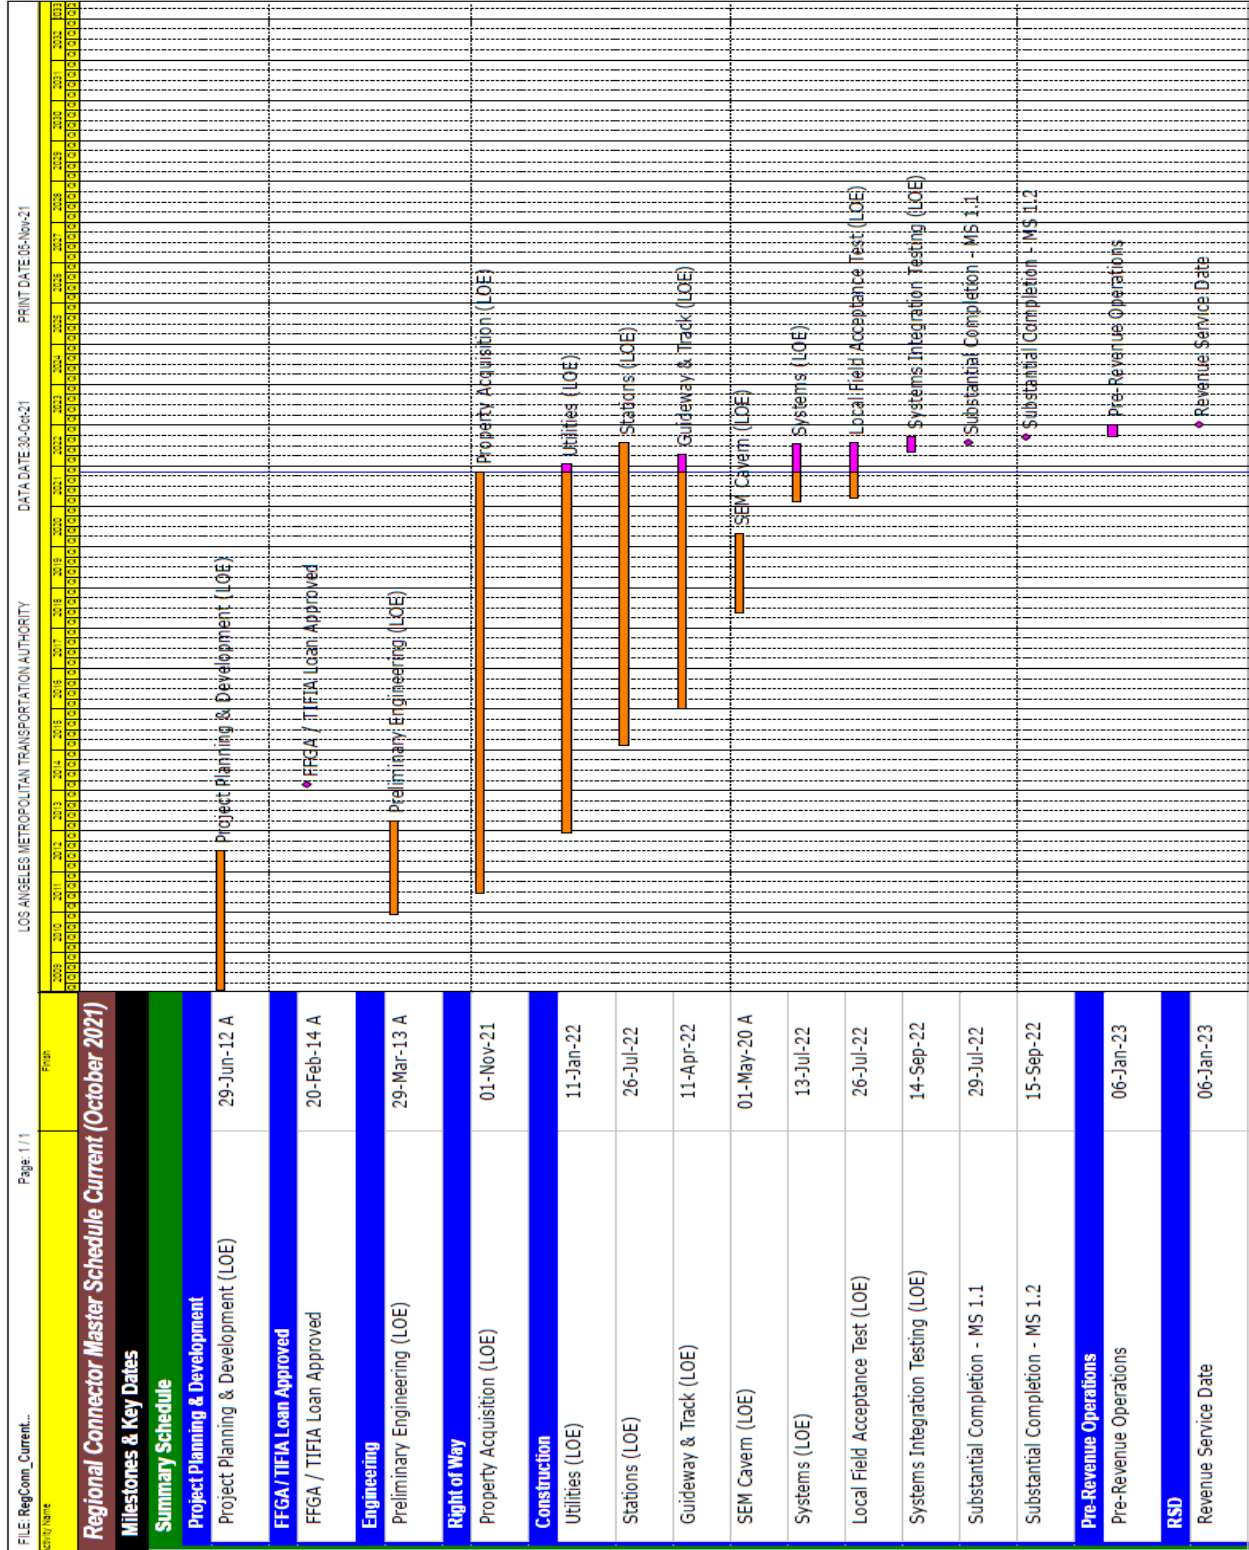


*Dates reflect unmitigated delays due to COVID-19. Mitigations in development by RCC.

Progress Summary

	Status	Change from Last Month	Comment
Forecast Revenue Service	Fall 2022	None	
Proposed FFGA Revenue Service	11/26/2023	None	
Final Design Progress:			
Contract C0980	100%	NA	
Construction Contracts Progress:			
Contract C0981R & C0980	86.1%	0.5%	

Note: Construction Progress excludes General Requirements, Construction and Design Mobilization, Final Design and Provisional Sum costs (Schedule C). Progress values include executed modifications and change orders.

Planned vs. Actual Progress

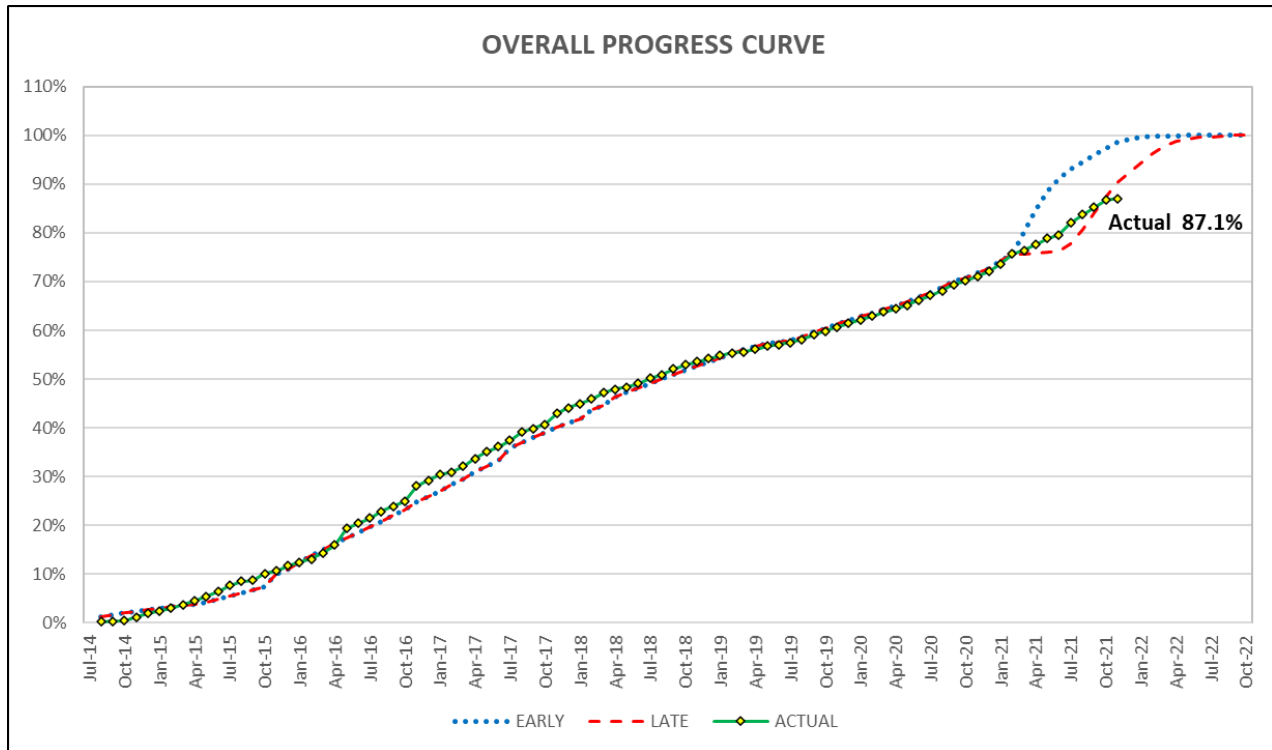

Key Milestone Six-Month Look Ahead

	Milestone Date	Oct-21	Nov-21	Dec-21	Jan-22	Feb-22	Mar-22
Complete West Vent Plenum at Historic Broadway Station	10/08/21 A	⬡					
Complete Wye Fan Plant Roof Deck	10/15/21 A	⬡					
Complete Concourse Level CMU Installation at Historic Broadway Station	11/05/21		⬡				
Complete Elevator Hoist Way Glazing at Grand Ave / Bunker Hill Station	11/11/21		⬡				
Complete #5 Turnouts and Diamond Track	11/15/21		⬡				
Complete LVT Track at 1st Street Cut & Cover/U-Channel	11/19/21		⬡				
Complete Plaza Drains & Catch Basins at Little Tokyo / Art District Station	12/20/21			⬡			
Complete #10 Crossover Track at Alameda Cut & Cover	12/20/21			⬡			
Complete East Vent Plenum at Historic Broadway Station	12/21/21			⬡			
Complete Backfill at Historic Broadway Station	01/11/22				⬡		
Complete OCR - 7th/Metro to Wye	02/16/22					⬡	
Complete LVT Track at Alameda Cut & Cover/U-Channel	03/30/22						⬡

MTA Staff	MTA Board Action	FTA (Federal Transit Administration)	Utility Company
Other Agencies	Contractors	Design Consultant	C0980 D/B Contractor
New Date			

Major Equipment Delivery

Metro Supplied Equipment

Equipment	Initial Procurement	Scheduled Delivery	Scheduled Installation
LRT Vehicles	(NTP) 08/20/2012 A	Option 2 12/31/2020 A	N/A
Ticket Vending Machines	~ 01/30/2018 A	07/08/19 A (warehoused)	12/23/2021 ~04/19/2022

PROJECT COST

Project Cost Analysis – 860228

REGIONAL CONNECTOR TRANSIT CORRIDOR PROJECT (860228)
COST REPORT
DOLLARS IN THOUSANDS

SCC CODE		FFGA BUDGET	ORIGINAL BUDGET	CURRENT BUDGET		COMMITMENTS		EXPENDITURES		CURRENT FORECAST		BUDGET/ FORECAST VARIANCE
				PERIOD	TO DATE	PERIOD	TO DATE	PERIOD	TO DATE	PERIOD	TO DATE	
10	GUIDEWAYS & TRACK ELEMENTS	280,622	204,691	0	273,671	0	276,097	2,149	260,399	0	272,628	-1,043
20	STATIONS, STOPS, TERMINALS, INTERMODAL	354,268	219,477	0	235,436	0	238,059	3,775	179,133	0	239,321	3,885
30	SUPPORT FACILITIES: YARDS, SHOPS, ADMIN, BLDGS	0	0	0	0	0	0	0	0	0	0	0
40	SITWORK & SPECIAL CONDITIONS	141,785	422,453	0	628,356	1,011	603,644	3,494	567,092	311	627,885	-471
50	SYSTEMS	69,667	73,848	0	78,852	231	69,174	3,770	39,607	-40	76,452	-2,399
	CONSTRUCTION SUBTOTAL (10-50)	846,343	920,468	0	1,216,314	1,242	1,186,974	13,189	1,046,232	271	1,216,286	-28
60	ROW, LAND, EXISTING IMPROVEMENTS	115,889	74,208	0	59,315	0	57,858	0	57,851	0	59,946	630
70	VEHICLES	16,275	16,275	0	16,275	0	16,275	0	12,579	0	16,275	0
80	PROFESSIONAL SERVICES	261,455	257,973	0	394,865	546	377,399	1,441	350,108	3,549	404,158	9,293
	SUBTOTAL (10-80)	1,239,963	1,268,925	0	1,686,770	1,788	1,638,507	14,631	1,466,770	3,821	1,696,666	9,896
90	UNALLOCATED CONTINGENCY	135,399	126,892	0	42,571	0	0	0	0	13,674	50,170	7,599
100	FINANCE CHARGES	27,571	7,115	0	14,301	0	0	0	0	0	14,301	0
	TOTAL PROJECTS (10-100)	1,402,932	1,402,932	0	1,743,642	1,788	1,638,507	14,631	1,466,770	17,495	1,761,137	17,495
	ENVIRONMENTAL/PLANNING - 400228		6,075	0	6,075	0	6,075	0	6,075	0	6,075	0
	ENVIRONMENTAL/PLANNING - 460228		18,125	0	20,425	0	20,425	0	18,988	0	20,425	0
	TOTAL PROJECTS (EVN/PLAN'G)		24,200	0	26,500	0	26,500	0	25,063	0	26,500	0
	TOTAL	1,402,932	1,427,132	0	1,770,142	1,788	1,665,006	14,631	1,491,833	17,495	1,787,637	17,495

NOTE: EXPENDITURES ARE CUMULATIVE THROUGH OCT 2021.

METRO AND TRIBUNE AGREED ON REIMBURSEMENT OF ~\$1.6 MILLION RELATED TO 2ND/BROADWAY OVERBUILD.

Original Budget:

The Original Budget of \$1.427 billion reflects the April 2014 Board approved LOP Budget, plus finance costs of \$7.1 million.

Current Budget:

In January 2017, the Metro Board revised the LOP Budget for Project 860228 to \$1.756 billion to reflect then current and present Project scope. Finance costs, estimated at \$14.3 million, are also reflected leading to a total of \$1.770 billion.

Commitments:

Overall commitments increased by \$ 1.8 million this month to \$1.67 billion which represents 94.1% of the Current Budget.

Expenditures:

Expenditures are cumulative through *October 2021* and increased by \$14.6 million this month for costs across the Project. One billion four hundred *ninety-one* million (\$1.49 billion) in expenditures to date represent 84.3% of the Current Budget.

Current Forecast:

The total current forecast is \$17.5 million more than the total current budget. *The Project plans to go to the Board in February 2022 to request additional funding to address specific request of FTA to increase Project Contingency in-line with their recent Risk Refresh conclusions.*

Project Cost Analysis – 861228

CONCURRENT NON-FFGA ACTIVITIES (861228)
PROJECT COST STATUS BY FTA SCC
DOLLARS IN THOUSANDS

SCC CODE		ORIGINAL BUDGET	CURRENT BUDGET		COMMITMENTS		EXPENDITURES		CURRENT FORECAST		BUDGET/ FORECAST VARIANCE
			PERIOD	TO DATE	PERIOD	TO DATE	PERIOD	TO DATE	PERIOD	TO DATE	
10	GUIDEWAYS & TRACK ELEMENTS	0	0	0	0	0	0	0	0	0	0
20	STATIONS, STOPS, TERMINALS, INTERMODAL	0	0	0	0	0	0	0	0	0	0
30	SUPPORT FACILITIES: YARDS, SHOPS, ADMIN, BLDGS	10,480	0	0	0	0	0	0	0	0	0
40	SITework & SPECIAL CONDITIONS	0	0	13,548	0	13,548	489	9,979	0	13,548	0
50	SYSTEMS	0	0	5,950	0	5,014	54	3,621	0	5,950	0
	CONSTRUCTION SUBTOTAL (10-50)	10,480	0	19,498	0	18,562	544	13,600	0	19,498	0
60	ROW, LAND, EXISTING IMPROVEMENTS	27,748	0	38,228	0	38,377	0	37,475	149	38,377	-149
70	VEHICLES	0	0	0	0	0	0	0	0	0	0
80	PROFESSIONAL SERVICES	650	0	1,150	0	758	0	428	0	1,150	0
	SUBTOTAL (10-80)	38,878	0	58,876	0	57,697	544	51,503	149	59,025	-149
90	UNALLOCATED CONTINGENCY	1,113	0	513	0	0	0	0	-149	365	149
100	FINANCE CHARGES	0	0	0	0	0	0	0	0	0	0
	TOTAL PROJECTS (10-100)	39,991	0	59,389	0	57,697	544	51,503	0	59,389	0
	861228 TOTAL	39,991	0	59,389	0	57,697	544	51,503	0	59,389	0

NOTE: EXPENDITURES ARE CUMULATIVE THROUGH OCT 2021.

Original Budget:

The Original Budget reflects the Board approved LOP Budget established April 24, 2014.

Current Budget:

In January 2021, the Metro Board approved an additional budget increase of \$12.9 million for the Early Completion Incentive Agreement increasing the Project 861228 LOP budget to \$59.4 million, to reflect the current Project scope.

Commitments:

Commitments unchanged this month at \$57.7 million which represents 97% of the Current budget.


Expenditures:

Expenditures are cumulative through *October* 2021 and increased by \$0.54 million for costs related to the Modification 187. The cumulative \$60.0 million through *October* 2021 represent 87% of the Current Budget.

Current Forecast:

The total current forecast remains equal to the total current budget.

Cost Contingency Drawdown

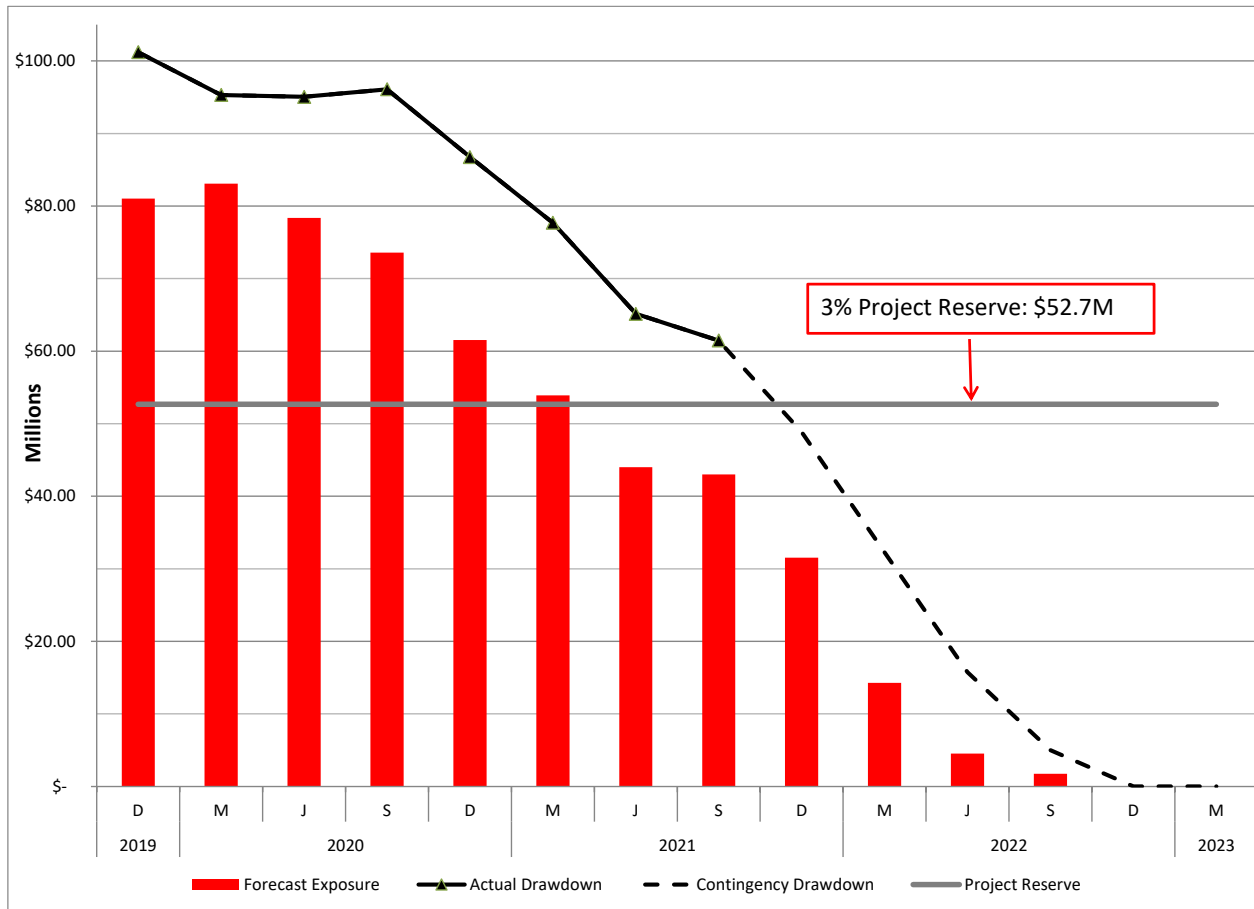

Cost Contingency Drawdown Analysis


The Cost Contingency Drawdown curve reflects cost commitments and forecast exposure, thereby providing a depiction of overall contingency status. Basing the drawdown on exposures rather than executed contract modifications eliminates the administrative processing time involved to finalize contract modifications from the drawdown projections. Planned expenditures per quarter have also been updated to reflect the current schedule and risks. The Project is expected to reach the 3% Project Reserve (Total Contingency) threshold in Fall 2021.

In *October*, there was a \$5.4 million contingency drawdown into executed modifications. The remaining unallocated contingency is \$32.7 million which is forecast to be fully utilized by the Project.

PROJECT COST CONTINGENCY						
DOLLARS IN THOUSANDS						
	Original Contingency	LOP Contingency	Previous Period	Current Period	To-Date	Remaining Contingency (Forecast)
Unallocated Contingency	124,919	89,946	(53,450)	(3,821)	(57,270)	32,675
Allocated Contingency	86,345	92,809	(67,866)	(1,621)	(69,487)	23,321
Total Contingency	211,263	182,754	(121,316)	(5,442)	(126,758)	55,997

Summary of Contract Modifications

Contract Modifications (MODs) by Cost Level



	C0980		Total
	219 Executed	38 Pending	
■ Under \$100K	4,213,493	557,528	4,771,021
■ \$100K to \$250K	7,699,235	1,457,000	9,156,235
■ \$250K to \$1M	25,602,491	4,351,000	29,953,491
■ Over \$1M	249,781,830	1,350,000	251,131,830
Total Contract MODs	287,297,049	7,715,528	295,012,577
Contract Award Amount	927,226,995	927,226,995	
% of Contract MODs	31.0%	0.8%	

Note:

1. Percent of Contract MODs equals the Total Contract MODs divided by the Contract Award Amount.
2. Pending Mods are under negotiation.

Two hundred and *eighteen* (218) changes with a total value of \$287.3 million have been executed since NTP of Contract C0980. An additional 38 changes, with a total estimated value of \$7.7 million, are pending. *Twenty-four million and fifty thousands of the \$287.3 million executed modifications are funded from Eastside Access Project and Non-FFGA Project, \$5.03M and \$19.02M, respectively.*

DISADVANTAGED BUSINESS ENTERPRISE (DBE)

As of *September 2021*:

DBE Commitment – Design The percentage of funds apportioned to Design Contracts	22.63%
Current DBE Commitment Design Total DBE Committed Dollars divided by Total Contract Value for Design	\$14.8M (22.63%)
Current DBE Participation Total amount paid to date to DBEs divided by the amount paid to date to Prime	24.36%

Fourteen (14) Design DBE sub-consultants have been identified to date.

DBE Commitment – Construction The percentage of funds apportioned to Construction Contracts	18%
Current DBE Commitment Construction Contract commitment divided by current contract value for Construction	\$196.3M (18%)
Current DBE Participation Total amount paid to date to DBEs divided by the amount paid to date to Prime	19.44%

Construction DBE sub-contractors that have been identified increased to one hundred twenty-six (126).

PROJECT LABOR AGREEMENTS (PLA)

As of *September 2021*:

Targeted Worker Goal Construction work to be performed by residents from Economically Disadvantaged Area in the United States	40.00%
Targeted Worker Current Attainment	61.48%
Apprentice Worker Goal Construction work to be performed by Apprentices	20.00%
Apprentice Worker Current Attainment	20.03%
Disadvantaged Worker Goal Construction work to be performed by Disadvantaged Workers who are residents of the United States	10.00%
Disadvantaged Worker Current Attainment	11.20%

FINANCIAL/GRANT

Status of Funds by Source

October 2021


SOURCE	ORIGINAL BUDGET	TOTAL FUNDS ANTICIPATED	TOTAL FUNDS AVAILABLE	COMMITMENTS		EXPENDITURES		BILLED TO FUNDING SOURCE	
				\$	%	\$	%	\$	%
FEDERAL - CMAQ	\$64.00	\$228.01	\$64.00	\$177.30	78%	\$64.00	28%	\$50.96	22%
FEDERAL - SECTION 5309 NEW STARTS	\$669.90	\$669.90	\$669.90	\$669.90	100%	\$609.00	91%	\$604.21	90%
FEDERAL - SECTION 5309 NEW STARTS - AMERICAN RESCUE PLAN ACT		\$ 59.23	\$0.00	\$0.99	2%	\$0.00	0	\$0.00	0
FEDERAL - RIP	\$0.00	\$1.41	\$1.41	\$1.41	100%	\$1.41	100%	\$1.41	100%
MEASURE R - TIFIA LOAN****	\$160.00	\$141.89	\$141.89	\$141.89	100%	\$141.89	100%	\$141.89	100%
MEASURE R BONDS****	\$0.00	\$18.11	\$18.11	\$18.11	100%	\$11.35	63%	\$9.35	52%
STATE PROPOSITION 1A HSRB *	\$114.87	\$114.87	\$114.87	\$114.87	100%	\$114.87	100%	\$114.87	100%
STATE PROPOSITION 1B PTMISEA **	\$149.50	\$135.16	\$135.16	\$135.16	100%	\$135.16	100%	\$135.16	100%
STATE STIP RIP	\$2.59	\$19.55	\$15.90	\$19.55	100%	\$18.90	97%	\$9.97	51%
STATE CAPITAL PROJECT LOANS - OTHERS ***	\$132.47	\$236.38	\$236.38	\$236.38	100%	\$236.38	100%	\$224.14	95%
MEASURE R	\$27.57	\$0.00	\$0.00	\$0.00	0%	\$0.00	0%	\$0.00	0%
CITY OF LOS ANGELES	\$41.98	\$41.98	\$41.98	\$41.98	100%	\$41.98	100%	\$41.98	100%
ROW LEASE REVENUES	\$64.25	\$19.85	\$19.85	\$19.85	100%	\$19.85	100%	\$19.47	98%
GENERAL FUND - METRO	\$0.00	\$69.49	\$79.80	\$87.61	126%	\$97.04	140%	\$97.04	140%
TOTAL	\$1,427.13	\$1,755.84	\$1,539.26	\$1,665.01	95%	\$1,491.83	85%	\$1,450.46	83%

NOTES:

1. EXPENDITURES ARE CUMULATIVE THROUGH OCTOBER 31, 2021.
 2. METRO AND TRIBUNE AGREED ON REIMBURSEMENT OF \$1.6 MILLION RELATED TO 2ND/BOARDWAY OVERBUILD.
 3. ORIGINAL BUDGET BASED ON FUNDING PLAN INCLUDED IN THE APPROVED FULL FUNDING GRANT AGREEMENT
 4. LACMTA RESERVES THE ABILITY TO UPDATE COSTS AND CHANGE FUND SOURCES AS REQUIRED.
- * STATE PROPOSITION 1A HIGH SPEED RAIL BONDS
 ** STATE PROPOSITION 1B PUBLIC TRANSPORTATION MODERNIZATION, IMPROVEMENT AND SERVICE ENHANCEMENT ACCOUNT
 *** OTHERS INCLUDE TDA ADMINISTRATION, AND NB PROPOSITION A ADMINISTRATION (FOR A TOTAL OF \$.255M)
 **** OTHERS INCLUDE TDA ADMINISTRATION, AND NB PROPOSITION A ADMINISTRATION (FOR A TOTAL OF \$.255M)
 ***** TIFIA LOAN CLOSED ON AUGUST 27, 2020. BALANCE OF ORIGINAL TIFIA BUDGET WILL BE MEASURE R BONDS.

PROJECT ORGANIZATION AND STAFFING


The D/B contract is being managed by a joint team of Metro and consultant personnel located at the Integrated Project Management Office (IPMO).

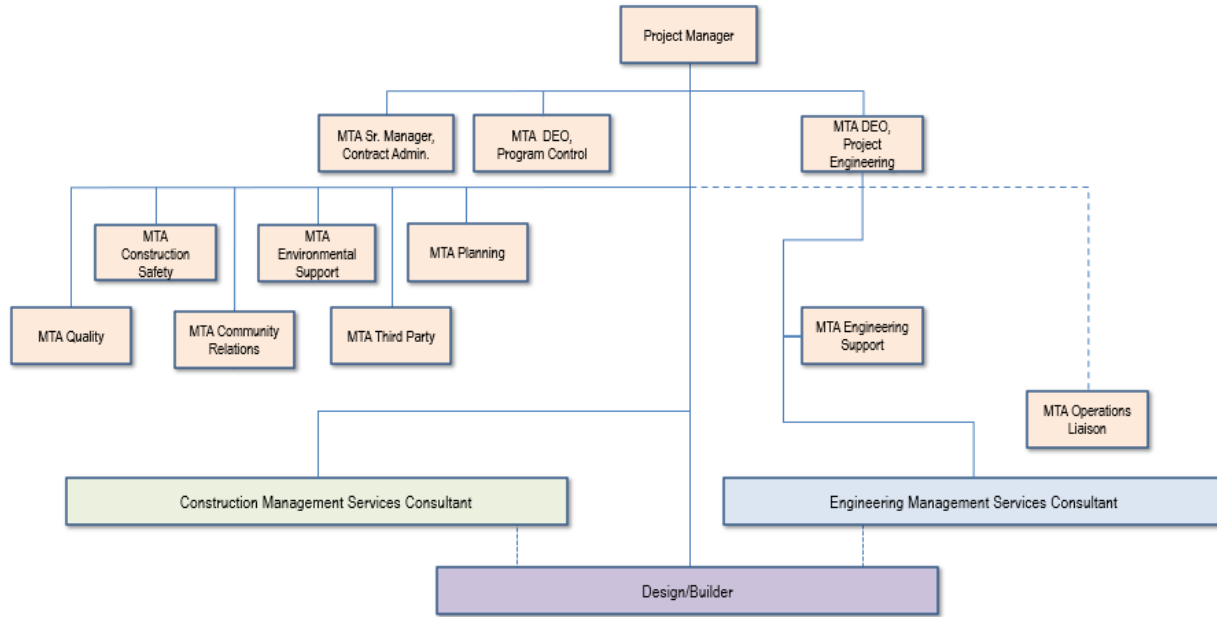


Updated: 03/2021

The overall FY22 Total Project Staffing plan averages 66.5 FTEs per month. The total actual project staffing for *September 2021* was 60.07; 22.98 FTEs for Metro's Project Administration staff and 31.1 FTEs for consulting staff. Consulting staff FTEs are based on monthly invoice billable hours. Review of staffing plans is on-going to ensure staffing needs are appropriately managed. Metro August actuals FTEs doubled the forecast number due to Bus Bridge closure, Operations training, and incorrect charging. Corrections will be adjusted.

Total Project Staffing – Metro and Consultants

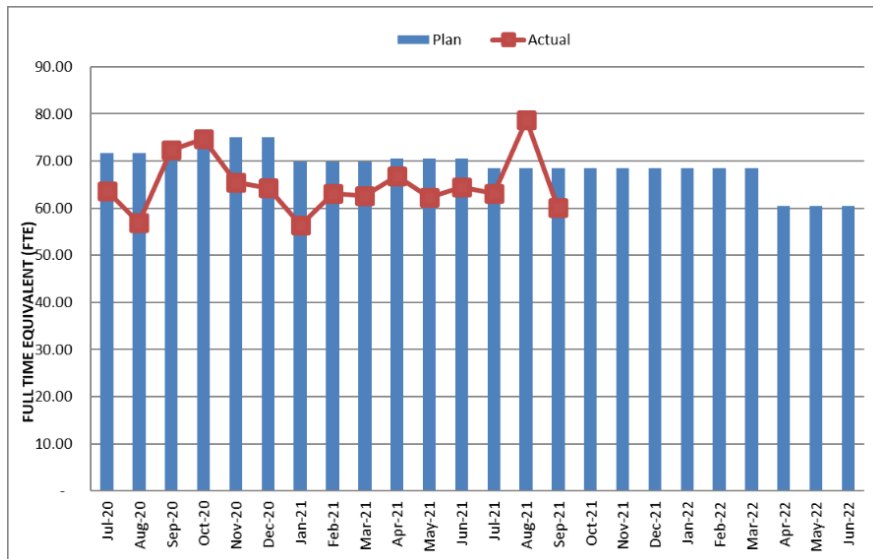

Metro Staff

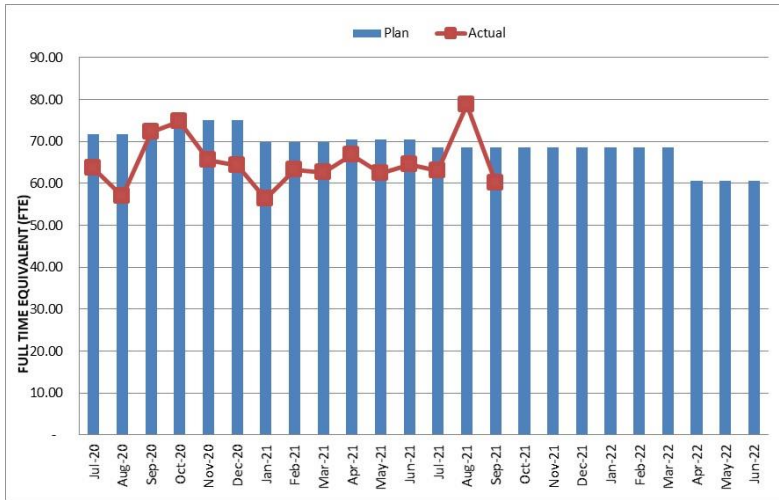

Staffing by Group


The opposing graphs represent planned vs. actual staffing levels by group.

Metro staffing includes full-time staff located in the IPMO as well as part-time support located at Gateway Headquarters.


The spike in charges was an anomaly that is being attended to.

Staffing plans are developed for each fiscal year based on Project needs.

CM Support Services Staff (Consultant)

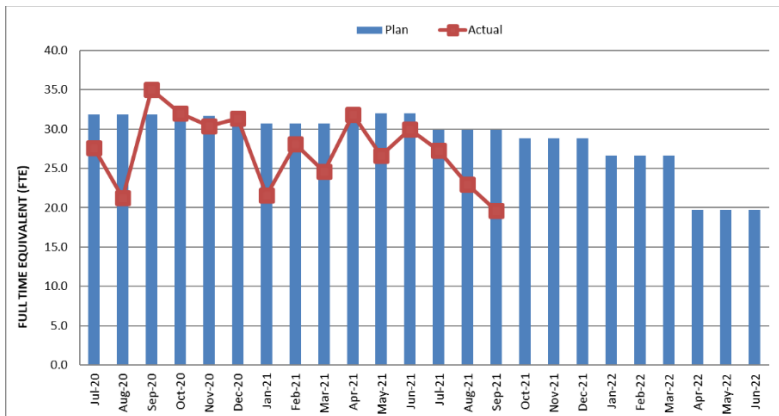

Engineering Services Staff (Consultant)

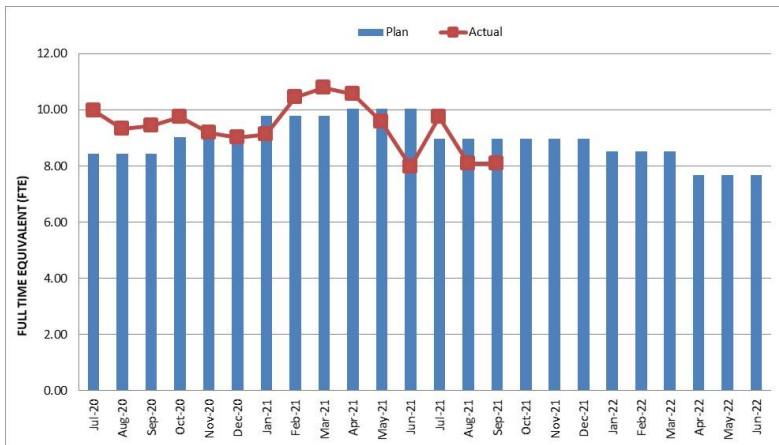

All above data through September 2021

REAL ESTATE

Open Real Estate Matters – Seven Parcels Remaining

City of Los Angeles (Mangrove Parcels)

- No further action required on this parcel until June 2022.

Department of Water and Power ‘Duco Yard’ – DWP (RC-473)

- The Purchase Agreement has been reviewed and accepted by Metro. The Chief Administrative Officer has approved the agreement; now pending LADWP Board approval. City Council approved the agreement in early May. The agreement has been signed, pending original to open escrow. Once escrow is opened LADWP will provide the executed deeds. *There were no changes in the month of October.*

2nd and Hope

- City of Los Angeles Parcel - The City agreed to the transfer based on the City's and LACMTA's Memorandum of Agreement. The City finalized conveyance documents and is coordinating council action to approve. City approved the motion, LACMTA Real Estate coordinating with City of LA BOE on next steps to transfer property. The Project has approved the purchase price, Real Estate coordinating with City on transaction process. The City confirmed the property is subject to the Surplus Land Act. City staff is working on Council motion to declare property as exempt surplus property. Once the motion/declaration is approved, the City can proceed with transfer. *There were no changes in the month of October.*

QUALITY ASSURANCE

Metro QA performed the following activities during the month of *October 2021*:

- Performed oversight verification of RCC's design and construction activities
- Reviewed and provided comments on RCC's Quality related submittals
- Attended daily meeting/briefing, CMSS personnel
- Reviewed test results for Portland Cement Concrete, Soils Testing, Asphalt Testing and Non-Destructive Testing of Welding
- Attended CQWP and "Readiness Review" meetings with RCC
- Attended Bi-Weekly Quality Review Meetings with RCC Quality Management
- There were no surveillances was conducted during the period.
- *Metro accepted the disposition by the EOR and closed RCC NCRs 0109, 0120, and 0130 during the month of October.*

There were no new NCRs issued by RCC during the month of October.

As of *October 2021*, there have been a total of 130 NCRs issued, with seven (7) NCRs that remain open.

ENVIRONMENTAL

Project holds bi-weekly coordination meeting between Metro and Contractor.

Stormwater Pollution Prevention Plan (SWPPP) inspections of active Project work areas are conducted weekly by RCC. *The QSP was updated from Mike Lucey to Kurt Kroner with Anerea Morales as QSP-designee.* Metro performs additional inspections and shares observations with RCC for corrective action. Metro receives copies of communication sent between field sites and QSP-designee related to observed deficiencies and corrective actions. Change of Information to extend construction end date *in SMARTS under Water Board review.*

Dewatering no longer required at Flower. Permit deactivation in process. Flowmeter at Broadway moved to track level from surface.

Noise and vibration spot checks continue to be conducted weekly at multiple sensitive locations and at locations of new activities along the alignment. RCC conducted weekly monitoring at active construction sites or when work and/or equipment changed. In addition, noise and vibration monitoring was conducted continuously and data was gathered in an online system. RCC also provided a weekly compliance report.

There have been inquiries relevant to environmental compliance from stakeholders adjacent to the future Grand Av Arts/Bunker Hill Station; however, Metro/RCC's Community Relations continue to be responsive and actively address community concerns in coordination with Area Leads, Resident Engineers, and field staff with respect to each construction site.

No historic period features were encountered during *October.*

CONSTRUCTION AND COMMUNITY RELATIONS

Construction Relations

- Responded and addressed Project related inquiries from the public received via the hotline, and email. The Little Tokyo Community Office remains closed due to the COVID-19 pandemic.
- Distributed 12 construction notices to the public on the following activities through email and made it available on the Project website and social media outlets: activities throughout the alignment: concrete placement, utility work, and geotechnical instrumentation removal/maintenance, *and* backfill activities. Rail integration: service interruption to the A & E lines on selected weekends only, and L Line bus bridge shuttle relocation. Other activities included: *street restoration and civil improvements, and bike detour* on westbound 1st St.
- Coordinated and provided update on construction activities with 157 stakeholders throughout the alignment.
- Presented virtually to 11 community organizations, interest groups and homeowner associations on planned activities, and the status of the project.
- Continued briefings with: LA City Council District 14, and the Mayor's Office.

Eat, Shop, Play – Construction Impact Business Mitigation Program Highlights

Highlighted *seven (7)* businesses near the Project's alignment on social media posts, and e-newsletters: *YMCA, Limerick's Tavern, Prime Pizza, A Beautiful Life Jamaican Café, Drago Centro, Public School 213, and Colburn School.*

Community Relations

The monthly Little Tokyo Marketing & Advertisement/Go Little Tokyo coordination meeting was held on *October 27, 2021* to *discuss upcoming events and Hunted Little Tokyo event.*

CREATIVE SERVICES

Art Program

- *Reviewed glass mosaic, porcelain enamel steel artwork and art glass submittals.*
- Reviewed RFIs and Provisional Sum and Change-related submittals.
- *Provided review in glass mosaic installation coordination with RCC.*
- *Led glass mosaic installation coordination with the fabricator.*
- *Facilitated porcelain enamel steel artwork fabrication inspection by artist.*
- Continued assessment of Project operating impacts to signage systemwide.

SAFETY & SECURITY

C0980 Regional Connector

- In response to the COVID-19 pandemic, Project Safety Management continued to monitor compliance by RCC and IPMO staff with Federal, State, and City requirements for 'Essential Workers' on 'Critical Infrastructure' projects.
- Monitored RCC's pre-employment drug/alcohol testing and new employee safety orientation to ensure compliance with contract specifications.
- Conducted Project Safety Orientation for new Metro/Consultants and IPMO project staff. Training sessions included Safety Orientation, Underground Safety, and Self Rescuer Training.
- Participated in work plan reviews, daily crew safety meetings, and the RCC 'Safety Stand Down' sessions.
- Monitored construction field activities daily to ensure compliance with contract specifications. Participated with RCC staff in field safety inspection walks of multiple project worksites, laydown areas, and storage yards.
- Monitored Third Party contractor's work activities to ensure safety compliance.

Project Safety Record

- *RCC reported no Recordable Injuries in the month of September 2021.*
- RCC reported 94,067 work hours for *September 2021*. RCC's total Contract to Date work hours through *September 2021* are 5,546,229 with a total of 22 Recordable Injuries and no Lost Workday (Days Away) case injuries. The C0980 Contract Recordable Injury Rate is 0.79. The Bureau of Labor Statistics reports that the National Average Recordable Injury Rate is 2.4 for heavy civil construction projects.
- Total Contractors' Project to Date Work Hours, including both the C0980 and the completed C0981 AUR contract, through *September 2021* is 5,657,288 hours with 23 recordable injuries. The Total Project Contractor Recordable Injury Rate is 0.81.
- Total Aggregate Project work hours for Contractors, Metro, and Support Services Consultants, through *September 2021* is 6,651,066 with 24 Recordable Injuries and no Lost Workday (Days Away) injury cases. The Total Project Aggregate Safety Rate is 0.72.*

* Using RIR method of calculating.

APPENDIX CHRONOLOGY OF EVENTS

June 2007	Began Alternatives Analysis study
January 2009	Board approval of Alternatives Analysis study and next phase
February 2009	Began Draft Environmental Impact Statement / Report (EIS / EIR)
October 2010	Board approval of Draft EIS / EIR and selection of locally preferred alternative
January 2011	FTA approval to Enter into Preliminary Engineering
January 2011	Began Preliminary Engineering
August 2011	Board authorized to solicit major D/B contract C0980
October 2011	Issued RFQs for D/B contract C0980
December 2011	Began Real Estate Acquisition
March 2012	Completed PE and began Advanced PE
April 2012	Board certification of Final EIS / EIR and adoption of project
April 2012	Began Final Design - Advanced Utility Relocations (AUR)
June 2012	FTA Record of Decision
August 2012	Issued RFQs for D/B contract C0980
January 2013	Issued RFPs for D/Build contract C0980
March 2013	Completed Final Design - Advanced Utilities Relocation (AUR)
May 2013	NTP for Construction Management Services contract MC070
June 2013	Beginning of AUR contract C0981R Bid Period
July 2013	Submitted TIFIA loan application
July 2013	Submitted first draft FFGA application to FTA for review

September 2013	Received proposals for D/B Contract C0980
September 2013	Submitted second draft FFGA application to FTA, incorporating FTA comments
October 2013	Submitted Application to FTA Requesting an FFGA
November 2013	Started Emergency Generator Replacement Tank at 2nd Street and Historic Broadway Station (LA Times Building)
December 2013	Issued "Notice of Intent to Award" letter to contract C0981R contractor Pulice Construction Inc.
January 2014	Awarded AUR contract C0981R to Pulice Construction Inc.
February 2014	Issued Notice to Proceed for AUR Contract C0981R
February 2014	FTA issued Full Funding Grant Agreement to Metro
March 2014	Issued Amendment # 11 for D/B Contract C0980
March 2014	Started Survey for AUR Contract C0981R
April 2014	Metro Board approved the award of D/B Contract C0980 and established a LOP Budget
May 2014	Awarded D/B Contract C0980 to Regional Connector Constructors, Joint Venture
June 2014	Obtained possession of the Mangrove property from the City of Los Angeles
July 2014	Issued Notice to Proceed for D/B contract C0980
August 2014	C0980 D/B Contractor (RCC) began Final Design
September 2014	Metro performed the ground-breaking ceremony for C0980 D/B Contract
October 2014	EN077 Contractor, Arcadis, removed the underground storage tank at LA Times Parking Lot
November 2014	C0981R AUR Contractor completed DWP power work at 1st St. and Alameda
December 2014	Metro completed Field Vibration Testing for existing Expo and Gold Lines
January 2015	Demolish Buildings at 1st/Central Station
February 2015	Metro approved the Baseline Schedule for C0980 D/B Contract

March 2015	RCC started Historic Broadway Station Site Move-In
April 2015	Metro terminated C0981R Contract for convenience
May 2015	RCC started pile installation at Mangrove Launch Pit
June 2015	RCC started decking for shoofly bridge (Pile Cap & Grade Beam)
July 2015	DWP Water started installing 36" Water Valve at Alameda St.
August 2015	RCC completed DWP Power work at Flower & 5th Street
September 2015	RCC started Phase 2 DWP Power Relocation work at Broadway (Behind K Rail).
October 2015	RCC started pile installation at 1st/Central Station
November 2015	RCC completed Central Ave Full Closure (Pile & Decking)
December 2015	Metro Board approved the increase (\$131.8M) of the Project LOP Budget to \$1,589.9 million.
January 2016	RCC began implementation of Bus Bridge # 1 (Shoofly Tie-In Work at Little Tokyo).
February 2016	RCC began implementation of full closure at 2nd/Broadway intersection.
March 2016	RCC completed Bus Bridge # 1 (Shoofly Tie-In at Little Tokyo) work.
March 2016	Excavation of 1st/Central Station was initiated.
April 2016	TBM (Tunnel Boring Machine) was delivered to the temporary storage site.
May 2016	Closed 1st Street between Alameda and Central Streets. Opened northbound 1st East of Alameda Street.
June 2016	RCC completed excavation at 1st/Central Station Box
June 2016	RCC began pile installation on west side of Flower Street between 4th and 5th Street
July 2016	RCC initiated pile installation at Historic Broadway Station (West Hammer Head)
July 2016	RCC Initiated CIP invert at 1st/Central Station Box
August 2016	RCC completed 36" waterline replacement at 1st/Alameda

September 2016	RCC completed temporary decking at 1st/Alameda intersection (Wye)
October 2016	Metro performed TBM lowering ceremony
October 2016	RCC completed CIP invert at 1st/Central Station Box
November 2016	RCC completed CIP invert at Mangrove Launch Pit and Wye
December 2016	RCC completed Phase 1, 2nd Street Decking in front of LA Times Bldg.
January 2017	Metro Board approved a LOP Budget increase
February 2017	RCC initiated TBM mining (1st – Left)
March 2017	RCC completed TBM mining under JVP (first 500 ft.)
March 2017	RCC completed temporary decking on Flower St. (between 4th and 5th)
April 2017	RCC completed sub-invert at TBM retrieval pit
April 2017	RCC completed CIP invert at Grand Av Arts/Bunker Hill Station Box
May 2017	RCC completed temporary decking at Historic Broadway Station
May 2017	RCC completed water relocation work along Flower Street
June 2017	RCC completed mining and broke through at Grand Av Arts/Bunker Hill Station
June 2017	Five-month full closure of 6th Street approved by LADOT, Caltrans and LADWP
July 2017	RCC completed TBM mining of the first tunnel
August 2017	RCC extracted TBM shields from the Retrieval Shaft
September 2017	RCC began TBM mining of the second tunnel (right)
October 2017	RCC completed TBM mining under JVP (first 500 ft.)
October 2017	RCC completed temporary decking on Flower St. (between 5th and 6th, deck beam 16 to deck beam 58)
November 2017	Completed five-month full closure of 6th Street

November 2017	Initiated underpinning related to the Historic Broadway Station
December 2017	RCC completed mining and broke through at Grand Av Arts/Bunker Hill Station (Right Tunnel)
January 2018	RCC completed TBM mining of the second tunnel (right)
February 2018	RCC began excavation of cross passages
February 2018	RCC began SEM canopy pipe installation
March 2018	RCC began tunnel invert concrete
March 2018	RCC completed infrastructure for power relocation work at 6th/Flower
April 2018	RCC completed entrance structure excavation of Historic Broadway Station
May 2018	RCC began SEM excavation
June 2018	LADWP Power completed cable pulling at 6th/Flower
June 2018	Completed underpinning related to the Historic Broadway Station
July 2018	RCC completed station box excavation of Historic Broadway Station
August 2018	Completed entrance structure invert of Historic Broadway Station
September 2018	Completed temporary decking of Flower Street
October 2018	RCC started the CN 106.2 Final Design of the Revised Cable Transmission System for the Gold Line
October 2018	Metro completed approval of floating slab test results
October 2018	RCC completed SEM left drift excavation
October 2018	RCC completed Trainway Feeder duct bank at Flower St & 7th St
November 2018	RCC completed Little Tokyo / Arts District Station Box Excavation
November 2018	RCC completed Grand Av Arts/Bunker Hill Station East Platform Level Exterior Walls
December 2018	RCC completed SEM right drift excavation

December 2018	RCC completed the Historic Broadway Station west invert
December 2018	RCC started tunnel walkways between the future Little Tokyo/Arts District Station to Historic Broadway Station
December 2018	RCC started the future Little Tokyo/Arts District Station east invert
December 2018	RCC completed Grand Av Arts/Bunker Hill Station mezzanine concrete
January 2019	RCC completed Grand Av Arts/Bunker Hill Station invert concrete
January 2019	RCC completed SEM center top drift excavation.
January 2019	RCC started Little Tokyo/Arts District Station west cable pit and sump pit
February 2019	RCC completed SEM excavation
February 2019	RCC completed platform level exterior walls at Grand Av Arts/Bunker Hill Station
February 2019	RCC started fire protection in tunnels
March 2019	RCC completed Little Tokyo/Arts District Station invert concrete
March 2019	RCC completed Bored Tunnels walkway concrete
April 2019	RCC completed Grand Av Arts/Bunker Hill Station east concourse deck concrete
April 2019	RCC completed 1st Street Cut & Cover / U-Channel Level 1 excavation
May 2019	RCC completed North Flower Cut & Cover tunnel invert concrete
May 2019	RCC completed Wye Cut & Cover tunnel invert concrete
June 2019	RCC completed Right Tunnel floating slab curb
July 2019	RCC completed Left Tunnel floating slab curb
July 2019	RCC completed SEM Cavern concrete invert
August 2019	RCC completed 7th Street / Metro Center Wall Demolition
August 2019	RCC completed the Historic Broadway Station West Concourse Deck

September 2019	RCC completed Historic Broadway Station east invert
September 2019	RCC completed South Flower Cut & Cover tunnel excavation
October 2019	RCC completed Wye Tunnel Cut & Cover walls
October 2019	RCC completed Grand Av Arts/Bunker Hill Station concourse walls
November 2019	RCC completed Wye Tunnel Cut & Cover Roof Deck
November 2019	RCC completed SEM Cavern Exterior Walls
December 2019	RCC completed Little Tokyo/Arts District Station plenum deck concrete
January 2020	RCC completed SEM Cavern Interior Walls
January 2020	RCC completed 1st Street Tunnel Cut & Cover Roof Deck
February 2020	RCC completed Wye Cut & Cover Tunnel Pin Pile Removal
February 2020	RCC completed Grand Av Arts/Bunker Hill Station platform walls
March 2020	RCC completed Grand Av Arts/Bunker Hill Station lower ancillary level walls
March 2020	RCC completed SEM plenum deck
April 2020	RCC completed Historic Broadway Station west concourse exterior walls
April 2020	RCC completed Historic Broadway Station concourse deck
May 2020	RCC completed SEM Cavern Arch Walls
May 2020	RCC completed Grand Av Arts/Bunker Hill Station upper ancillary level walls
May 2020	RCC completed South Flower Cut & Cover invert
June 2020	RCC completed fabrication pre-cast floating slabs
June 2020	RCC completed North Flower Cut & Cover roof deck
July 2020	RCC completed Historic Broadway Station entrance concourse level walls

July 2020	RCC completed installation pre-cast floating slabs
August 2020	RCC completed Wye backfill, deck removal and paving
September 2020	RCC completed Grand Av Arts/Bunker Hill Station upper roof deck
September 2020	RCC completed Little Tokyo/Arts District Station ancillary walls
September 2020	TIFIA loan paid off and account closed
October 2020	RCC completed Gold Line Communications Relocation Cutover
October 2020	RCC completed Flower Cut & Cover Tunnel roof deck
November 2020	RCC completed Little Tokyo/Arts District Station ancillary roof deck
November 2020	RCC completed Grand Av Arts/Bunker Hill Station ES1/ES2 walls
December 2020	RCC completed delivery of rail stockpile to Flower Cut & Cover
December 2020	RCC completed demolition of the Little Tokyo/Arts District Station
January 2021	RCC completed Historic Broadway Station box roof deck
January 2021	RCC completed Alameda MSE Wall demolition
February 2021	RCC completed Flower Tunnel Wet Standpipe
February 2021	RCC completed Flower Tunnel Emergency Walkways
March 2021	RCC completed Historic Broadway Station Entrance Roof Deck
April 2021	RCC completed Little Tokyo/Arts District Station West Tunnel Vent excavation
May 2021	RCC completed Grand Av Arts/Bunker Hill Station Upper Plaza Deck
June 2021	RCC completed Little Tokyo/Arts District Station East Tunnel Vent structure
June 2021	Regional Connector received \$59.23M American Rescue Plan Act of 2021
July 2021	RCC completed Historic Broadway Station East Tunnel Vent Shaft Excavation
July 2021	Completed deck removal on Flower Street.

August 2021	RCC completed Little Tokyo/Arts District Station Track Installation
August 2021	RCC completed Grand Av Arts/Bunker Hill Station PS3 stair structure.
September 2021	RCC completed Flower Street emergency exit stair structure.
September 2021	RCC completed Train Control Installation from 7 th /Metro Center Station to Historic Broadway Station.
September 2021	RCC completed Platform Edge Paver Installation Grand Av Arts/Bunker Hill Station.
<i>October 2021</i>	<i>RCC completed West Vent Plenum at Historic Broadway Station.</i>
<i>October 2021</i>	<i>RCC completed roof deck at the Wye Fan Plant.</i>
