


# Chief Capital Management Officer Report

April 19, 2007


# Metro Gold Line Eastside Extension Project Update

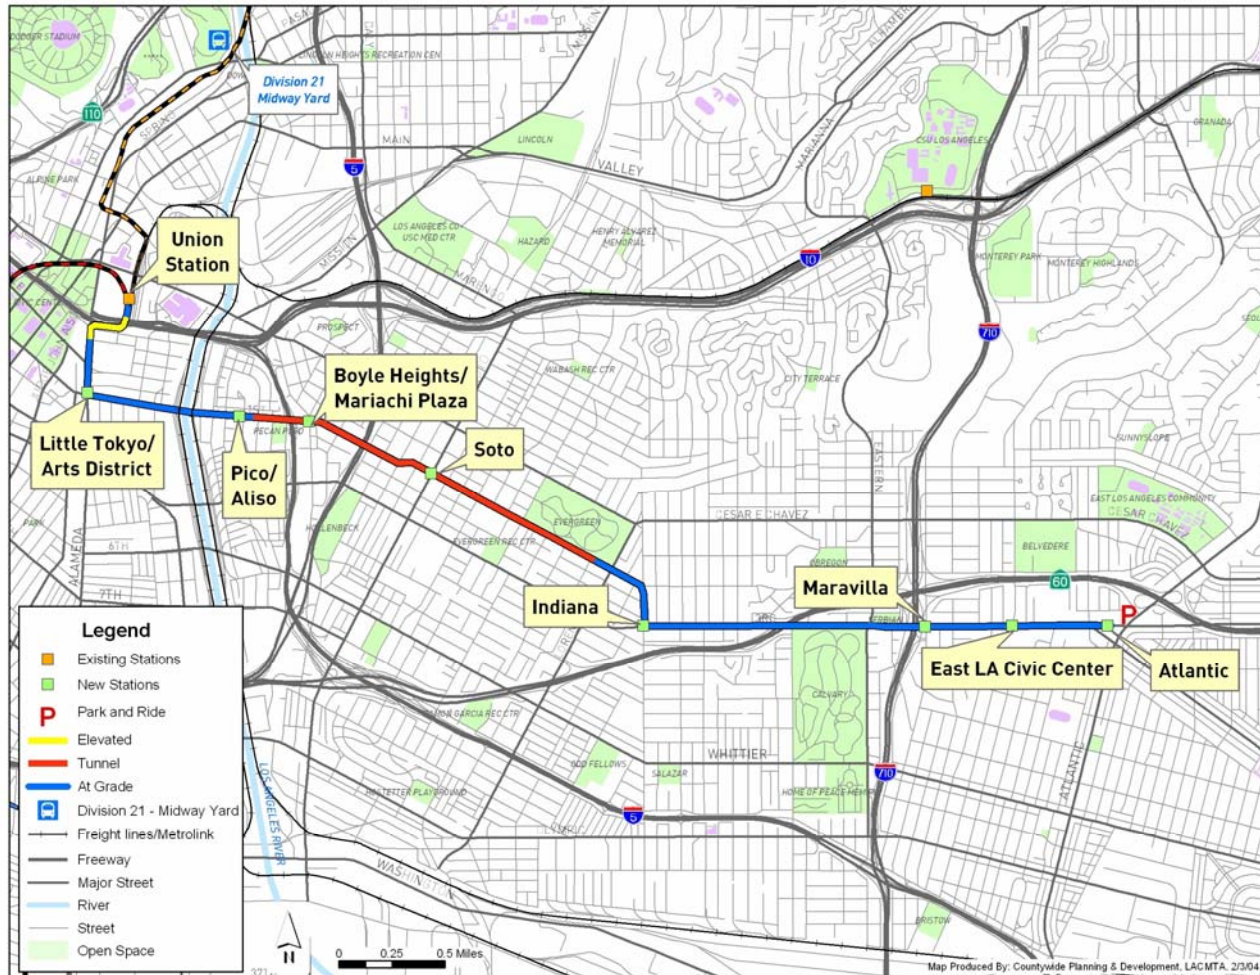

Metro

Gold Line

# Metro Gold Line Eastside Extension Major Construction Activities Project Overview

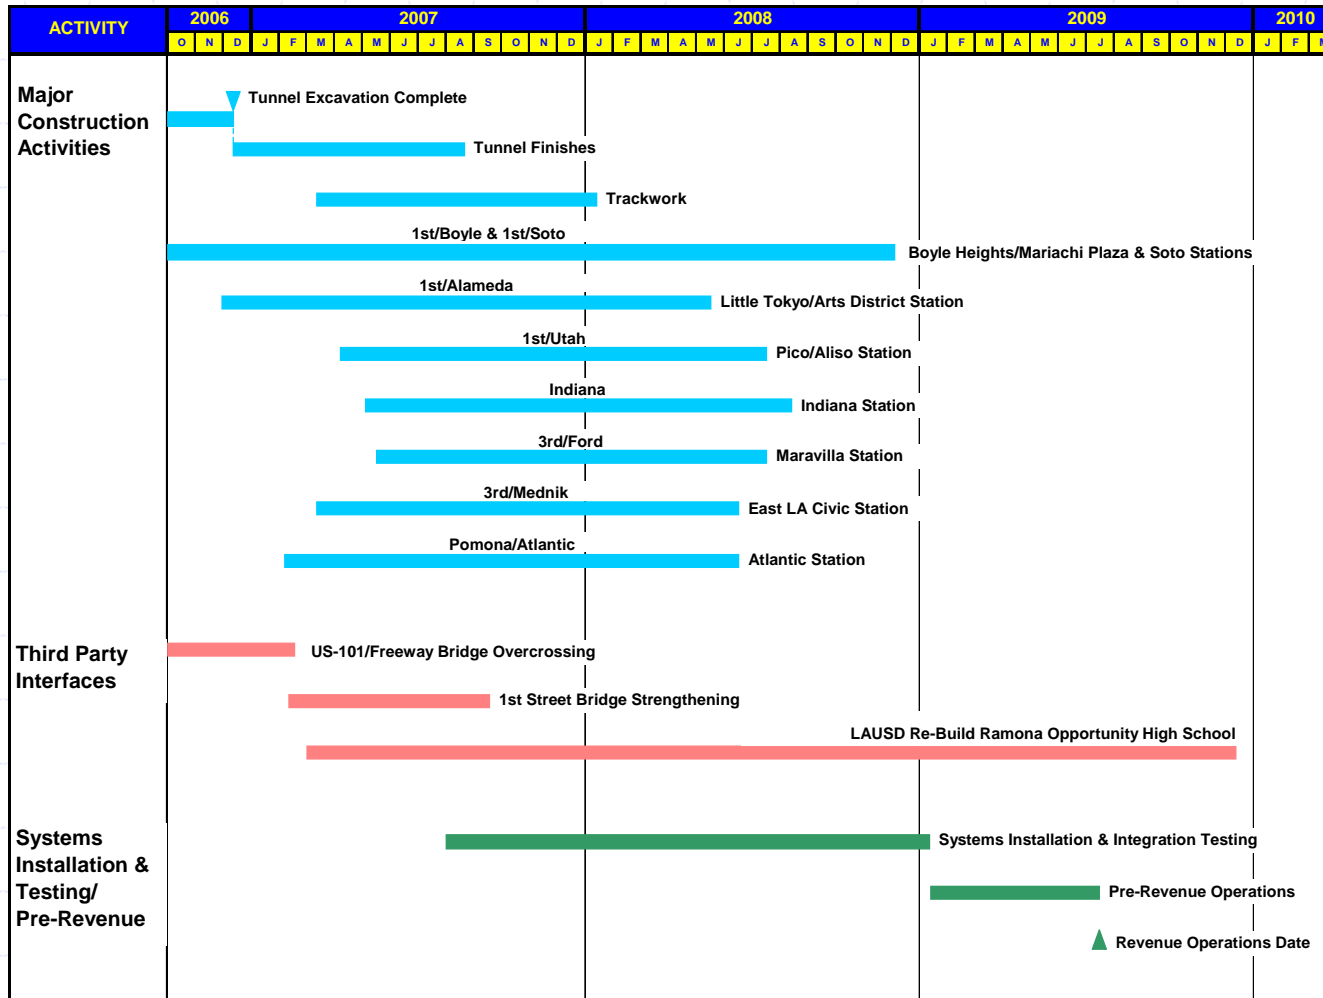

Metro

Gold Line

# Metro Gold Line Eastside Extension 101 Freeway LRT Bridge Overcrossing Caltrans Coordination



- Caltrans turned over the LRT Bridge Structure to Metro on March 15, 2007, for Metro's contractor to begin trackwork and systems installation.

# Metro Gold Line Eastside Extension Little Tokyo/Arts District Station



- Concrete placement of the station platform deck has been completed.
- Pedestrian walkways and platform stairs are being constructed.



Metro

Gold  
Line

# Metro Gold Line Eastside Extension 1<sup>st</sup> Street Bridge & Street Widening City of Los Angeles Coordination



The 1<sup>st</sup> Street Bridge Project will be constructed in three phases.

- Metro has performed Phase I intersection improvements for the City of LA.
- Phase II construction began on February 6, 2007 with completion scheduled to meet the turnover date to Metro in October 2007.
- The City of LA is scheduled to solicit bids for Phase III Bridge Widening in June 2007.
- One-way traffic will be required as construction on the 1<sup>st</sup> Street Bridge increases over the next two years.

# Metro Gold Line Eastside Extension

## 1<sup>st</sup> Street/Utah Street

### Pico/Aliso Station



- Metro's street and sidewalk improvements along the south side of 1<sup>st</sup> Street have been completed.
- Improvements along the north side of 1<sup>st</sup> Street are well underway.
- Construction of LAUSD's East Los Angeles High School #1 began in March 2007.
- Construction of the Light Rail Station will begin in April 2007.

# Metro Gold Line Eastside Extension

## 1<sup>st</sup> Street/Utah Street

### Pico/Aliso Station





# Metro Gold Line Eastside Extension Tunnel Construction Activities



- Excavation of both tunnels was completed in December 2006.
- Construction of the tunnel track level invert slab and walkways is underway.



Metro

Gold  
Line

# Metro Gold Line Eastside Extension West and East Tunnel Portals



West Tunnel Portal at 1<sup>st</sup>/Gless



East Tunnel Portal at 1<sup>st</sup>/Lorena

- The concrete roof structure on the West Tunnel Portal is nearly completed and the roof structure on the East Portal is being poured.

# Metro Gold Line Eastside Extension Project

## Metro and LAUSD Coordination

### Indiana Station/Ramona Opportunity High School



Indiana Light Rail Transit Station



LAUSD Ramona Opportunity High School

- LAUSD received the Re-build of Ramona Opportunity High School construction bids on October 10, 2006 and issued the construction notice to proceed on February 7, 2007.
- The \$47.2 million funding plan for the reconstruction of the school was approved by both the Metro Board of Directors and the LAUSD Board of Education.
- The property exchange between Metro and LAUSD occurred on April 6, 2007 to allow the Indiana Light Rail Transit Station to be constructed on the east side of Indiana Street.

# Metro Gold Line Eastside Extension Project

## Indiana Station

### Final Design Streetscape and Landscape



# Metro Gold Line Eastside Extension Project

## U-Channel Along 3<sup>rd</sup> Street



- Construction of the u-channel exterior walls is ongoing.
- Embedded track rail installation has begun within the u-channel.

# Metro Gold Line Eastside Extension Project Atlantic Station



- Placement of the station platform invert slab.

# Metro Gold Line Eastside Extension



## End of Presentation
