


SOUTHERN CALIFORNIA RAPID TRANSIT DISTRICT

METRO RAIL PROJECT


MOS — 1

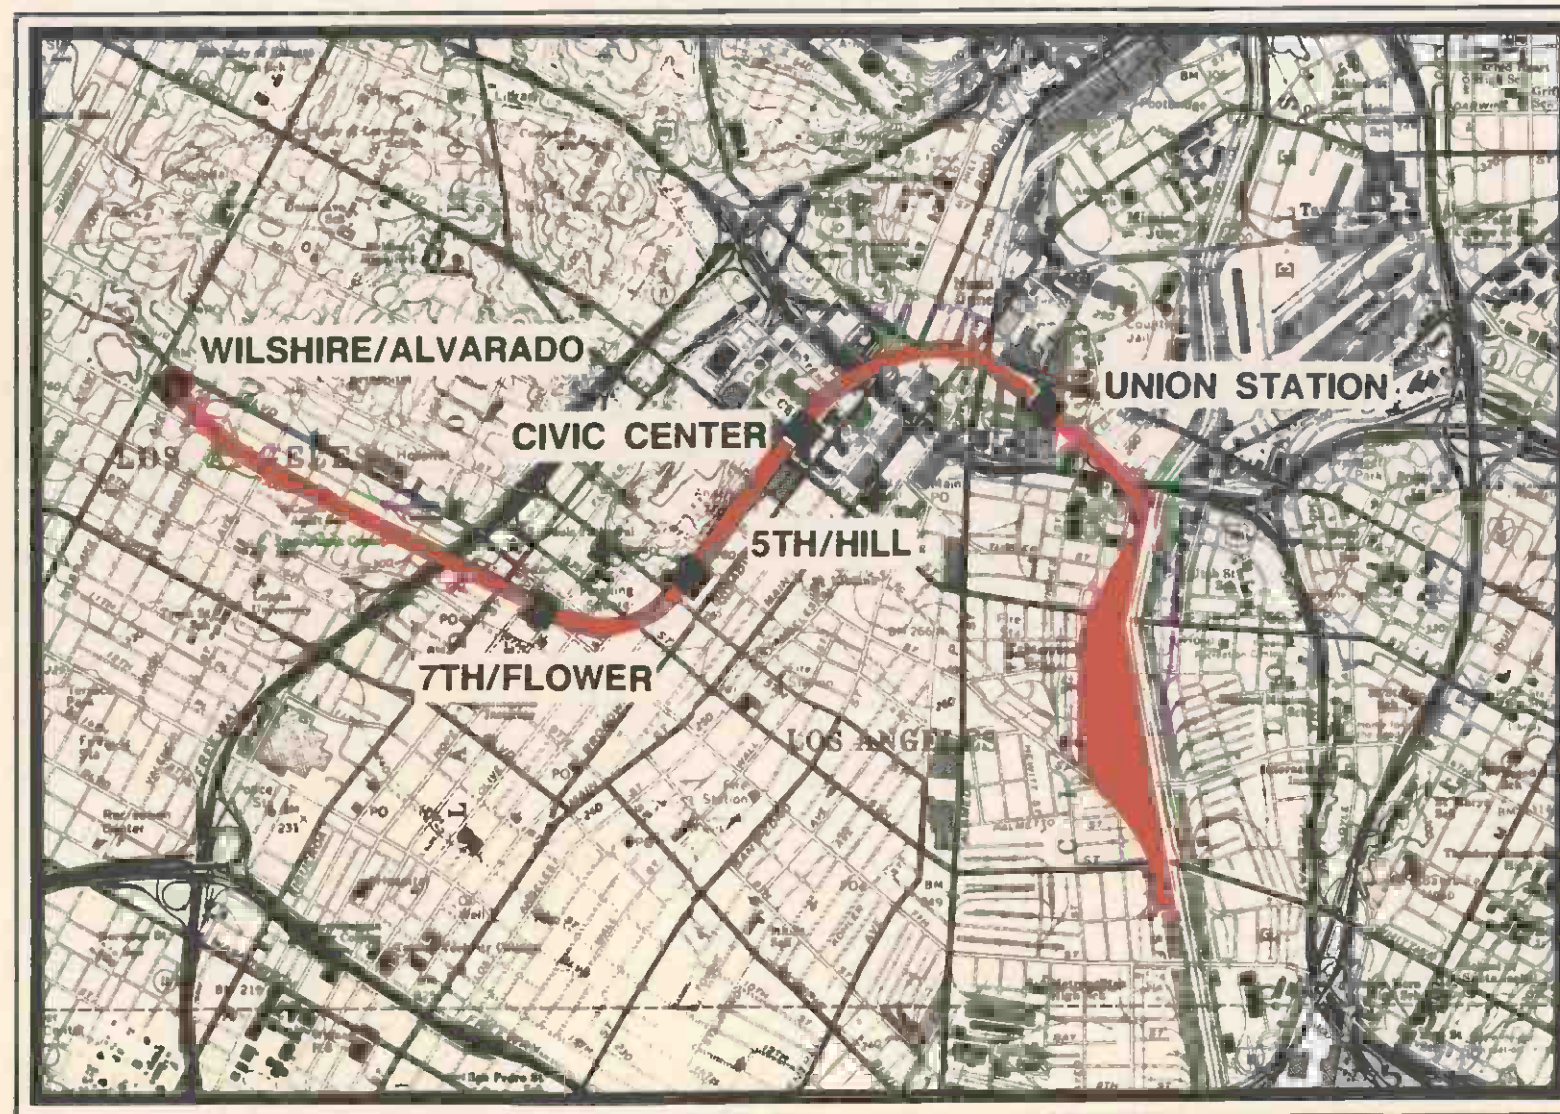

EXECUTIVE SCHEDULE

APRIL 1989

SCRTD
1989
.M81
E97
Apr
1989

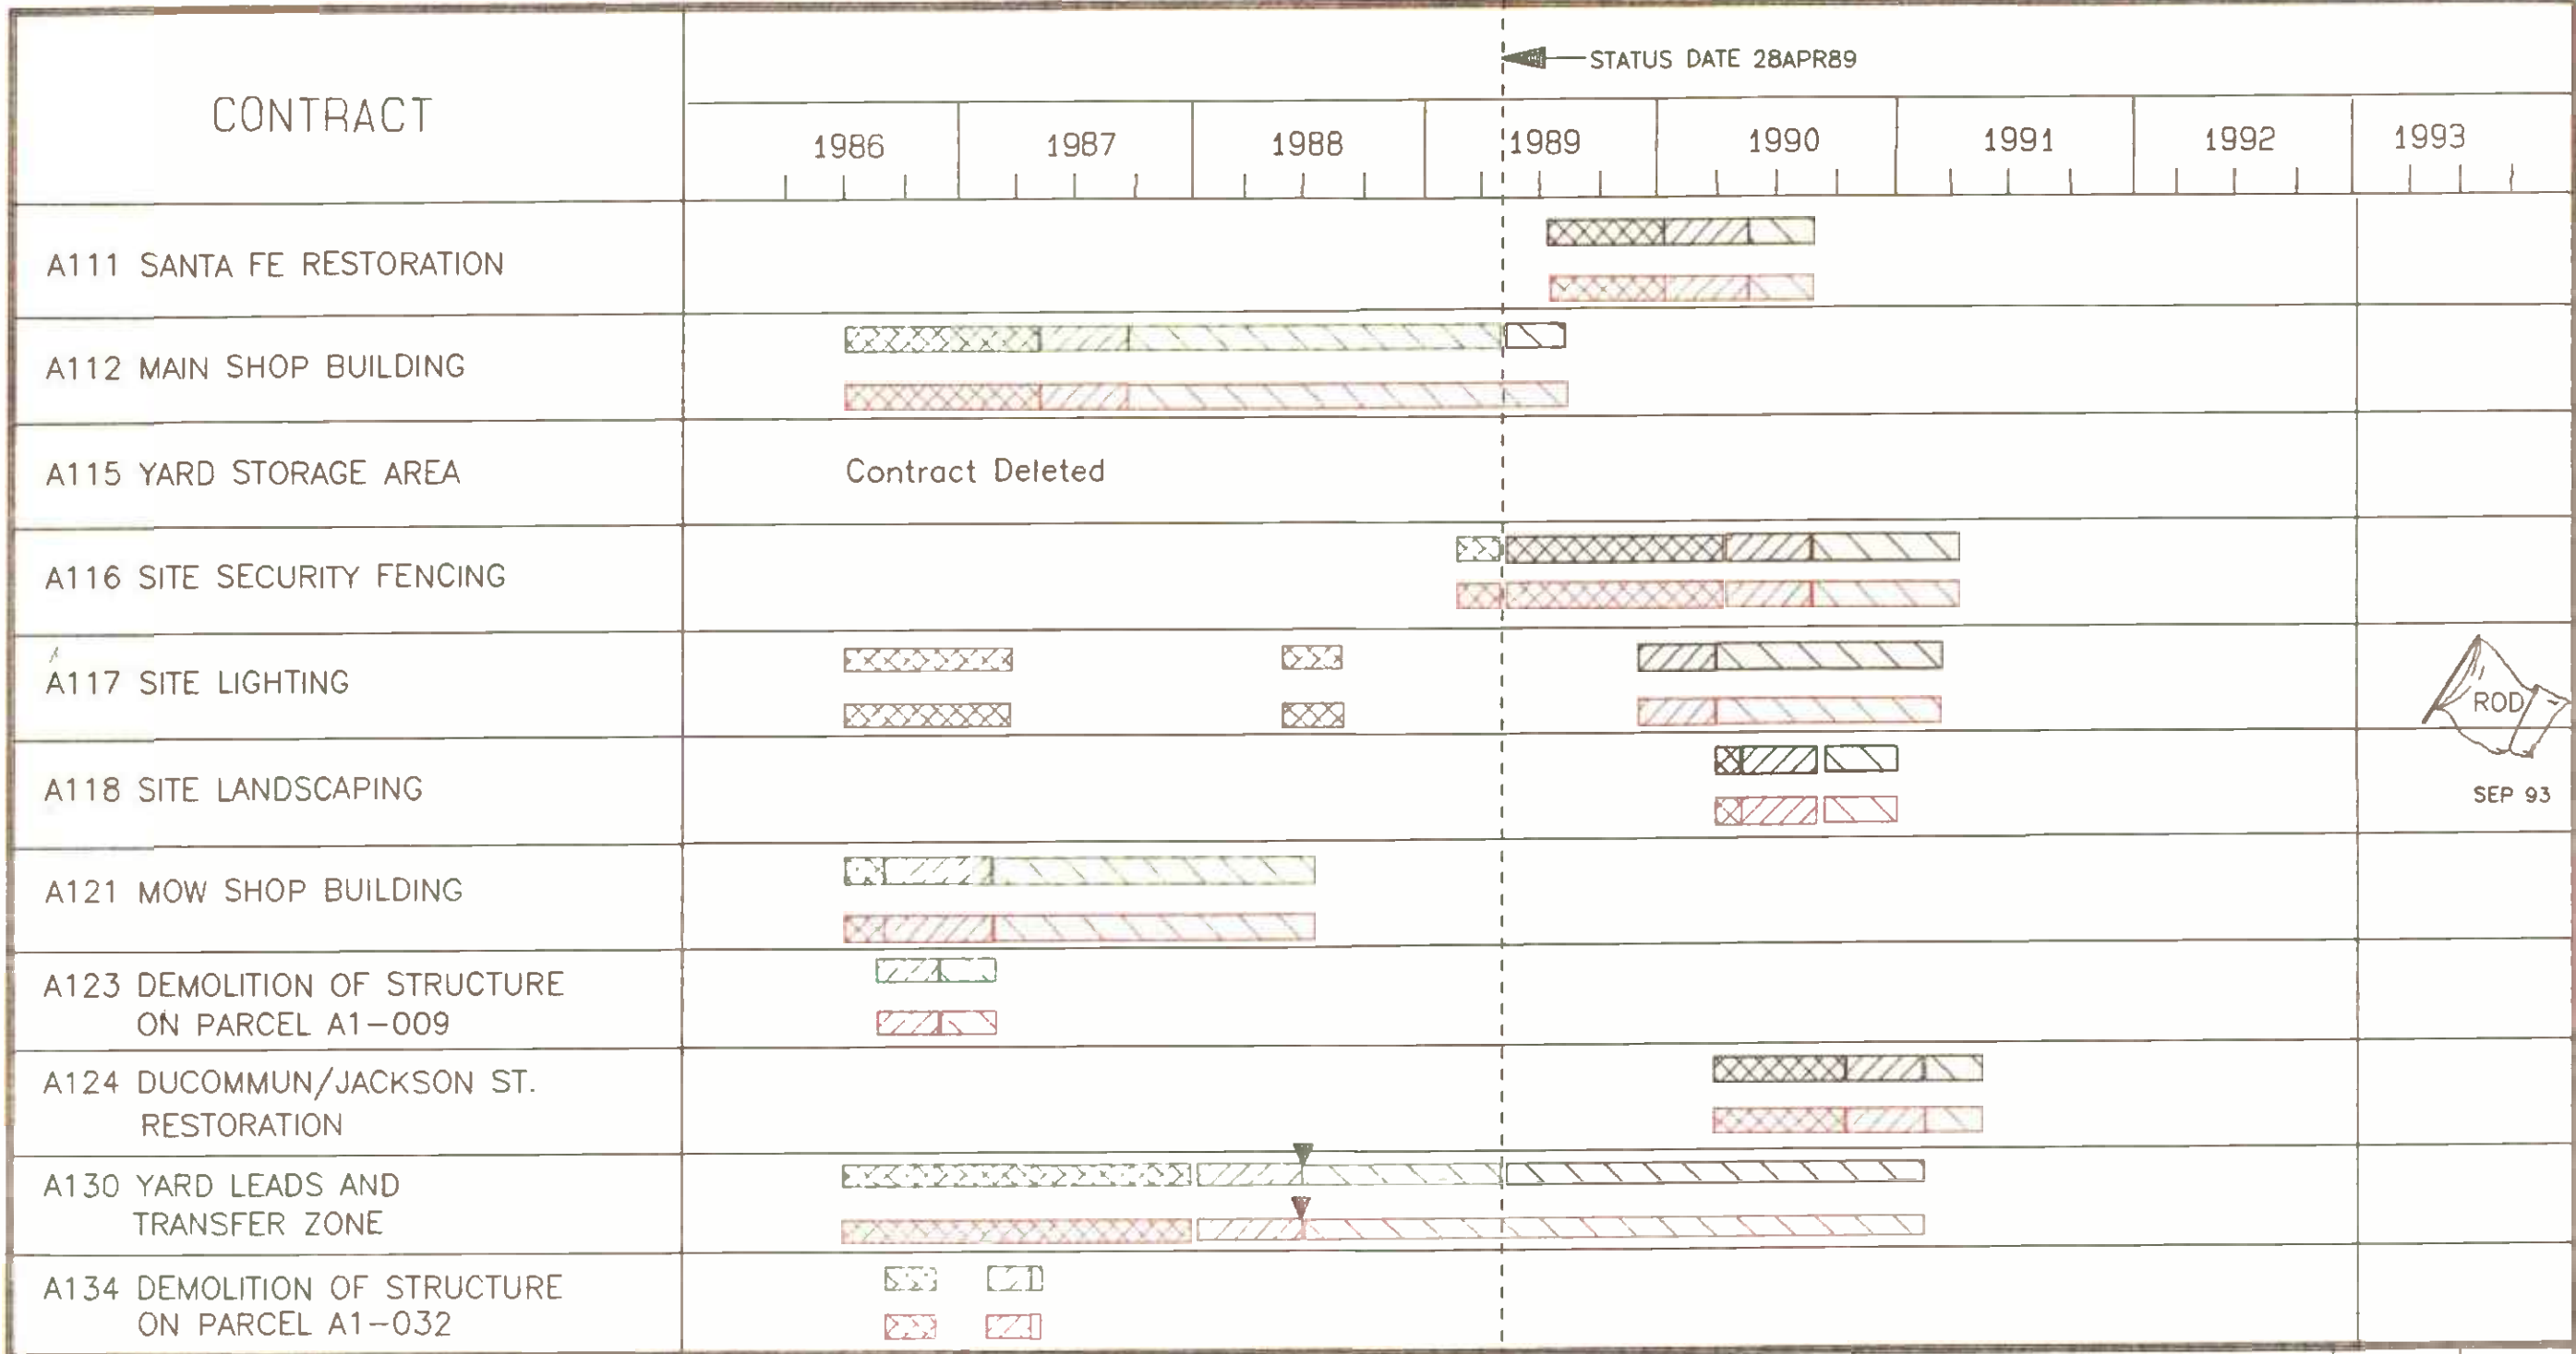

SEP 93

LEGEND	CURRENT SCHEDULE	PROGRESS	APPROVED SCHEDULE
DESIGN	█	█	█
BID & AWARD	█	█	█
CONSTRUCTION	█	█	█
▼	RIGHT OF WAY AVAILABLE		

SOUTHERN CALIFORNIA RAPID TRANSIT DISTRICT
 METRO RED LINE PROJECT (MOS-1)
 EXECUTIVE SCHEDULE


PAGE 1 OF 11

PREPARED BY *T.C. Sherry*
PROGRAM CONTROL MANAGER (SCHEDULES)

CHECKED BY *Jeffrey R. Williams*
DIRECTOR OF PROGRAM CONTROL

APPROVED BY *W. J. Thine*
ASSISTANT GENERAL MANAGER

DATE	REV
25SEP86	5
14JAN88	6
30DEC88	6D
13APR89	7

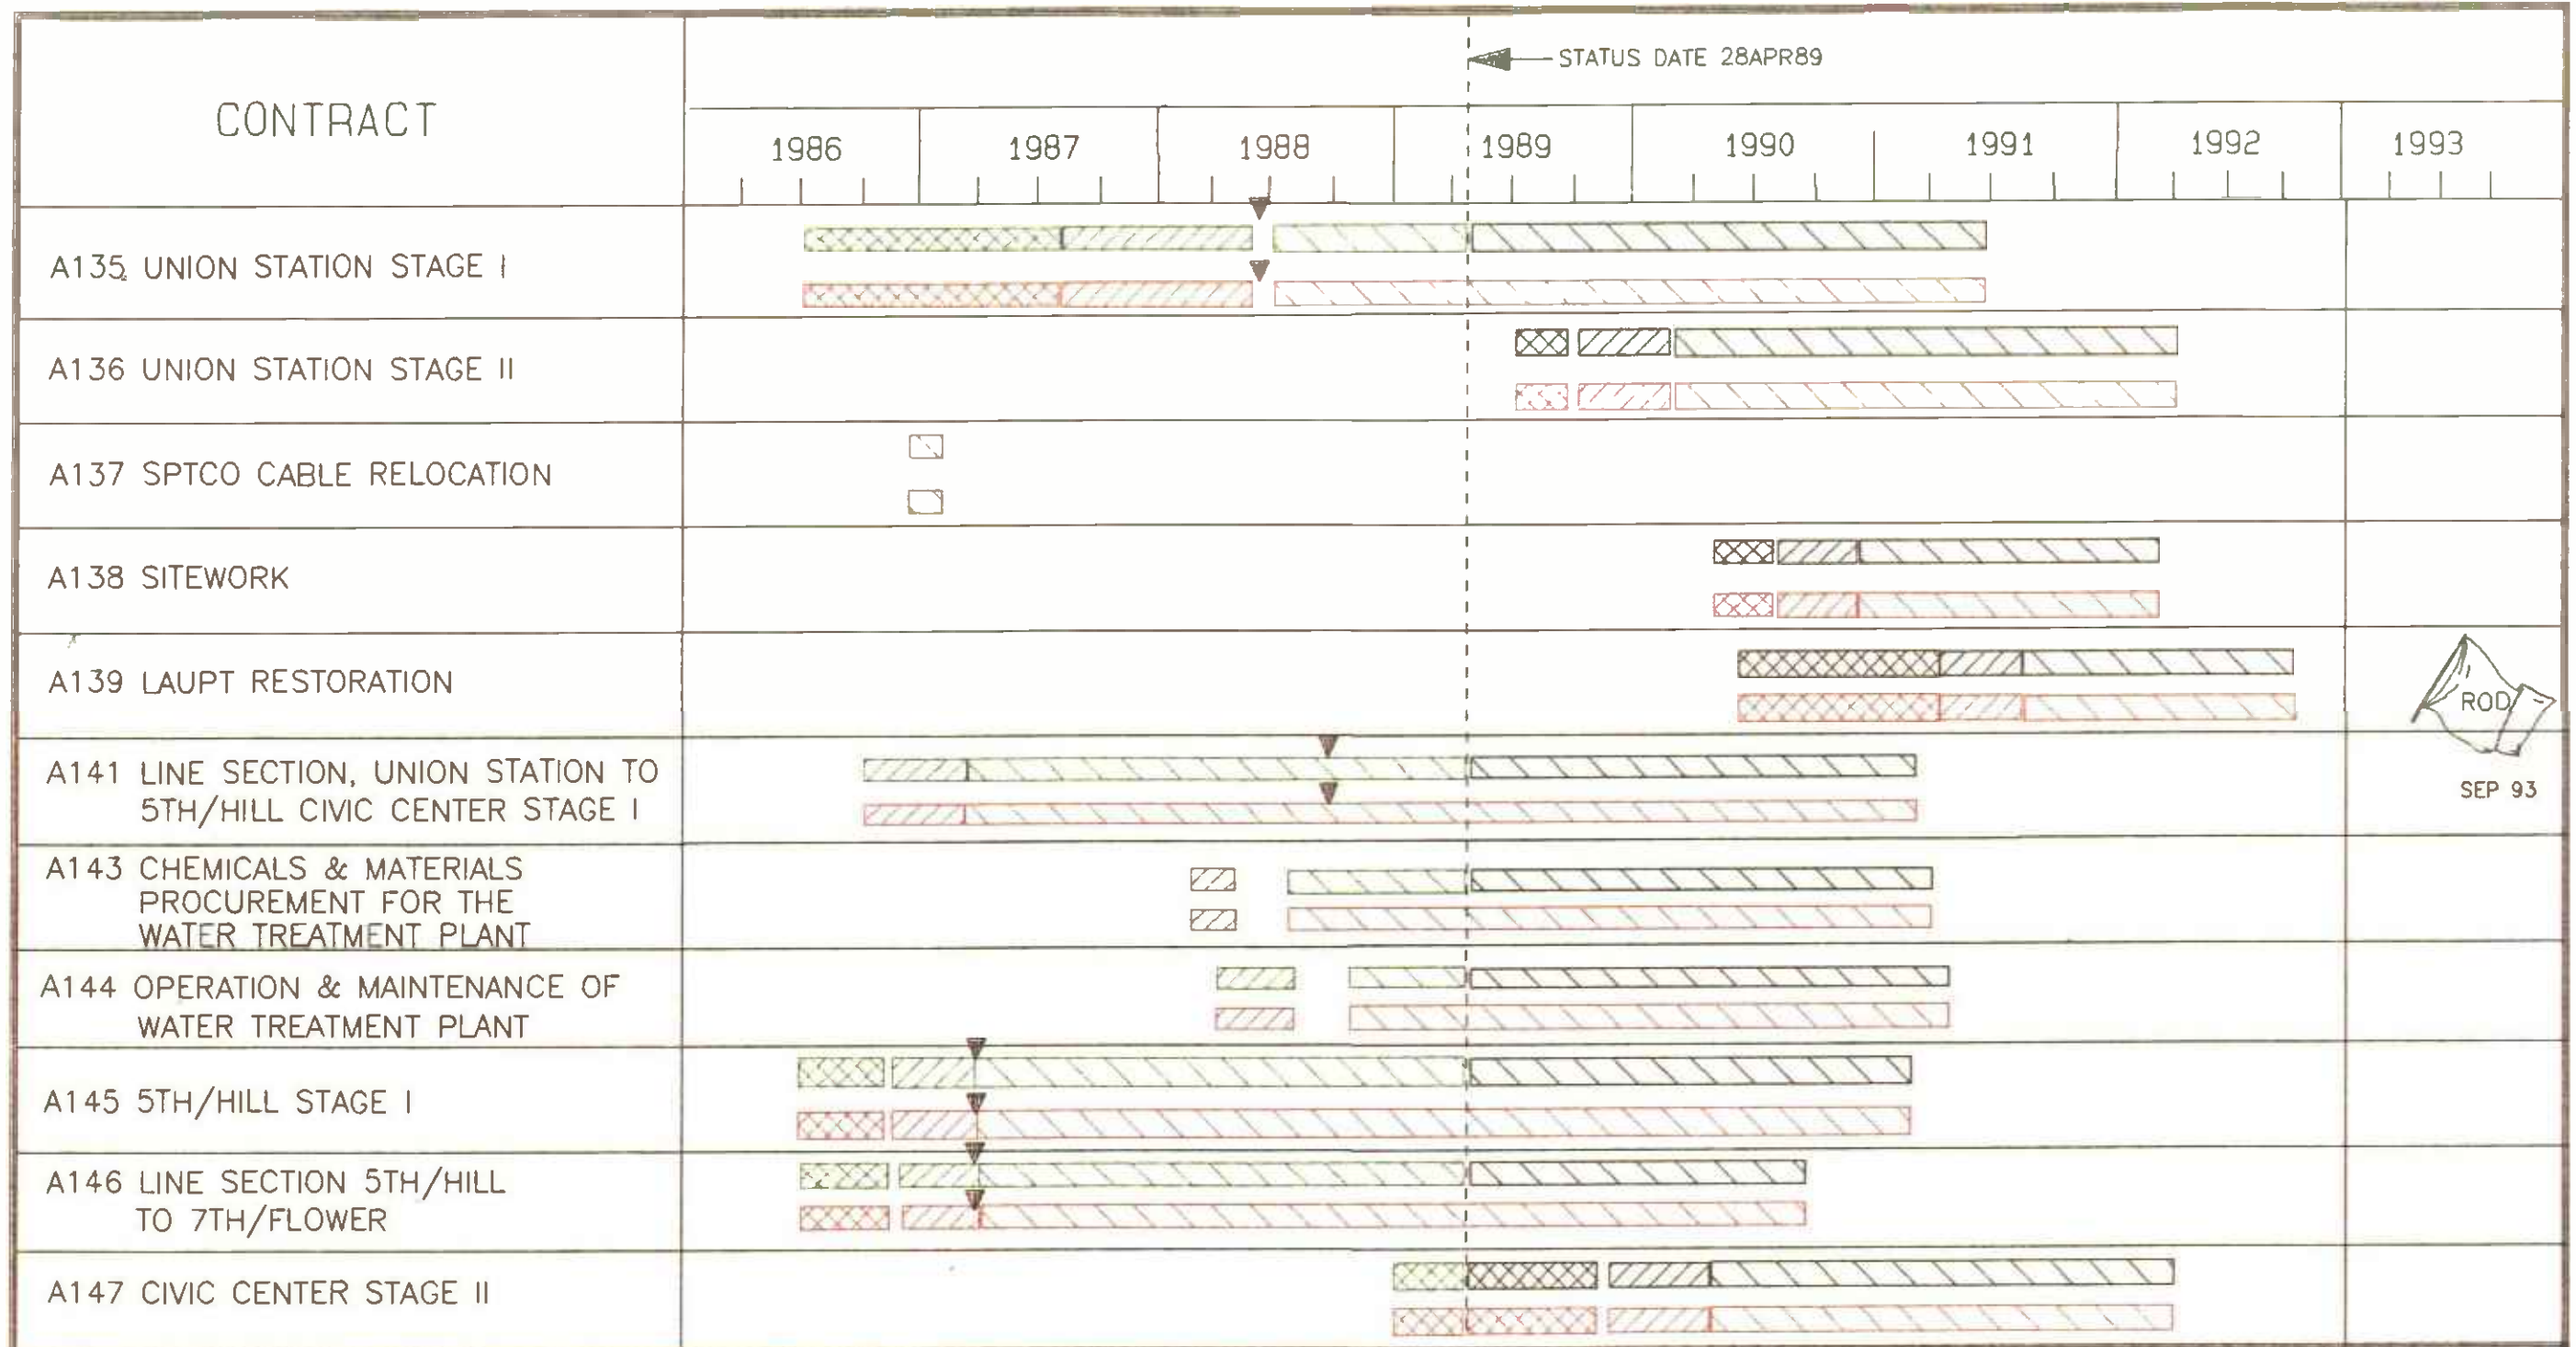

LEGEND			
	CURRENT SCHEDULE	PROGRESS	APPROVED SCHEDULE
DESIGN			
BID & AWARD			
CONSTRUCTION			
	▼ RIGHT OF WAY AVAILABLE		

SOUTHERN CALIFORNIA RAPID TRANSIT DISTRICT
METRO RED LINE PROJECT (MOS-1)
EXECUTIVE SCHEDULE


PAGE 2 OF 11

PREPARED BY *W.C. Sherry*
PROGRAM CONTROL MANAGER (SCHEDULES)

CHECKED BY *Joseph J. ...*
DIRECTOR OF PROGRAM CONTROL

APPROVED BY *JOC FOR W.J. RHINE*
ASSISTANT GENERAL MANAGER

DATE	REV
25SEP86	5
14JAN88	6
30DEC88	6D
13APR89	7

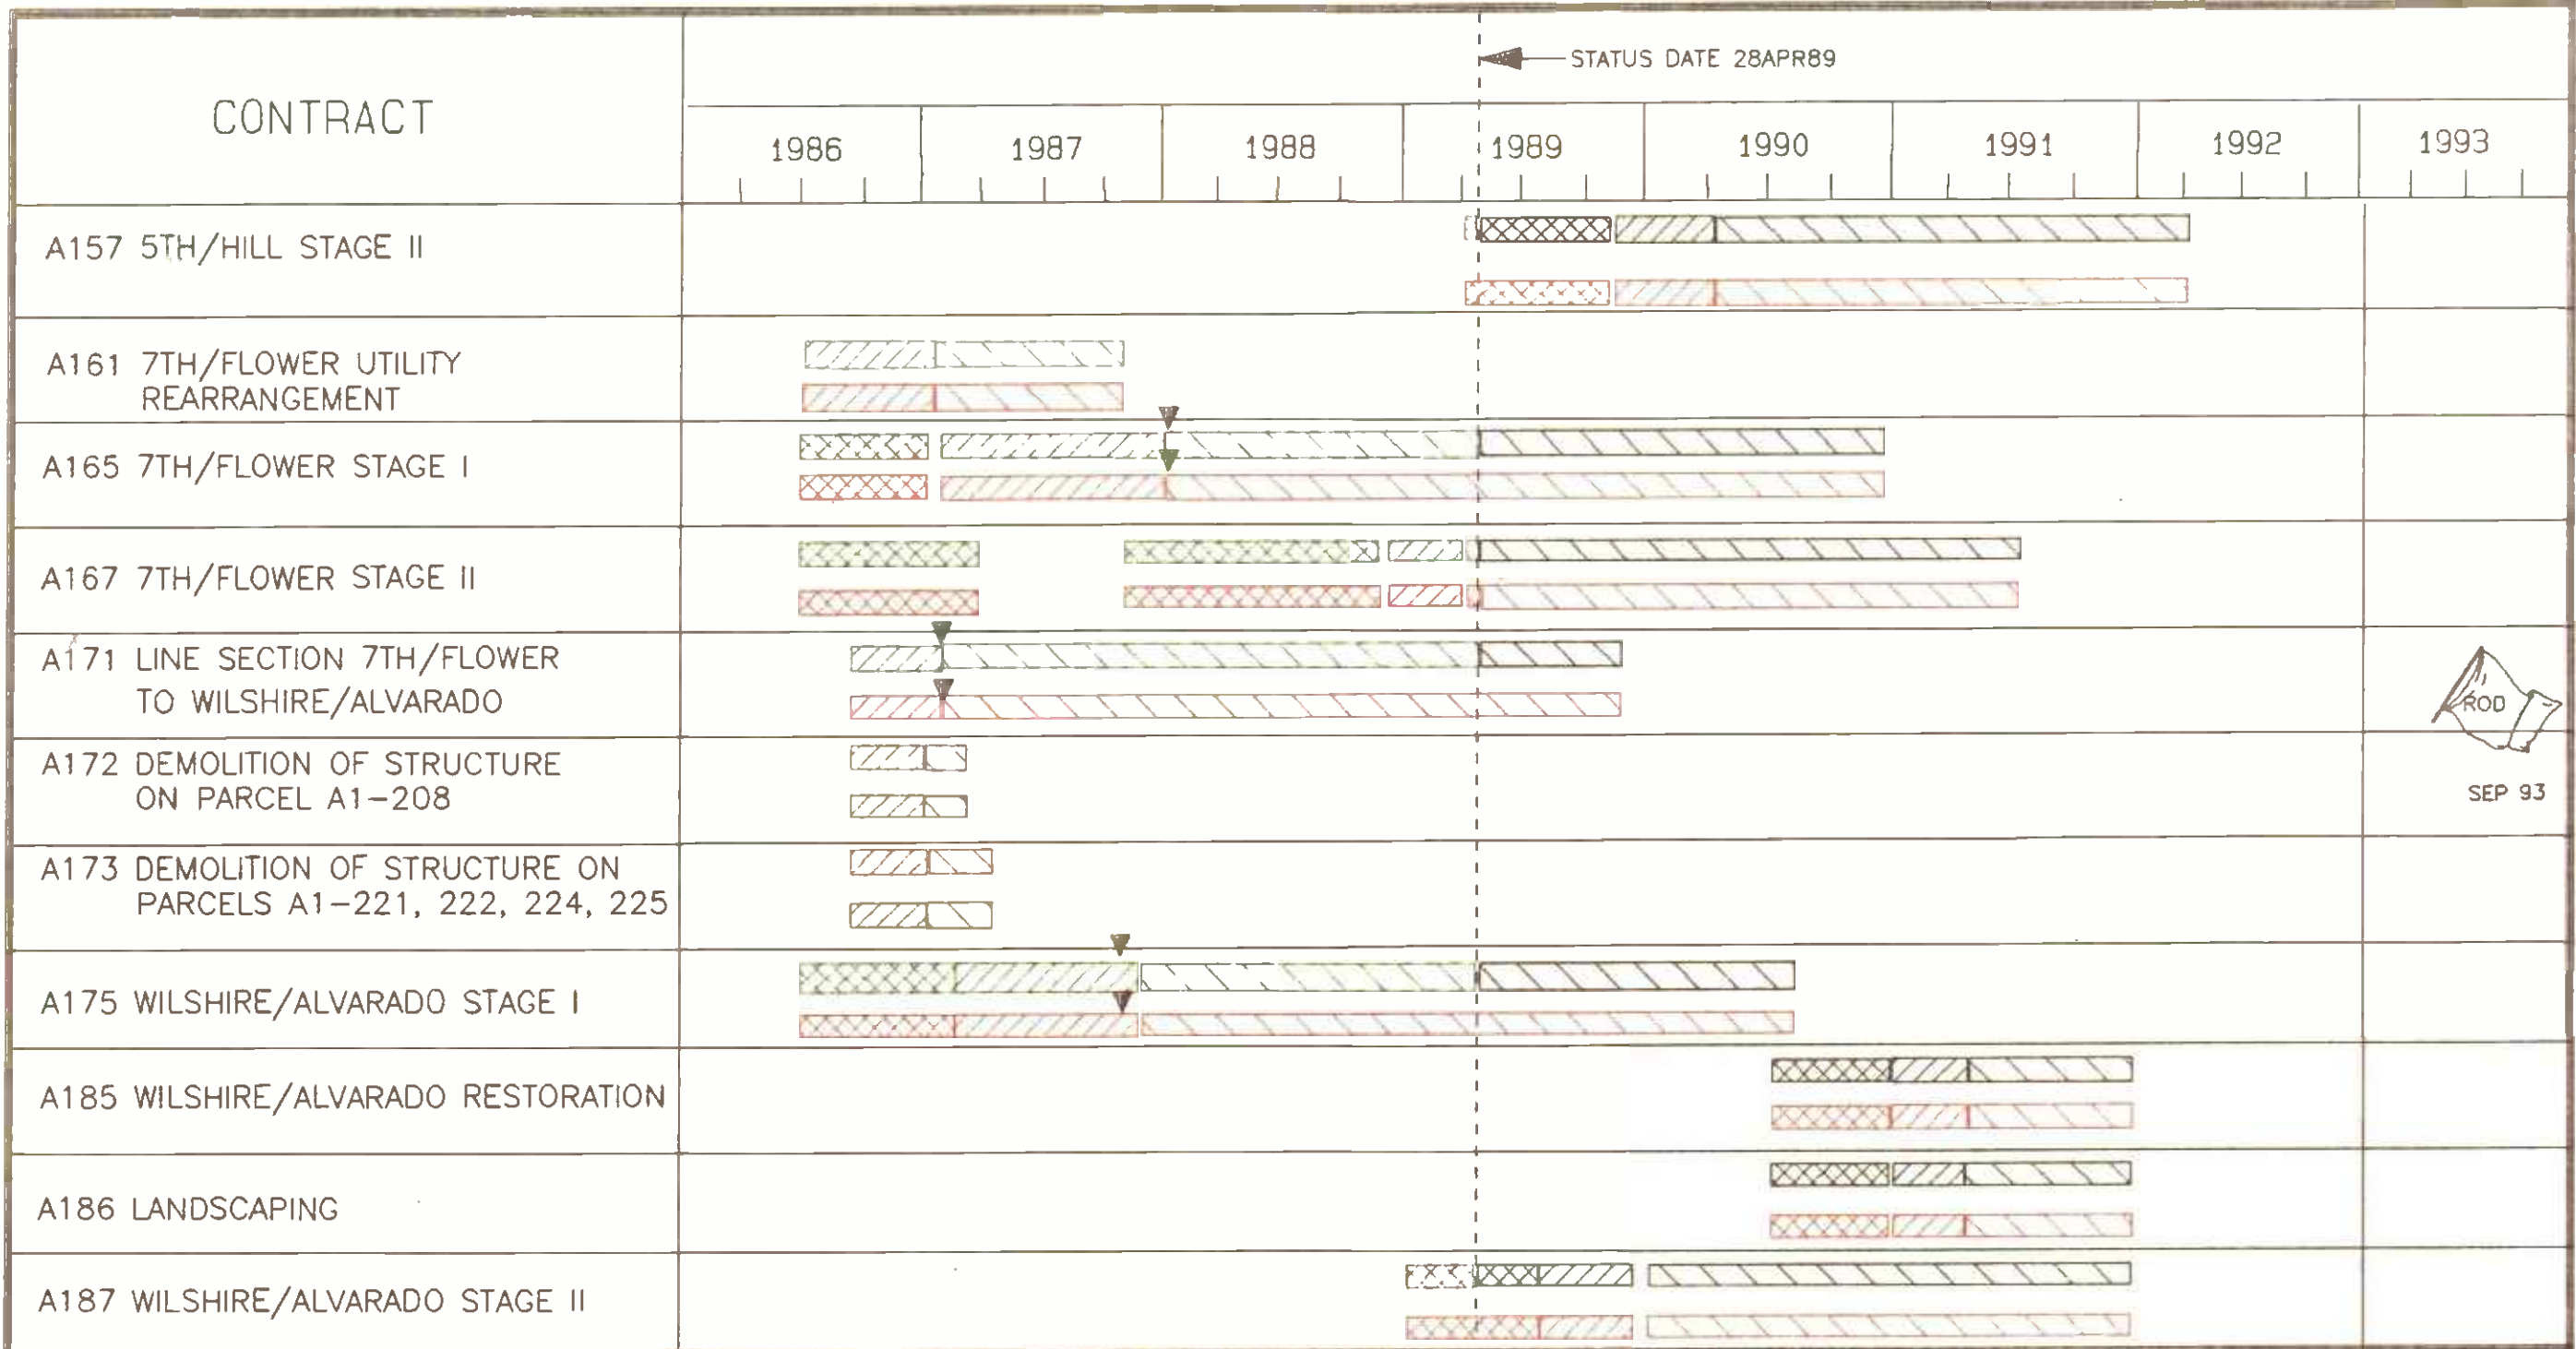

LEGEND	CURRENT SCHEDULE	PROGRESS	APPROVED SCHEDULE
DESIGN			
BID & AWARD			
CONSTRUCTION			
	▼ RIGHT OF WAY AVAILABLE		

SOUTHERN CALIFORNIA RAPID TRANSIT DISTRICT
METRO RED LINE PROJECT (MOS-1)
EXECUTIVE SCHEDULE


PAGE 3 OF 11

PREPARED BY *J.C. Sherry*
PROGRAM CONTROL MANAGER (SCHEDULES)

CHECKED BY *[Signature]*
DIRECTOR OF PROGRAM CONTROL

APPROVED BY *[Signature]*
ASSISTANT GENERAL MANAGER


DATE	REV
25SEP88	5
14JAN88	6
30DEC88	6D
13APR89	7

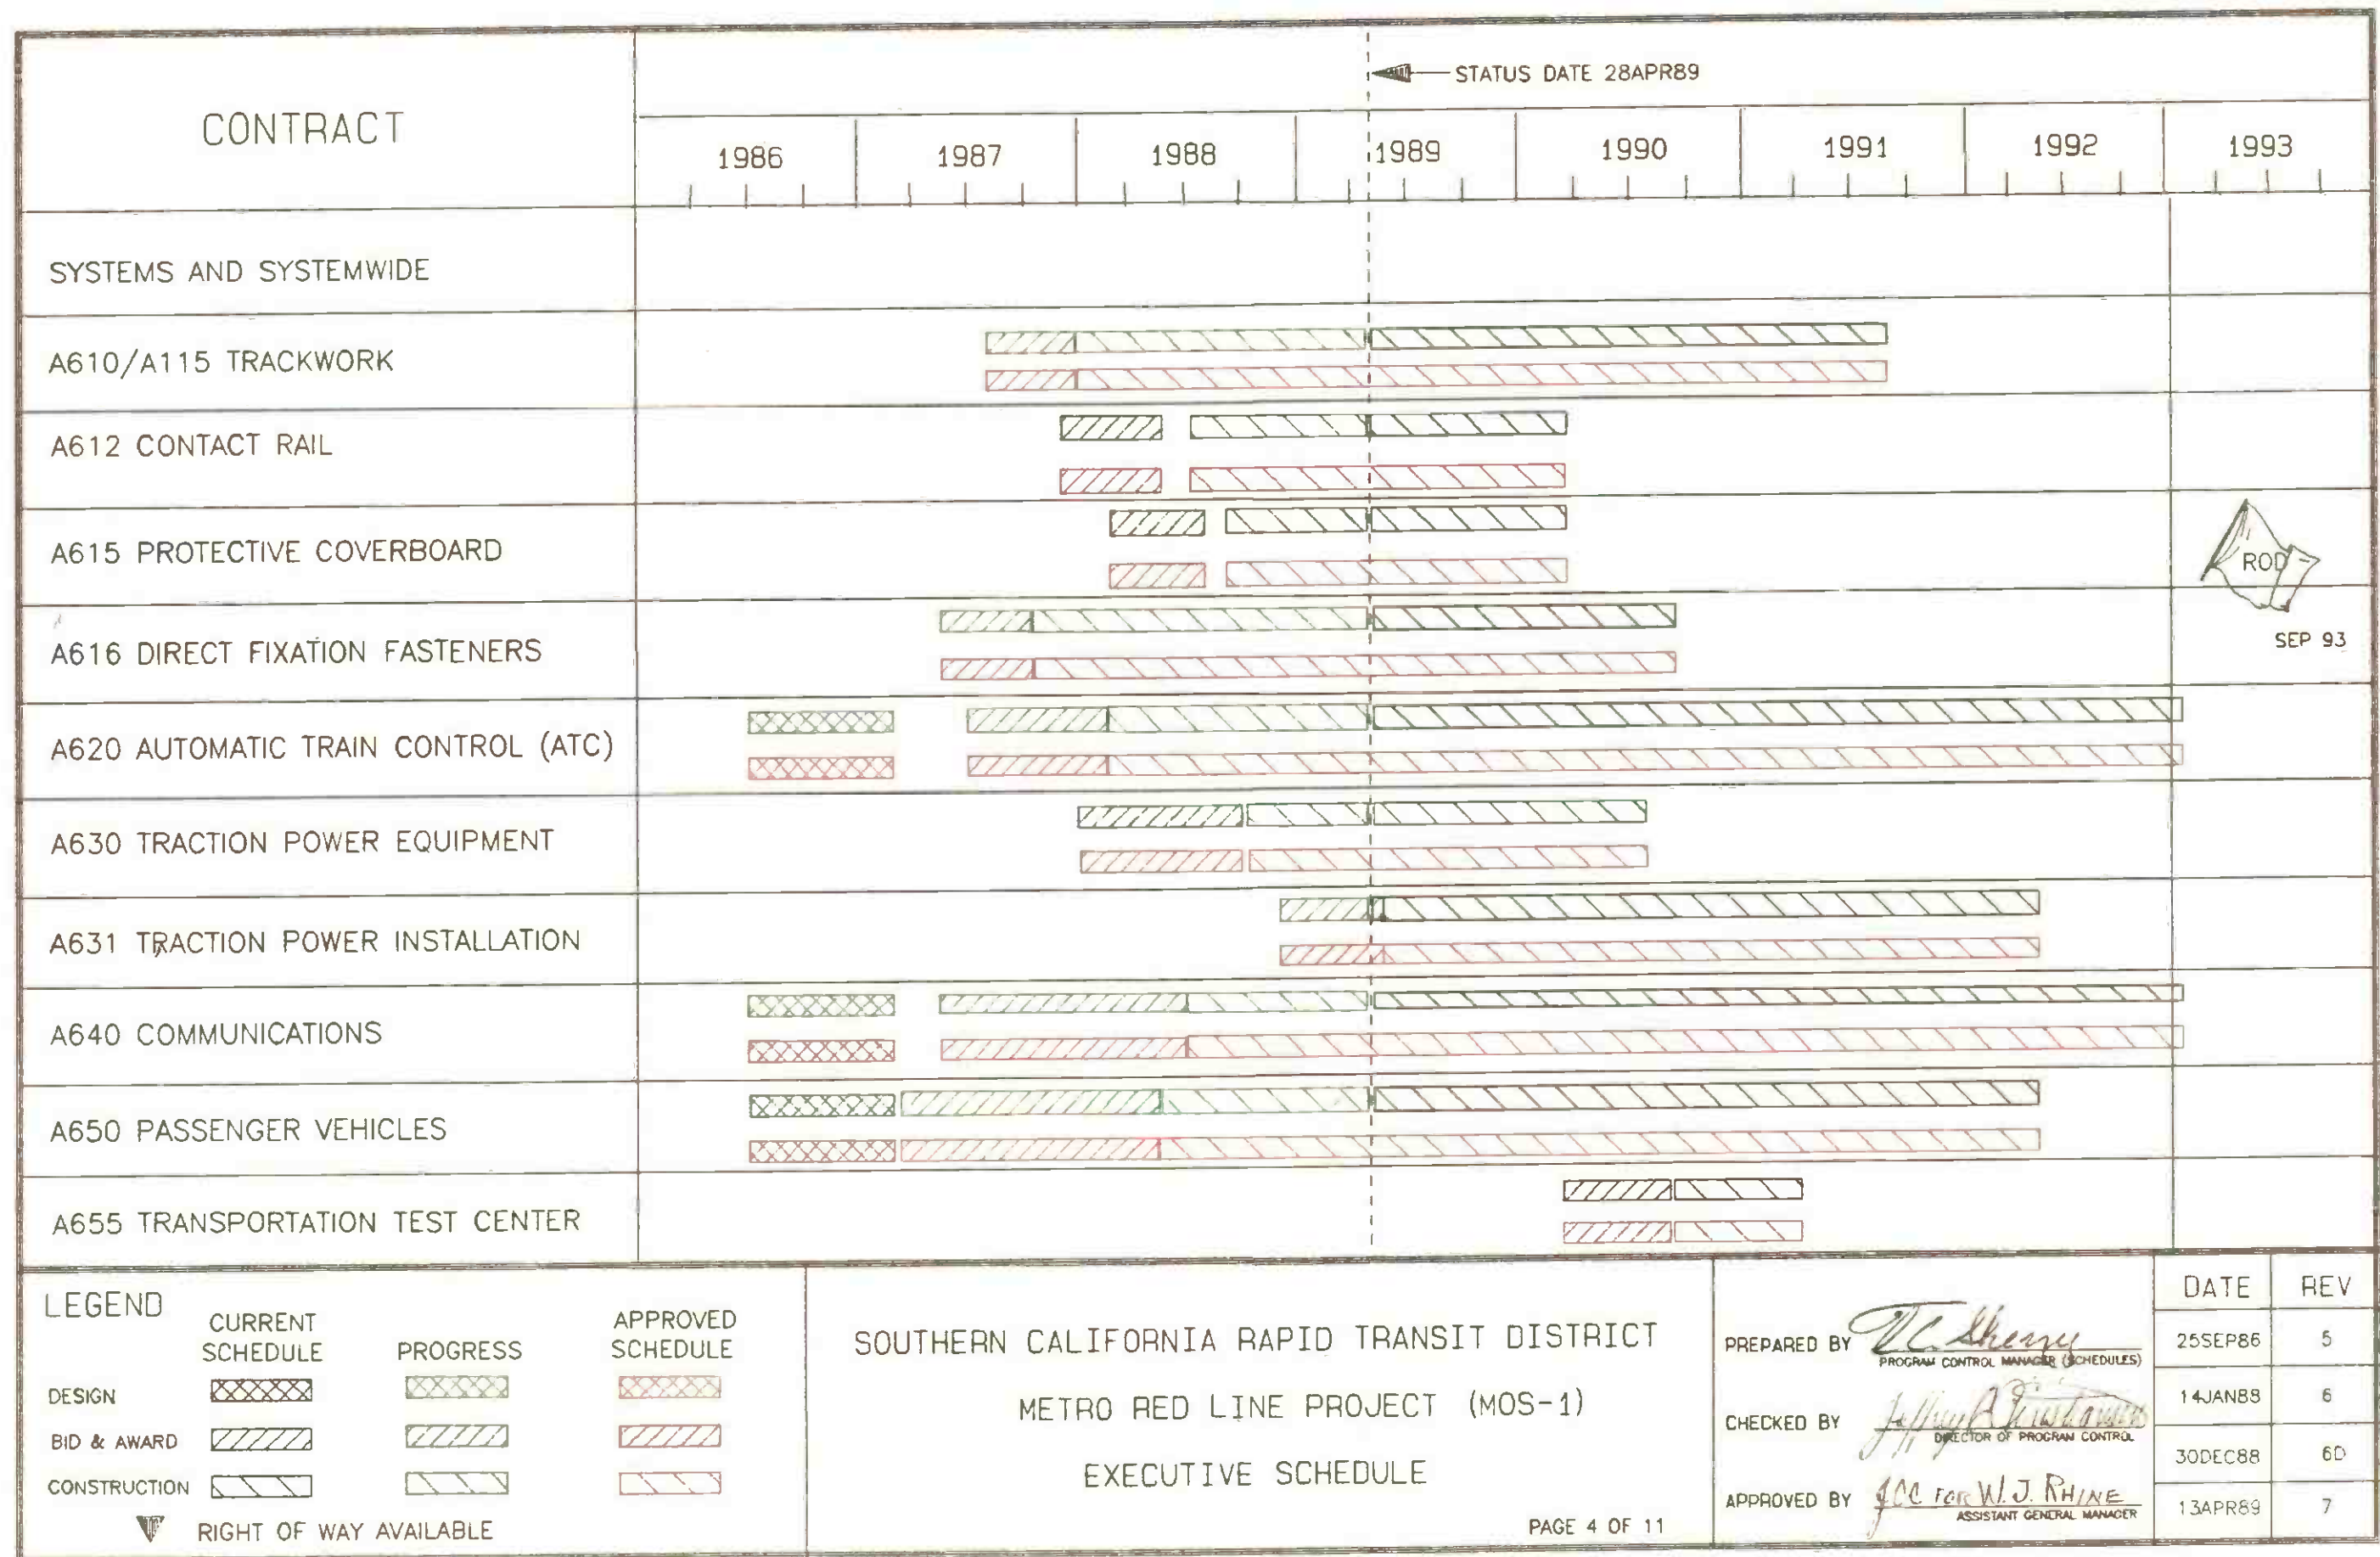

LEGEND	CURRENT SCHEDULE	PROGRESS	APPROVED SCHEDULE
DESIGN			
BID & AWARD			
CONSTRUCTION			
	RIGHT OF WAY AVAILABLE		

SOUTHERN CALIFORNIA RAPID TRANSIT DISTRICT
 METRO RED LINE PROJECT (MOS-1)
 EXECUTIVE SCHEDULE

	DATE	REV
PREPARED BY <i>J.C. Sherry</i> PROGRAM CONTROL MANAGER (SCHEDULES)	25SEP86	5
CHECKED BY <i>Jeffrey A. ...</i> DIRECTOR OF PROGRAM CONTROL	14JAN88	6
APPROVED BY <i>JCC FOR W.J. RHINE</i> ASSISTANT GENERAL MANAGER	30DEC88	6D
	13APR89	7

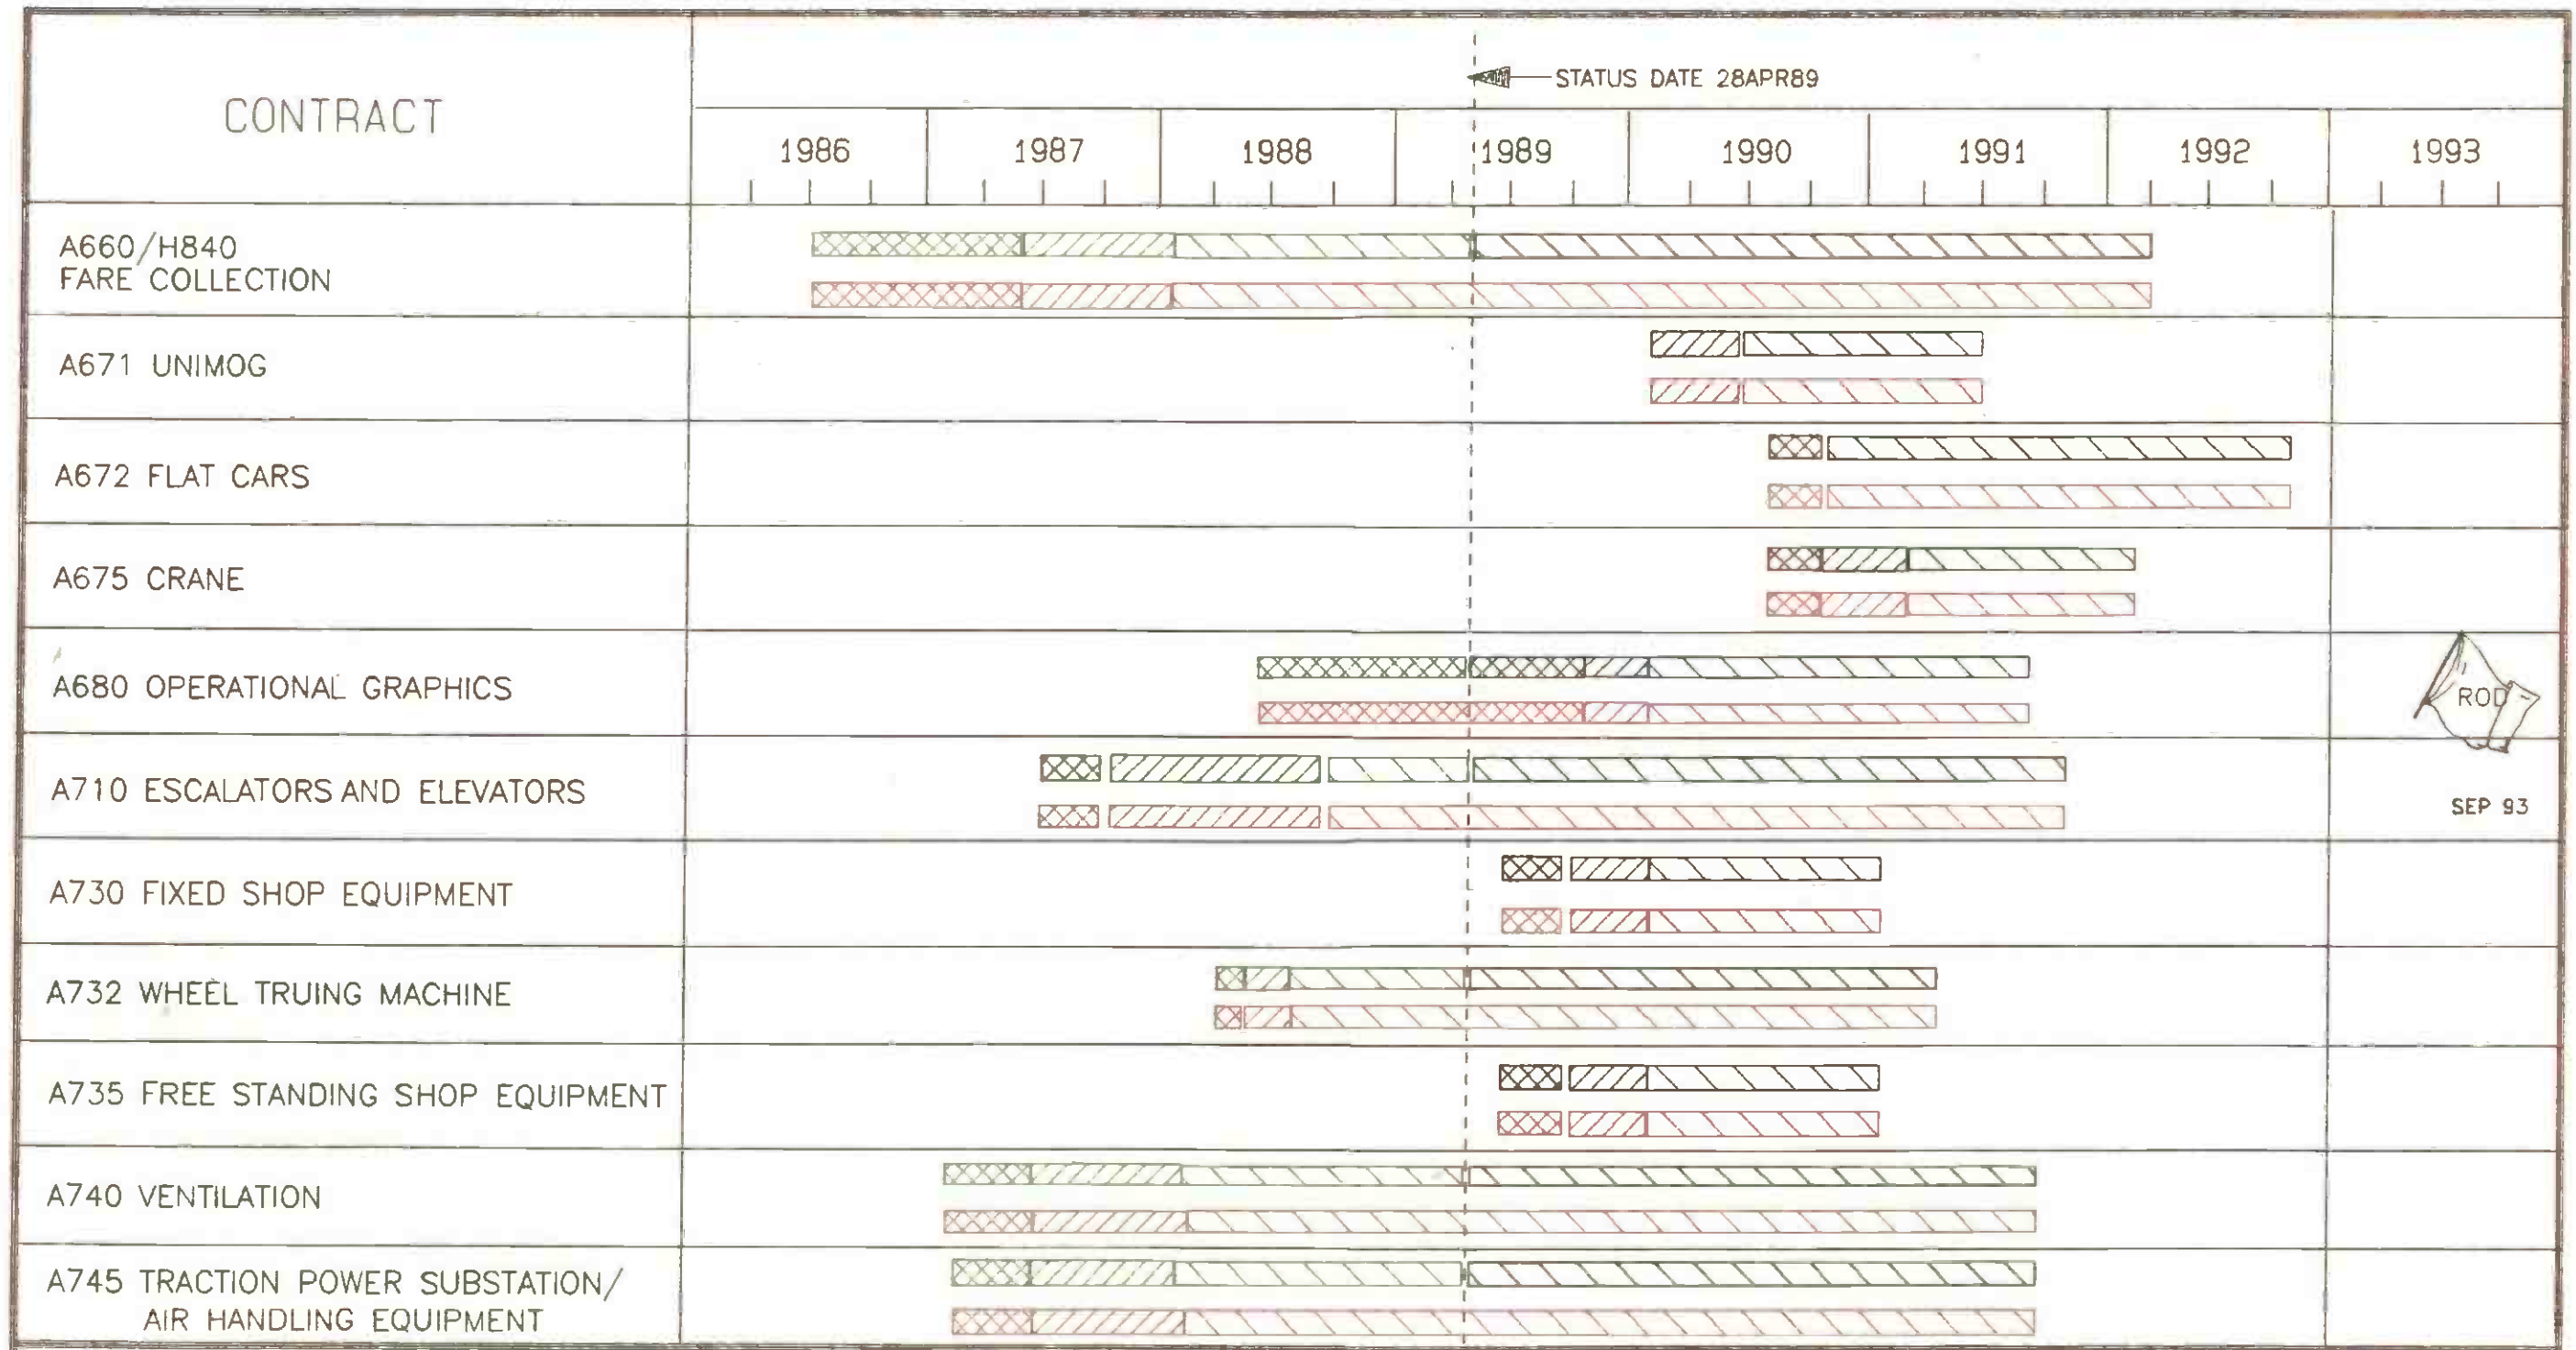


LEGEND	CURRENT SCHEDULE	PROGRESS	APPROVED SCHEDULE
DESIGN	[Cross-hatch]	[Diagonal lines]	[Cross-hatch]
BID & AWARD	[Diagonal lines]	[Diagonal lines]	[Diagonal lines]
CONSTRUCTION	[Diagonal lines]	[Diagonal lines]	[Diagonal lines]
	▼ RIGHT OF WAY AVAILABLE		

SOUTHERN CALIFORNIA RAPID TRANSIT DISTRICT
 METRO RED LINE PROJECT (MOS-1)
 EXECUTIVE SCHEDULE

PAGE 5 OF 11

	DATE	REV
PREPARED BY <i>J.C. Cherry</i> PROGRAM CONTROL MANAGER (SCHEDULES)	25SEP86	5
CHECKED BY <i>J. P. ...</i> DIRECTOR OF PROGRAM CONTROL	14JAN88	6
APPROVED BY <i>JCC FOR W.J. RHINE</i> ASSISTANT GENERAL MANAGER	30DEC88	6D
	13APR89	7

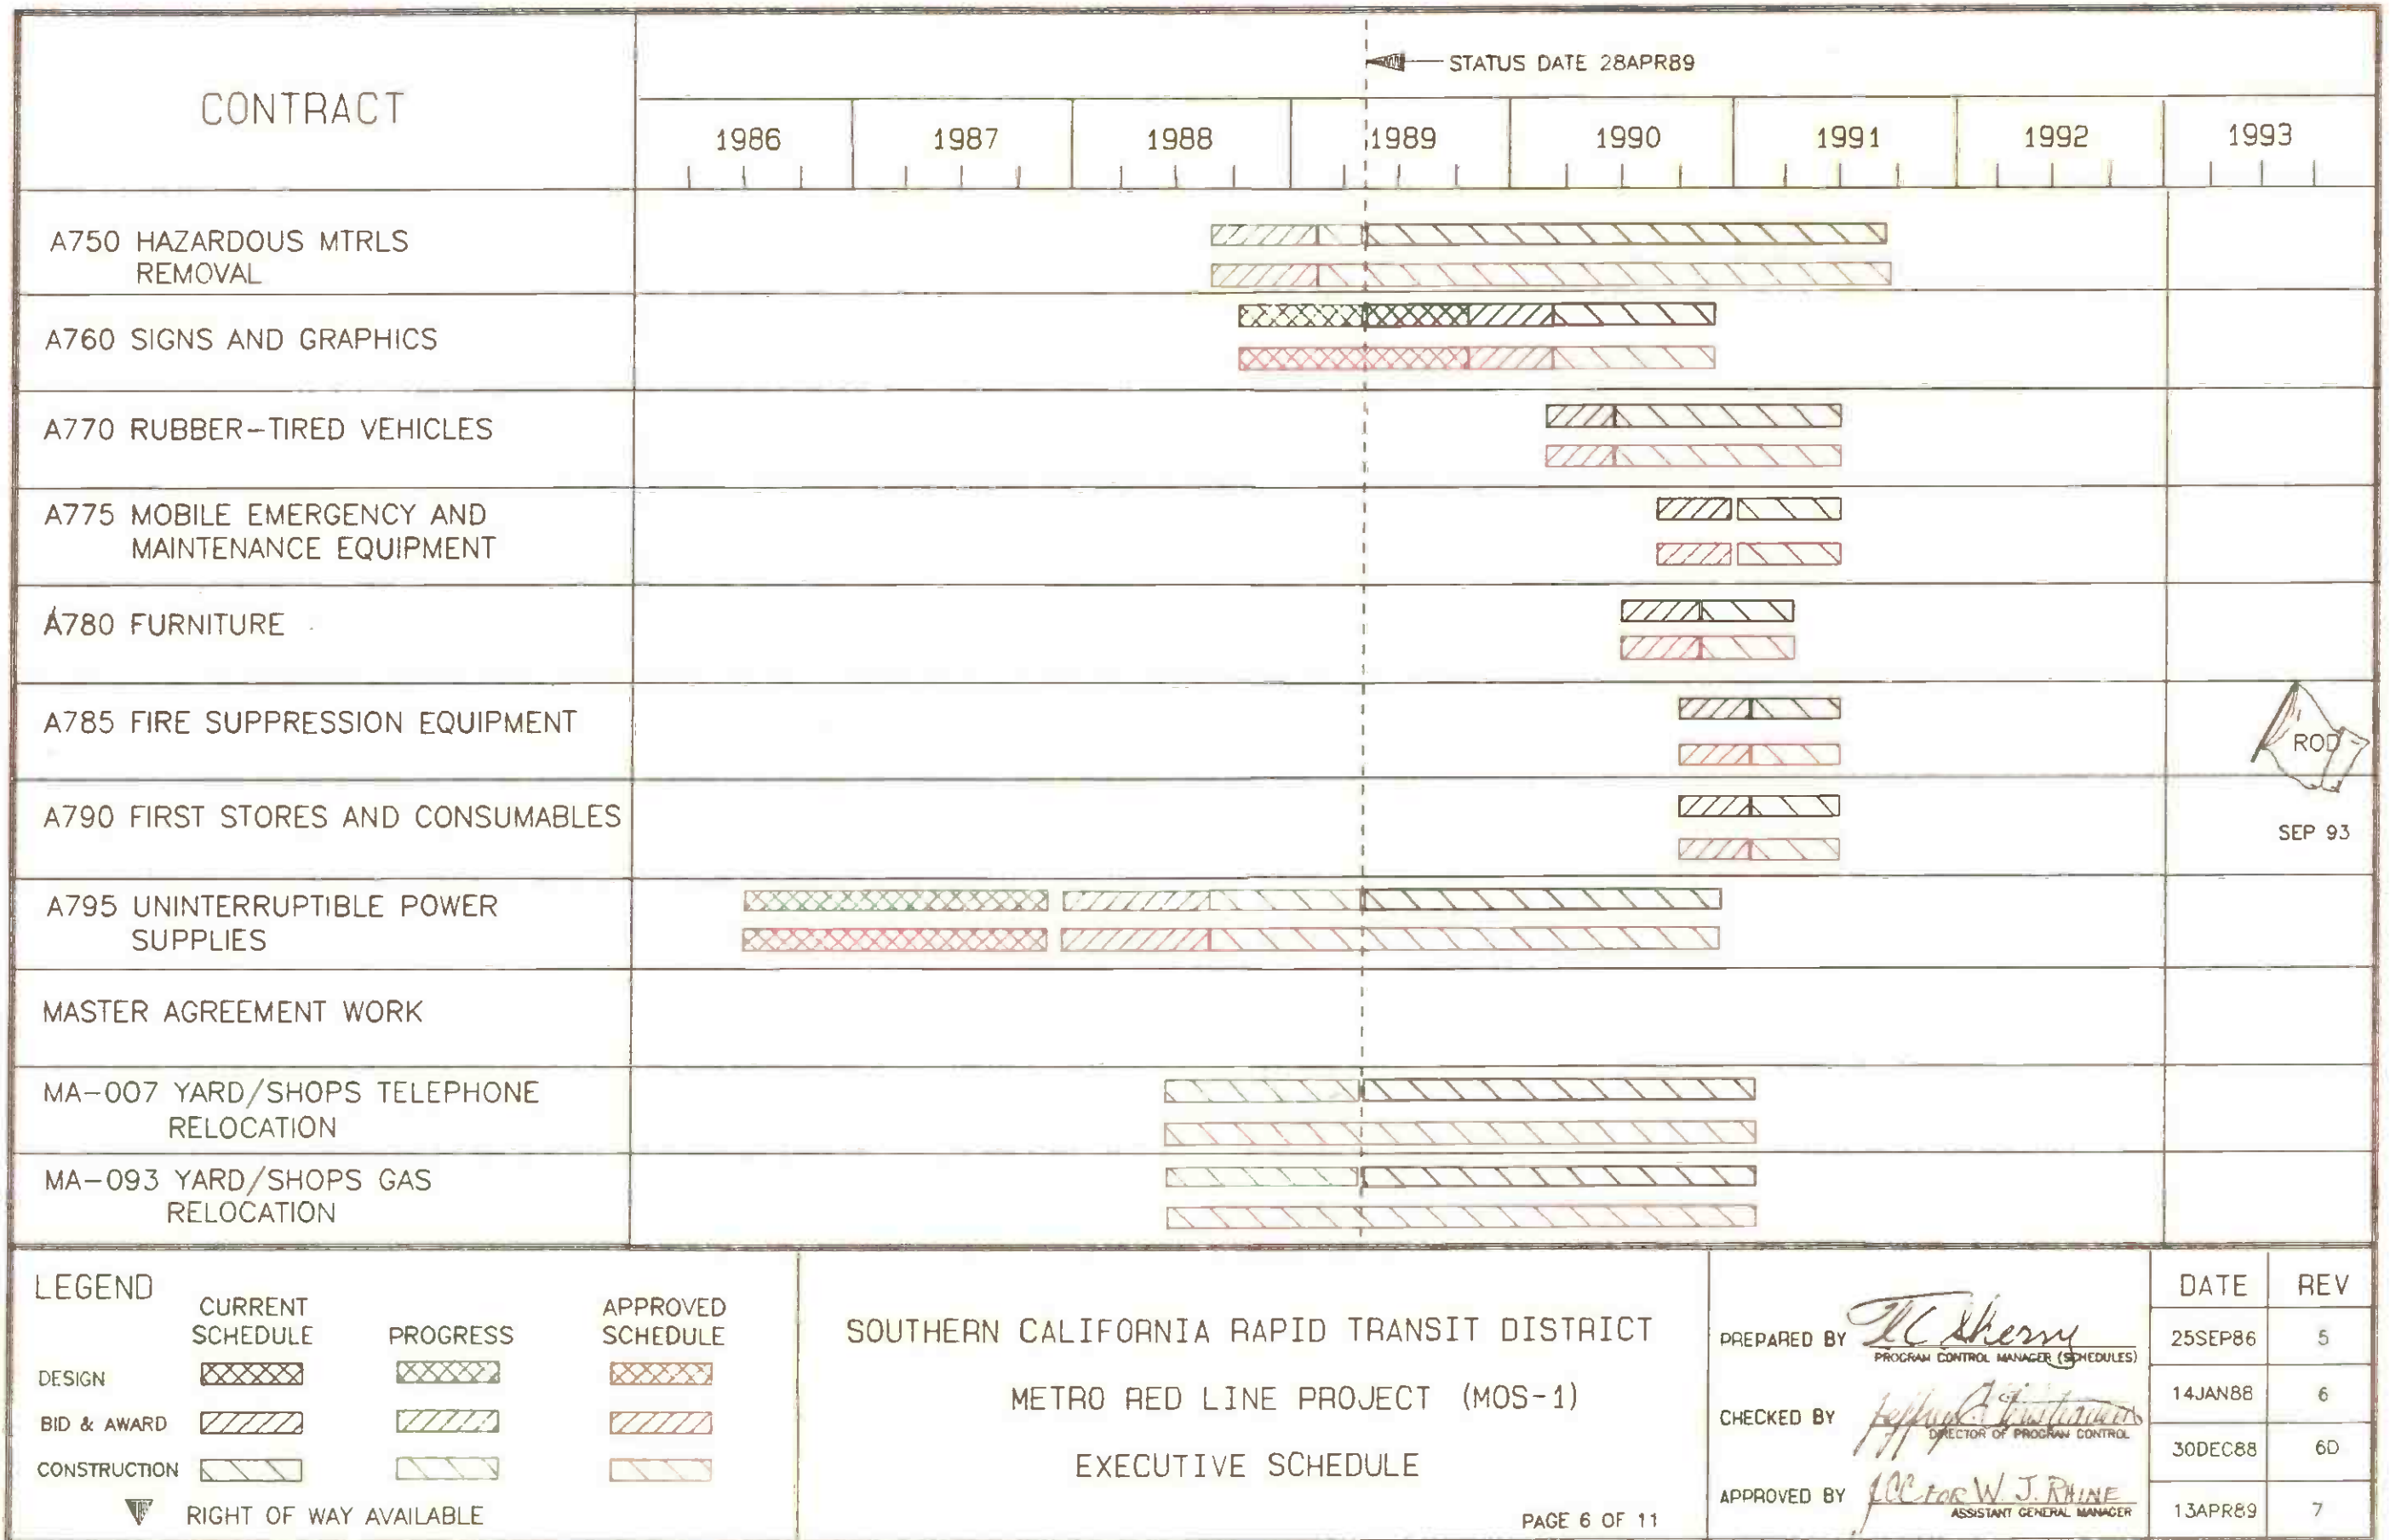


LEGEND	CURRENT SCHEDULE	PROGRESS	APPROVED SCHEDULE
DESIGN			
BID & AWARD			
CONSTRUCTION			
	RIGHT OF WAY AVAILABLE		

SOUTHERN CALIFORNIA RAPID TRANSIT DISTRICT
METRO RED LINE PROJECT (MOS-1)
EXECUTIVE SCHEDULE

PAGE 6 OF 11

	DATE	REV
PREPARED BY PROGRAM CONTROL MANAGER (SCHEDULES)	25SEP86	5
CHECKED BY DIRECTOR OF PROGRAM CONTROL	14JAN88	6
APPROVED BY ASSISTANT GENERAL MANAGER	30DEC88	6D
	13APR89	7

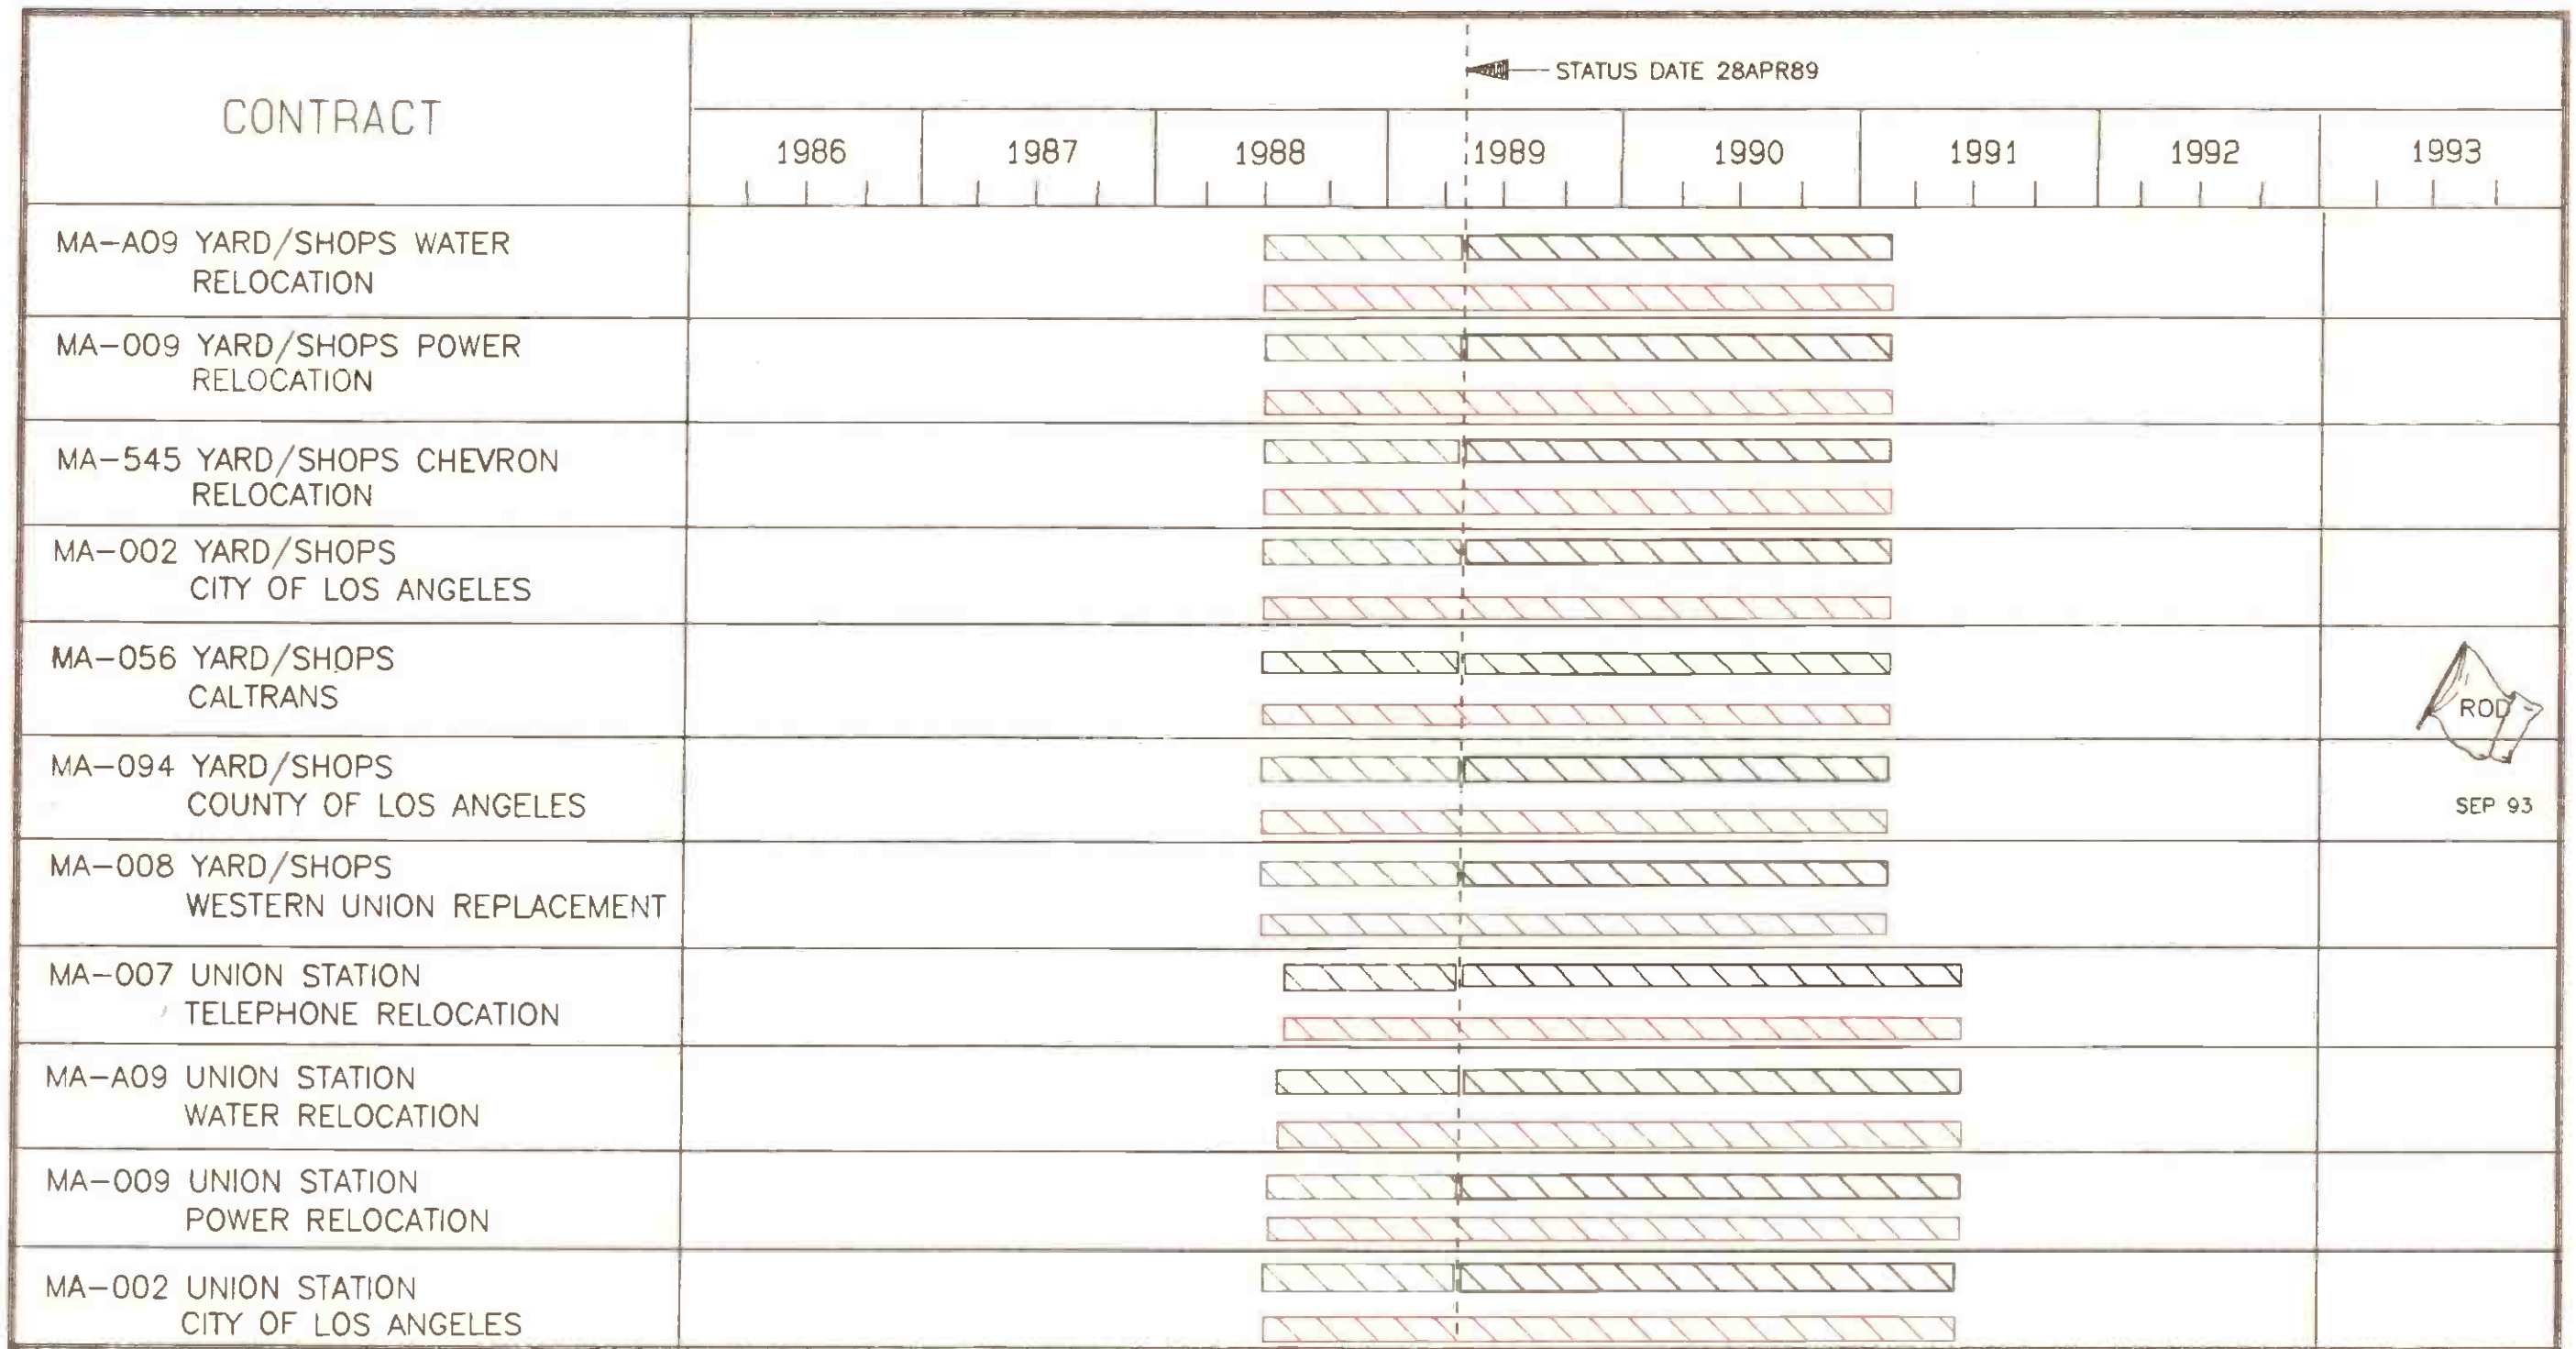


LEGEND			
	CURRENT SCHEDULE	PROGRESS	APPROVED SCHEDULE
DESIGN	▨	▨	▨
BID & AWARD	▨	▨	▨
CONSTRUCTION	▨	▨	▨
	▼ RIGHT OF WAY AVAILABLE		

SOUTHERN CALIFORNIA RAPID TRANSIT DISTRICT
 METRO RED LINE PROJECT (MOS-1)
 EXECUTIVE SCHEDULE

PAGE 7 OF 11

	DATE	REV
PREPARED BY <i>J.C. Cherry</i> PROGRAM CONTROL MANAGER (SCHEDULES)	25SEP86	5
CHECKED BY <i>Jeffrey A. ...</i> DIRECTOR OF PROGRAM CONTROL	14JAN88	6
APPROVED BY <i>W.J. Rhine</i> ASSISTANT GENERAL MANAGER	30DEC88	60
	13APR89	7

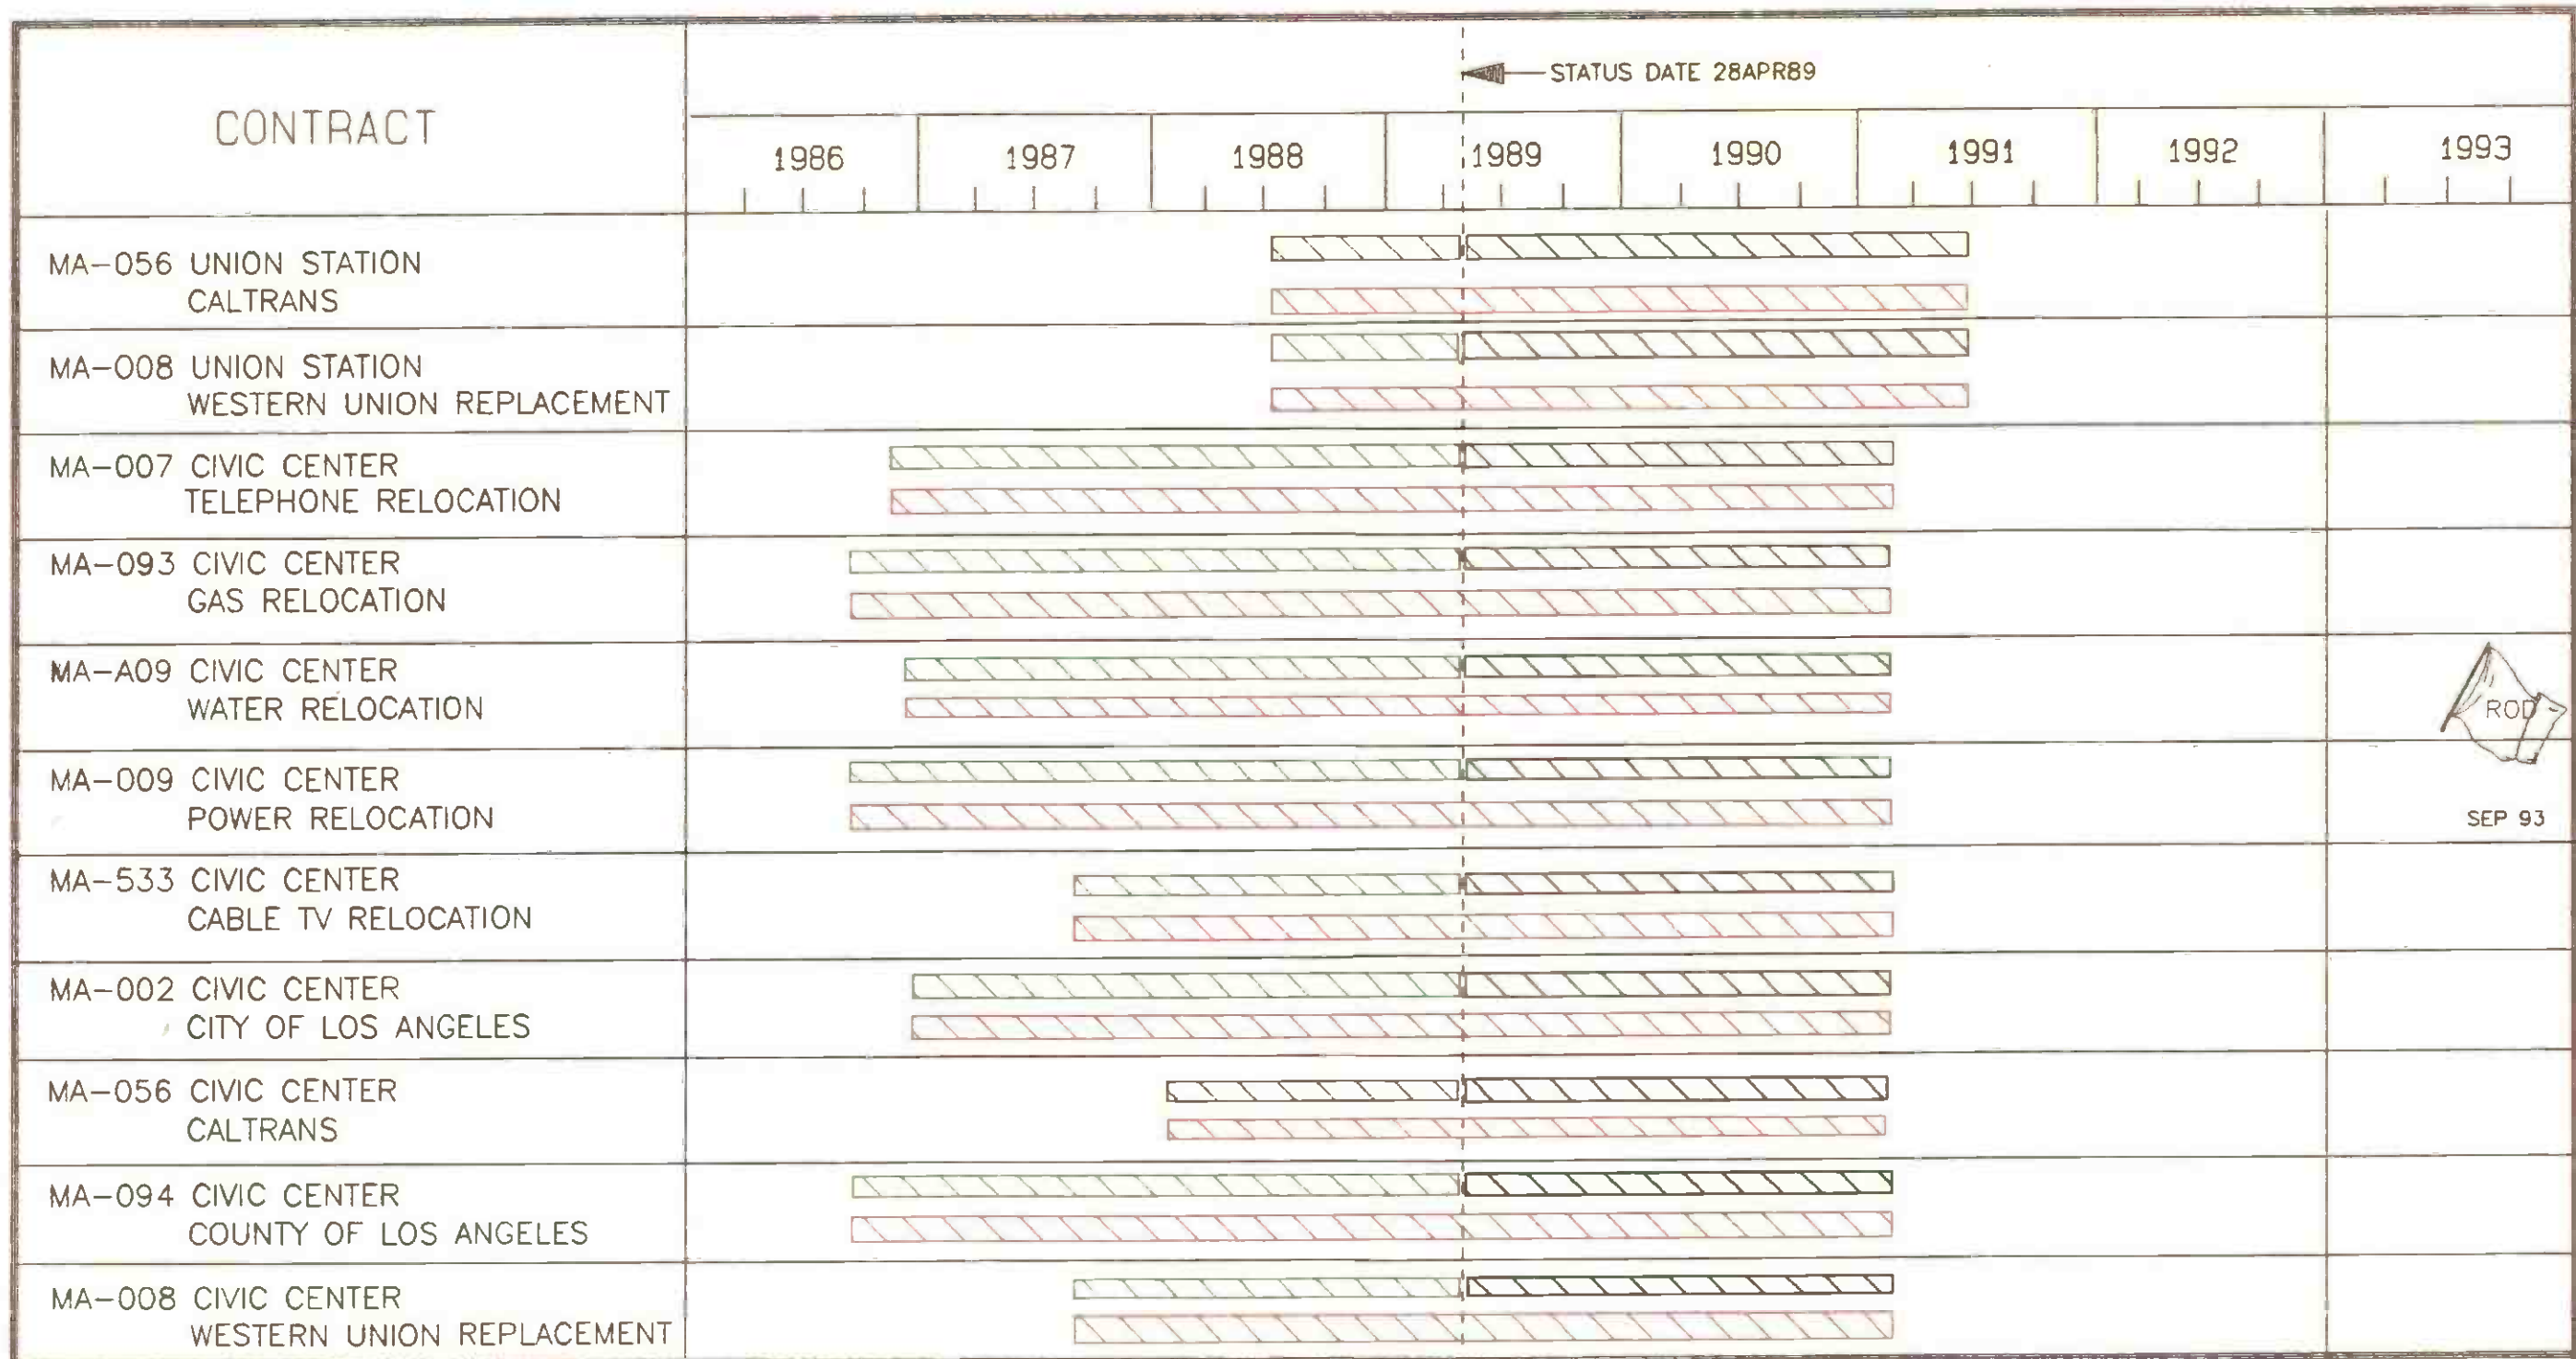

SEP 93



LEGEND		CURRENT SCHEDULE	PROGRESS	APPROVED SCHEDULE
DESIGN				
BID & AWARD				
CONSTRUCTION				
		RIGHT OF WAY AVAILABLE		











SOUTHERN CALIFORNIA RAPID TRANSIT DISTRICT
METRO RED LINE PROJECT (MOS-1)
EXECUTIVE SCHEDULE

PAGE 8 OF 11

	DATE	REV
PREPARED BY <i>TC Sherry</i> PROGRAM CONTROL MANAGER (SCHEDULES)	25SEP86	5
CHECKED BY <i>J.P. Williams</i> DIRECTOR OF PROGRAM CONTROL	14JAN88	6
APPROVED BY <i>W.J. Rhine</i> ASSISTANT GENERAL MANAGER	30DEC88	6D
	13APR89	7




CONTRACT	← STATUS DATE 28APR89									
	1986	1987	1988	1989	1990	1991	1992	1993		
MA-002 HILL STREET 1-WAY CITY OF LOS ANGELES	[Hatched]									
MA-007 5TH/HILL TELEPHONE RELOCATION	[Hatched]			[Hatched]						
MA-093 5TH/HILL GAS RELOCATION		[Hatched]		[Hatched]						
MA-A09 5TH/HILL WATER RELOCATION		[Hatched]		[Hatched]						
MA-009 5TH/HILL POWER RELOCATION	[Hatched]	[Hatched]		[Hatched]					ROD SEP 93	
MA-002 5TH/HILL CITY OF LOS ANGELES	[Hatched]	[Hatched]		[Hatched]						
MA-533 5TH/HILL CABLE TV RELOCATION		[Hatched]		[Hatched]						
MA-008 5TH/HILL WESTERN UNION REPLACEMENT		[Hatched]		[Hatched]						
MA-007 7TH/FLOWER TELEPHONE RELOCATION		[Hatched]		[Hatched]						
MA-093 7TH/FLOWER GAS RELOCATION		[Hatched]		[Hatched]						
MA-A09 7TH/FLOWER WATER RELOCATION		[Hatched]		[Hatched]						
LEGEND	CURRENT SCHEDULE	PROGRESS	APPROVED SCHEDULE	SOUTHERN CALIFORNIA RAPID TRANSIT DISTRICT METRO RED LINE PROJECT (MOS-1) EXECUTIVE SCHEDULE				DATE	REV	
DESIGN	[Cross-hatched]	[Diagonal lines]	[Diagonal lines]					PREPARED BY <i>J.C. Sherry</i> PROGRAM CONTROL MANAGER (SCHEDULES)	25SEP86	5
BID & AWARD	[Diagonal lines]	[Diagonal lines]	[Diagonal lines]					CHECKED BY <i>J. J. [Signature]</i> DIRECTOR OF PROGRAM CONTROL	14JAN88	6
CONSTRUCTION	[Diagonal lines]	[Diagonal lines]	[Diagonal lines]					APPROVED BY <i>J.C. [Signature]</i> ASSISTANT GENERAL MANAGER	30DEC88	6D
▼	RIGHT OF WAY AVAILABLE						13APR89	7		
				PAGE 9 OF 11						


CONTRACT	← STATUS DATE 28APR89							
	1986	1987	1988	1989	1990	1991	1992	1993
MA-009 7TH/FLOWER POWER RELOCATION		 		 				
MA-002 7TH/FLOWER CITY OF LOS ANGELES		 		 				
MA-533 7TH/FLOWER CABLE TV REPLACEMENT		 		 				
MA-008 7TH/FLOWER WESTERN UNION REPLACEMENT		 		 				
MA-007 WILSHIRE/ALVARADO TELEPHONE RELOCATION			 	 				
MA-093 WILSHIRE/ALVARADO GAS RELOCATION			 	 				SEP 93
MA-A09 WILSHIRE/ALVARADO WATER RELOCATION			 	 				
MA-009 WILSHIRE/ALVARADO POWER RELOCATION			 	 				
MA-002 WILSHIRE/ALVARADO CITY OF LOS ANGELES			 	 				
MA-533 WILSHIRE/ALVARADO CABLE TV RELOCATION			 	 				
MA-056 WILSHIRE/ALVARADO CALTRANS			 	 				

LEGEND	CURRENT SCHEDULE	PROGRESS	APPROVED SCHEDULE
DESIGN			
BID & AWARD			
CONSTRUCTION			
	RIGHT OF WAY AVAILABLE		

SOUTHERN CALIFORNIA RAPID TRANSIT DISTRICT
METRO RED LINE PROJECT (MOS-1)
EXECUTIVE SCHEDULE

PAGE 10 OF 11

	DATE	REV
PREPARED BY  PROGRAM CONTROL MANAGER (SCHEDULES)	25SEP86	5
CHECKED BY  DIRECTOR OF PROGRAM CONTROL	14JAN88	6
APPROVED BY  ASSISTANT GENERAL MANAGER	30DEC88	6D
	13APR89	7

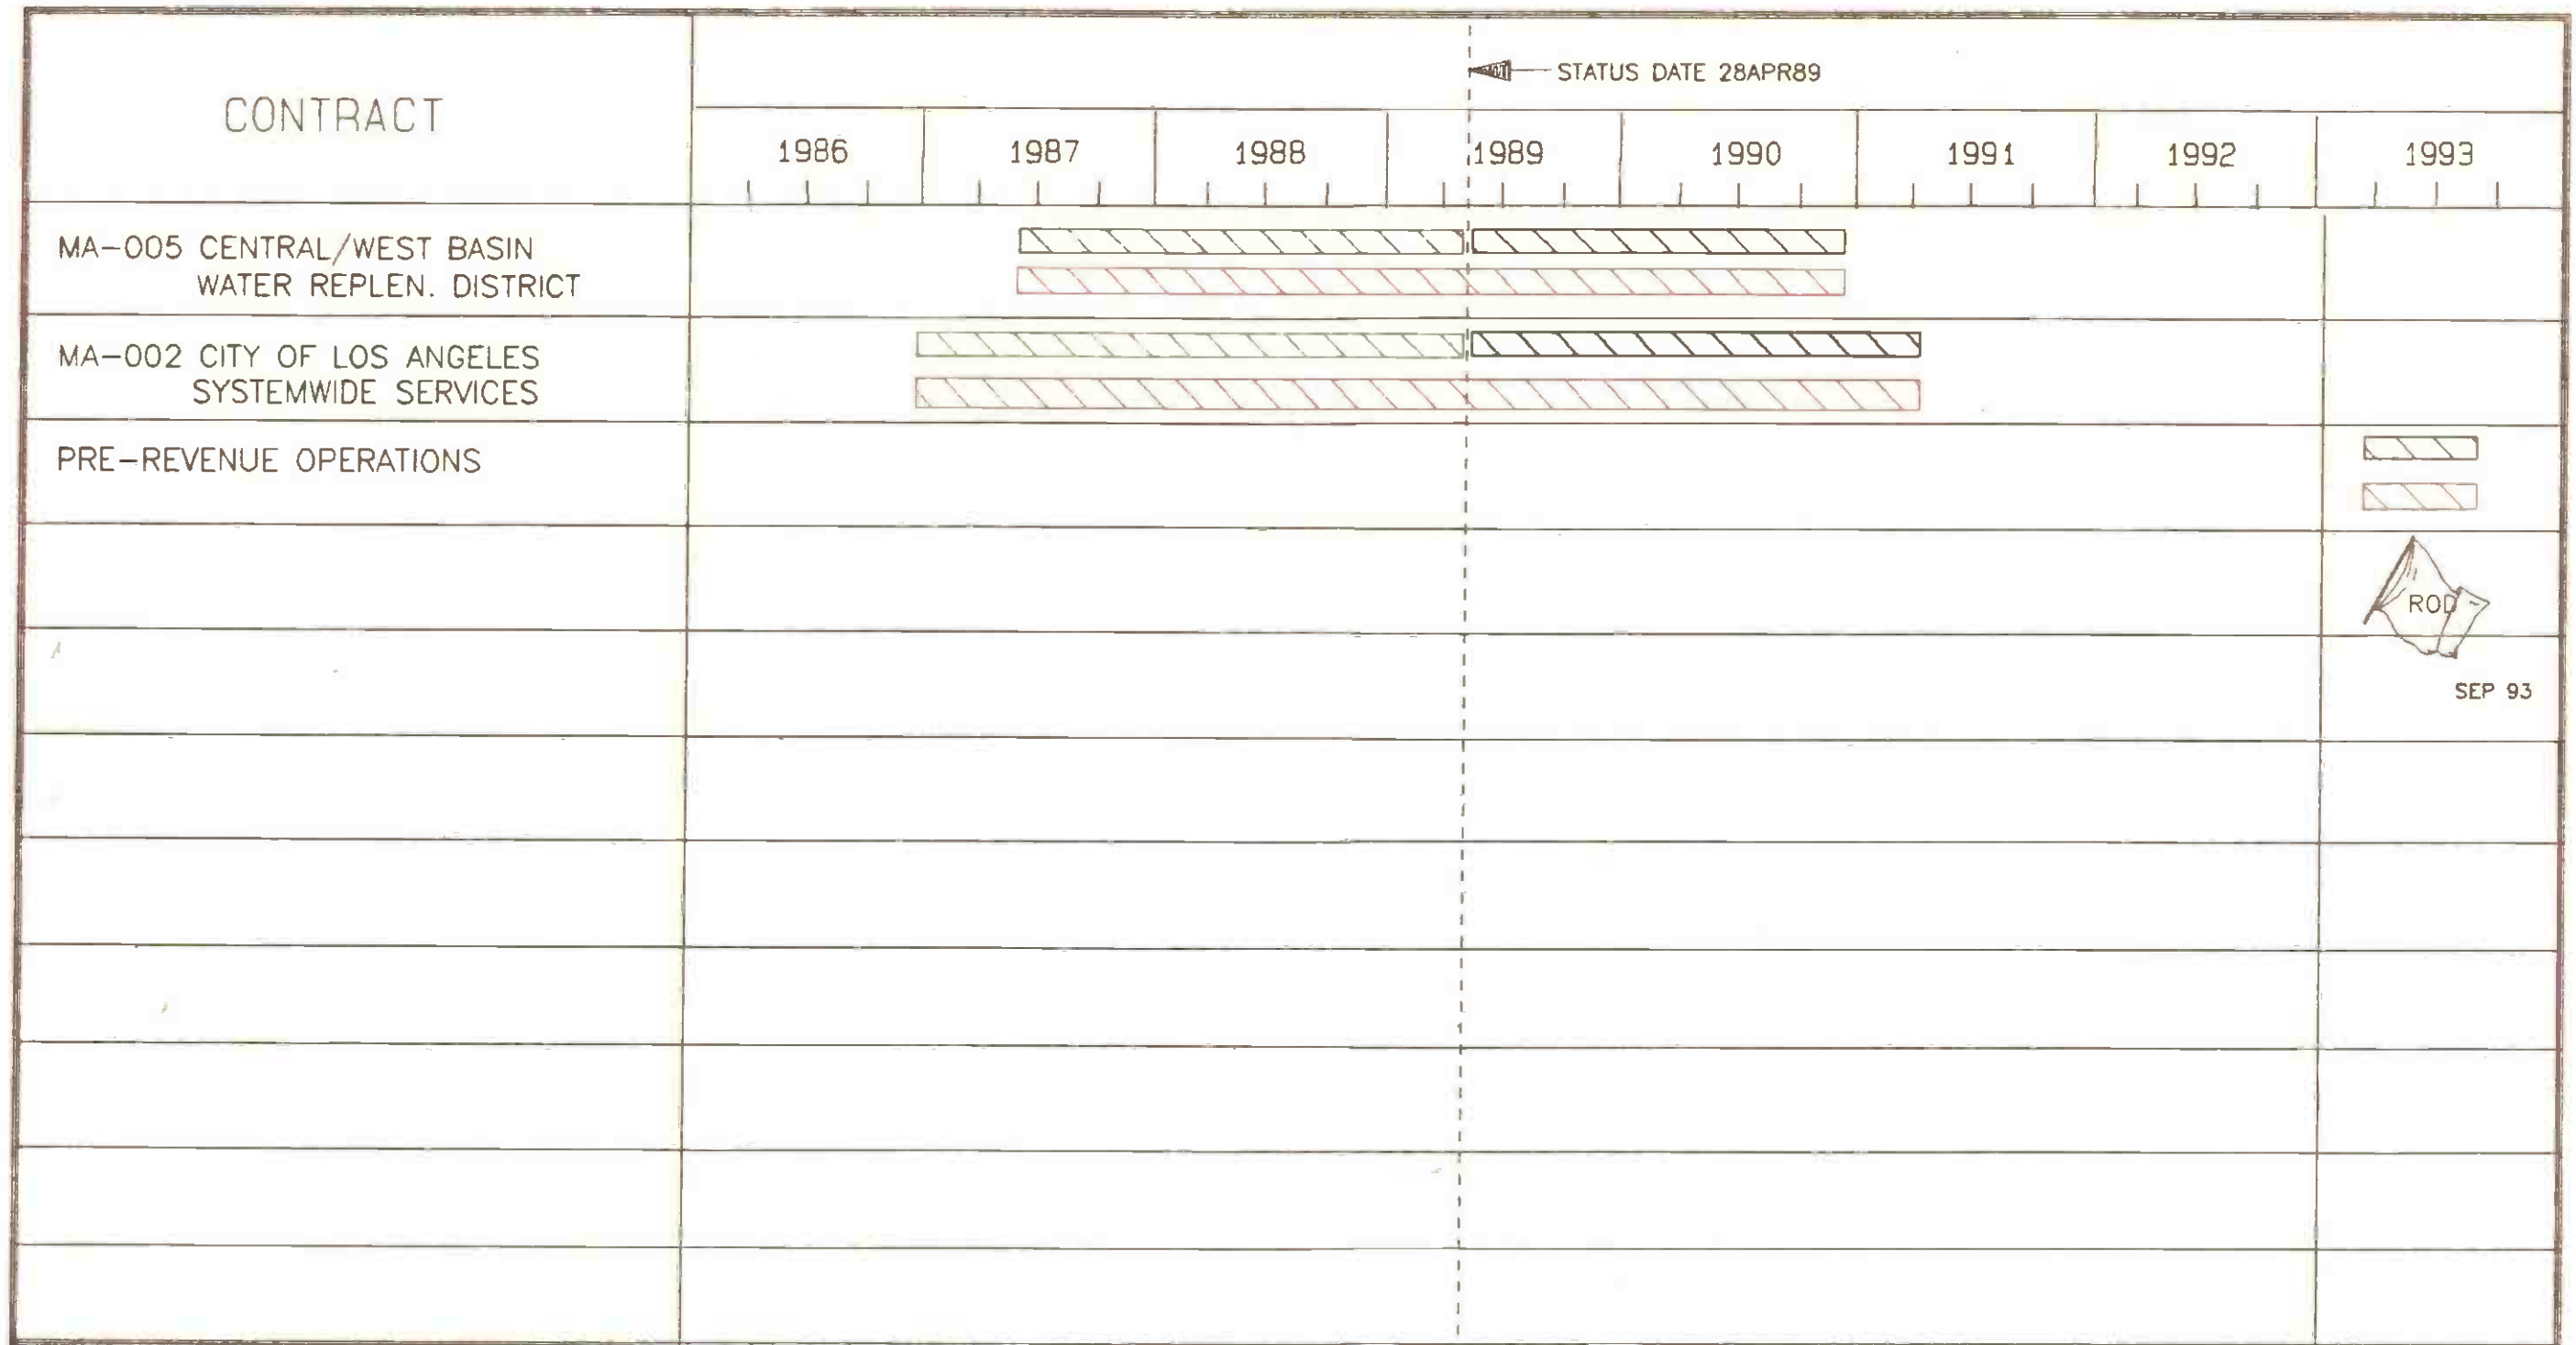

LEGEND	CURRENT SCHEDULE	PROGRESS	APPROVED SCHEDULE
DESIGN			
BID & AWARD			
CONSTRUCTION			
	RIGHT OF WAY AVAILABLE		

SOUTHERN CALIFORNIA RAPID TRANSIT DISTRICT
METRO RED LINE PROJECT (MOS-1)
EXECUTIVE SCHEDULE

PAGE 11 OF 11

PREPARED BY *J.C. Sherry*
PROGRAM CONTROL MANAGER (SCHEDULES)

CHECKED BY *J. J. Stewart*
DIRECTOR OF PROGRAM CONTROL

APPROVED BY *J.C. For W.J. Rhine*
ASSISTANT GENERAL MANAGER

DATE	REV
25SEP86	5
14JAN88	6
30DEC88	6D
13APR89	7

ROD
SEP 93

APPENDIX
STATUS OF EXECUTIVE SCHEDULE
As of April 28, 1989

There are no schedule changes
since the February 1989 Status Report.

As a result of unforeseen disruptions to the approved schedule, the RTD Board of Directors, at the April 13, 1989, meeting, approved a new Revenue Operation Date of September 1993. Contract schedules have been adjusted to reflect this update which is called Revision 7 of the Metro Red Line MOS-1 Project Schedule. This schedule is now the basis against which all future activity will be measured.

Listed below is a summary of the impact to the contracts:

<u>Contract Number</u>	<u>Contract Description</u>	<u>Type of Change Required</u>	<u>Contract Number</u>	<u>Contract Description</u>	<u>Type of Change Required</u>
A115	Santa Fe Ave. Restoration	Reschedule NTP and contract completion.	A175	Wilshire/Alvarado Station, Stage I	Extend contract duration
A112	Main Shop Building	Extend contract duration.	A185	Wilshire/Alvarado Site Work	Reschedule NTP and contract completion.
A116	Yard Site Security Fencing	Reschedule NTP and contract completion.	A186	Wilshire/Alvarado Landscaping	Reschedule NTP and contract completion.
A117	Yard Site Lighting	Reschedule NTP and contract completion.	A187	Wilshire/Alvarado Station, Stage II	Reschedule NTP and contract completion.
A118	Yard Site Landscaping	Reschedule NTP and contract completion.	A610/A115	Trackwork Installation/Yard Storage Area	Extend contract duration.
A124	Ducommun St. & Jackson St. Restoration	Reschedule NTP and contract completion.	A620	Automatic Train Control	Extend contract duration.
A130	Yard Leads & Transfer Zone	Extend contract duration.	A631	Traction Power Installation	Reschedule NTP and contract completion.
A135	Union Station, Stage I	Extend contract duration.	A640	Communications	Extend contract duration.
A136	Union Station, Stage II	Reschedule NTP and contract completion.	A671	Unimog	Reschedule NTP and contract completion.
A141	Line Section US-5th/Hill & Civic Center Station, Stage I	Extend contract duration.	A672	Flat Cars	Reschedule NTP and contract completion.
A145	5th/Hill Station, Stage I	Extend contract duration.	A710/A720	Escalators/Elevators	Extend contract duration.
A146	Line Section, 5th/Hill to 7th/Flower	Extend contract duration.	A770	Rubber-Tired Vehicles	Reschedule NTP and contract completion.
A147	Civic Center Station, Stage II	Reschedule NTP and contract completion.	A775	Mobile Emergency & Maintenance Equipment	Reschedule NTP and contract completion.
A157	5th/Hill Station, Stage II	Reschedule NTP and contract completion.	A785	Fire Suppression Equipment	Reschedule NTP and contract completion.
A165	7th/Flower Station, Stage I	Extend contract duration.	A790	First Stores & Consumables	Reschedule NTP and contract completion.
A167	7th/Flower Station, Stage II	Reschedule NTP and contract duration.	H840	Fare Collection	Extend contract duration.
