





- Sully-Miller Contracting Inc. is approximately 60% complete and on schedule for Metro to open the new station and a 611-space parking lot by December 2006
- Paving operations are ongoing
- Commenced installation of station electrical and systems equipment






Overview of site looking west







Asphalt paving on extension of busway leaving station area looking east

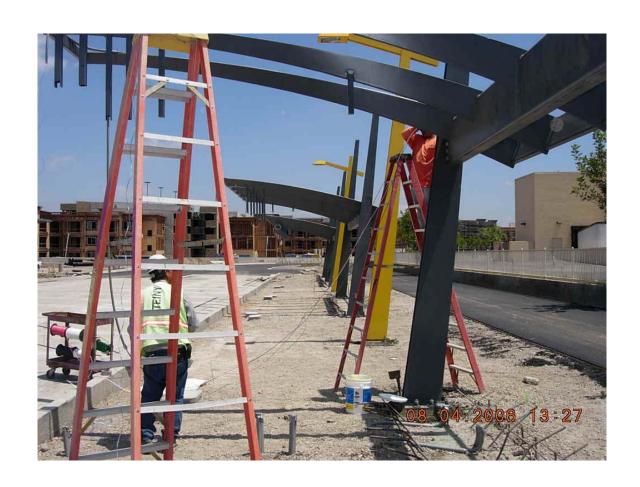

Wire pulling at eastbound platform





611-space Parking Lot A looking south







Paving of widened portion of Canoga Avenue looking north
