



Metro Gold Line Eastside Extension Project Update March 8, 2007

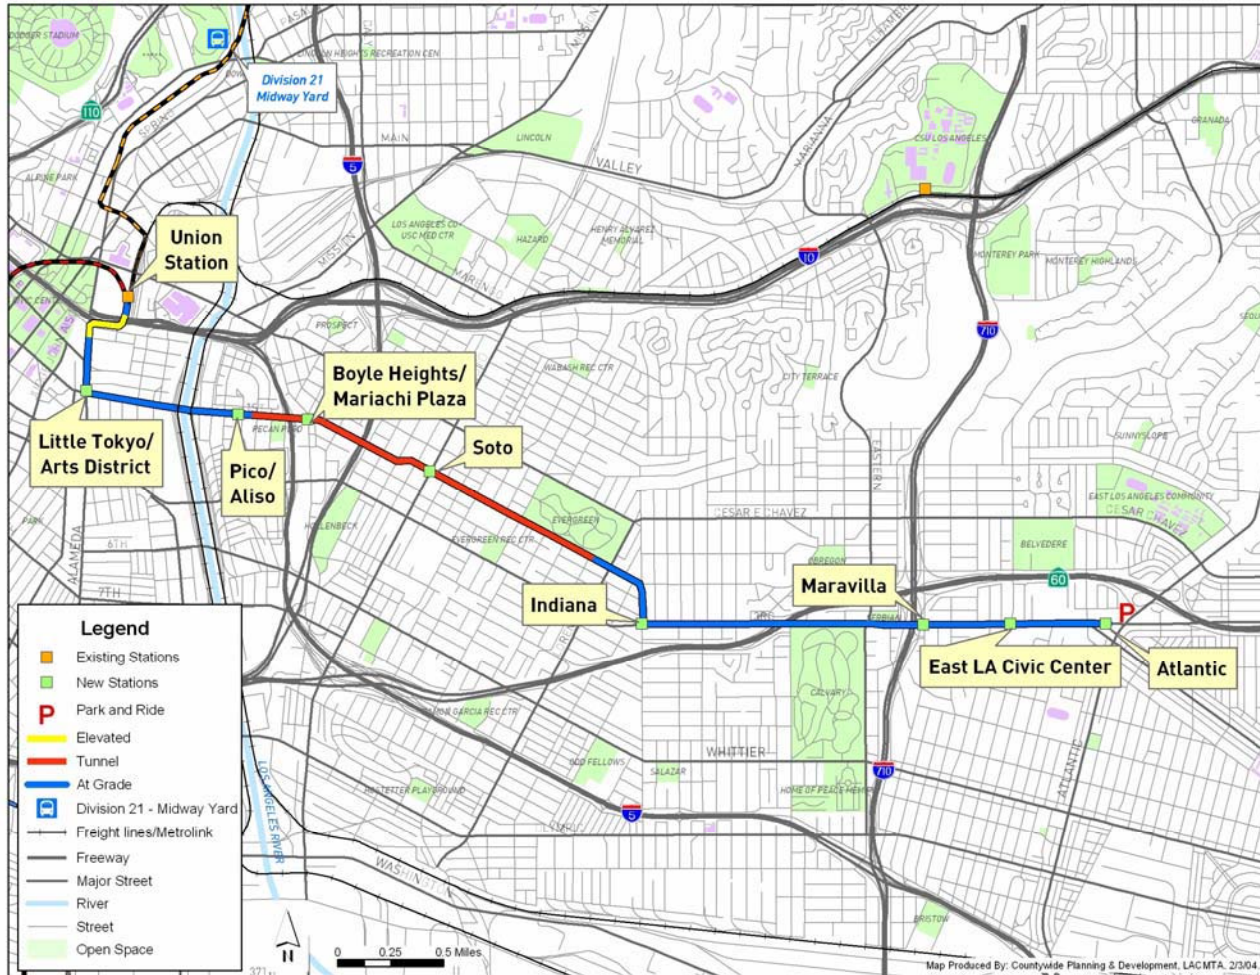

Metro

Gold
Line

Metro Gold Line Eastside Extension Overview of Major Construction Activities

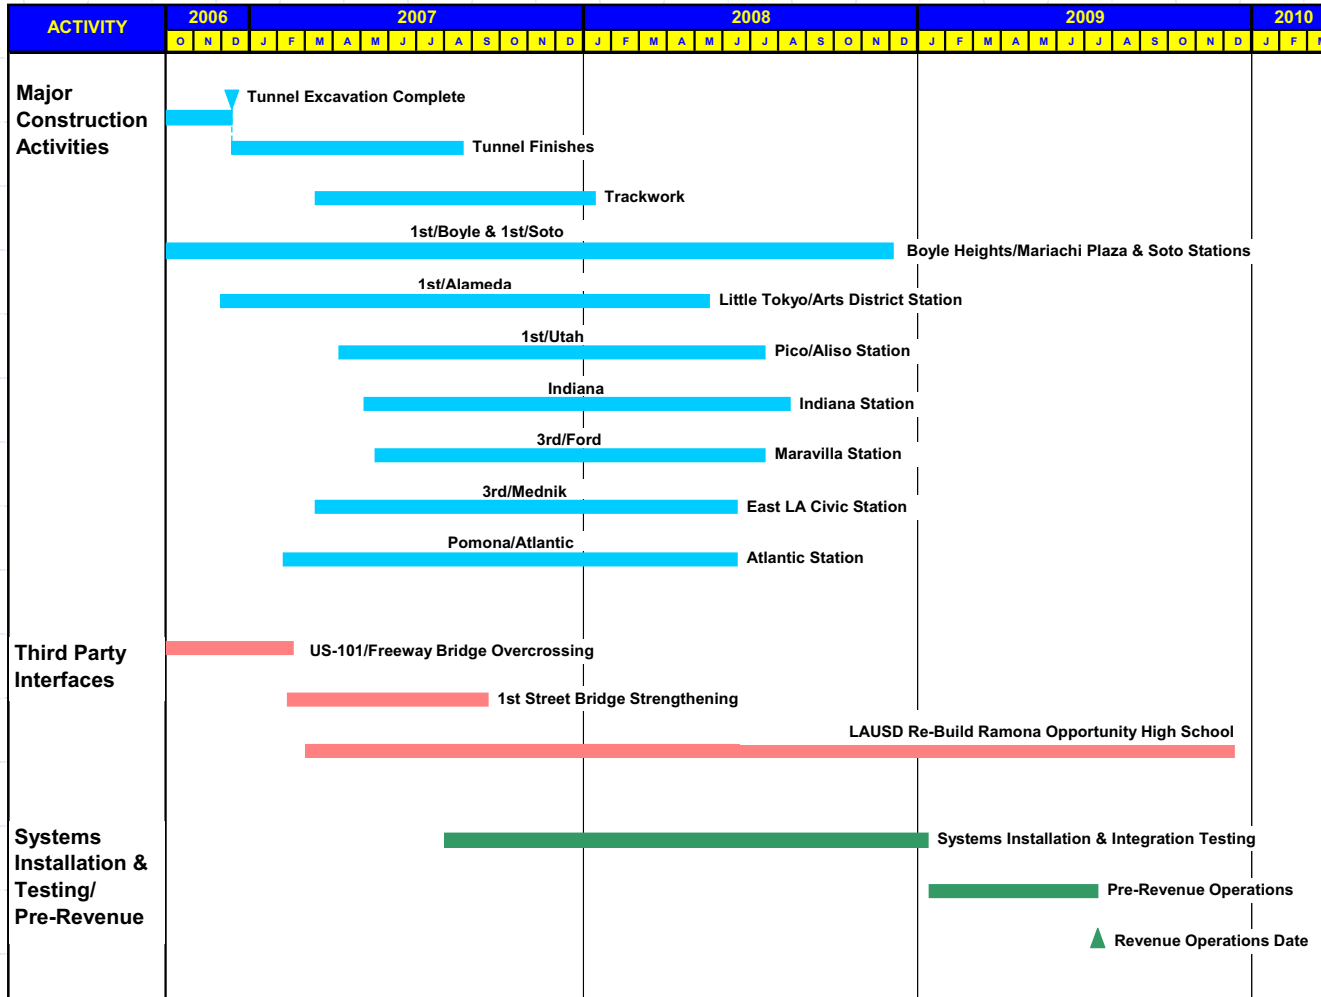

Metro

Gold Line

Metro Gold Line Eastside Extension Light Rail Transit Stations



LittleTokyo/
Arts District



Pico/Aliso



Boyle Heights/
Mariachi Plaza



1st/Soto



Maravilla



East Los Angeles
Civic Center



Pomona/Atlantic



Indiana Station

Construction has begun on four of the eight Light Rail Transit Stations. All of the stations will be in construction in 2007.



Metro



**Gold
Line**

Metro Gold Line Eastside Extension Tunnel Invert Slab & Walkways



- Excavation of both tunnels was completed in December 2006.
- Construction of the tunnel track level invert slab and walkways is underway.

Metro Gold Line Eastside Extension Boyle Heights/Mariachi Plaza Station



- Excavation of the station entrance has been completed.
- Placement of the concrete for the Station track level invert slab is underway.
- Construction of the station interior walls has begun.

Metro Gold Line Eastside Extension 1st/Soto Station



- The Soto Station entrance structure is fully excavated.
- Portions of the underground entrance floor slab are being constructed.

Metro Gold Line Eastside Extension West Portal Near 1st/Gless



- Concrete work for the West Portal is nearing completion.

Metro Gold Line Eastside Extension East Portal Near 1st/Lorena



- Placement of concrete for the ground slab and walls at the East Portal opening has been completed.
- Formwork is being placed to receive concrete for the roof slab.

Metro Gold Line Eastside Extension 101 Freeway LRT Bridge Overcrossing Caltrans Coordination



- Caltrans' contractor is preparing to turn over the LRT Bridge Structure to Metro before the end of March 2007.
- Metro's contractor is scheduled to begin trackwork and systems installation preparation work in April 2007.

Metro Gold Line Eastside Extension 1st Street – Alameda Street to Vignes Street Little Tokyo/Arts District Station



- Construction of the Little Tokyo/Arts District Station has begun.
- The station foundation and stem walls have been completed.
- Reinforcement steel is being placed prior to pouring the concrete for the station platform slab.



Metro

Gold
Line

Metro Gold Line Eastside Extension 1st Street Bridge & Street Widening City of Los Angeles Coordination



- Metro has performed Phase I intersection improvements for the City of LA related to the 1st Street Bridge.
- The City of LA issued construction notice to proceed for the Phase II Girder Strengthening construction contract on February 6, 2007.
- Phase II construction completion will meet the scheduled turnover date to Metro.
- The City of LA is scheduled to solicit bids for Phase III Bridge Widening in June 2007.

Metro Gold Line Eastside Extension Project

Metro and LAUSD Coordination

Indiana Station/Ramona Opportunity High School



Indiana Light Rail Transit Station



LAUSD Ramona Opportunity High School

- LAUSD received the Re-build of Ramona Opportunity High School construction bids on October 10, 2006 and issued the construction notice to proceed on February 7, 2007.
- The funding plan for the reconstruction of the school has been approved by both the Metro Board of Directors and the LAUSD Board of Education, which will allow the land exchange for the construction of the Indiana Station on the east side of Indiana Street.
- The February 15, 2007 escrow closing date will be extended to provide more time to transfer the ownership of the Alma Avenue properties from Metro to LAUSD.



Metro

**Gold
Line**



Metro Gold Line Eastside Extension Project

Metro and LAUSD Coordination

Indiana Station/Ramona Opportunity High School



3rd Street and Alma Avenue



3rd Street and Indiana Street Intersection

- LAUSD requires a letter of “No Further Action” from the Department of Toxic Substance Control for the Alma Avenue properties prior to the transfer of ownership from Metro to LAUSD.
- Soil removal and testing was completed by Metro in accordance with the Remedial Action Work Plan that was approved by the Department of Toxic Substance Control.
- DTSC has reviewed the Final Report Test Results and is in the process of issuing a letter of “No Further Action”.



Metro

**Gold
Line**

Metro Gold Line Eastside Extension U-Channel Guideway Between 3rd Street and Eastern Avenue



- Construction of the U-channel section of the at-grade guideway on 3rd Street between the 60 Freeway and Eastern Avenue is underway.



Metro

Gold
Line

Metro Gold Line Eastside Extension I-710 Freeway/3rd Street Caltrans Coordination



- Structural modifications and retrofitting of the I-710 Freeway Bridge near 3rd Street and Ford Street are under construction.
- The work is being done in coordination with Caltrans median and shoulder widening work that is also under construction.



Metro

**Gold
Line**

Metro Gold Line Eastside Extension Pomona/Atlantic Station



- Construction of the Pomona/Atlantic Station has begun.
- Construction of the under-platform areas and foundation is well underway.

Metro Gold Line Eastside Extension



End of Presentation



Metro

**Gold
Line**
