


SOUTHERN CALIFORNIA RAPID TRANSIT DISTRICT

METRO RAIL PROJECT

MOS — 1

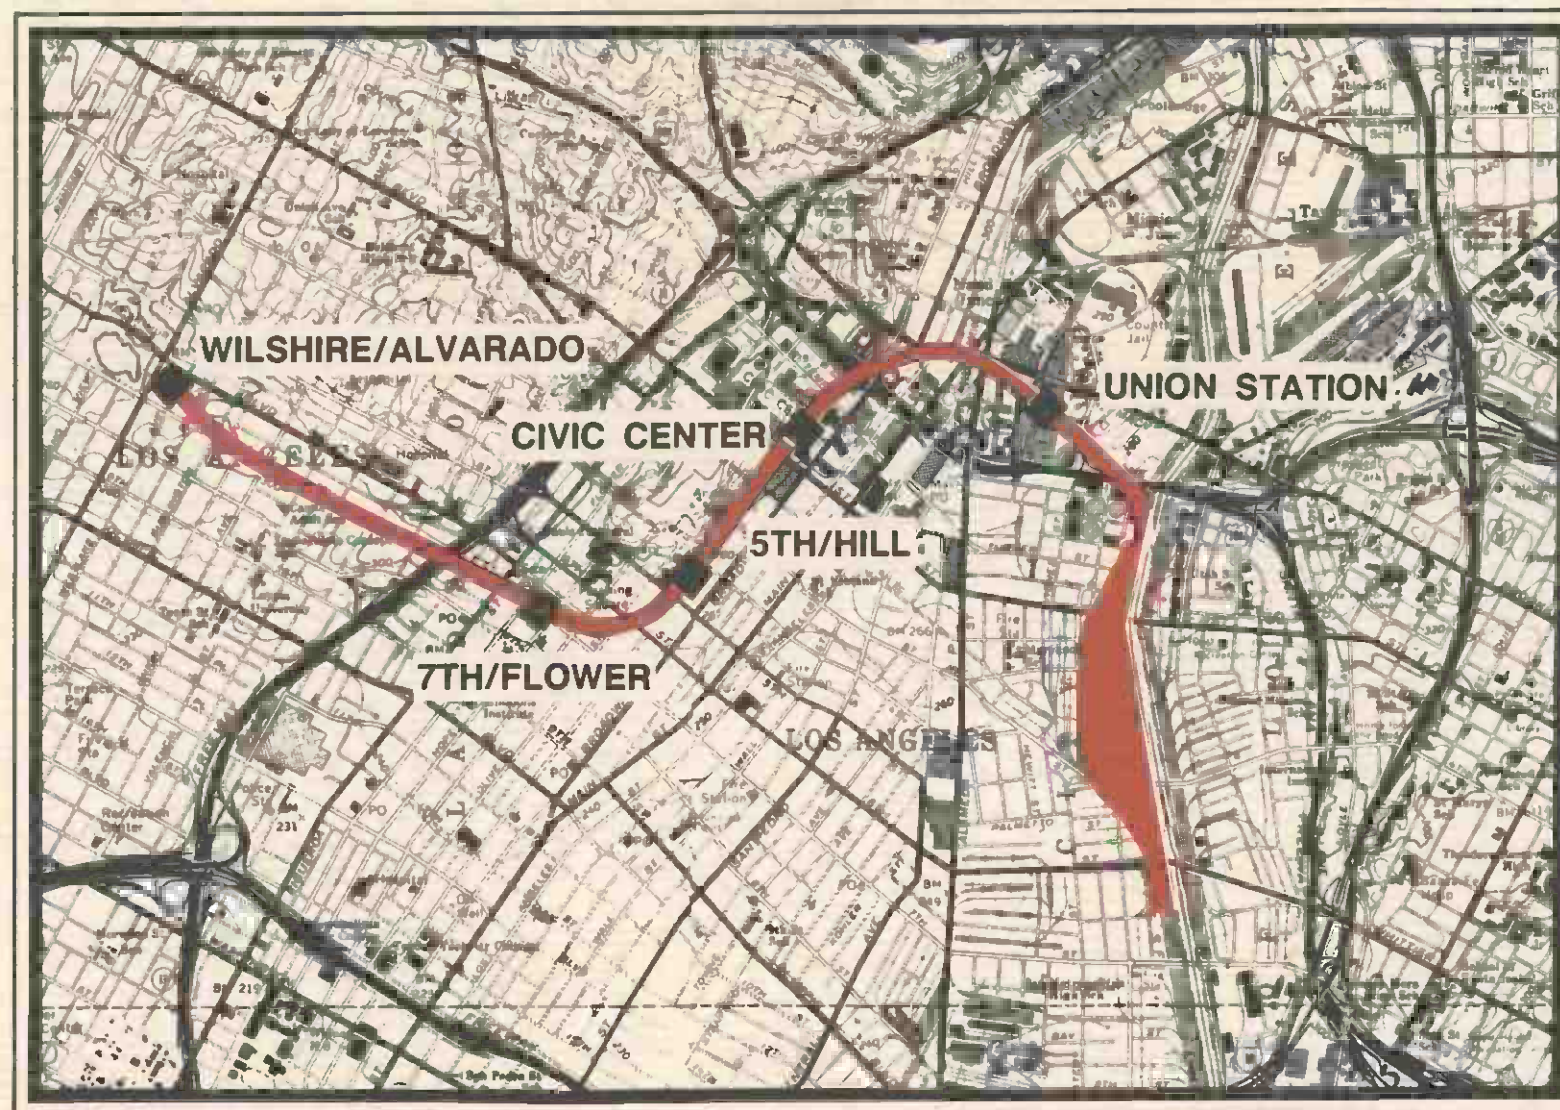


EXECUTIVE SCHEDULE

FEBRUARY 1989

SCRTD
1989
.M81
E97
Feb
1989

MOS-1
EXECUTIVE SCHEDULE

STATUS AS OF FEBRUARY 24, 1989

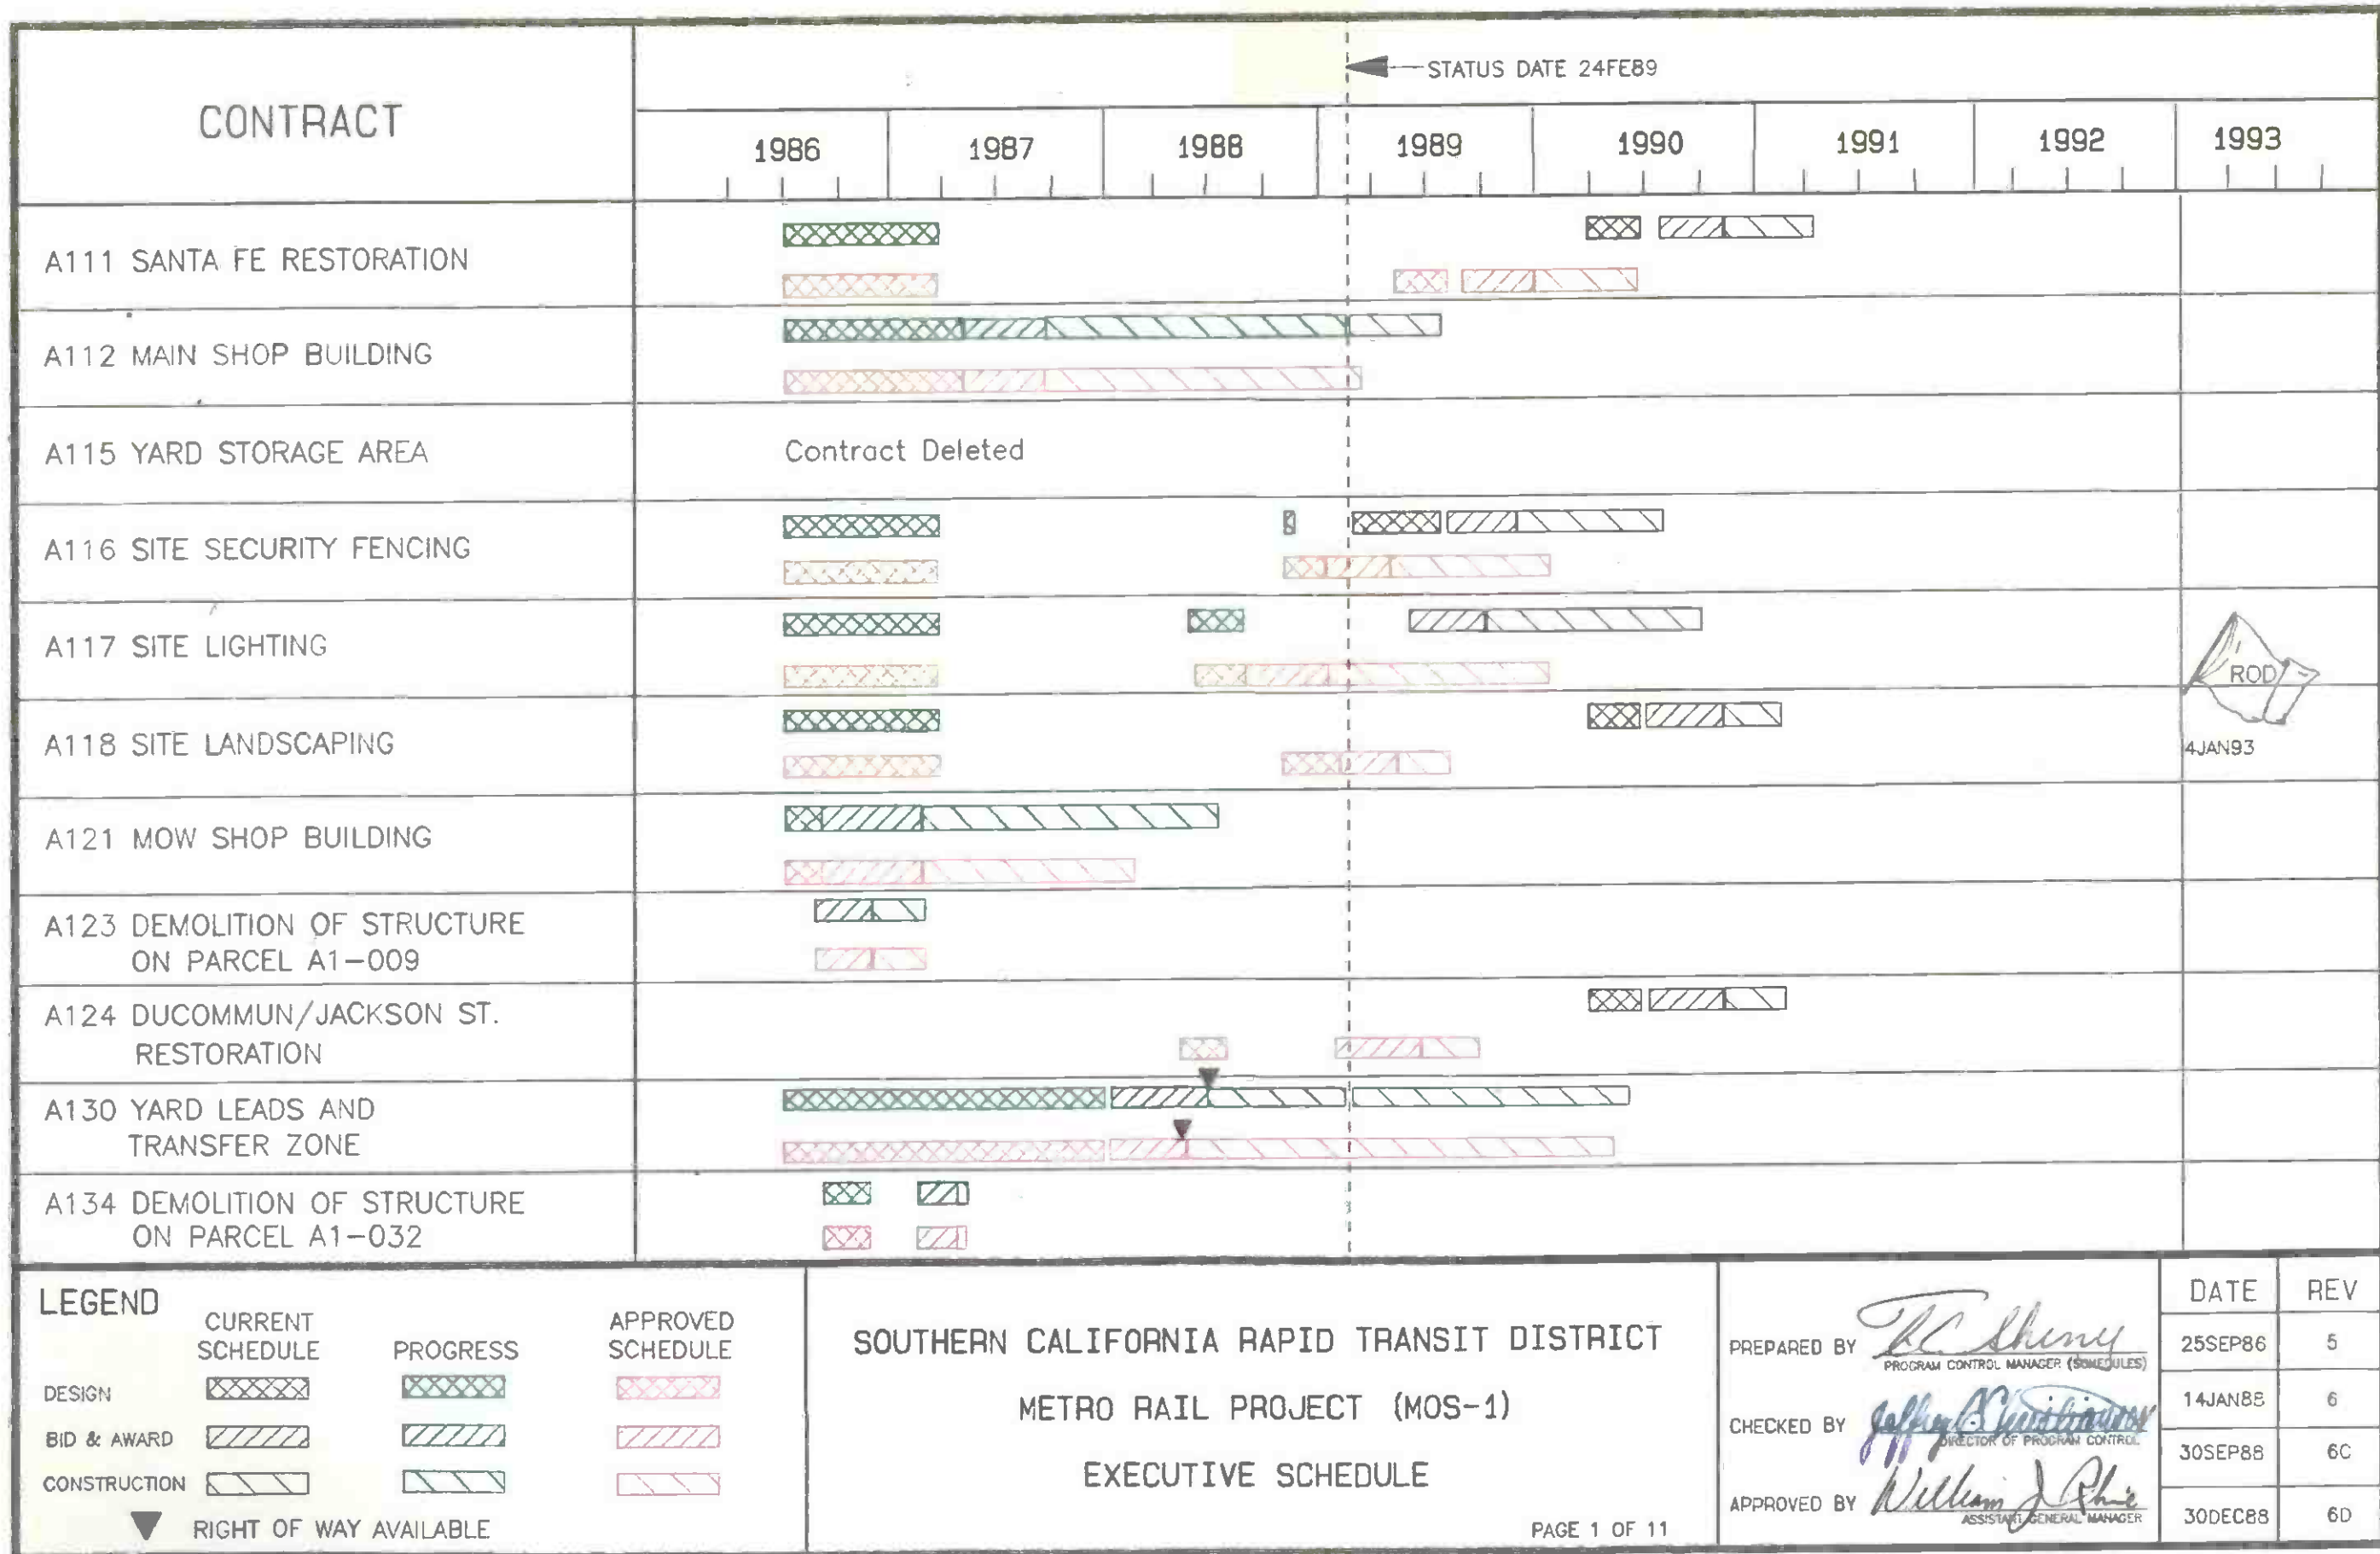


ROD
4 JAN 93

LEGEND	CURRENT SCHEDULE	PROGRESS	APPROVED SCHEDULE
DESIGN	[Cross-hatched]	[Cross-hatched]	[Cross-hatched]
BID & AWARD	[Diagonal lines]	[Diagonal lines]	[Diagonal lines]
CONSTRUCTION	[Diagonal lines]	[Diagonal lines]	[Diagonal lines]
▼	RIGHT OF WAY AVAILABLE		

SOUTHERN CALIFORNIA RAPID TRANSIT DISTRICT
METRO RAIL PROJECT (MOS-1)
EXECUTIVE SCHEDULE

PREPARED BY *TC Sherry*
PROGRAM CONTROL MANAGER (SCHEDULES)
CHECKED BY *Jeffrey B. Williams*
DIRECTOR OF PROGRAM CONTROL
APPROVED BY *William J. Rhie*
ASSISTANT GENERAL MANAGER

DATE	REV
25SEP86	5
14JAN88	6
30SEP88	6C
30DEC88	6D

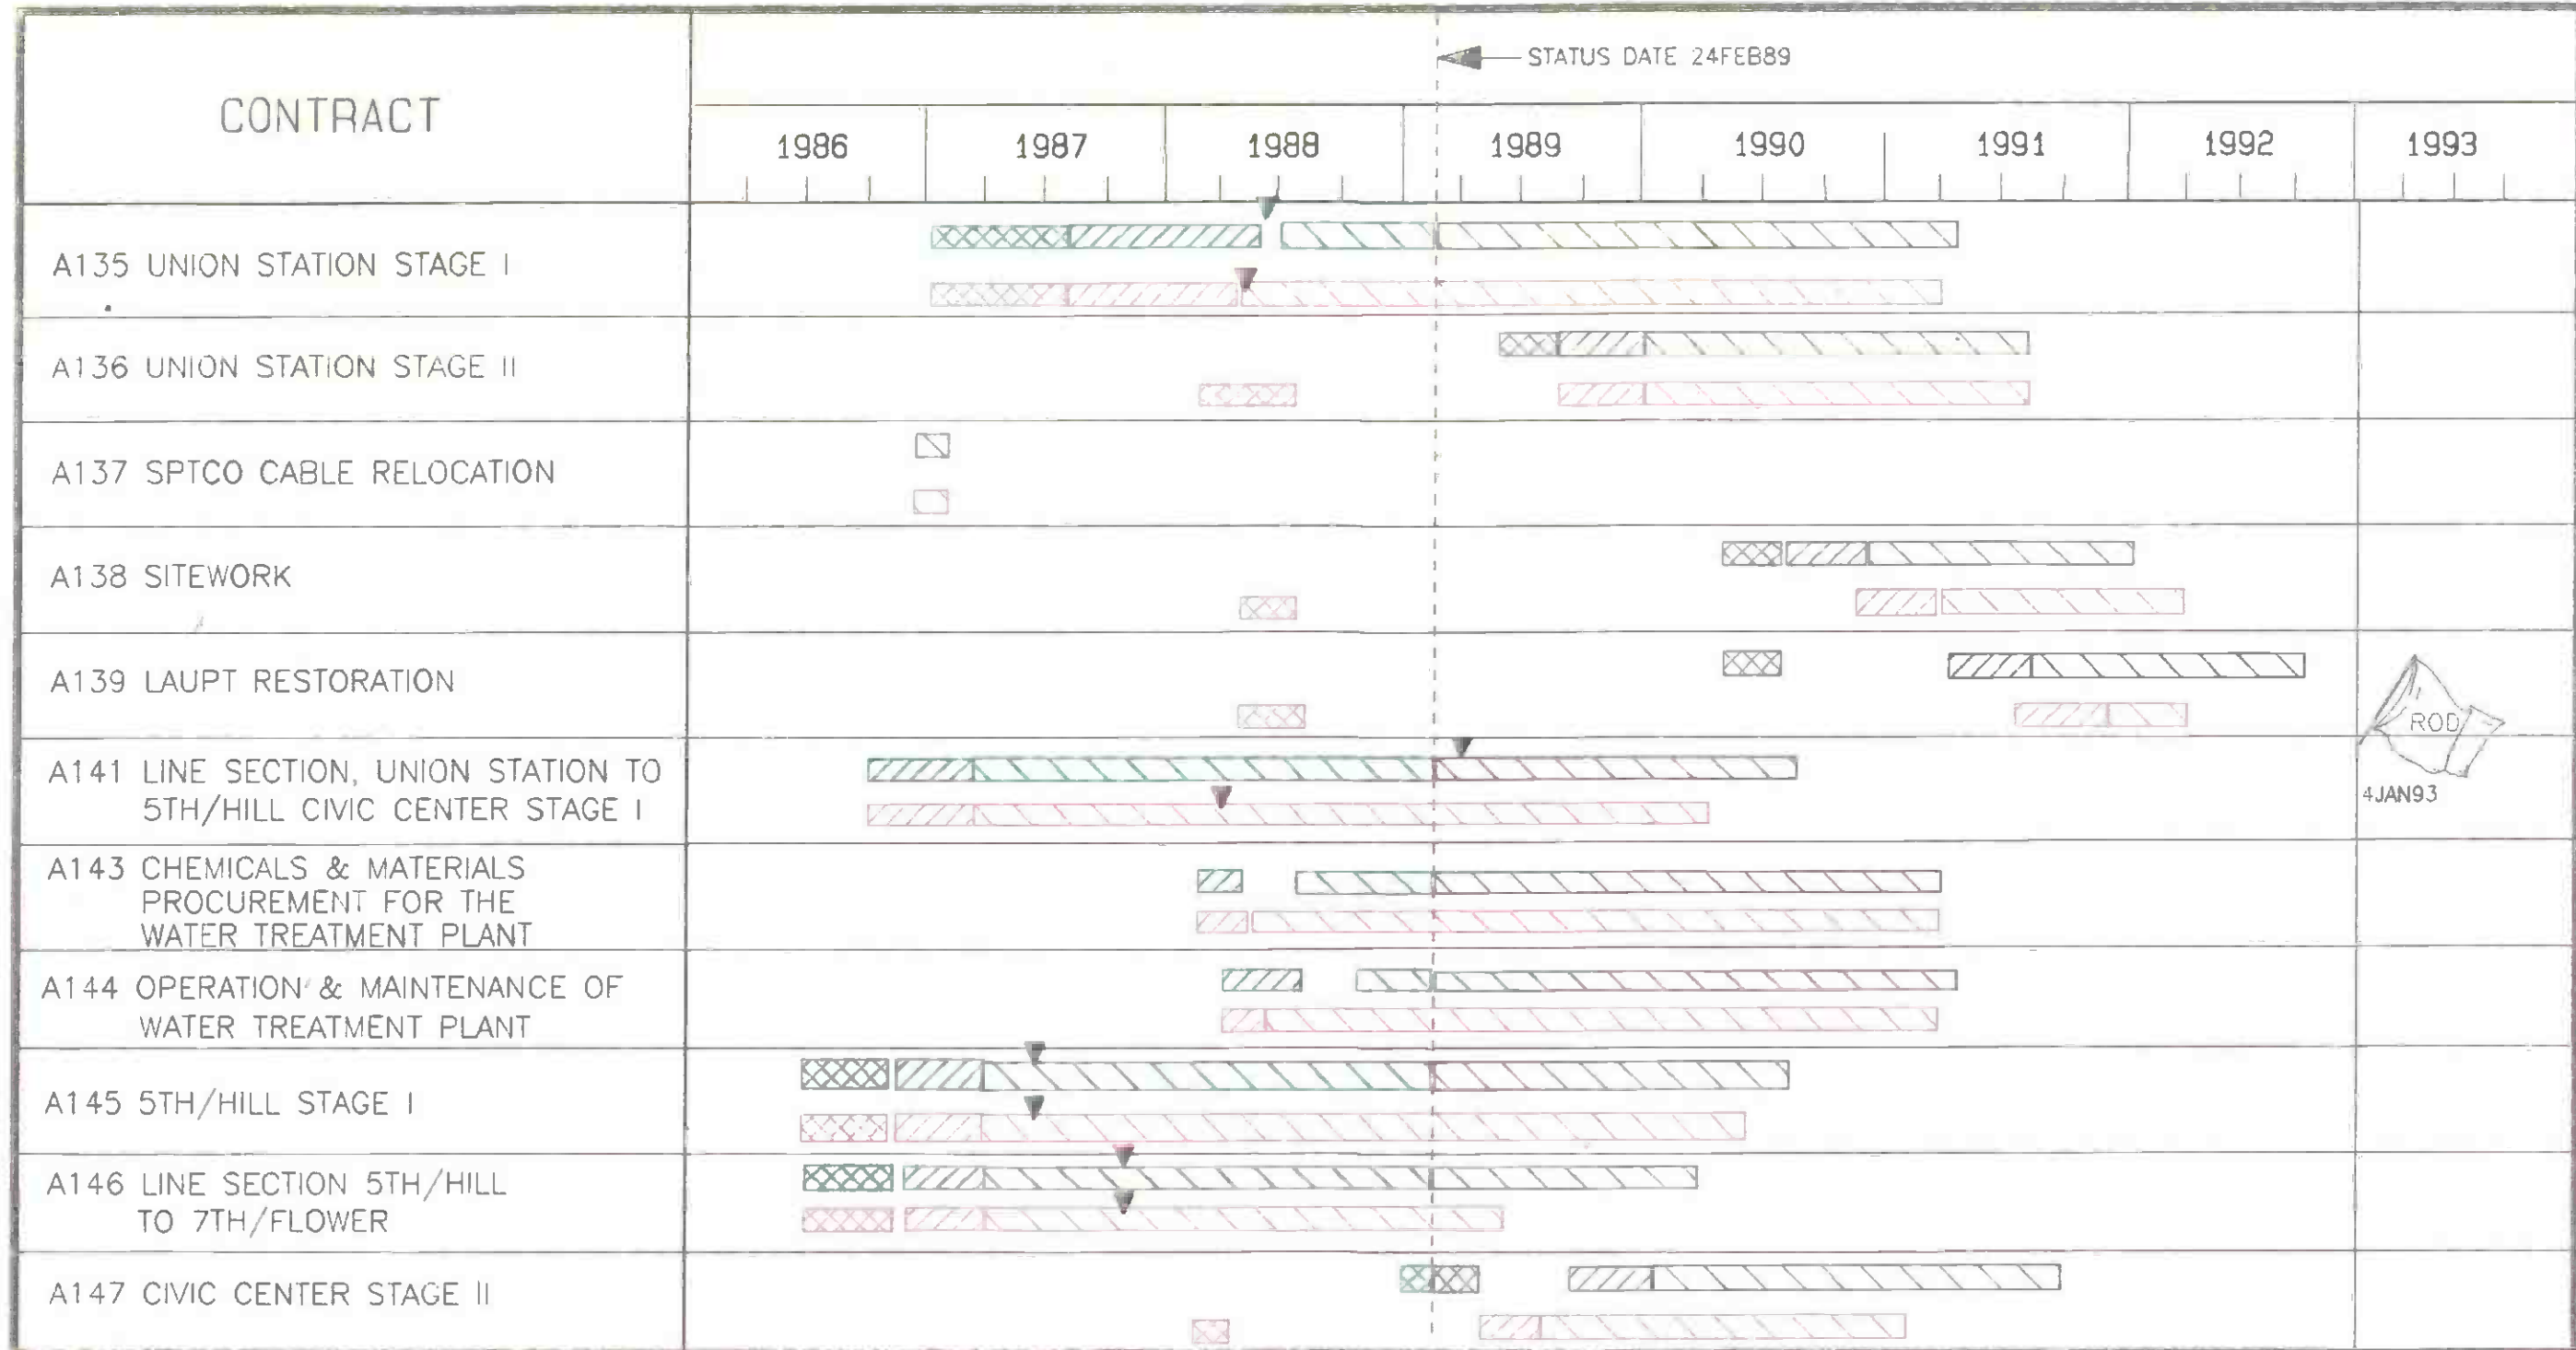

ROD
4 JAN 93

LEGEND	CURRENT SCHEDULE	PROGRESS	APPROVED SCHEDULE
DESIGN			
BID & AWARD			
CONSTRUCTION			
		RIGHT OF WAY AVAILABLE	

SOUTHERN CALIFORNIA RAPID TRANSIT DISTRICT
METRO RAIL PROJECT (MOS-1)
EXECUTIVE SCHEDULE


PAGE 2 OF 11

PREPARED BY *T.C. Sherry*
PROGRAM CONTROL MANAGER (SCHEDULES)

CHECKED BY *Jeffrey B. Christman*
DIRECTOR OF PROGRAM CONTROL

APPROVED BY *William J. Rhee*
ASSISTANT GENERAL MANAGER

DATE	REV
25SEP86	5
14JAN88	6
30SEP88	6C
30DEC88	6D

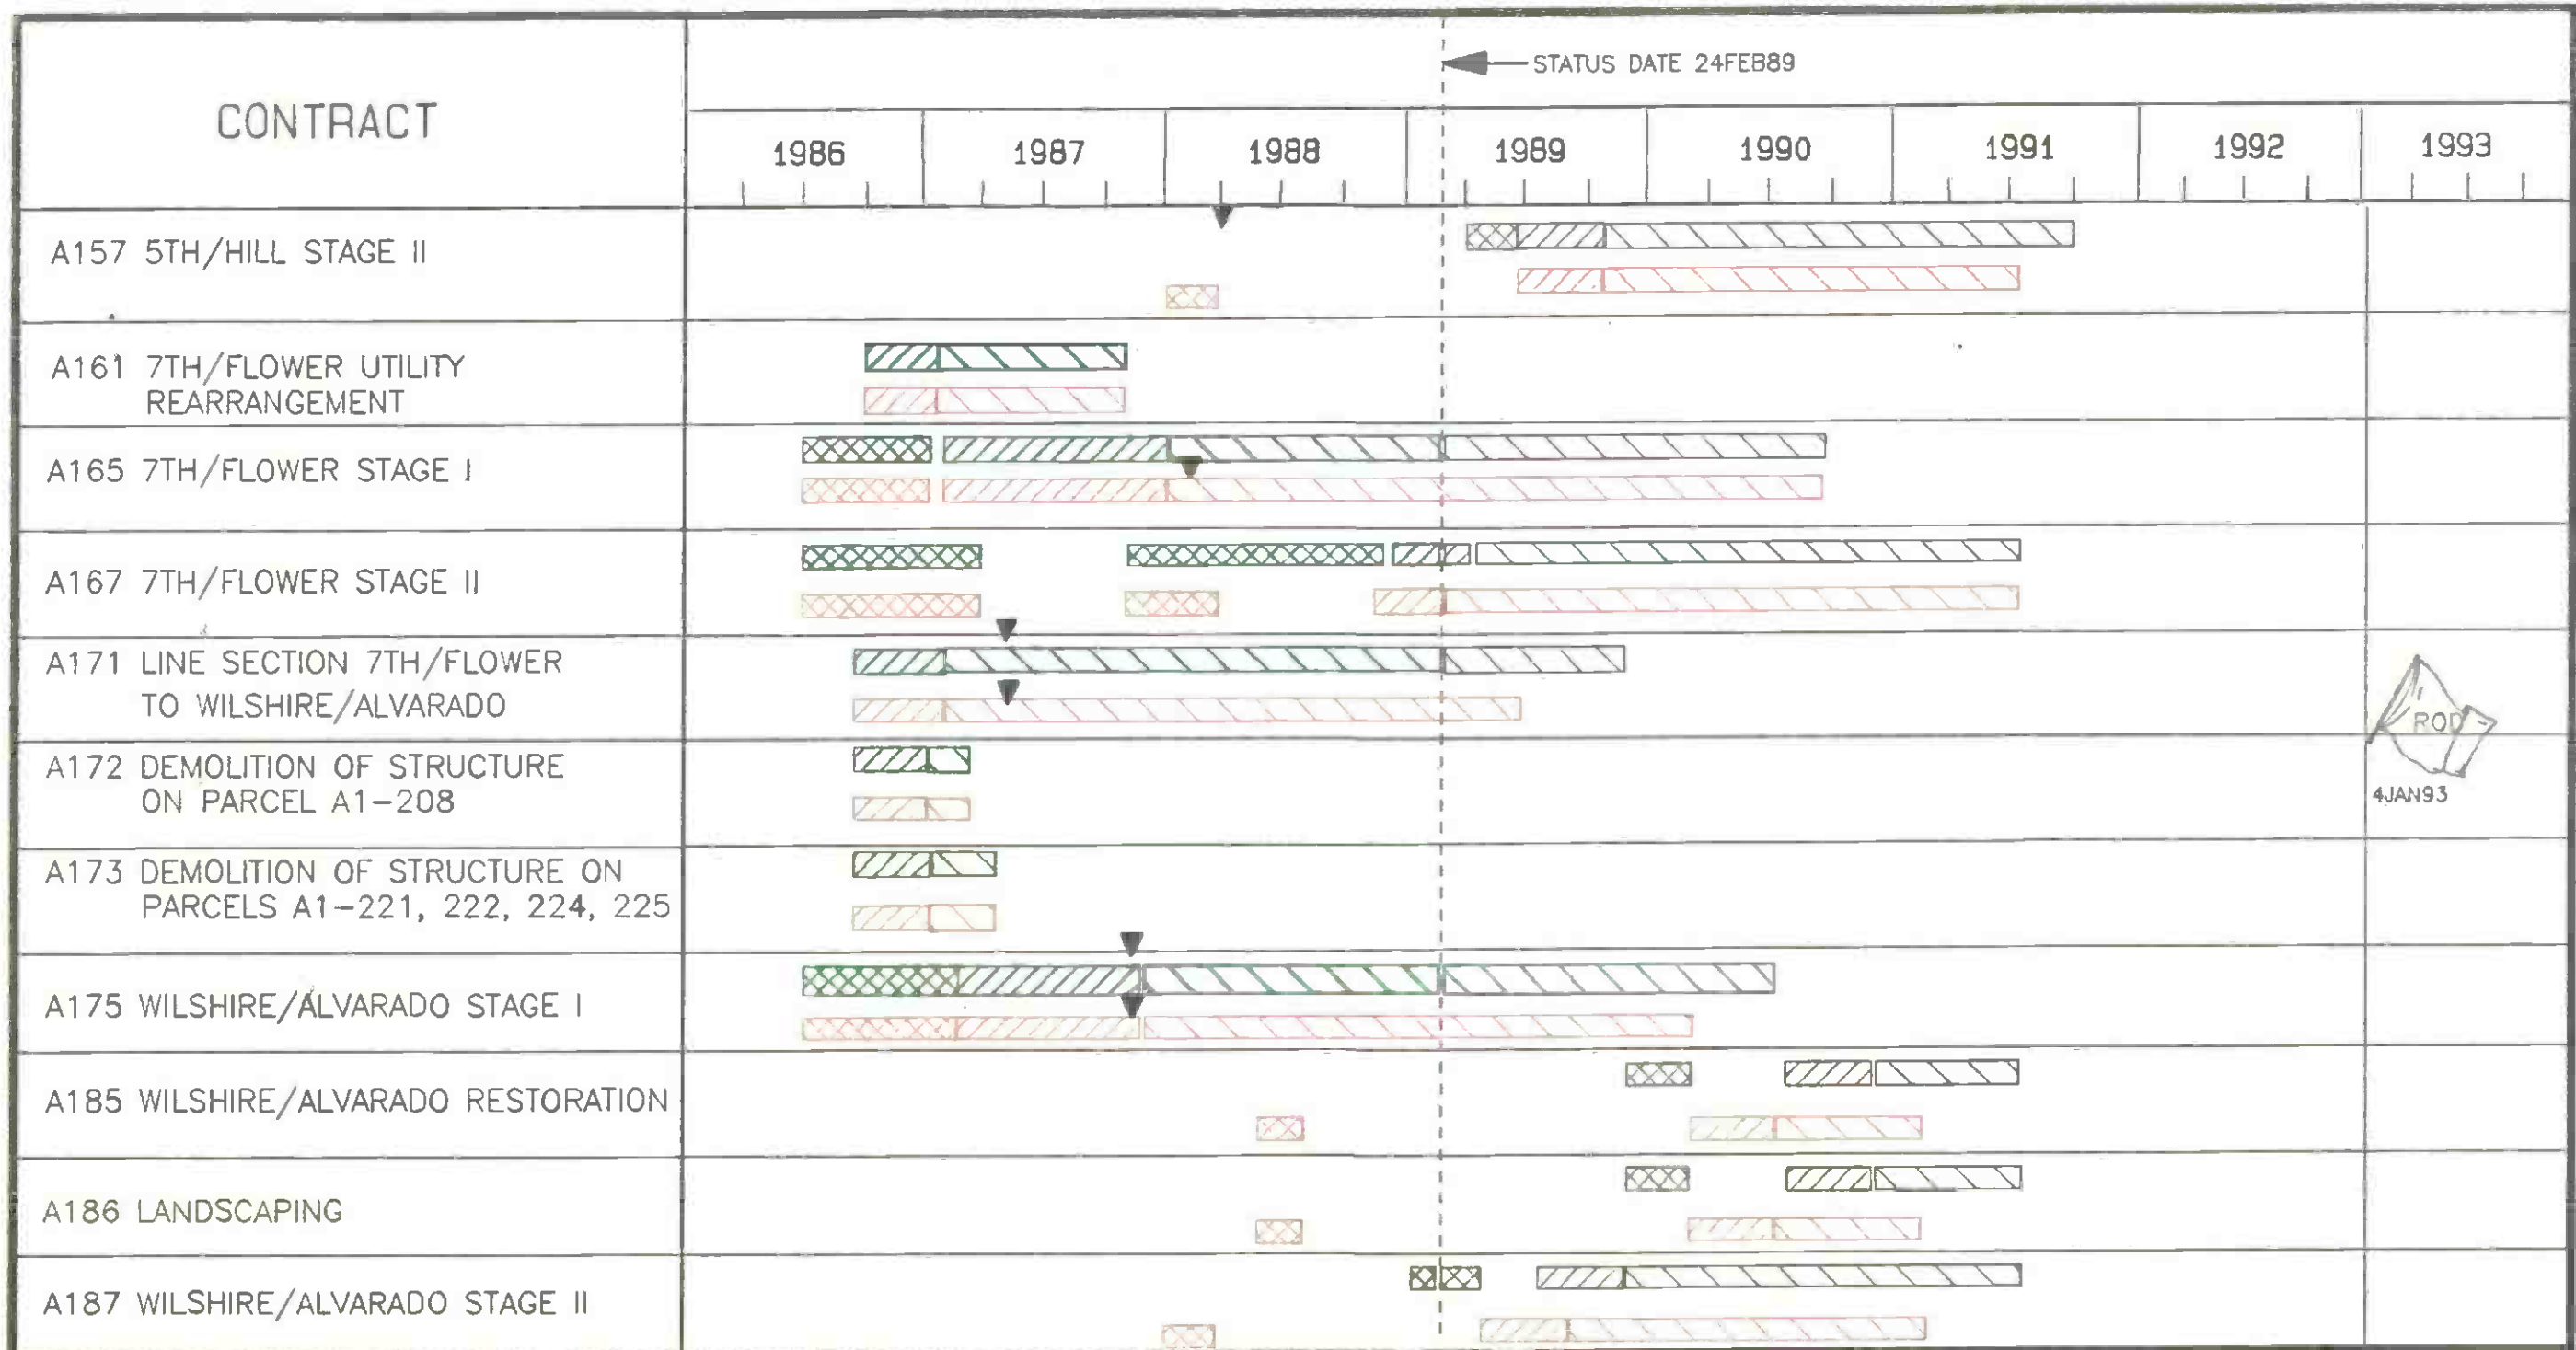

LEGEND	CURRENT SCHEDULE	PROGRESS	APPROVED SCHEDULE
DESIGN			
BID & AWARD			
CONSTRUCTION			
	▼ RIGHT OF WAY AVAILABLE		


SOUTHERN CALIFORNIA RAPID TRANSIT DISTRICT
 METRO RAIL PROJECT (MOS-1)
 EXECUTIVE SCHEDULE

PAGE 3 OF 11

PREPARED BY *T.C. Sherry*
PROGRAM CONTROL MANAGER (SCHEDULES)
 CHECKED BY *Jeffrey Christensen*
DIRECTOR OF PROGRAM CONTROL
 APPROVED BY *William J. Rho*
ASSISTANT GENERAL MANAGER

DATE	REV
25SEP88	5
14JAN88	6
30SEP88	6C
30DEC88	6D

4JAN93

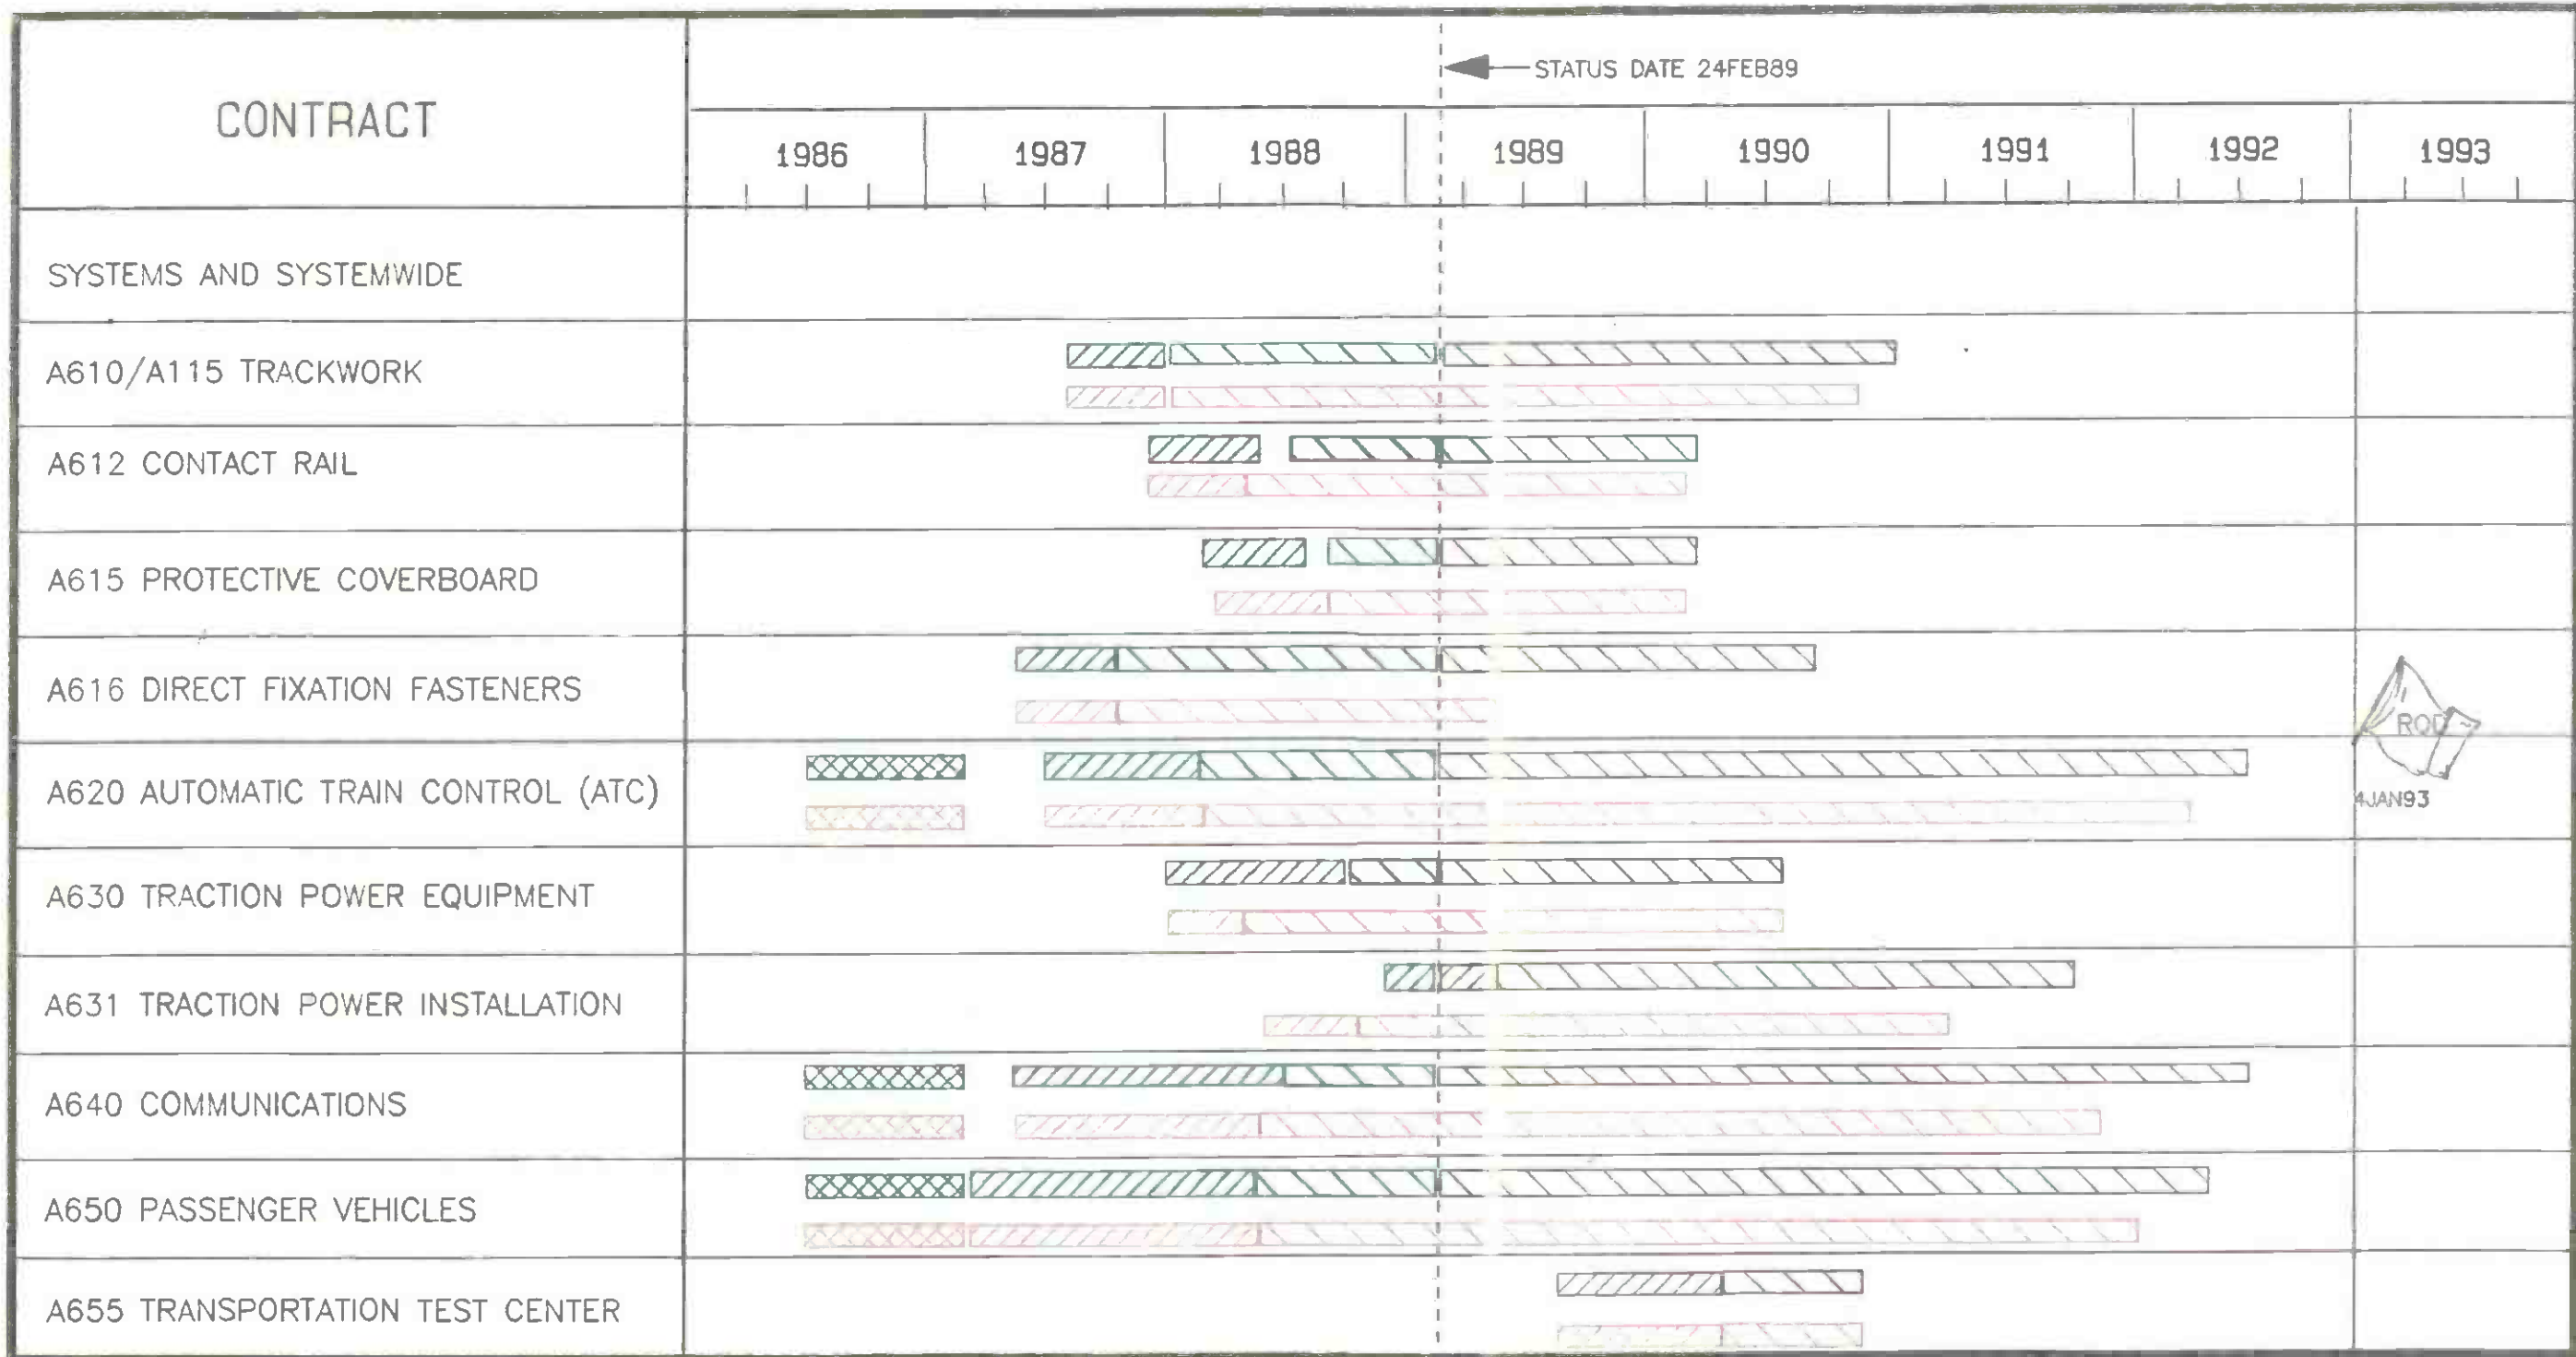

LEGEND	CURRENT SCHEDULE	PROGRESS	APPROVED SCHEDULE
DESIGN			
BID & AWARD			
CONSTRUCTION			
	▼ RIGHT OF WAY AVAILABLE		

SOUTHERN CALIFORNIA RAPID TRANSIT DISTRICT
METRO RAIL PROJECT (MOS-1)
EXECUTIVE SCHEDULE


PAGE 4 OF 11

PREPARED BY *TC Sherry*
PROGRAM CONTROL MANAGER (SCHEDULES)

CHECKED BY *Jeffrey Christensen*
DIRECTOR OF PROGRAM CONTROL

APPROVED BY *William J. Rhee*
ASSISTANT GENERAL MANAGER

DATE	REV
25 SEP 86	5
14 JAN 88	6
30 SEP 88	6C
30 DEC 88	6D

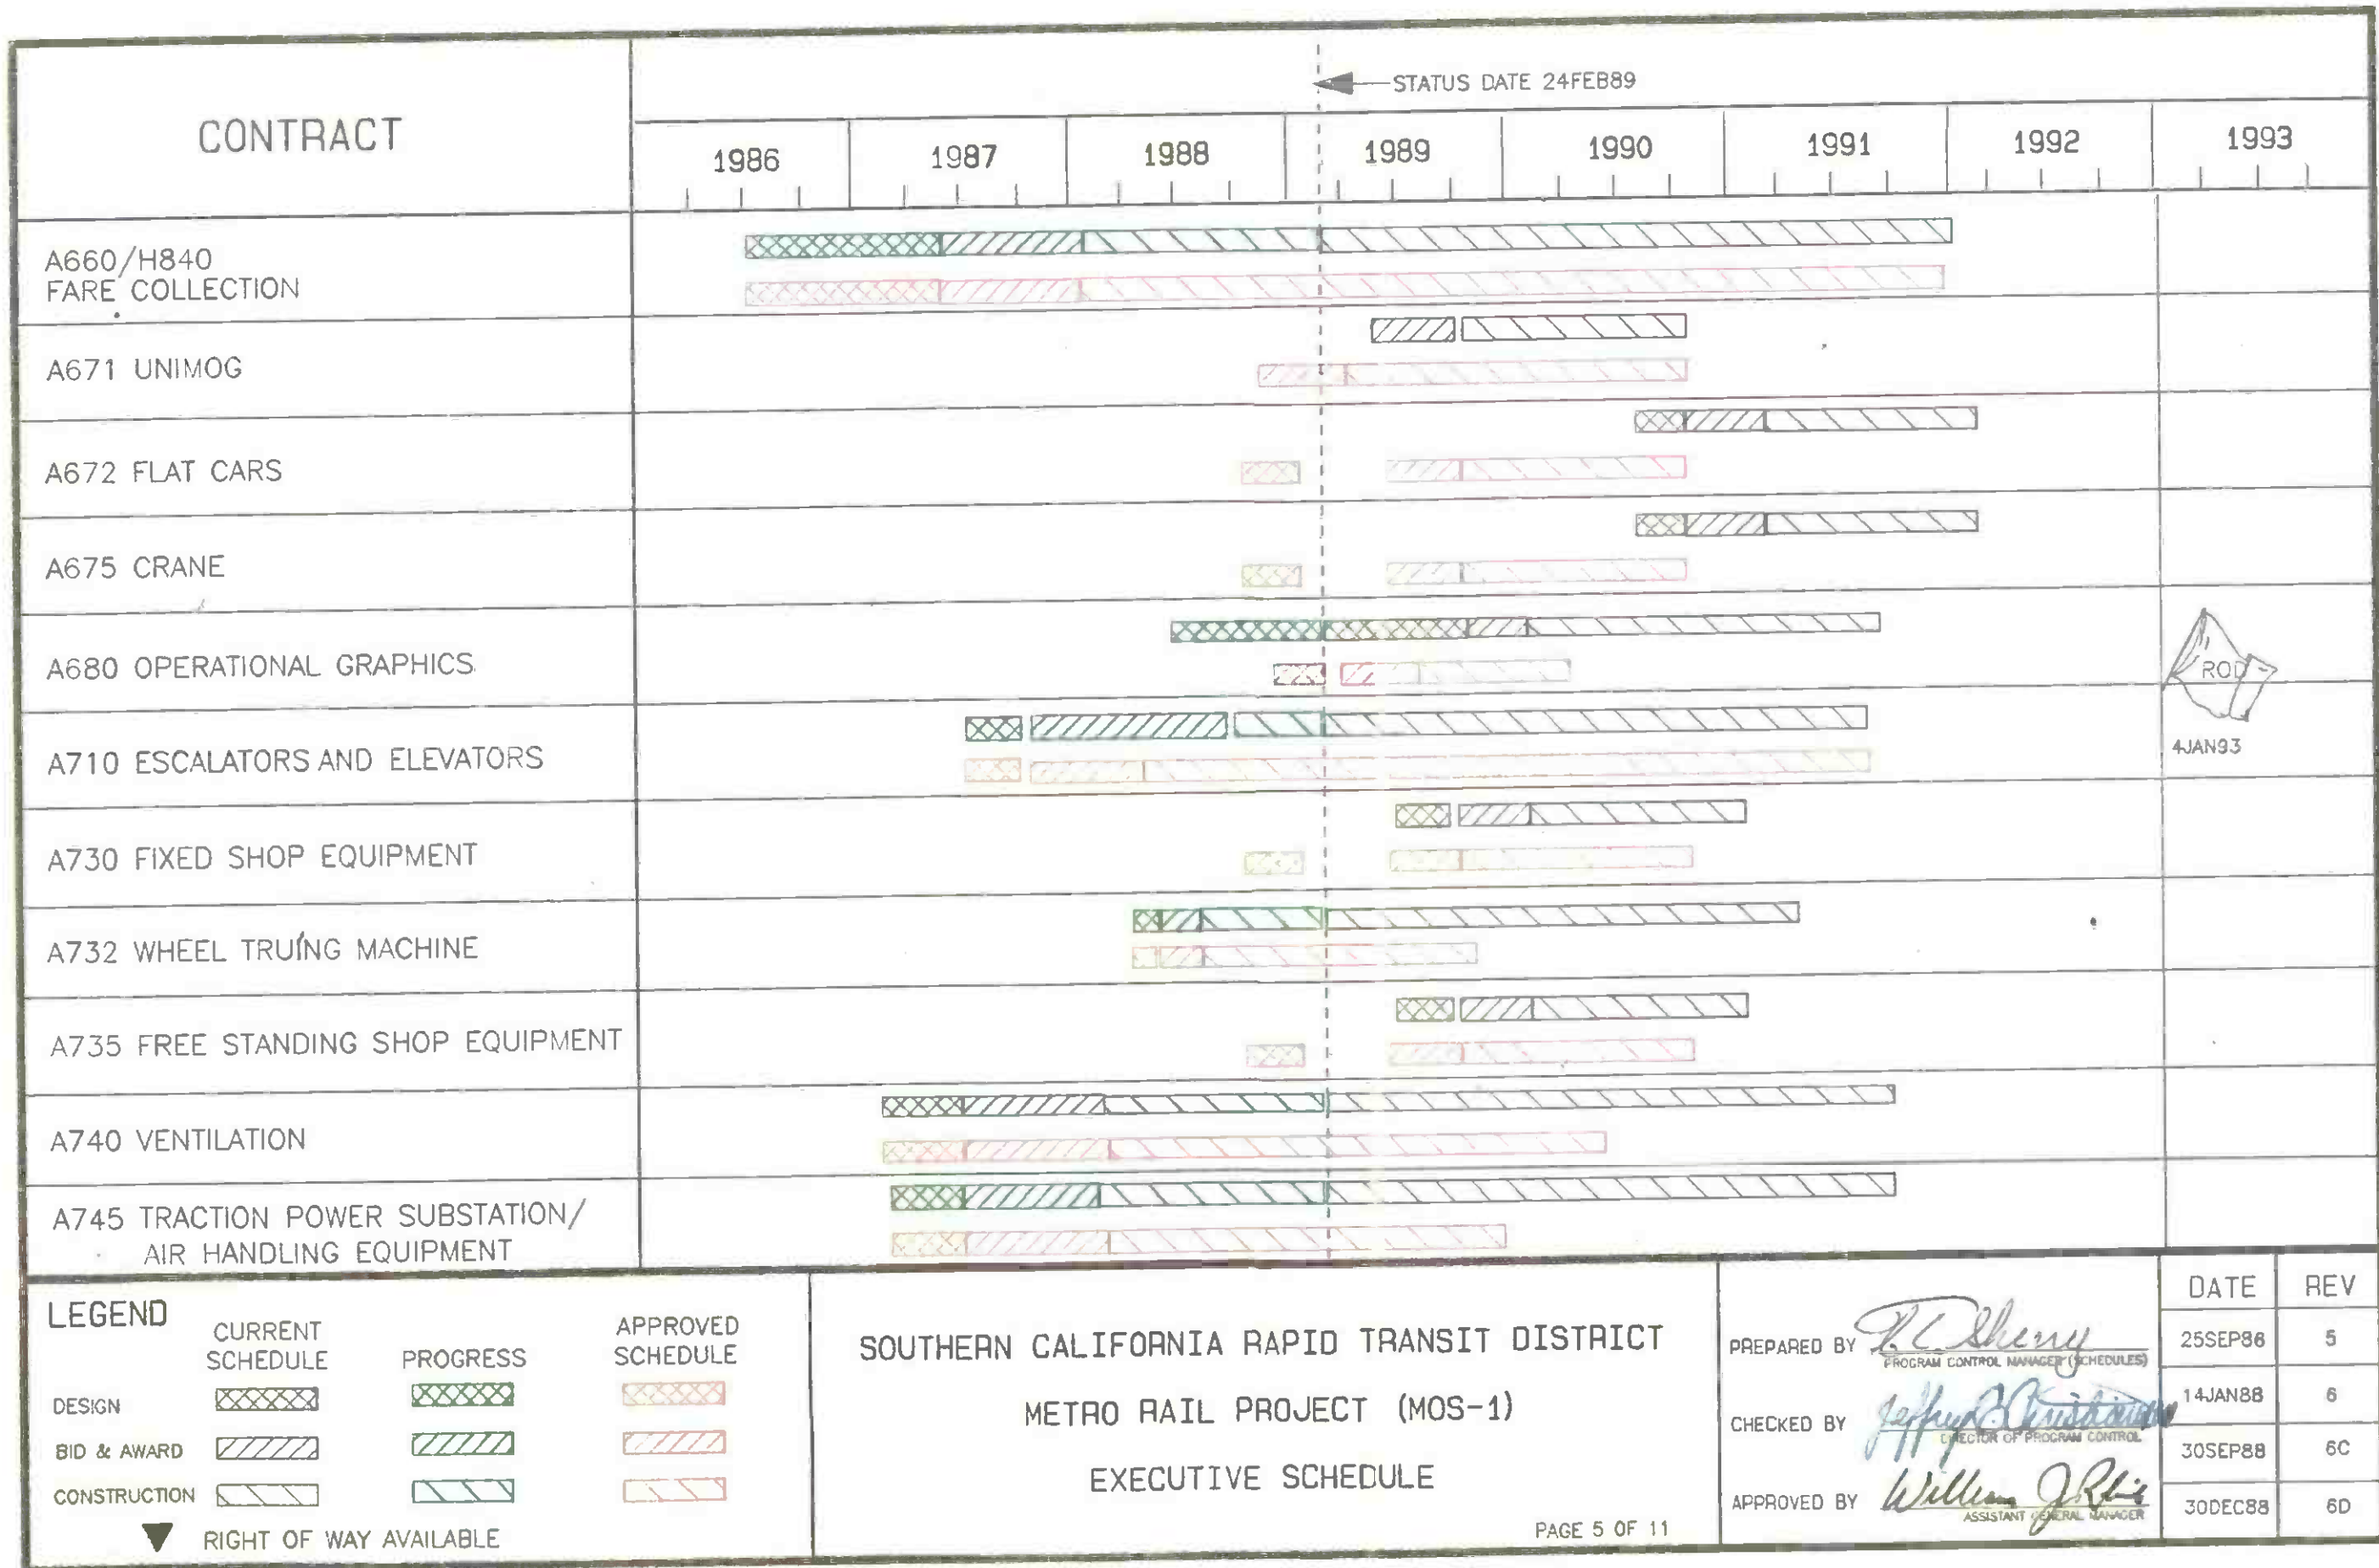

LEGEND	CURRENT SCHEDULE	PROGRESS	APPROVED SCHEDULE
DESIGN	[Cross-hatch pattern]	[Green diagonal pattern]	[Orange diagonal pattern]
BID & AWARD	[Blue diagonal pattern]	[Green diagonal pattern]	[Red diagonal pattern]
CONSTRUCTION	[White diagonal pattern]	[Green diagonal pattern]	[Red diagonal pattern]
	▼ RIGHT OF WAY AVAILABLE		


SOUTHERN CALIFORNIA RAPID TRANSIT DISTRICT
METRO RAIL PROJECT (MOS-1)
EXECUTIVE SCHEDULE

PREPARED BY *P. C. Sherry*
PROGRAM CONTROL MANAGER (SCHEDULES)

CHECKED BY *Jeffrey B. Smith*
DIRECTOR OF PROGRAM CONTROL

APPROVED BY *William J. Rice*
ASSISTANT GENERAL MANAGER

DATE	REV
25SEP86	5
14JAN88	6
30SEP88	6C
30DEC88	6D

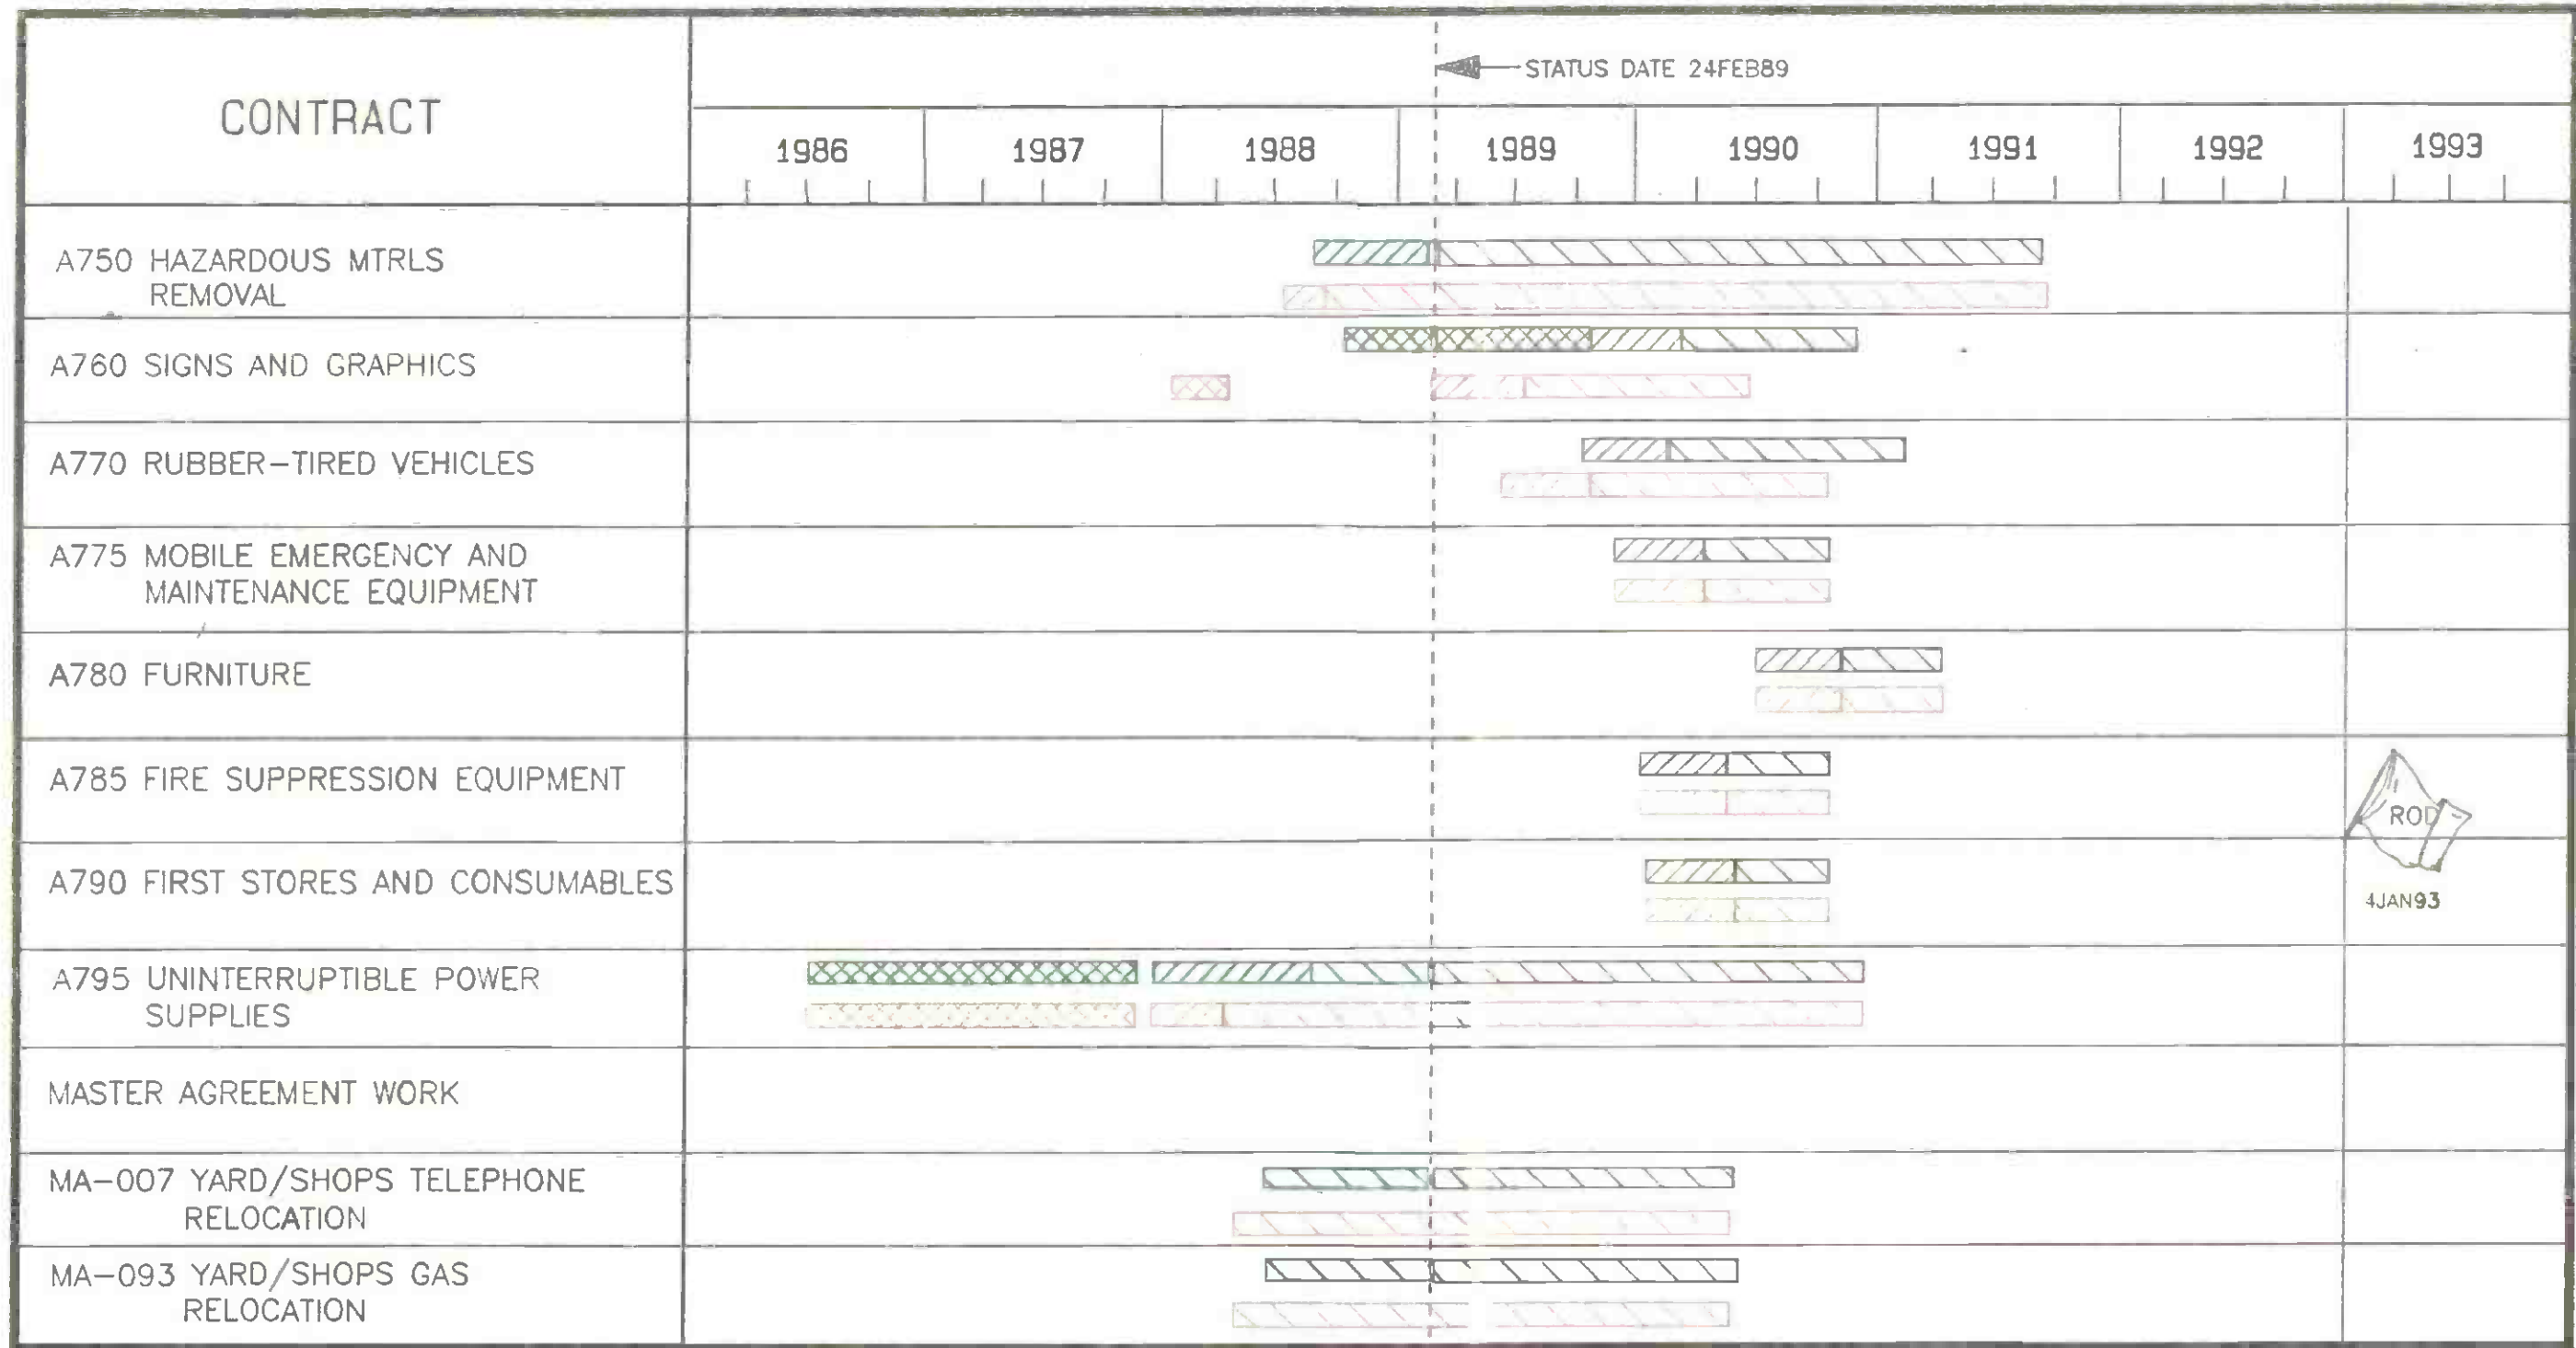


LEGEND	CURRENT SCHEDULE	PROGRESS	APPROVED SCHEDULE
DESIGN			
BID & AWARD			
CONSTRUCTION			
	RIGHT OF WAY AVAILABLE		


SOUTHERN CALIFORNIA RAPID TRANSIT DISTRICT
 METRO RAIL PROJECT (MOS-1)
 EXECUTIVE SCHEDULE

PAGE 6 OF 11

	DATE	REV
PREPARED BY <i>T.C. Sherry</i> PROGRAM CONTROL MANAGER (SCHEDULES)	25SEP88	5
CHECKED BY <i>Jeffrey...</i> DIRECTOR OF PROGRAM CONTROL	14JAN88	6
APPROVED BY <i>William J. Rhee</i> ASSISTANT GENERAL MANAGER	30SEP88	6C
	30DEC88	6D

CONTRACT	← STATUS DATE 24FEB89							
	1986	1987	1988	1989	1990	1991	1992	1993
MA-A09 YARD/SHOPS WATER RELOCATION			▨	▨				
MA-009 YARD/SHOPS POWER RELOCATION			▨	▨				
MA-545 YARD/SHOPS CHEVRON RELOCATION			▨	▨				
MA-002 YARD/SHOPS CITY OF LOS ANGELES			▨	▨				
MA-056 YARD/SHOPS CALTRANS			▨	▨				
MA-094 YARD/SHOPS COUNTY OF LOS ANGELES			▨	▨				 4JAN93
MA-008 YARD/SHOPS WESTERN UNION REPLACEMENT			▨	▨				
MA-007 UNION STATION TELEPHONE RELOCATION			▨	▨				
MA-A09 UNION STATION WATER RELOCATION			▨	▨				
MA-009 UNION STATION POWER RELOCATION			▨	▨				
MA-002 UNION STATION CITY OF LOS ANGELES			▨	▨				

LEGEND			SOUTHERN CALIFORNIA RAPID TRANSIT DISTRICT METRO RAIL PROJECT (MOS-1) EXECUTIVE SCHEDULE	PREPARED BY <i>T.C. Sherry</i> <small>PROGRAM CONTROL MANAGER (SCHEDULES)</small> CHECKED BY <i>Jeffrey Christensen</i> <small>DIRECTOR OF PROGRAM CONTROL</small> APPROVED BY <i>William J. Rhee</i> <small>ASSISTANT GENERAL MANAGER</small>	DATE	REV
DESIGN	▨	▨			25SEP86	5
BID & AWARD	▨	▨			14JAN88	6
CONSTRUCTION	▨	▨			30SEP88	6C
▼	RIGHT OF WAY AVAILABLE		30DEC88	6D		

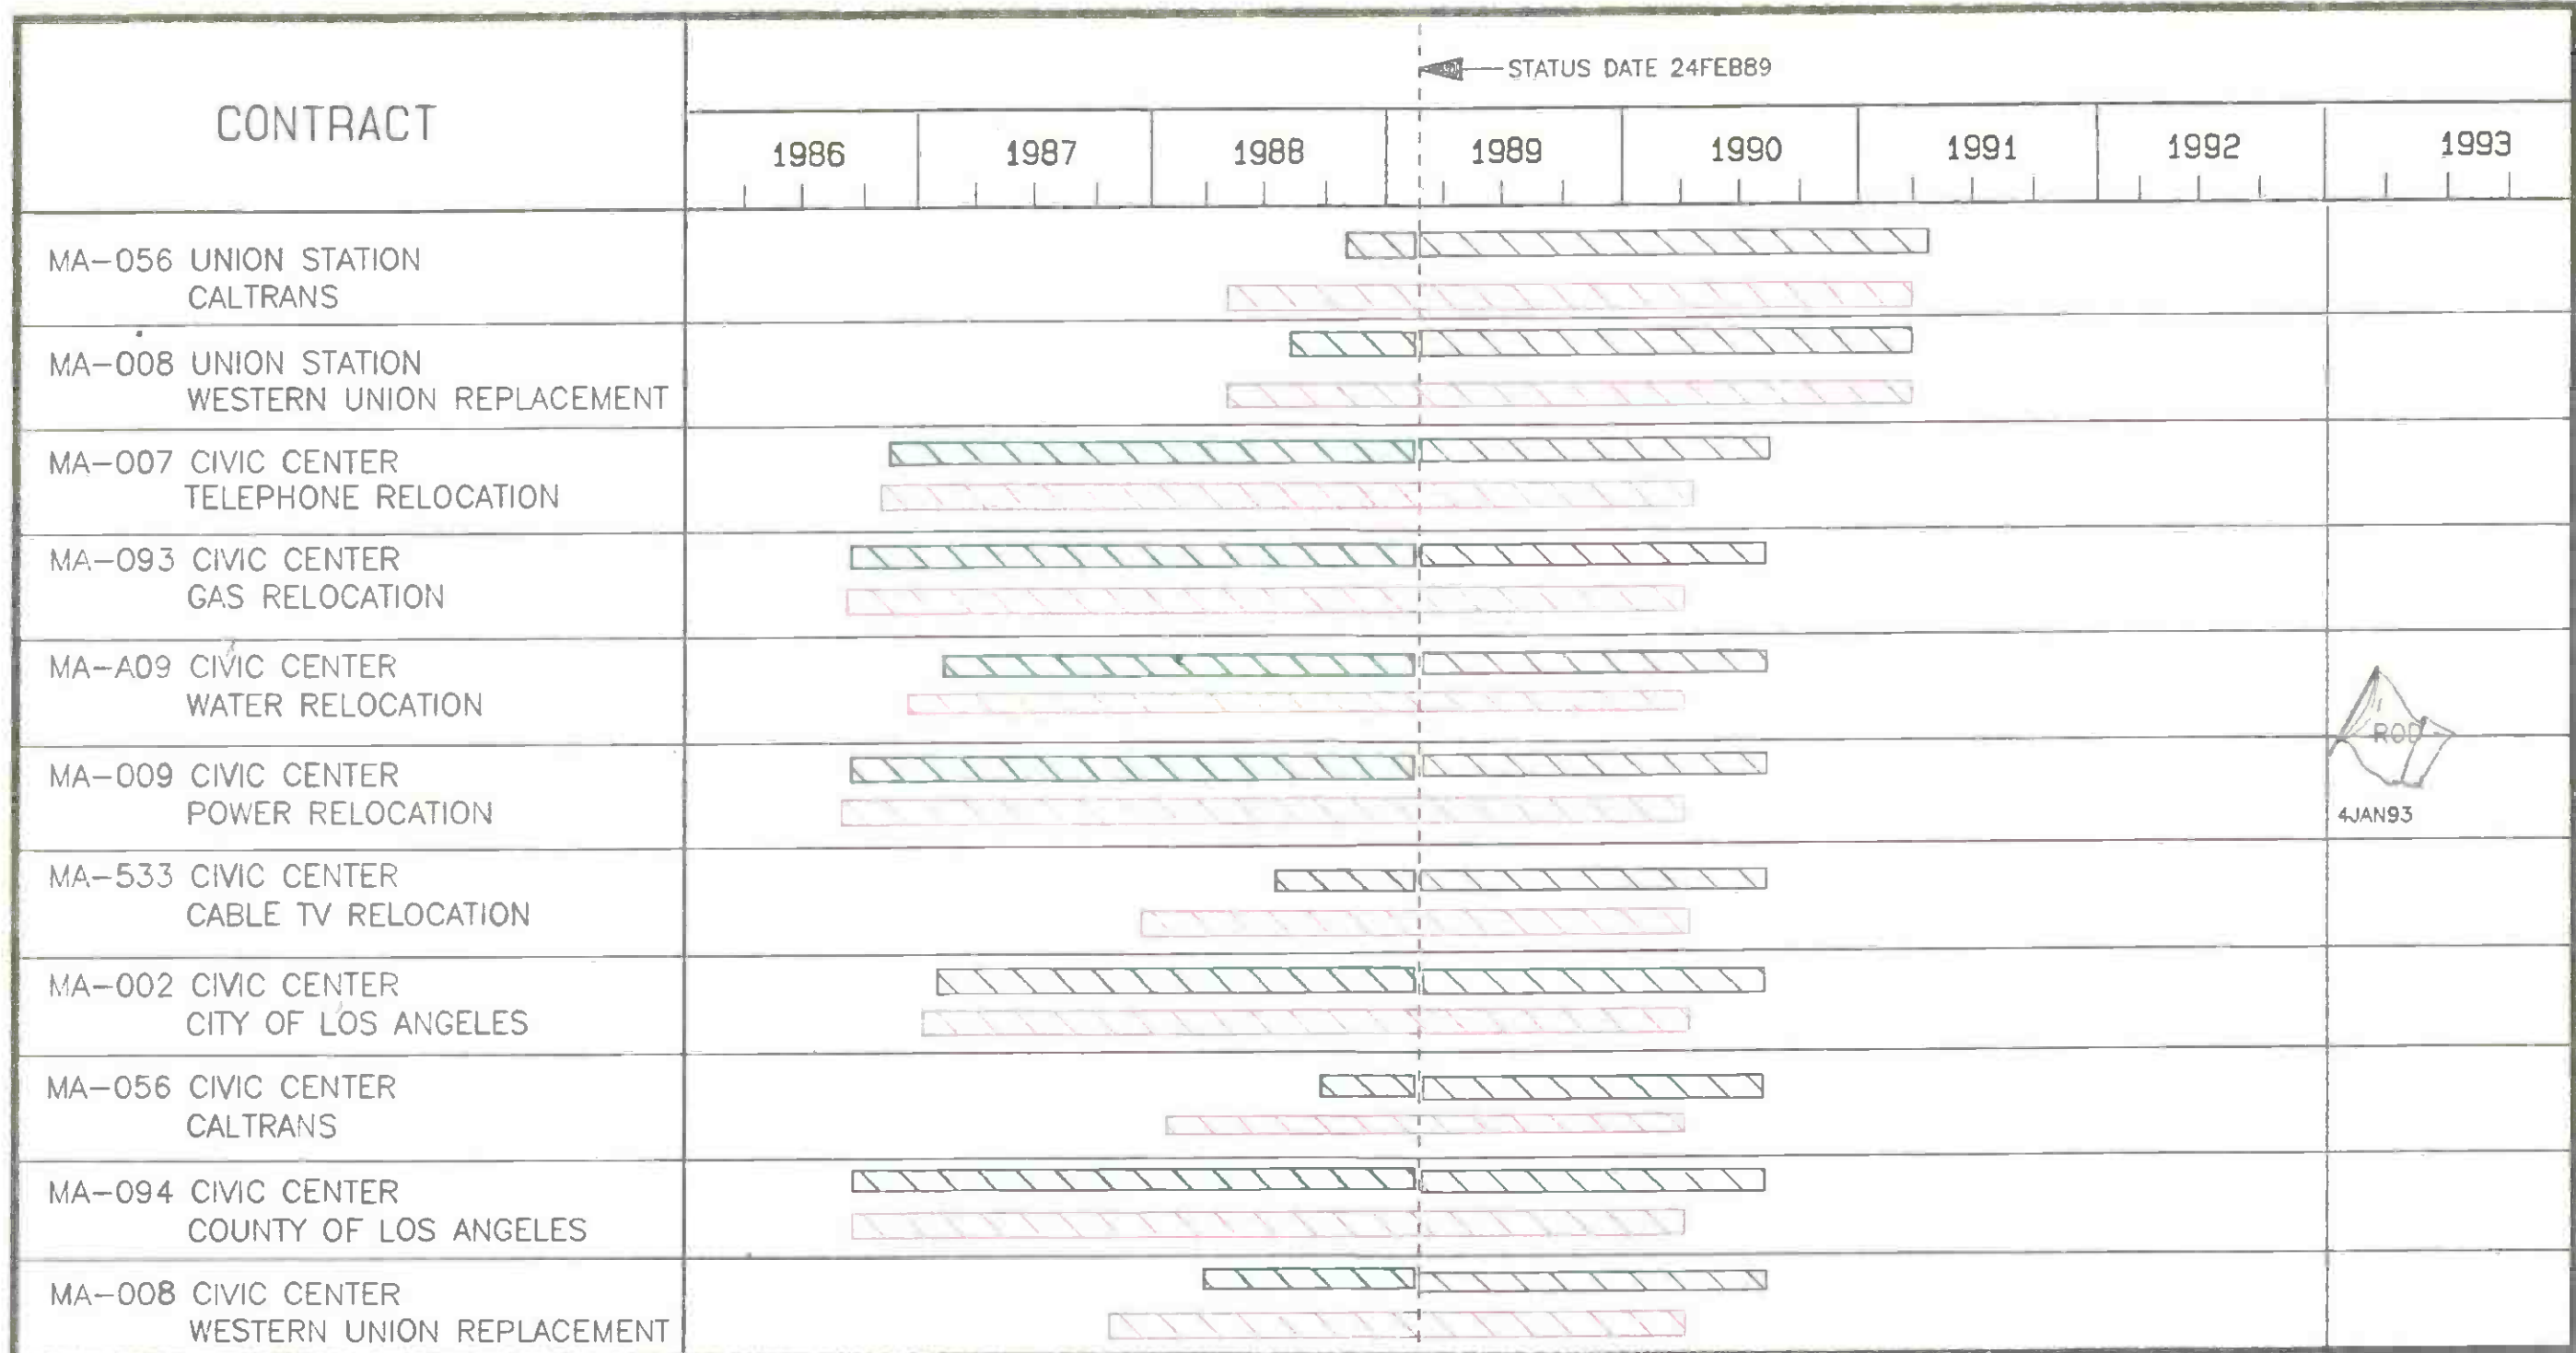

LEGEND	CURRENT SCHEDULE	PROGRESS	APPROVED SCHEDULE
DESIGN			
BID & AWARD			
CONSTRUCTION			
	RIGHT OF WAY AVAILABLE		


SOUTHERN CALIFORNIA RAPID TRANSIT DISTRICT
METRO RAIL PROJECT (MOS-1)
EXECUTIVE SCHEDULE


PREPARED BY *T. Sherry*
PROGRAM CONTROL MANAGER (SCHEDULES)

CHECKED BY *Jeffrey B. Strickland*
DIRECTOR OF PROGRAM CONTROL





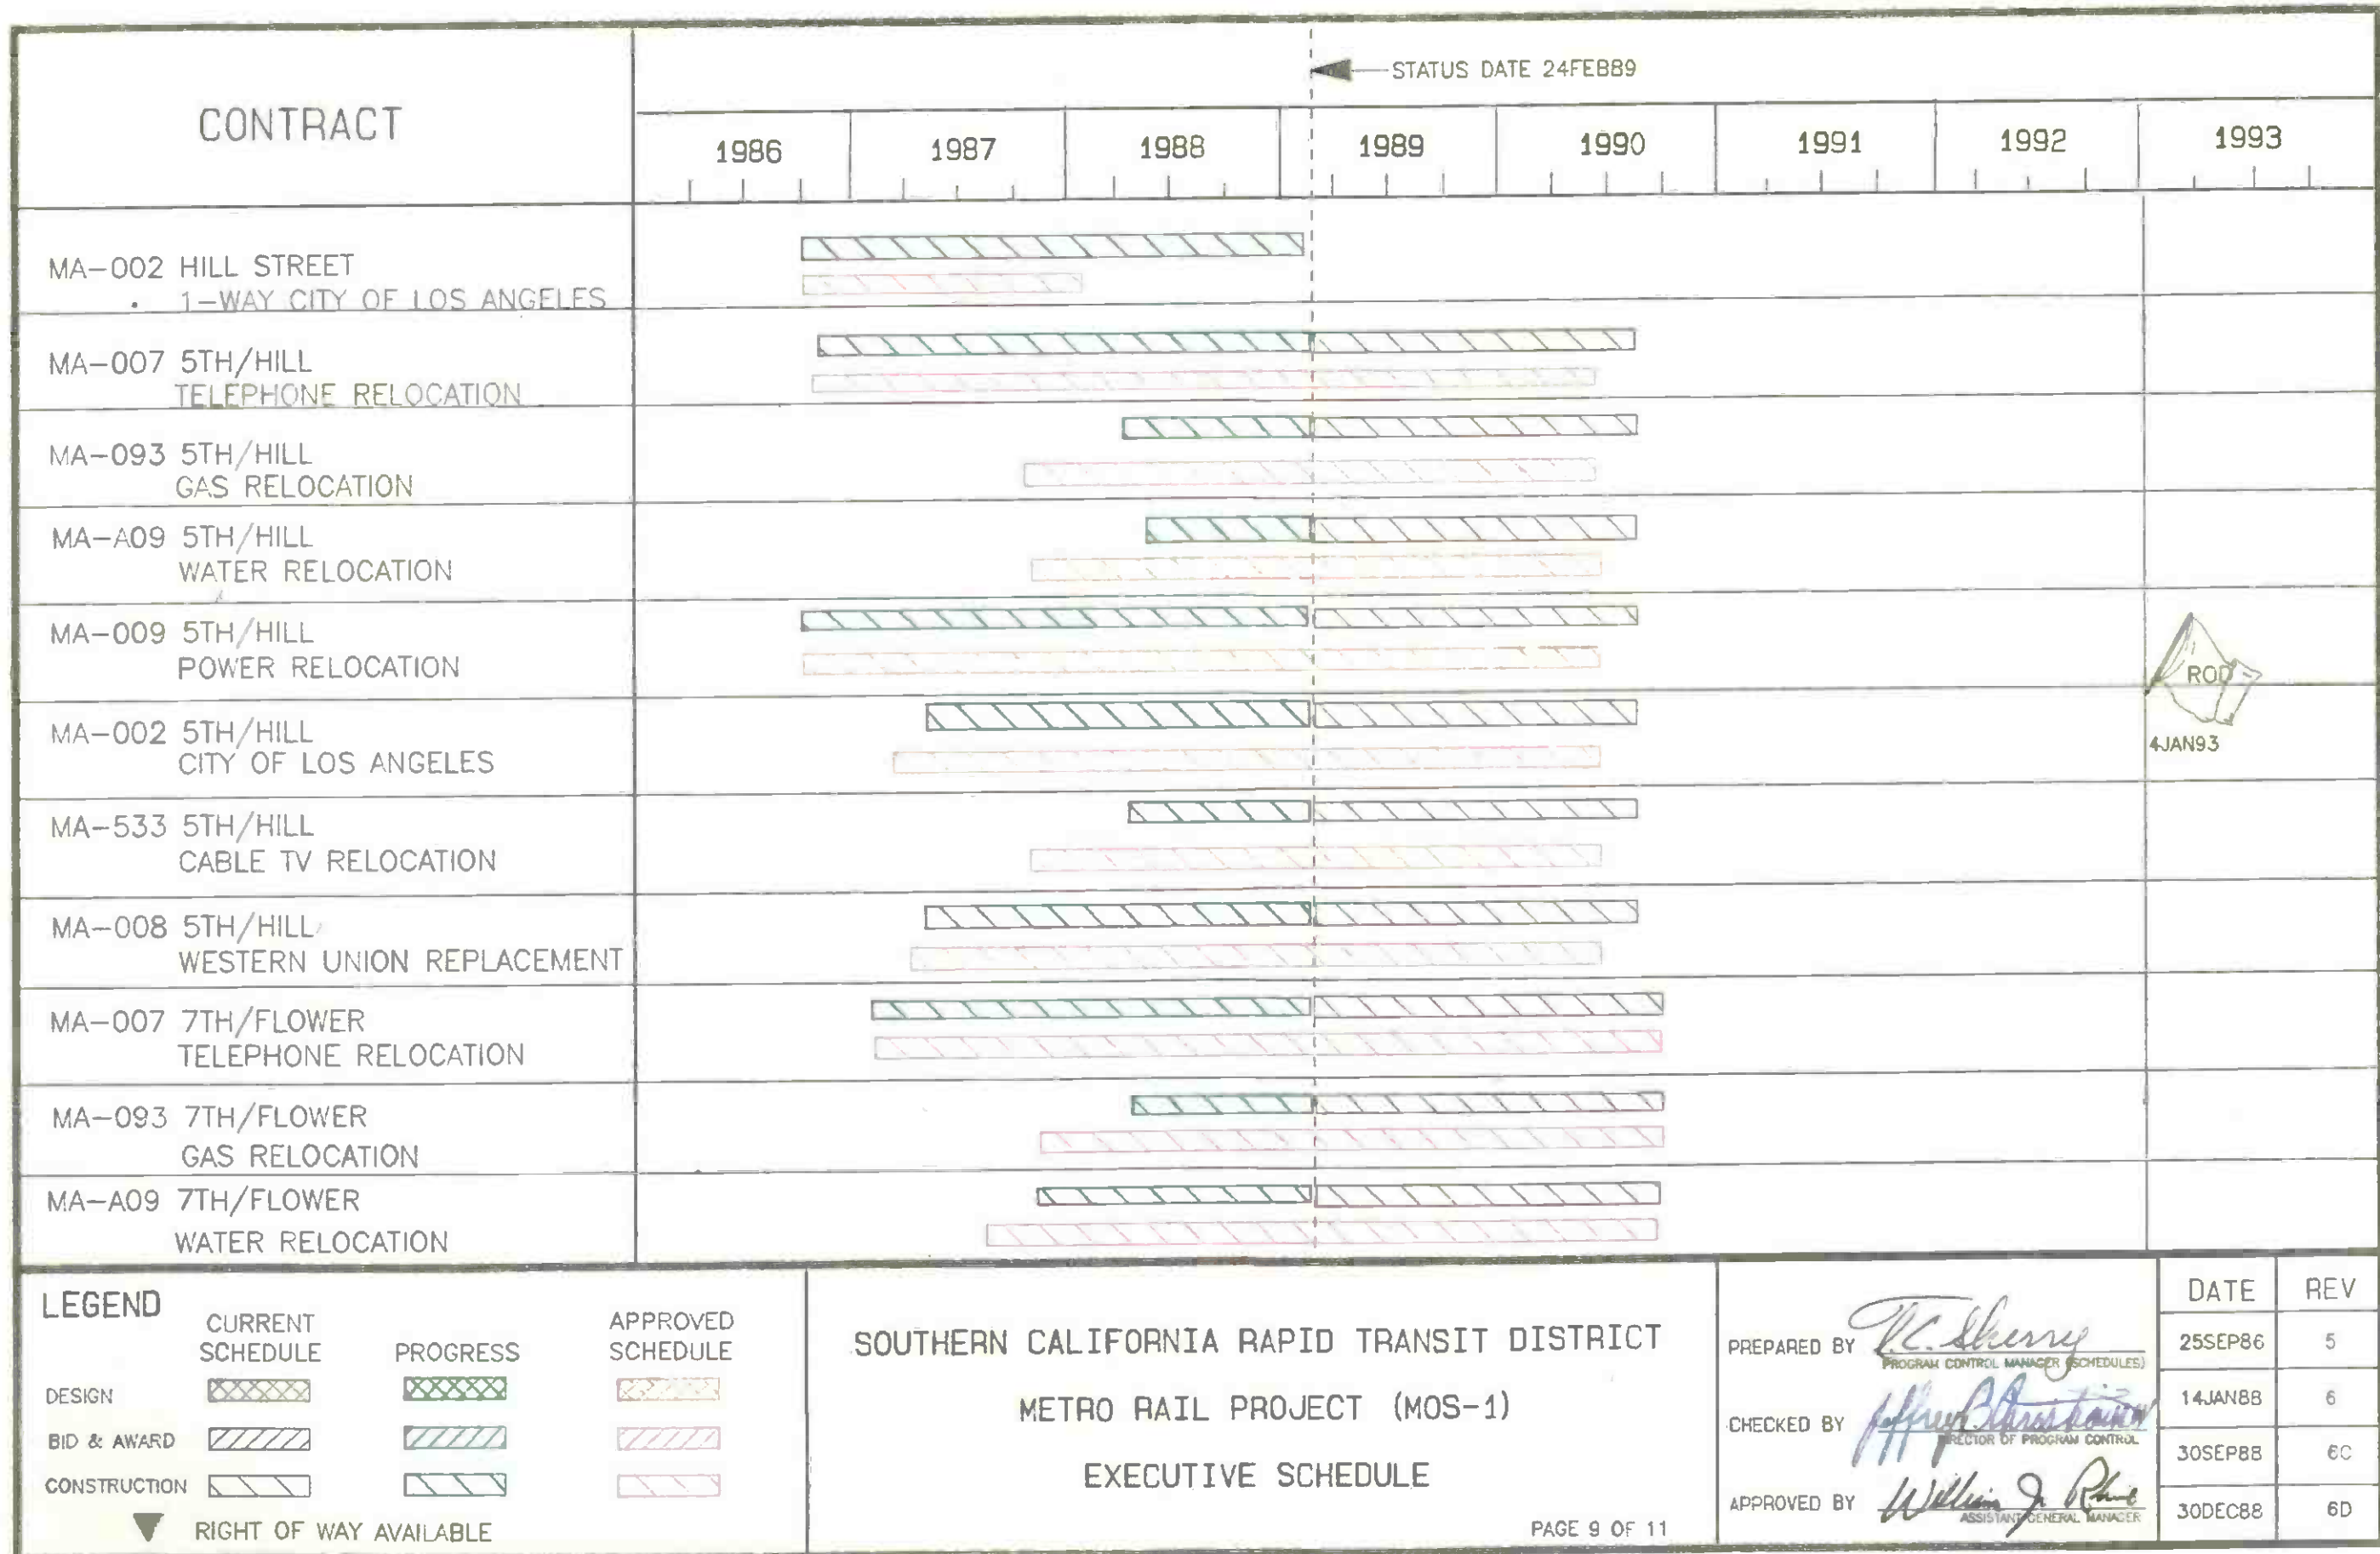

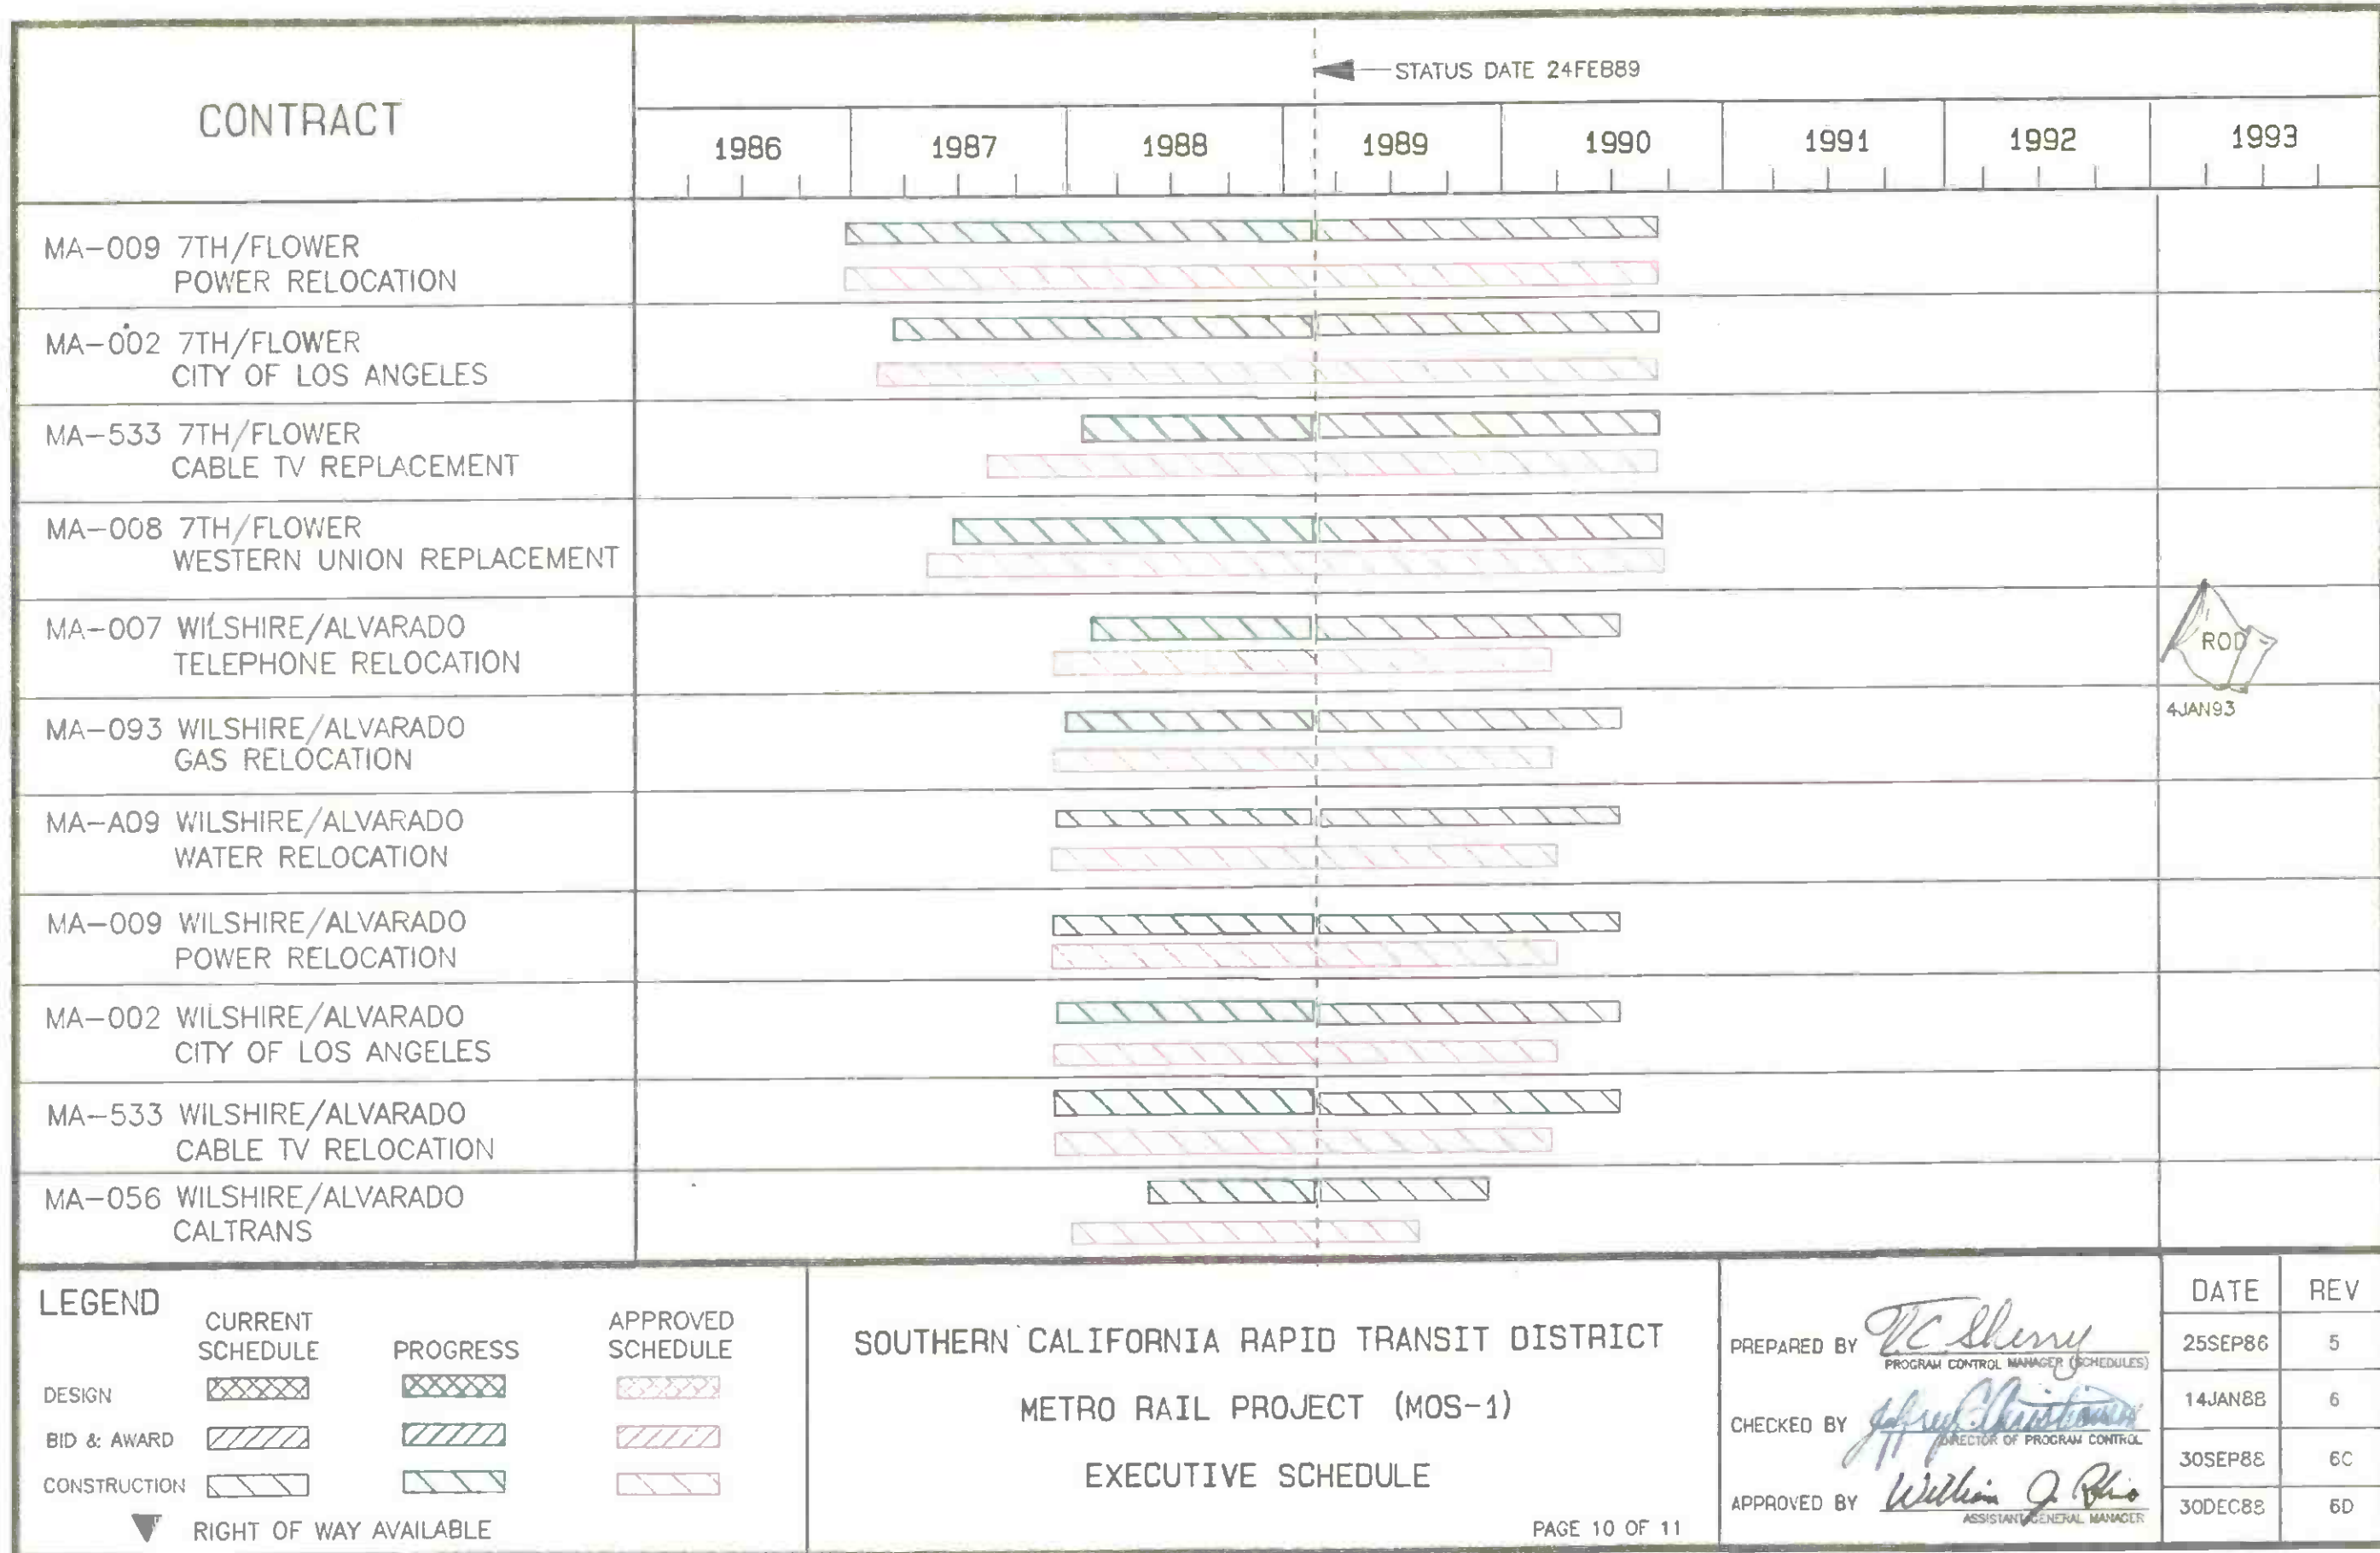






APPROVED BY *William J. Rhoads*
ASSISTANT GENERAL MANAGER

DATE	REV
25SEP86	5
14JAN88	6
30SEP88	6C
30DEC88	6D








LEGEND

			
DESIGN			
BID & AWARD			
CONSTRUCTION			
		RIGHT OF WAY AVAILABLE	


SOUTHERN CALIFORNIA RAPID TRANSIT DISTRICT
METRO RAIL PROJECT (MOS-1)
EXECUTIVE SCHEDULE

PREPARED BY 
PROGRAM CONTROL MANAGER (SCHEDULES)

CHECKED BY 
DIRECTOR OF PROGRAM CONTROL

APPROVED BY 
ASSISTANT GENERAL MANAGER

DATE	REV
25SEP86	5
14JAN88	6
30SEP88	6C
30DEC88	6D

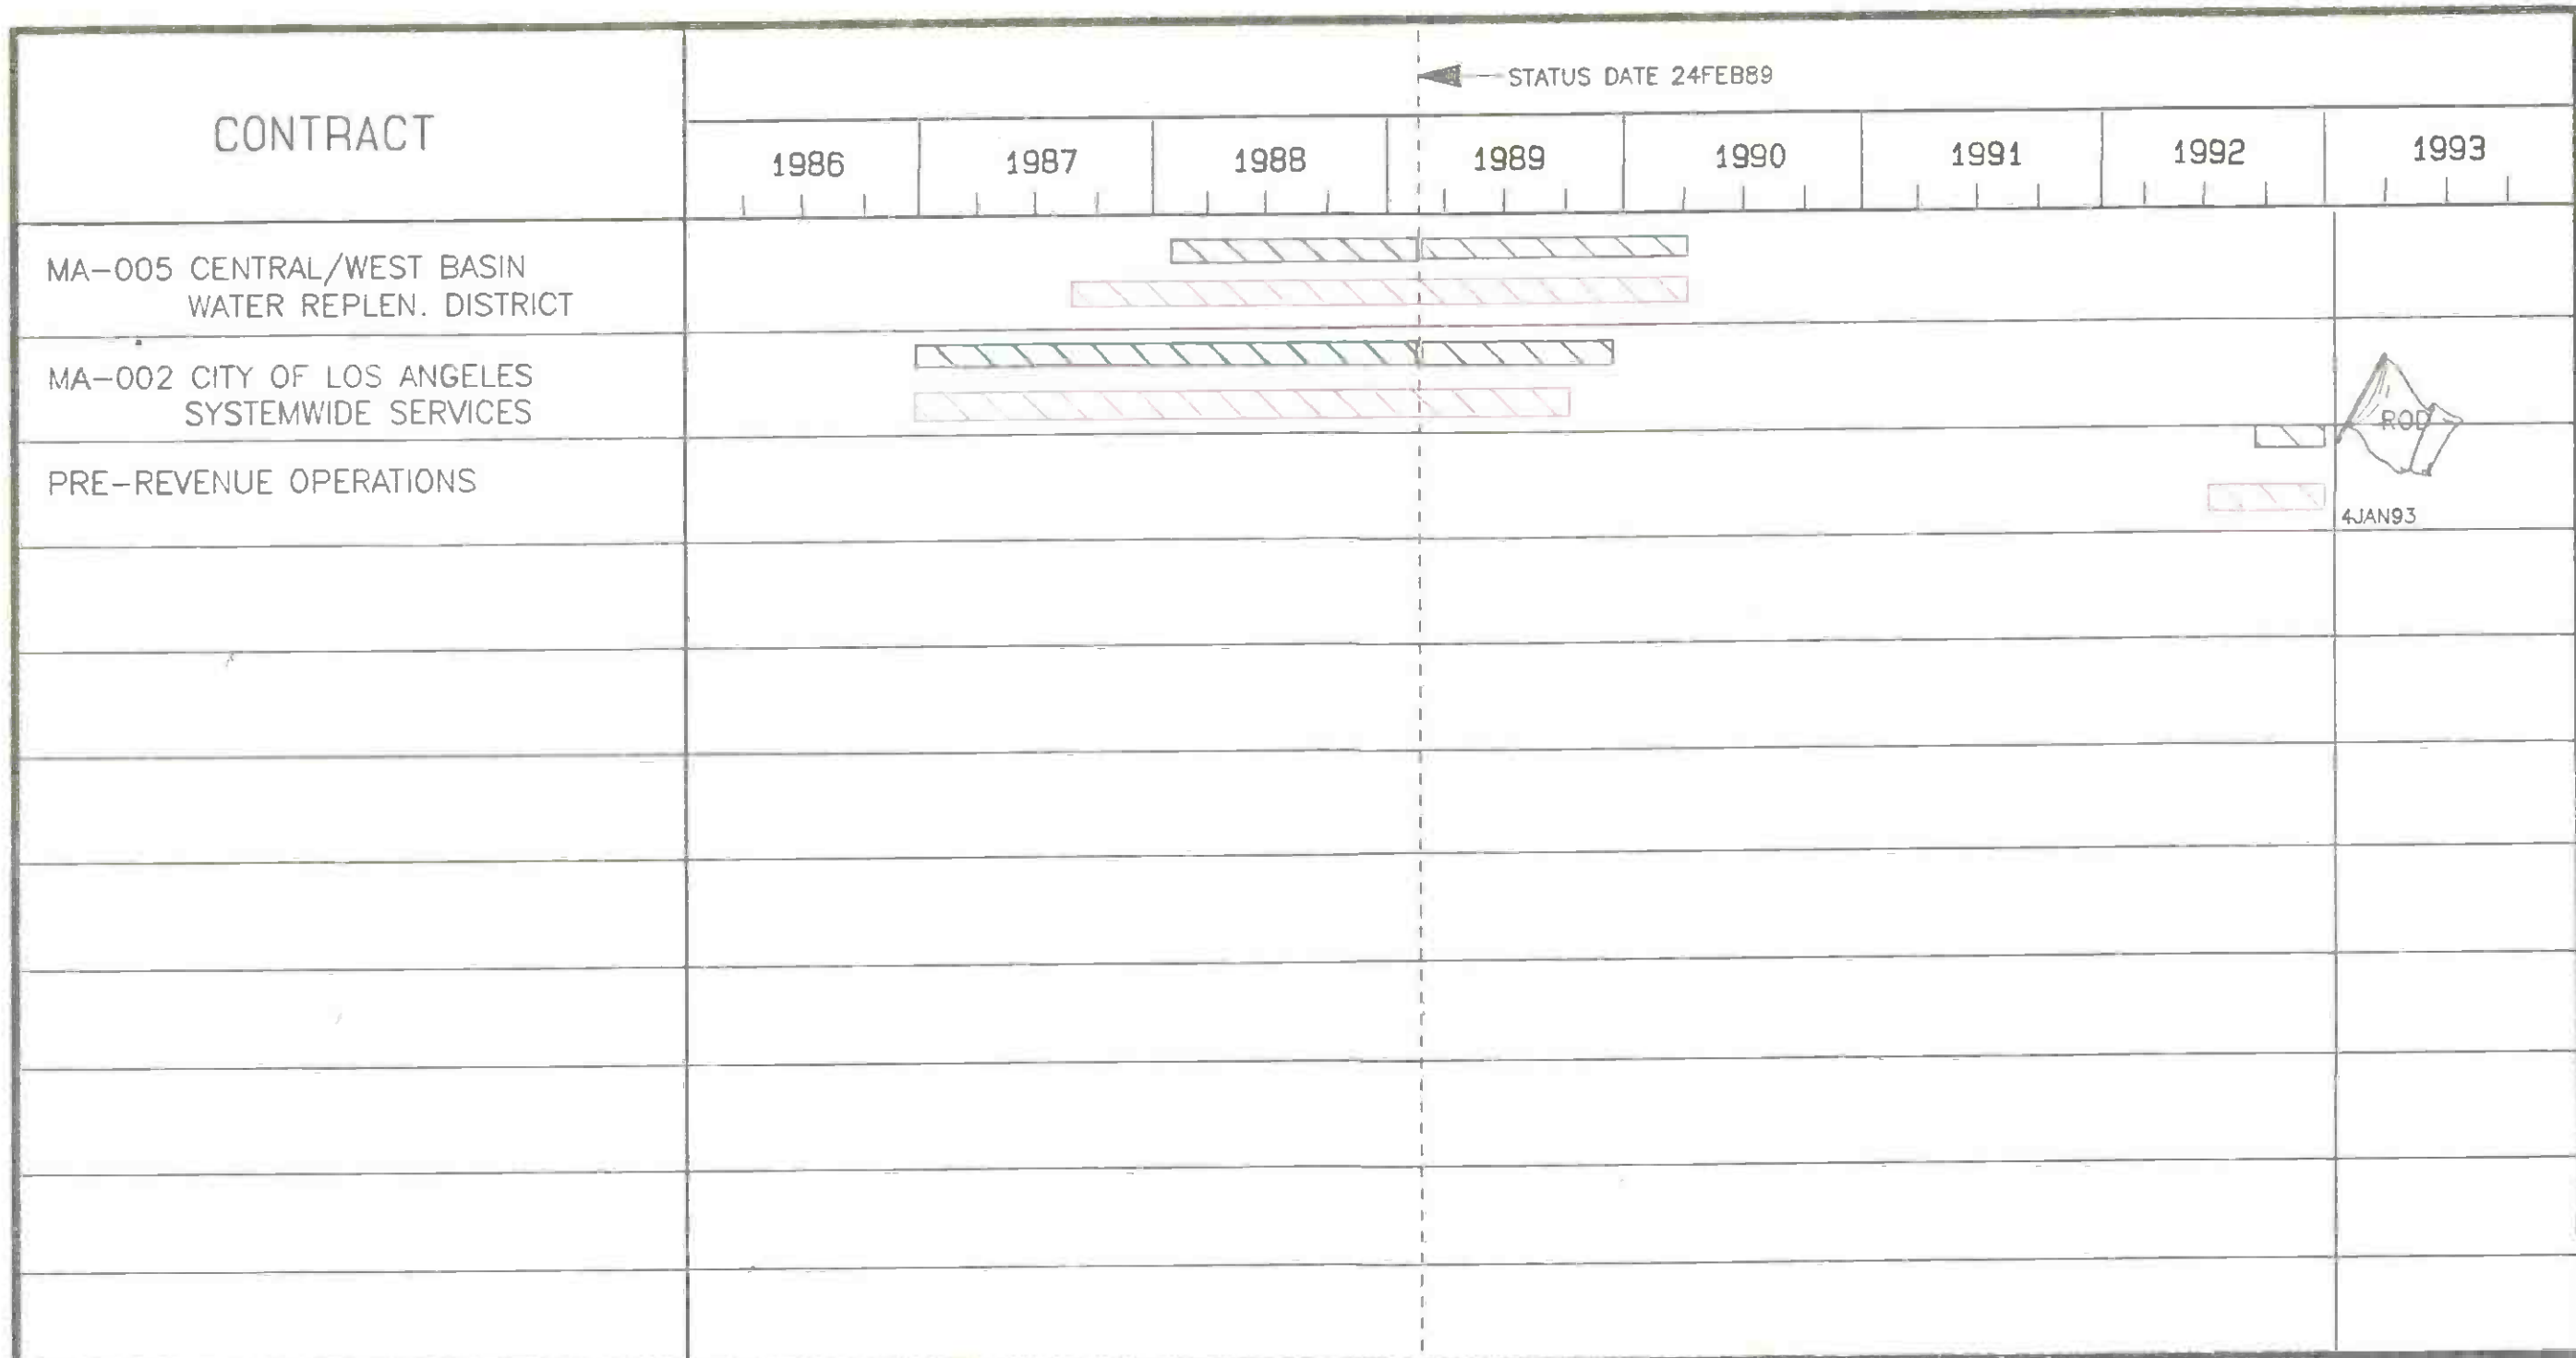

LEGEND

	CURRENT SCHEDULE	PROGRESS	APPROVED SCHEDULE
DESIGN			
BID & AWARD			
CONSTRUCTION			

RIGHT OF WAY AVAILABLE

SOUTHERN CALIFORNIA RAPID TRANSIT DISTRICT
 METRO RAIL PROJECT (MOS-1)
 EXECUTIVE SCHEDULE

PREPARED BY *TC Skerry*
PROGRAM CONTROL MANAGER (SCHEDULES)

CHECKED BY *Jeffrey Christensen*
DIRECTOR OF PROGRAM CONTROL

APPROVED BY *William J. Rho*
ASSISTANT GENERAL MANAGER

DATE	REV
25SEP86	5
14JAN88	6
30SEP88	6C
30DEC88	6D

APPENDIX
STATUS OF EXECUTIVE SCHEDULE
As of February 24, 1989

There are no schedule changes
since the January 27, 1989, Status Report.
